

Contract No. HK/2009/01

Wan Chai Development Phase II – Central -Wan Chai Bypass at
Hong Kong Convention and Exhibition Centre

Construction Activities for Three Months Rolling

Construction Activities	January 2018	February 2018	March 2018
Reinstatement of Amenity Area			

[illegible]

[illegible]

[illegible][illegible]

Activity ID	Activity Name	Rem Dur	Start	Finish	2018															
					March						April				May					
					18	25	04	11	18	25	01	08	15	22	29	06	13	20	27	
3MRP (Feb 2018 - May 2018)																				
10 - SECTION X OF THE WORKS																				
10.3 - Middle Bridge (Bridge F)																				
10.3.2 - Bridge Construction																				
Bridge F3B																				
1032-2564	Divert 2 Lane Traffic (Stage 2)	0	25-Feb-18*		◆ Divert 2 Lane Traffic (Stage 2)															
Bridge F1B2																				
1032-3880	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2	8	13-Jan-18 A	28-Feb-18	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2															
1032-3900	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking	7	01-Mar-18	08-Mar-18	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking															
Bridge F1B1																				
1032-1780	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2	15	16-Jan-18 A	08-Mar-18	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2															
1032-1800	Bridge F1B1 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking	7	09-Mar-18	16-Mar-18	Bridge F1B1 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking															
Bridge F5																				
1032-4040	Cutting of Deck Between Temp. TD & E/B > Pier F5-F8	12	26-Feb-18	10-Mar-18	Cutting of Deck Between Temp. TD & E/B > Pier F5-F8															
1032-4060	Cutting of Deck Between Temp. TD & E/B > Pier F8-F11	12	12-Mar-18	24-Mar-18	Cutting of Deck Between Temp. TD & E/B > Pier F8-F11															
1032-4080	Cutting of Deck Between Temp. TD & E/B > Pier F11-F14	12	26-Mar-18	11-Apr-18	Cutting of Deck Between Temp. TD & E/B > Pier F11-F14															
1032-4100	Construction Parapet (Northside) > Pier F5-F8	12	05-Mar-18	17-Mar-18	Construction Parapet (Northside) > Pier F5-F8															
1032-4120	Construction Parapet (Northside) > Pier F8-F11	12	19-Mar-18	03-Apr-18	Construction Parapet (Northside) > Pier F8-F11															
1032-4140	Construction Parapet (Northside) > Pier F11-F14	12	04-Apr-18	18-Apr-18	Construction Parapet (Northside) > Pier F11-F14															
1032-4160	Construct Noise Enclosure (Northside) > Pier F5 - F8	24	19-Mar-18	18-Apr-18	Construct Noise Enclosure (Northside) > Pier F5 - F8															
1032-4180	Reinstate Deck Pier F8 - F14 (Northside) > Surfacing & Marking	5	19-Apr-18	24-Apr-18	Reinstate Deck Pier F8 - F14 (Northside) > Surfacing & Marking															
1032-4200	Reinstate Deck Pier F5 - F8 (Northside) > Surfacing & Marking	5	25-Apr-18	30-Apr-18	Reinstate Deck Pier F5 - F8 (Northside) > Surfacing & Marking															
All Middle Bridge F (Common)																				
1032-4240	Fresh Water Main 150DI at Bridge F Deck	39	27-Nov-17 A	09-Apr-18	Fresh Water Main 150DI at Bridge F Deck															
1032-4260	Bridge F Sign Gantries and Misc. Mounting Structure/Support	2	26-Dec-17 A	21-Feb-18*	Bridge F Sign Gantries and Misc. Mounting Structure/Support															
1032-4356	Sign Gantry (DS06B,DS06A & FADS06) (Nigth work)	50	22-Feb-18	24-Apr-18	Sign Gantry (DS06B,DS06A & FADS06) (Nigth work)															
10.5 - Temporary Bridge																				
10.5.3 - Temporary Bridge "TD"																				
1053-1140	Demolition of Temporary Bridge "TD" at VI	32	19-Mar-18	27-Apr-18	Demolition of Temporary Bridge "TD" at VI															
10.6 - Tunnel Approach Ramp																				
10.6.1 - Approach Ramp (Excluding Portion IIB)																				
Retaining Walls & Trough Structure B,C & D																				
1061-6860	Construct Retaining Wall E Pile Cap (7 nos)	45	06-Mar-17 A	16-Apr-18	Construct Retaining Wall E Pile Cap (7 nos)															
1061-6900	Construct Retaining Wall E1 (Ch 5332 - 5371)	18	17-Apr-18	08-May-18	Construct Retaining Wall E1 (Ch 5332 - 5371)															
1061-6989	Parapet at Wall above Retaining Wall E2	14	12-Mar-18	27-Mar-18	Parapet at Wall above Retaining Wall E2															
1061-6990	Parapet at Wall above Retaining Wall E1	18	09-May-18	29-May-18	Parapet at Wall above Retaining Wall E1															
1061-7020	Falseworks System for Landscape Deck	18	29-Jan-18 A	12-Mar-18	Falseworks System for Landscape Deck															
1061-7040	Excavate for Foundation of Retaing Wall D	7	13-Mar-18	20-Mar-18	Excavate for Foundation of Retaing Wall D															
1061-7060	Construct Retaining Wall D Footing (Ch 190 - 170)	18	21-Mar-18	13-Apr-18	Construct Retaining Wall D Footing (Ch 190 - 170)															

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

◆

 Milestone

◆

 Milestone

Contract HY/2009/19

Three Months Rolling Programme (20.Feb.2018 to 19.May.2018)

Page 1 of 3

Activity ID	Activity Name	Rem Dur	Start	Finish	2018																
									March				April				May				
					18	25	04	11	18	25	01	08	15	22	29	06	13	20	27		
	1061-7080	Construct Retaining Wall D (Ch 190 - 170)	24	14-Apr-18	12-May-18																Construct Retaining Wall D (Ch
	1061-7120	Excavate to Founding Level Trough B Structure	12	21-Mar-18	06-Apr-18																Excavate to Founding Level Trough B Structure
	1061-7140	Construct Trough Structure B Base Slab	24	07-Apr-18	05-May-18																Construct Trough Structure B Base Slab
	1061-7160	Construct Trough Structure B Side Walls	24	07-May-18	02-Jun-18																
	1061-7180	Excavate to Founding Level Trough C Structure	14	28-Mar-18	16-Apr-18																Excavate to Founding Level Trough C Structure
	1061-7200	Construct Trough Structure C Base Slab	18	17-Apr-18	08-May-18																Construct Trough Structure C Base Slab
	1061-7220	Construct Trough Structure C Side Walls	24	07-May-18	02-Jun-18																
Landscape Deck																					
	1061-7420	Bay 1 to 3 > Ch 5303 - 5331 > Beam & Deck	23	03-Feb-18 A	17-Mar-18																Bay 1 to 3 > Ch 5303 - 5331 > Beam & Deck
	1061-7440	Ch 5331 - 5419 > Construct Columns (23nos)	12	29-Jan-18 A	05-Mar-18																Ch 5331 - 5419 > Construct Columns (23nos)
	1061-7460	Ch 5331 - 5419 > Beam & Deck	23	06-Mar-18	03-Apr-18																Ch 5331 - 5419 > Beam & Deck
	1061-7480	Ch 5303 - 5419 > Noise Panel Installations	32	16-Mar-18	25-Apr-18																Ch 5303 - 5419 > Noise Panel Installations
10.6.2 - Approach Ramp (Within Portion IIB)																					
Structure																					
Bay 1																					
Wall - Lower Portion																					
	A1200	Vertical Water Proofing	1	22-Feb-18	22-Feb-18																Vertical Water Proofing
	A1210	Backfilling	3	23-Feb-18	26-Feb-18																Backfilling
Wall - Upper Portion																					
	A1220	Remove S1 and S2 Strut + Waling	2	27-Feb-18	28-Feb-18																Remove S1 and S2 Strut + Waling
	A1230	Erect Working Platform and Rebar Fixing	3	01-Mar-18	03-Mar-18																Erect Working Platform and Rebar Fixing
	A1240	Erect and Formwork	3	05-Mar-18	07-Mar-18																Erect and Formwork
	A1250	Concreting	1	08-Mar-18	08-Mar-18																Concreting
	A1260	Vertical Water Proofing	1	09-Mar-18	09-Mar-18																Vertical Water Proofing
Bay 2																					
Wall - Lower Portion																					
	A1360	Vertical Water Proofing	1	22-Feb-18	22-Feb-18																Vertical Water Proofing
	A1370	Backfilling	3	23-Feb-18	26-Feb-18																Backfilling
Wall - Upper Portion																					
	A1380	Remove S1 and S2 Strut + Waling	2	27-Feb-18	28-Feb-18																Remove S1 and S2 Strut + Waling
	A1390	Erect Working Platform and Rebar Fixing	3	01-Mar-18	03-Mar-18																Erect Working Platform and Rebar Fixing
	A1400	Erect and Formwork	3	05-Mar-18	07-Mar-18																Erect and Formwork
	A1410	Concreting	1	08-Mar-18	08-Mar-18																Concreting
	A1420	Vertical Water Proofing	1	09-Mar-18	09-Mar-18																Vertical Water Proofing
Bay 3																					
Wall - Lower Portion																					
	A1500	Erect and Formwork	3	12-Feb-18 A	24-Feb-18																Erect and Formwork
	A1510	Concreting	1	26-Feb-18	26-Feb-18																Concreting
	A1520	Vertical Water Proofing	1	27-Feb-18	27-Feb-18																Vertical Water Proofing

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID		Activity Name	Rem Dur	Start	Finish	2018															
						March						April				May					
						18	25	04	11	18	25	01	08	15	22	29	06	13	20	27	
	A1530	Backfilling	3	28-Feb-18	02-Mar-18	Backfilling															
	Wall - Upper Portion																				
	A1540	Remove S1 and S2 Strut + Waling	2	03-Mar-18	05-Mar-18	Remove S1 and S2 Strut + Waling															
	A1550	Erect Working Platform and Rebar Fixing	2	06-Mar-18	07-Mar-18	Erect Working Platform and Rebar Fixing															
	A1560	Erect and Formwork	3	08-Mar-18	10-Mar-18	Erect and Formwork															
	A1570	Concreting	1	12-Mar-18	12-Mar-18	Concreting															
	A1580	Vertical Water Proofing	1	13-Mar-18	13-Mar-18	Vertical Water Proofing															
	Bay 4																				
	Wall - Lower Portion																				
	A1660	Erect and Formwork	3	12-Feb-18 A	24-Feb-18	Erect and Formwork															
	A1670	Concreting	1	26-Feb-18	26-Feb-18	Concreting															
	A1680	Vertical Water Proofing	1	27-Feb-18	27-Feb-18	Vertical Water Proofing															
	A1690	Backfilling	3	28-Feb-18	02-Mar-18	Backfilling															
	Wall - Upper Portion																				
	A1710	Remove S1 and S2 Strut + Waling	2	03-Mar-18	05-Mar-18	Remove S1 and S2 Strut + Waling															
	A1720	Erect Working Platform and Rebar Fixing	2	06-Mar-18	07-Mar-18	Erect Working Platform and Rebar Fixing															
	A1730	Erect and Formwork	3	08-Mar-18	10-Mar-18	Erect and Formwork															
	A1740	Concreting	1	12-Mar-18	12-Mar-18	Concreting															
	A1750	Vertical Water Proofing	1	13-Mar-18	13-Mar-18	Vertical Water Proofing															
	Bay 5																				
Wall - Lower Portion																					
A1810	Remove S3 and S4 Strut + Waling	2	20-Feb-18	21-Feb-18	Remove S3 and S4 Strut + Waling																
A1820	Erect Working Platform and Rebar Fixing	2	22-Feb-18	23-Feb-18	Erect Working Platform and Rebar Fixing																
A1830	Erect and Formwork	3	24-Feb-18	27-Feb-18	Erect and Formwork																
A1840	Concreting	1	28-Feb-18	28-Feb-18	Concreting																
A1850	Vertical Water Proofing	1	01-Mar-18	01-Mar-18	Vertical Water Proofing																
A1860	Backfilling	3	02-Mar-18	05-Mar-18	Backfilling																
Wall - Upper Portion																					
A1870	Remove S1 and S2 Strut + Waling	3	06-Mar-18	08-Mar-18	Remove S1 and S2 Strut + Waling																
A1880	Erect Working Platform and Rebar Fixing	2	09-Mar-18	10-Mar-18	Erect Working Platform and Rebar Fixing																
A1890	Erect and Formwork	3	12-Mar-18	14-Mar-18	Erect and Formwork																
A1900	Concreting	1	15-Mar-18	15-Mar-18	Concreting																
A1910	Vertical Water Proofing	1	16-Mar-18	16-Mar-18	Vertical Water Proofing																
Landscape Deck																					
1062-1240	Construct LD Column - Portion IIB (10nos)	36	28-Feb-18	13-Apr-18	Construct LD Column - Portion IIB (10nos)																
1062-1260	Construct Landscape Deck Beam/Slab Bay C1 & C2	45	14-Mar-18	09-May-18	Construct Landscape Deck Beam/Slab Bay C1 & C2																
1062-1280	Construct Noise Panel Trough A (within Portion IIB)	30	20-Apr-18	25-May-18	Construct Noise Panel Trough A (within Portion IIB)																

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

◆

 Milestone

◆

 Milestone

Activity ID		Activity Name			Rem Dur	Start	Finish	2018															
								April				May				June							
								18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	
3MRP (Mar 2018 - Jun 2018)																							
10 - SECTION X OF THE WORKS																							
10.3 - Middle Bridge (Bridge F)																							
10.3.2 - Bridge Construction																							
Bridge F1B2																							
1032-3880	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2				9	13-Jan-18 A	29-Mar-18	Bridge F1B2 - Construct Int. Double Noise Encl. Bridge F1B2															
1032-3900	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking				7	31-Mar-18	10-Apr-18	Bridge F1B2 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking															
Bridge F1B1																							
1032-1780	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2				9	16-Jan-18 A	29-Mar-18	Bridge F1B1 - Construct Int. Double Noise Encl. Bridge F1B2															
1032-1800	Bridge F1B1 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking				7	31-Mar-18	10-Apr-18	Bridge F1B1 - Bridge F1C Deck Road Waterproofing, Surfacing & Marking															
Bridge F5																							
1032-4080	Cutting of Deck Between Temp. TD & E/B > Pier F11-F14				6	19-Mar-18 A	26-Mar-18	Cutting of Deck Between Temp. TD & E/B > Pier F11-F14															
1032-4120	Construction Parapet (Northside) > Pier F8-F11				2	15-Mar-18 A	21-Mar-18	Construction Parapet (Northside) > Pier F8-F11															
1032-4140	Construction Parapet (Northside) > Pier F11-F14				8	22-Mar-18	31-Mar-18	Construction Parapet (Northside) > Pier F11-F14															
1032-4160	Construct Noise Enclosure (Northside) > Pier F5 - F8				10	15-Mar-18 A	31-Mar-18	Construct Noise Enclosure (Northside) > Pier F5 - F8															
1032-4180	Reinstate Deck Pier F8 - F14 (Northside) > Surfacing & Marking				5	03-Apr-18	09-Apr-18	Reinstate Deck Pier F8 - F14 (Northside) > Surfacing & Marking															
1032-4200	Reinstate Deck Pier F5 - F8 (Northside) > Surfacing & Marking				5	10-Apr-18	14-Apr-18	Reinstate Deck Pier F5 - F8 (Northside) > Surfacing & Marking															
All Middle Bridge F (Common)																							
1032-4240	Fresh Water Main 150DI at Bridge F Deck				20	27-Nov-17 A	14-Apr-18	Fresh Water Main 150DI at Bridge F Deck															
1032-4356	Sign Gantry (DS06B,DS06A & FADS06) (Nigth work)				30	22-Feb-18 A	26-Apr-18	Sign Gantry (DS06B,DS06A & FADS06) (Nigth work)															
10.5 - Temporary Bridge																							
10.5.3 - Temporary Bridge 'TD'																							
1053-1140	Demolition of Temporary Bridge "TD" at VI				32	14-Apr-18	22-May-18	Demolition of Temporary Bridge "TD" at VI															
10.6 - Tunnel Approach Ramp																							
10.6.1 - Approach Ramp (Excluding Portion IIB)																							
Retaining Walls & Trough Structure B,C & D																							
1061-6860	Construct Retaining Wal E Pile Cap (7 nos)				29	06-Mar-17 A	25-Apr-18	Construct Retaining Wal E Pile Cap (7 nos)															
1061-6900	Construct Retaining Wal E1 (Ch 5332 - 5371)				15	12-Mar-18 A	14-May-18	Construct Retaining Wal E1 (Ch 5332 - 5371)															
1061-6990	Parapet at Wall above Retaining Wall E1				15	14-Mar-18 A	31-May-18	Parapet at Wall above Retaining Wall E1															
1061-7020	Falseworks System for Landscape Deck				8	29-Jan-18 A	28-Mar-18	Falseworks System for Landscape Deck															
1061-7040	Excavate for Foundation of Retaing Wall D				7	29-Mar-18	09-Apr-18	Excavate for Foundation of Retaing Wall D															
1061-7060	Construct Retaining Wal D Footing (Ch 190 - 170)				15	10-Apr-18	26-Apr-18	Construct Retaining Wal D Footing (Ch 190 - 170)															
1061-7080	Construct Retaining Wal D (Ch 190 - 170)				18	27-Apr-18	18-May-18	Construct Retaining Wal D (Ch 190 - 170)															
1061-7100	Backfilling Works				12	19-May-18	01-Jun-18	Backfilling Works															
1061-7120	Excavate to Founding Level Trough B Structure				12	31-Mar-18	16-Apr-18	Excavate to Founding Level Trough B Structure															
Remaining Level of Effort Actual Level of Effort Actual Work					Remaining Work Critical Remaining Work Milestone																		
Contract HY/2009/19																							
Three Months Rolling Programme (20.Mar.2018 to 19.Jun.2018)																							
Page 1 of 3																							

Activity ID	Activity Name	Rem Dur	Start	Finish	2018															
					March		April				May				June					
					18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	
1061-7140	Construct Trough Structure B Base Slab	18	17-Apr-18	08-May-18																
1061-7160	Construct Trough Structure B Side Walls	18	09-May-18	29-May-18																
1061-7180	Excavate to Founding Level Trough C Structure	12	10-Apr-18	23-Apr-18																
1061-7200	Construct Trough Structure C Base Slab	15	24-Apr-18	11-May-18																
1061-7220	Construct Trough Structure C Side Walls	18	10-May-18	30-May-18																
1061-7240	Road & other Misc Works at Trough D	12	02-Jun-18	15-Jun-18																
Landscape Deck																				
1061-7460	Ch 5331 - 5419 > Beam & Deck	14	19-Feb-18 A	07-Apr-18																
1061-7480	Ch 5303 - 5419 > Noise Panel Installations	32	19-Apr-18	26-May-18																
10.6.2 - Approach Ramp (Within Portion IIB)																				
Structure																				
Bay 1																				
Wall - Upper Portion																				
A1220	Remove S1 and S2 Strut + Waling	4	03-Apr-18	07-Apr-18																
A1260	Vertical Water Proofing	2	09-Apr-18	10-Apr-18																
Bay 2																				
Wall - Upper Portion																				
A1380	Remove S1 and S2 Strut + Waling	4	03-Apr-18	07-Apr-18																
A1420	Vertical Water Proofing	2	09-Apr-18	10-Apr-18																
Bay 3																				
Wall - Upper Portion																				
A1540	Remove S1 and S2 Strut + Waling	4	03-Apr-18	07-Apr-18																
A1580	Vertical Water Proofing	2	09-Apr-18	10-Apr-18																
Bay 4																				
Wall - Upper Portion																				
A1710	Remove S1 and S2 Strut + Waling	4	03-Apr-18	07-Apr-18																
A1750	Vertical Water Proofing	2	09-Apr-18	10-Apr-18																
Bay 5																				
Wall - Lower Portion																				
A1830	Erect and Formwork	3	19-Mar-18 A	22-Mar-18																
A1840	Concreting	1	23-Mar-18	23-Mar-18																
A1850	Vertical Water Proofing	1	24-Mar-18	24-Mar-18																
A1860	Backfilling	3	26-Mar-18	28-Mar-18																
Wall - Upper Portion																				
A1870	Remove S1 and S2 Strut + Waling	4	03-Apr-18	07-Apr-18																

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

◆

 ◆ Milestone

Activity ID	Activity Name	Rem Dur	Start	Finish	2018															
					March				April				May				June			
					18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	
A1880	Erect Working Platform and Rebar Fixing	2	24-Mar-18	26-Mar-18	Erect Working Platform and Rebar Fixing															
	A1890	Erect and Formwork	3	27-Mar-18	29-Mar-18	Erect and Formwork														
	A1900	Concreting	1	31-Mar-18	31-Mar-18	Concreting														
	A1910	Vertical Water Proofing	2	09-Apr-18	10-Apr-18	Vertical Water Proofing														
Landscape Deck																				
1062-1240	Construct LD Column - Portion IIB (10nos)	9	12-Mar-18 A	29-Mar-18	Construct LD Column - Portion IIB (10nos)															
1062-1260	Construct Landscape Deck Beam/Slab Bay C1 & C2	18	14-Mar-18 A	12-Apr-18	Construct Landscape Deck Beam/Slab Bay C1 & C2															
1062-1280	Construct Noise Panel Trough A (within Portion IIB)	30	20-Apr-18	25-May-18					Construct Noise Panel Trough A (within Portion IIB)											
Road Works																				
1062-1300	Approach Ramp Road Drainage (within Portion IIB)	24	12-May-18	08-Jun-18					Approach Ramp Road Drainage (within Portion IIB)											
1062-1320	Approach Ramp Profile Barrier (within Portion IIB)	24	12-May-18	08-Jun-18					Approach Ramp Profile Barrier (within Portion IIB)											
1062-1340	Approach Ramp Street Furniture (within Portion IIB)	24	12-May-18	08-Jun-18					Approach Ramp Street Furniture (within Portion IIB)											
1062-1360	Approach Ramp TCSS/E&M Ducts and Supports (within Portion IIB)	24	12-May-18	08-Jun-18					Approach Ramp TCSS/E&M Ducts and Supports (within Portion IIB)											
1062-1380	Approach Ramp Road Surfacing & Marking (within Portion IIB)	10	09-Jun-18	21-Jun-18									Approach Ramp Road Surfacing & Marking (within Portion IIB)							

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

SR8_DWP_R08-02 MU59			SR8 - Layout for 3MRP_2108_02			Appendix C.5																	
Activity ID		Activity Name	Original Duration	Start	Finish	2018																	
						Feb			Mar			Apr			May			Jun					
Total			1876d	21-Mar-13 A	21-Jun-18																		
DWP-08 - (2) - Update Progress As of 20 Feb 18			1876d	21-Mar-13 A	21-Jun-18																		
Works in KD8			24d	05-Feb-18 A	27-Feb-18 A																		
TS3W - Remove Temporary Reclamation			24d	05-Feb-18 A	27-Feb-18 A																		
Stage 7 - Remove D-wall W4D13, 14 & W4D12, W4D15 - 16 + W3D8 - W3D11 & Seawall Reinstatement			24d	05-Feb-18 A	27-Feb-18 A																		
Reinstatement of Remaining Vertical Seawall by Land Plants			24d	05-Feb-18 A	27-Feb-18 A																		
MW_1610	Pour concrete behind 5th layer of facing stone		1d	05-Feb-18 A	05-Feb-18 A	te behind 5th layer of facing stone																	
MW_1630	Erect Formwork for coping		3d	06-Feb-18 A	09-Feb-18 A	t Formwork for coping																	
MW_1640	Pour concrete for coping		1d	10-Feb-18 A	10-Feb-18 A	ur concrete for coping																	
MW_1660	Lay footpath paving blocks		4d	11-Feb-18 A	14-Feb-18 A	■ Lay footpath paving blocks																	
MW_1650	Backfill up to formation level (6 layers)		13d	26-Feb-18 A	27-Feb-18 A	■ Backfill up to formation level (6 layers)																	
Works in KD6			132d	30-Aug-17 A	20-Mar-18																		
Works in SR8 (Open Cut Method)			132d	30-Aug-17 A	20-Mar-18																		
SR8 (Zone C) - Ch. 528 to Ch. 368			74d	30-Aug-17 A	20-Mar-18																		
Zone C - Tunnel Structure			74d	30-Aug-17 A	20-Mar-18																		
Egress Passage - EP01			74d	30-Aug-17 A	20-Mar-18																		
A9050	Steel Railing - Fabrication & Installation		74d	30-Aug-17 A	20-Mar-18	■ Steel Railing - Fabrication & Installation																	
SR8 (Zone B) - Ch.385.000 to Ch.317.500 - (Inside Victoria Park to Tunnel Portal)			16d	21-Feb-18 A	16-Mar-18																		
SR8 (Zone B) Tunnel - ELS / CCT / BF Works (7 Bays Ch. 385.000 to Ch.317.500)			16d	21-Feb-18 A	16-Mar-18																		
Portal Structure			16d	21-Feb-18 A	16-Mar-18																		
Pump House			7d	21-Feb-18 A	28-Feb-18 A																		
Remaining Works inside Pump Sump E			7d	21-Feb-18 A	28-Feb-18 A																		
Pump Sump E Hand Rail			7d	21-Feb-18 A	28-Feb-18 A																		
EXW_2530	Installation of handrail (agreed with CC contract)		7d	21-Feb-18 A	28-Feb-18 A	■ Installation of handrail (agreed with CC contract)																	
Remaining Works in Zone B			15d	28-Feb-18 A	16-Mar-18																		
Egress Passage			15d	28-Feb-18 A	16-Mar-18																		
EXW_2550	Railing installation (2 nos. - 10m)		15d	28-Feb-18 A	16-Mar-18	■ Railing installation (2 nos. - 10m)																	
Works in KD9 (Include Re-provisioning Works of KD4,KD5)			185d	23-Oct-17 A	15-May-18																		
External Works Under KD9			185d	25-Oct-17 A	15-May-18																		
Zone 1			90d	15-Dec-17 A	27-Mar-18																		
Drainage Alignment Confirmation for MH72, 73, 74 due to Tree T1106			90d	15-Dec-17 A	27-Mar-18																		
EXW_1125	Drawing Confirmation and construction for MH2-74A and asociated drainage		8d	15-Dec-17 A	25-Mar-18	■ Drawing Confirmation and construction for MH2-74A and asociated drainage																	
EXW_1145	Pedestrian walkway open to public during Christmas and CNY		90d	23-Jan-18 A	27-Mar-18	■ Pedestrian walkway open to public during Christmas and CNY																	
Zone 2			35d	25-Oct-17 A	04-Apr-18																		
EXW_1890	Irrigation system construction		15d	25-Oct-17 A	04-Apr-18	■ Irrigation system construction																	
EXW_1880	Boundary fence Installation		30d	01-Nov-17 A	04-Apr-18	■ Boundary fence Installation																	
Zone 3			35d	03-Mar-18	16-Apr-18																		
Traffic Island			35d	03-Mar-18	16-Apr-18																		
EXW_2050	Directional sign DS17 steel frame		7d	03-Mar-18*	10-Mar-18	■ Directional sign DS17 steel frame																	
EXW_2060	New VMS6 steel frame		7d	12-Mar-18	19-Mar-18	■ New VMS6 steel frame																	
EXW_2070	TCSS and lighting at island		7d	20-Mar-18	26-Mar-18	■ TCSS and lighting at island																	
EXW_2080	JTIS (3 nos. footings, 1 no. concrete plinth)		14d	27-Mar-18	16-Apr-18	■ JTIS (3 nos. footings, 1 no. concrete plinth)																	
Zone 4 up to Elderly Facilities			90d	30-Jan-18 A	15-May-18																		

Activity ID	Activity Name	Original Duration	Start	Finish	2018											
					Feb	Mar			Apr			May			Jun	
Elderly Facilities V/039 Received on 22 Jun 2017		90d	30-Jan-18 A	15-May-18												
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	15-May-18	Facilities fabrication											
Additional Walkway & Arbour V/040 Received on 22 Aug 2017		60d	15-Feb-18 A	12-Apr-18												
EXW_2300	Arbour confirmation and fabrication	60d	15-Feb-18 A	16-Mar-18	Arbour confirmation and fabrication											
EXW_2310	Assiciated drainage works for the walkway	20d	17-Mar-18	12-Apr-18	Assiciated drainage works for the walkway											
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		98d	18-Jan-18 A	05-May-18												
TTA Revert Traffic Back to Original Alignment		86d	18-Jan-18 A	23-Apr-18												
East Bound TTA - IEC East Bound, Victoria Park Road & footpath along Sea Side		45d	31-Jan-18 A	05-Apr-18												
TTM Stage 1 - IEC (East Bound)		6d	28-Feb-18	05-Mar-18												
Reinstatement Existing Structure		6d	28-Feb-18	05-Mar-18												
EB_1020	Install metal parapet on parapet wall (30m)	6d	28-Feb-18	05-Mar-18	Install metal parapet on parapet wall (30m)											
TTM Stage 2 - Revert Traffic back to Original Victoria Road		4d	06-Mar-18	09-Mar-18												
Existing Bridge Parapet Reinstatement		4d	06-Mar-18	09-Mar-18												
EB_1180	Install metal parapet on parapet wall (40m)	4d	06-Mar-18	09-Mar-18	Install metal parapet on parapet wall (40m)											
TTM Stage 3 - Reinstatement of Footpath along Seafront		45d	31-Jan-18 A	05-Apr-18												
Reinstatement Works in Traffic Deck Part A		31d	31-Jan-18 A	19-Mar-18												
EB_1540	Break two concrete footings	2d	31-Jan-18 A	16-Mar-18	Break two concrete footings											
EB_1520	Break pipe piles and cut sheet pile	6d	10-Feb-18 A	26-Feb-18 A	Break pipe piles and cut sheet pile											
EB_1530	Backfill Subbase material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)	3d	17-Mar-18	19-Mar-18	Backfill Subbase material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)											
Reinstatement of Existing Gas Main		17d	20-Mar-18	05-Apr-18												
EB_1560	Excavation for DN400mm Gas main	3d	20-Mar-18	22-Mar-18	Excavation for DN400mm Gas main											
EB_1570	Laying DN400mm gas main by HKCG at VPR footpath	14d	23-Mar-18	05-Apr-18	Laying DN400mm gas main by HKCG at VPR footpath											
West Bound - IEC West Bound & Tsing fung Street		86d	18-Jan-18 A	23-Apr-18												
TTM Stage 2 - Revert Traffic back to Original Tsing Fung Street		5d	28-Feb-18	04-Mar-18												
Existing Bridge Parapet Reinstatement		5d	28-Feb-18	04-Mar-18												
IECW_1140	Install metal parapet on parapet wall (60m)	5d	28-Feb-18	04-Mar-18	Install metal parapet on parapet wall (60m)											
TTM Stage 3 - Reinstatement of Victoria Park		86d	18-Jan-18 A	23-Apr-18												
Reinstatement Works in Traffic Deck		48d	18-Jan-18 A	16-Mar-18												
IECW_1390	Cut pipe piles and sheet pile	5d	18-Jan-18 A	13-Mar-18	Cut pipe piles and sheet pile											
IECW_1400	Backfill General Fill Material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)	3d	14-Mar-18	16-Mar-18	Backfill General Fill Material up to Formation Level (Avg. 1.5m height, by SRT method of 0.3m each layer, 5 layers)											
Reinstatement Works inside Victoria Park		60d	29-Jan-18 A	23-Apr-18												
IECW_1440	Reinstatement of Boundary Fence	21d	29-Jan-18 A	17-Mar-18	Reinstatement of Boundary Fence											
IECW_1460	Cutting sheet pile to 1.5m below finish slope profile (MS 169B)	10d	19-Mar-18	28-Mar-18	Cutting sheet pile to 1.5m below finish slope profile (MS 169B)											
IECW_1470	Slope Reinstatement of Victoria Park	21d	26-Mar-18	23-Apr-18	Slope Reinstatement of Victoria Park											
Completion of Minor Outstanding / Remaining Works for KD9		67d	28-Feb-18	05-May-18												
West Bound - Completion of Minor Outstanding / Remaining Works for KD9		67d	28-Feb-18	05-May-18												
Minor Reinstatement Works for Tsing Fung Street		13d	18-Mar-18	30-Mar-18												
IECW_1530	Laying Public Lighting duct	6d	18-Mar-18	23-Mar-18	Laying Public Lighting duct											
IECW_1540	Installation of public lighting post and connection by HyD	7d	24-Mar-18	30-Mar-18	Installation of public lighting post and connection by HyD											
IECW_1550	Well compact road formation level and subbase for SRT	6d	24-Mar-18	29-Mar-18	Well compact road formation level and subbase for SRT											
Minor Reinstatement Works in IEC West Bound		67d	28-Feb-18	05-May-18												
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	28-Feb-18	07-Mar-18	Replacement of new movement joint at IEC W/B (Sun midnight only)											
IECW_1630	Repairing of 300 dia. concrete pipeline by lining under slow lane of IEC W/B	2d	28-Feb-18*	01-Mar-18	Repairing of 300 dia. concrete pipeline by lining under slow lane of IEC W/B											
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	59d	08-Mar-18	05-May-18	Repairing of extg conc deck surface after milling of ten											




中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Date	Revision	Checked	Approved
20-Feb-18	DWP-08 (2) - 3 Months Rolling	TL	TL

Activity ID		Activity Name	Original Duration	Start	Finish	2018																	
						Feb			Mar			Apr			May			Jun					
Works in Victoria Park (KD4, KD5, KD9)			155d	23-Oct-17 A	24-Apr-18																		
Re-Provisioning Works			155d	23-Oct-17 A	24-Apr-18																		
Nursery Compound			155d	23-Oct-17 A	24-Apr-18																		
Nursery compound			155d	23-Oct-17 A	24-Apr-18																		
ABWF			115d	23-Oct-17 A	29-Mar-18																		
Finishes & Waterproofing			97d	23-Oct-17 A	20-Mar-18																		
VP_NC_1500	External wall tile cleaning	3d	23-Oct-17 A	20-Mar-18	External wall tile cleaning																		
VP_NC_1420	Painting to wall & ceiling in general (final coat)	4d	15-Mar-18*	19-Mar-18	Painting to wall & ceiling in general (final coat)																		
Switch room Cut-out Frame & Chequer Plate			1d	13-Feb-18 A	14-Feb-18 A																		
VP_NC_1690	Installation	1d	13-Feb-18 A	14-Feb-18 A	Installation																		
Signage			7d	21-Feb-18 A	28-Feb-18 A																		
VP_NC_1720	Installation	7d	21-Feb-18 A	28-Feb-18 A	Installation																		
Metal Fence			27d	15-Jan-18 A	29-Mar-18																		
VP_NC_1820	Installation	30d	15-Jan-18 A	29-Mar-18	Installation																		
E&M			14d	09-Feb-18 A	14-Feb-18 A																		
VP_NC_1890	Form WR1 submission	7d	09-Feb-18 A	13-Feb-18 A	Form WR1 submission																		
VP_NC_1900	Expected power on date	7d	14-Feb-18 A	14-Feb-18 A	Expected power on date																		
Fire Srevices			43d	22-Dec-17 A	10-Mar-18																		
VP_NC_1960	Pump and water pipe installation	10d	22-Dec-17 A	10-Mar-18	Pump and water pipe installation																		
VP_NC_1980	Hose Reel installation, Breakglass and Alarm	3d	10-Feb-18 A	13-Feb-18 A	Hose Reel installation, Breakglass and Alarm																		
VP_NC_1930	FS pipe connection from u/g to water meter room	2d	24-Feb-18 A	28-Feb-18 A	FS pipe connection from u/g to water meter room																		
Plimbing and Flushing Water Supplies			14d	30-Jan-18 A	15-Mar-18																		
VP_NC_2080	Cleaning of potable water pipe and sampling to WSD	7d	17-Feb-18 A	26-Feb-18 A	Cleaning of potable water pipe and sampling to WSD																		
VP_NC_2100	WSD Inspection	14d	28-Feb-18	15-Mar-18	WSD Inspection																		
GRP Water Tank Installation			7d	30-Jan-18 A	06-Feb-18 A																		
VP_NC_2130	Final As-fitted drawing submisison to WSD	7d	30-Jan-18 A	06-Feb-18 A	ted drawing submisison to WSD																		
External Works Aside Nursery Compound			75d	30-Jan-18 A	24-Apr-18																		
Drainage			45d	30-Jan-18 A	16-Mar-18																		
VP_NC_2150	U channel at toilet	2d	30-Jan-18 A	31-Jan-18 A	om u channel																		
VP_NC_2190	SS angle to shower room u channel	1d	31-Jan-18 A	31-Jan-18 A																			
VP_NC_2140	Drainage work at External area	15d	28-Feb-18	16-Mar-18	Drainage work at External area																		
Water Works			15d	07-Feb-18 A	27-Feb-18 A																		
VP_NC_2220	FS Fresh & Salt Water, Fresh Water and Irrigation System	15d	07-Feb-18 A	27-Feb-18 A	FS Fresh & Salt Water, Fresh Water and Irrigation System																		
External Works Around Nursery Compond			45d	28-Feb-18	24-Apr-18																		
VP_NC_2250	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound	45d	28-Feb-18	24-Apr-18	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound																		
KD10 - Preservation and Protection of Trees			1088d	21-Mar-13 A	21-Jun-18																		
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	21-Jun-18																			
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)			979d	15-May-14 A	28-Feb-18																		
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	28-Feb-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS																		

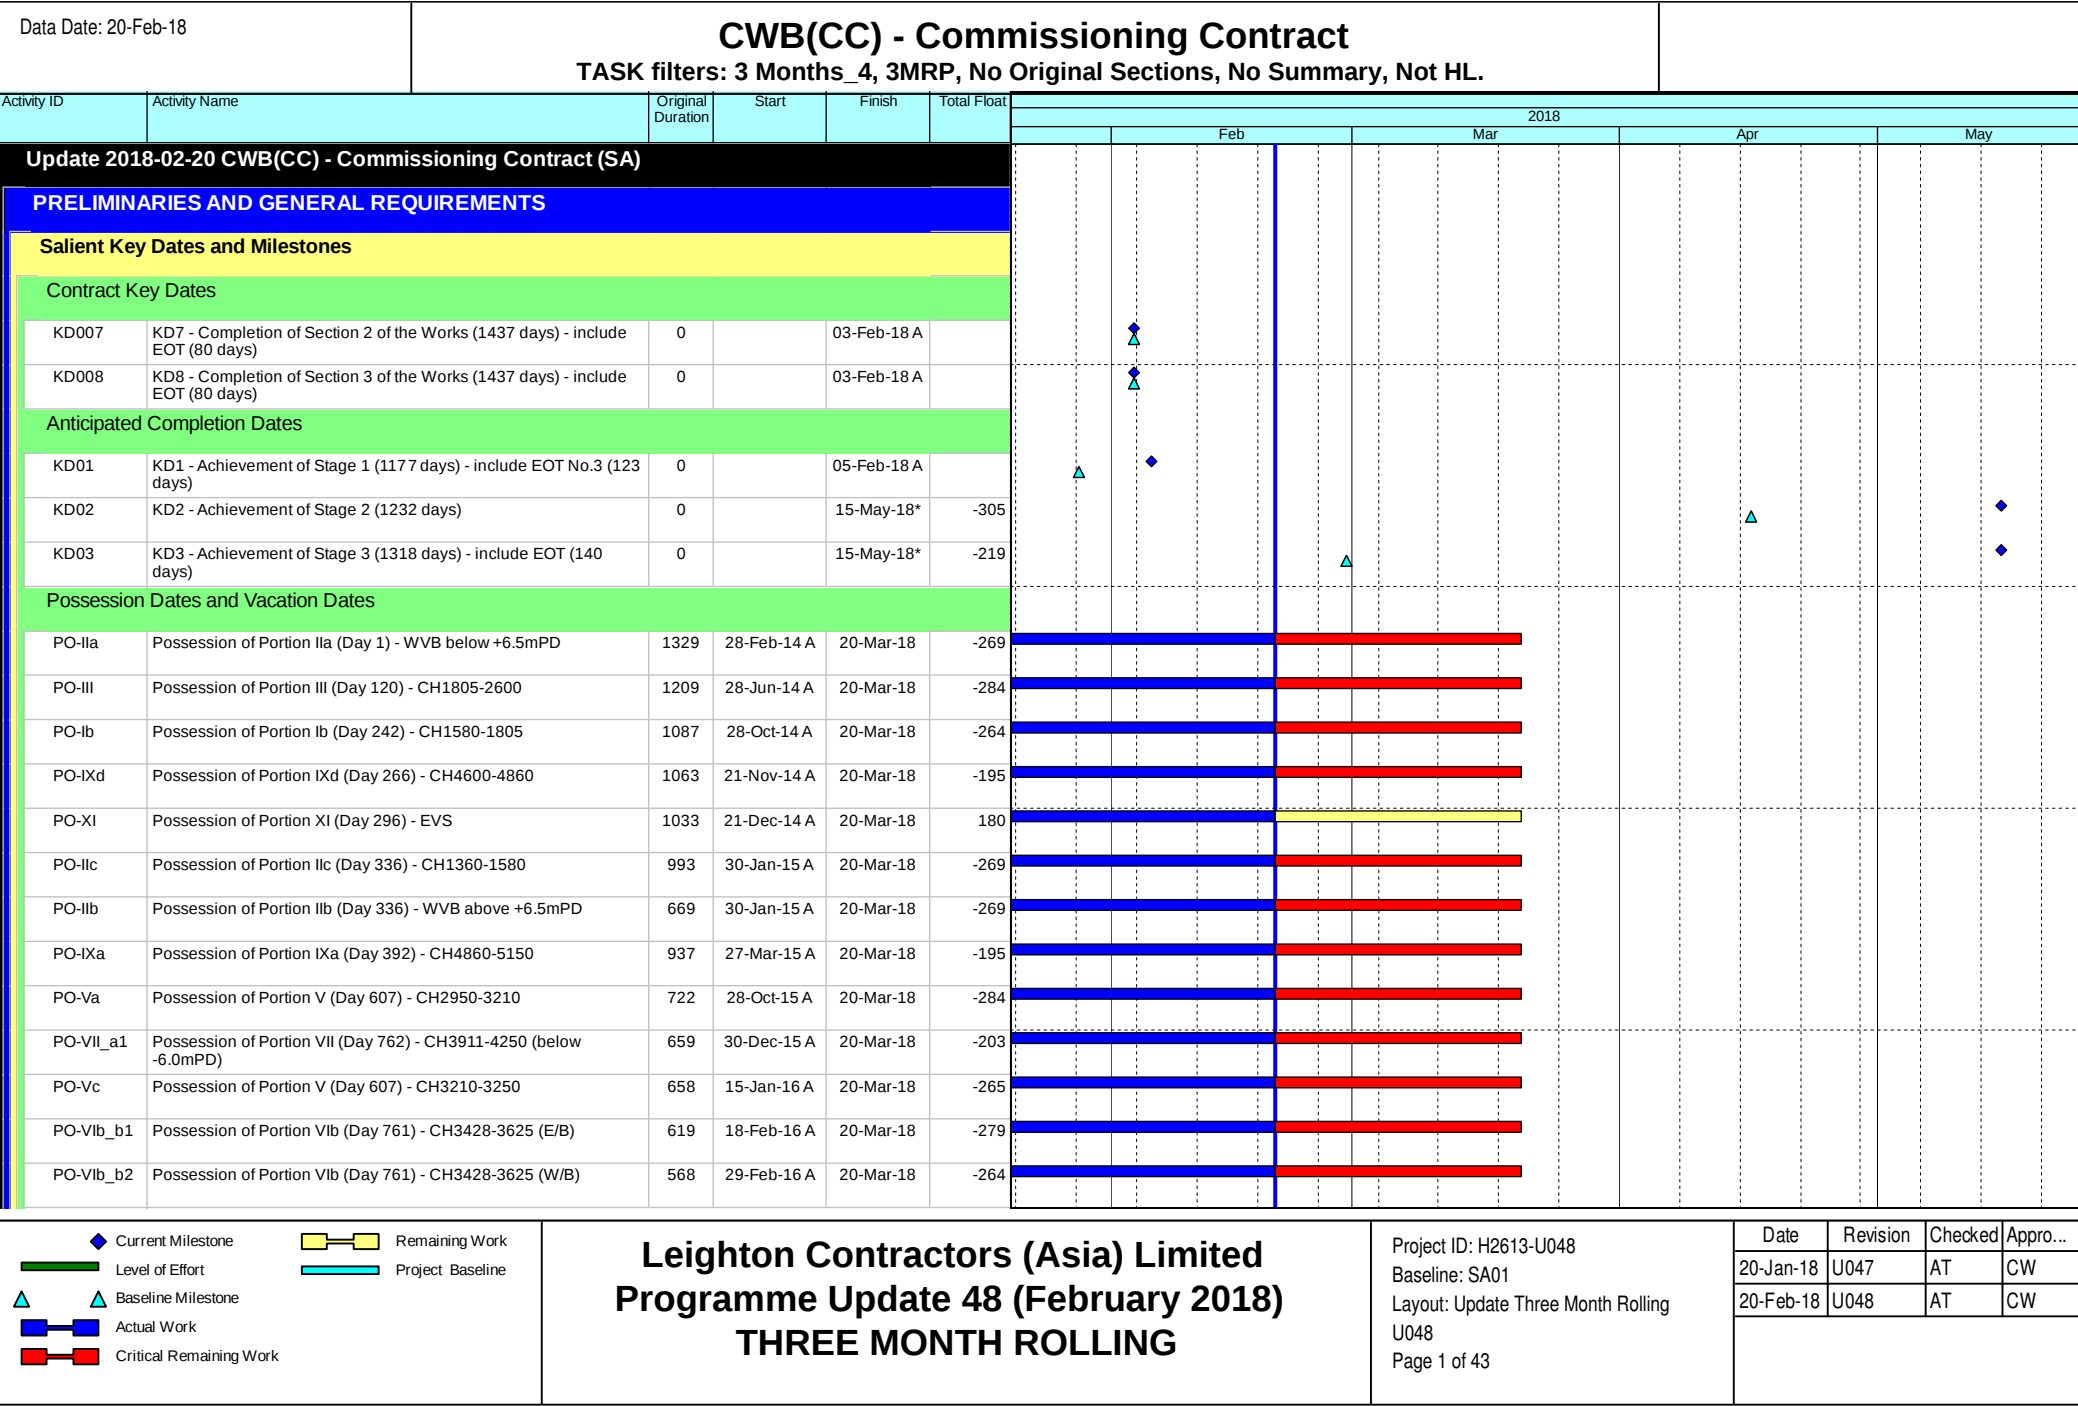

Data Date: 20-Feb-18			CWB(CC) - Commissioning Contract																
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																			
Activity ID	Activity Name		Original Duration	Start	Finish	Total Float	2018												
							Feb			Mar			Apr			May			
	PO-Xa_1		Possession of Portion Xa (Day 650) - ADB Southern Portion (AECOM letter ref: 2015007890T)	589	07-Mar-16 A	20-Mar-18	-323												
	PO-Xb_1		Possession of Portion Xb (Day 804) - ADB Northern Portion	589	07-Mar-16 A	20-Mar-18	-323												
	PO-Vb1		Possession of Portion V (Day 607) - SR3	587	11-Mar-16 A	20-Mar-18	180												
	PO-Ia		Possession of Portion Ia (Day 789) - SCB / SCP1 / SCP2 / Rumsey Street Flyover	600	28-Mar-16 A	20-Mar-18	-307												
	PO-VII_a2		Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	20-Mar-18	-250												
	PO-IXc_1		Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	20-Mar-18	-274												
	PO-IXb_1		Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	20-Mar-18	-274												
	PO-VIa_a		Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	20-Mar-18	-269												
	PO-Vb2_a		Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	20-Mar-18	-265												
	PO-VIc_a		Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	20-Mar-18	-264												
	PO-VIb_c		Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	20-Mar-18	-279												
	PO-IVa1		Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	20-Mar-18	-271												
	PO-IVb2		Possession of Portion IVb (Day 930) - MVB (GL D-H)	233	28-Feb-17 A	20-Mar-18	-320												
	PO-VIIIa_a		Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	20-Mar-18	-245												
	PO-VIIIa		Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	20-Mar-18	-245												
	PO-VIIIb		Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	20-Mar-18	-192												
	PO-VIIIc		Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	20-Mar-18	-241												
	PO-IVa2_a		Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	20-Mar-18	-267												
	PO-IVb1		Possession of Portion IVb (Day 930) - MVB (GL A-C)	239	14-Mar-17 A	20-Mar-18	-320												
	PO-IVa2_b		Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	20-Mar-18	-267												
	PO-Vb2_b		Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	20-Mar-18	-265												
	PO-VIb_a		Possession of Portion VIb (Day 761) - CH3400-3428	80	31-Jul-17 A	20-Mar-18	-264												
	PO-VIa_b		Possession of Portion VIa (Day 823) - CH3283-3400	80	31-Jul-17 A	20-Mar-18	-284												
	PO-IVc		Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Feb-18	10-Jun-18	-262												


Current Milestone
 Level of Effort
 Baseline Milestone
 Actual Work
 Critical Remaining Work


Remaining Work
 Project Baseline

Leighton Contractors (Asia) Limited
Programme Update 48 (February 2018)
THREE MONTH ROLLING

Project ID: H2613-U048
Baseline: SA01
Layout: Update Three Month Rolling
U048
Page 2 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW


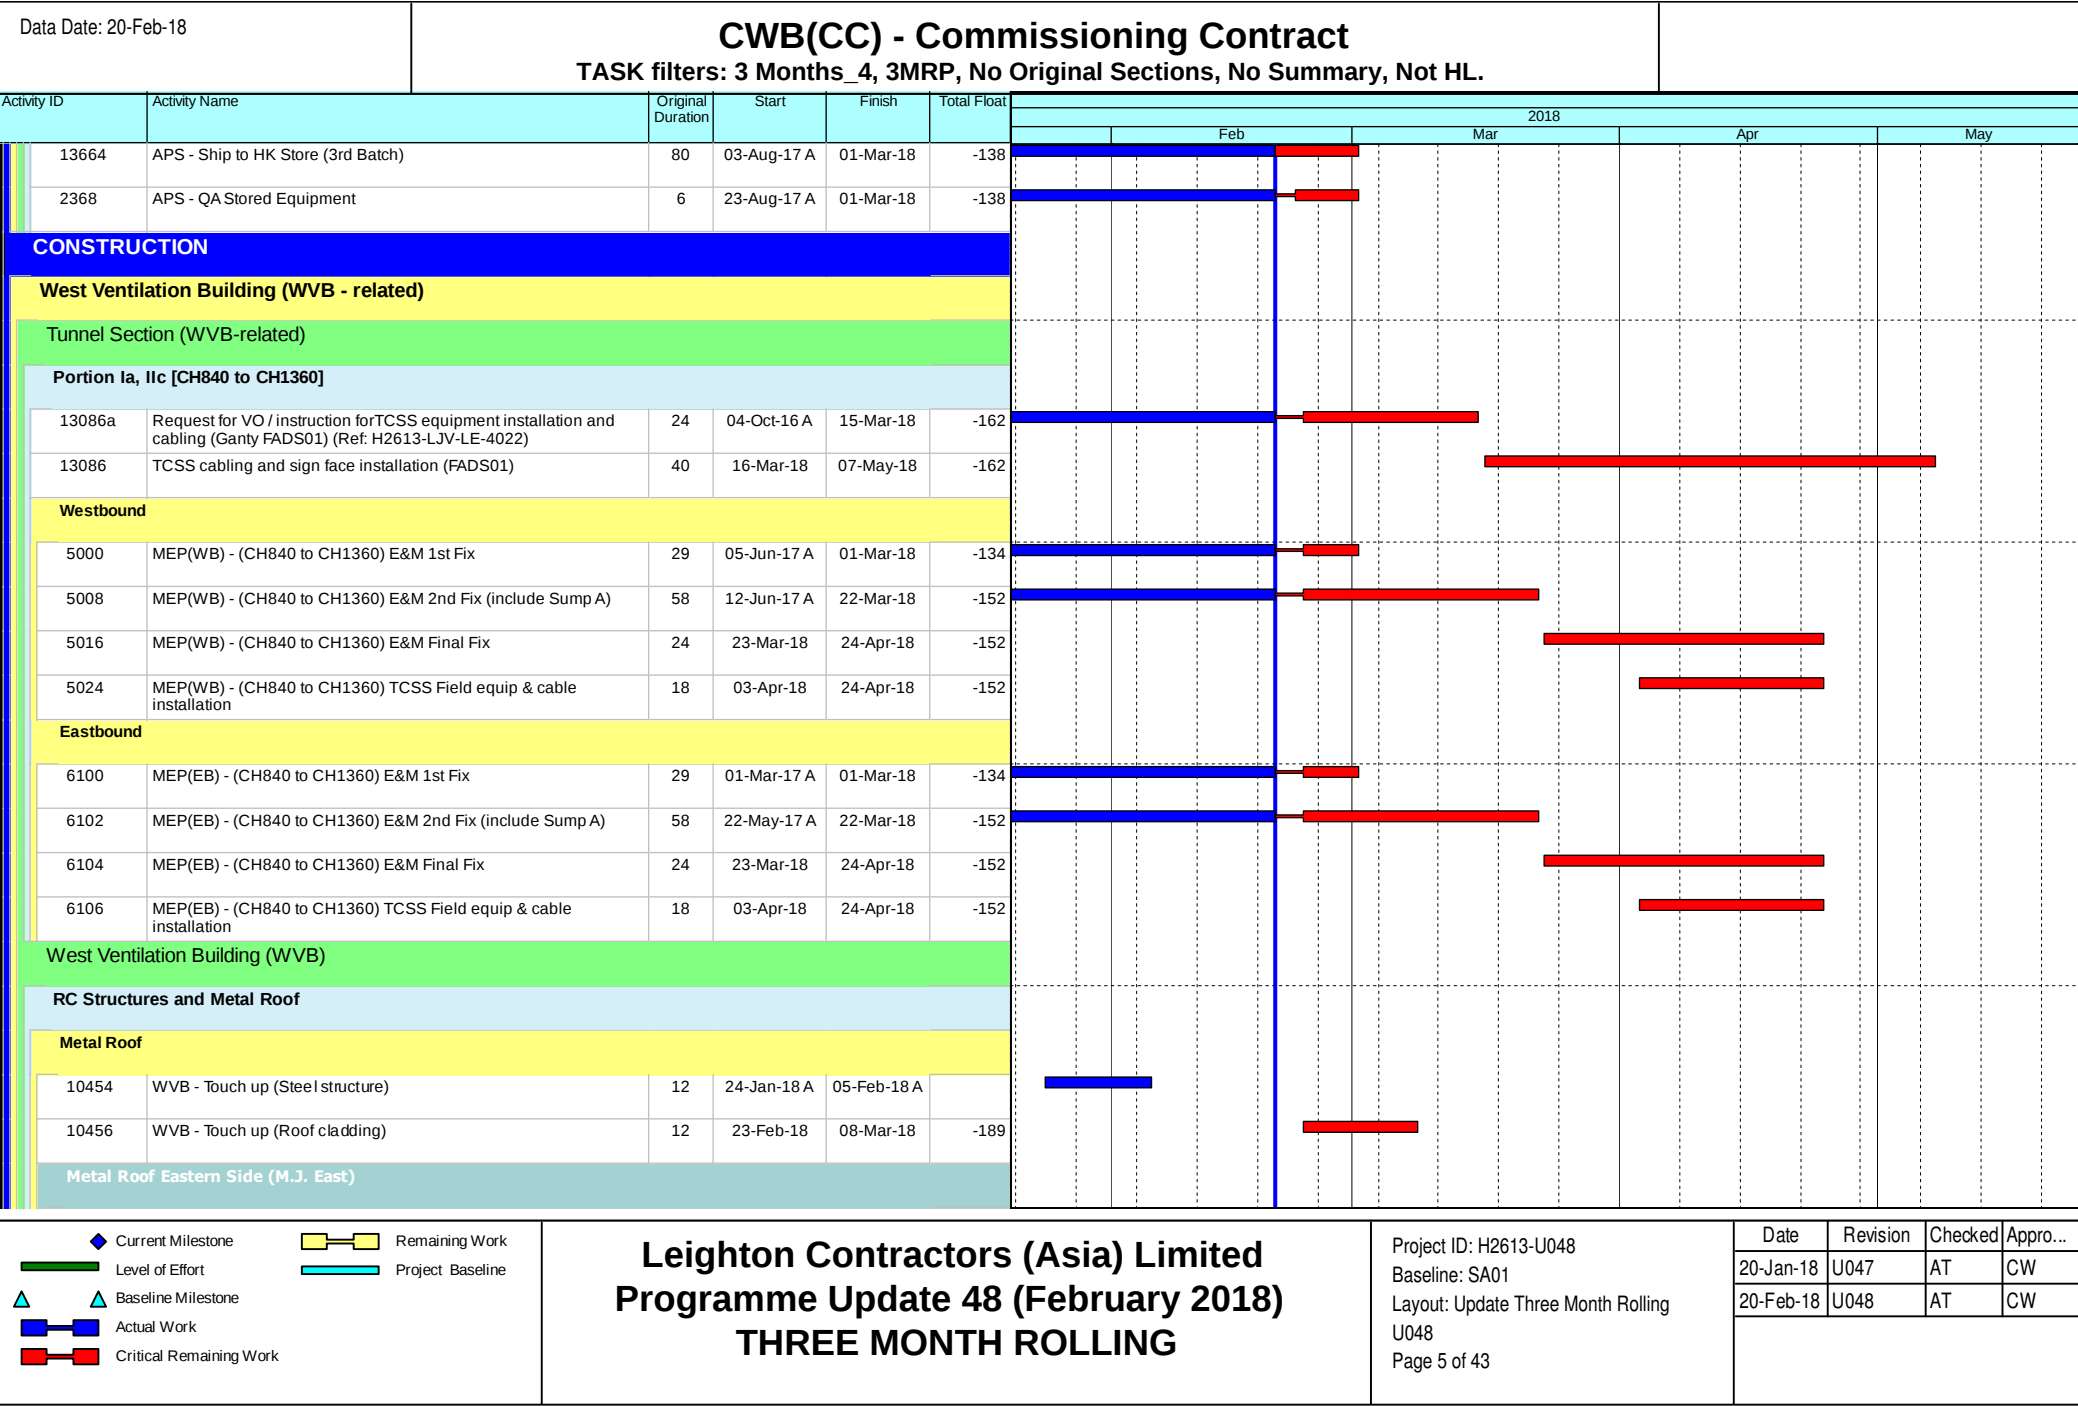


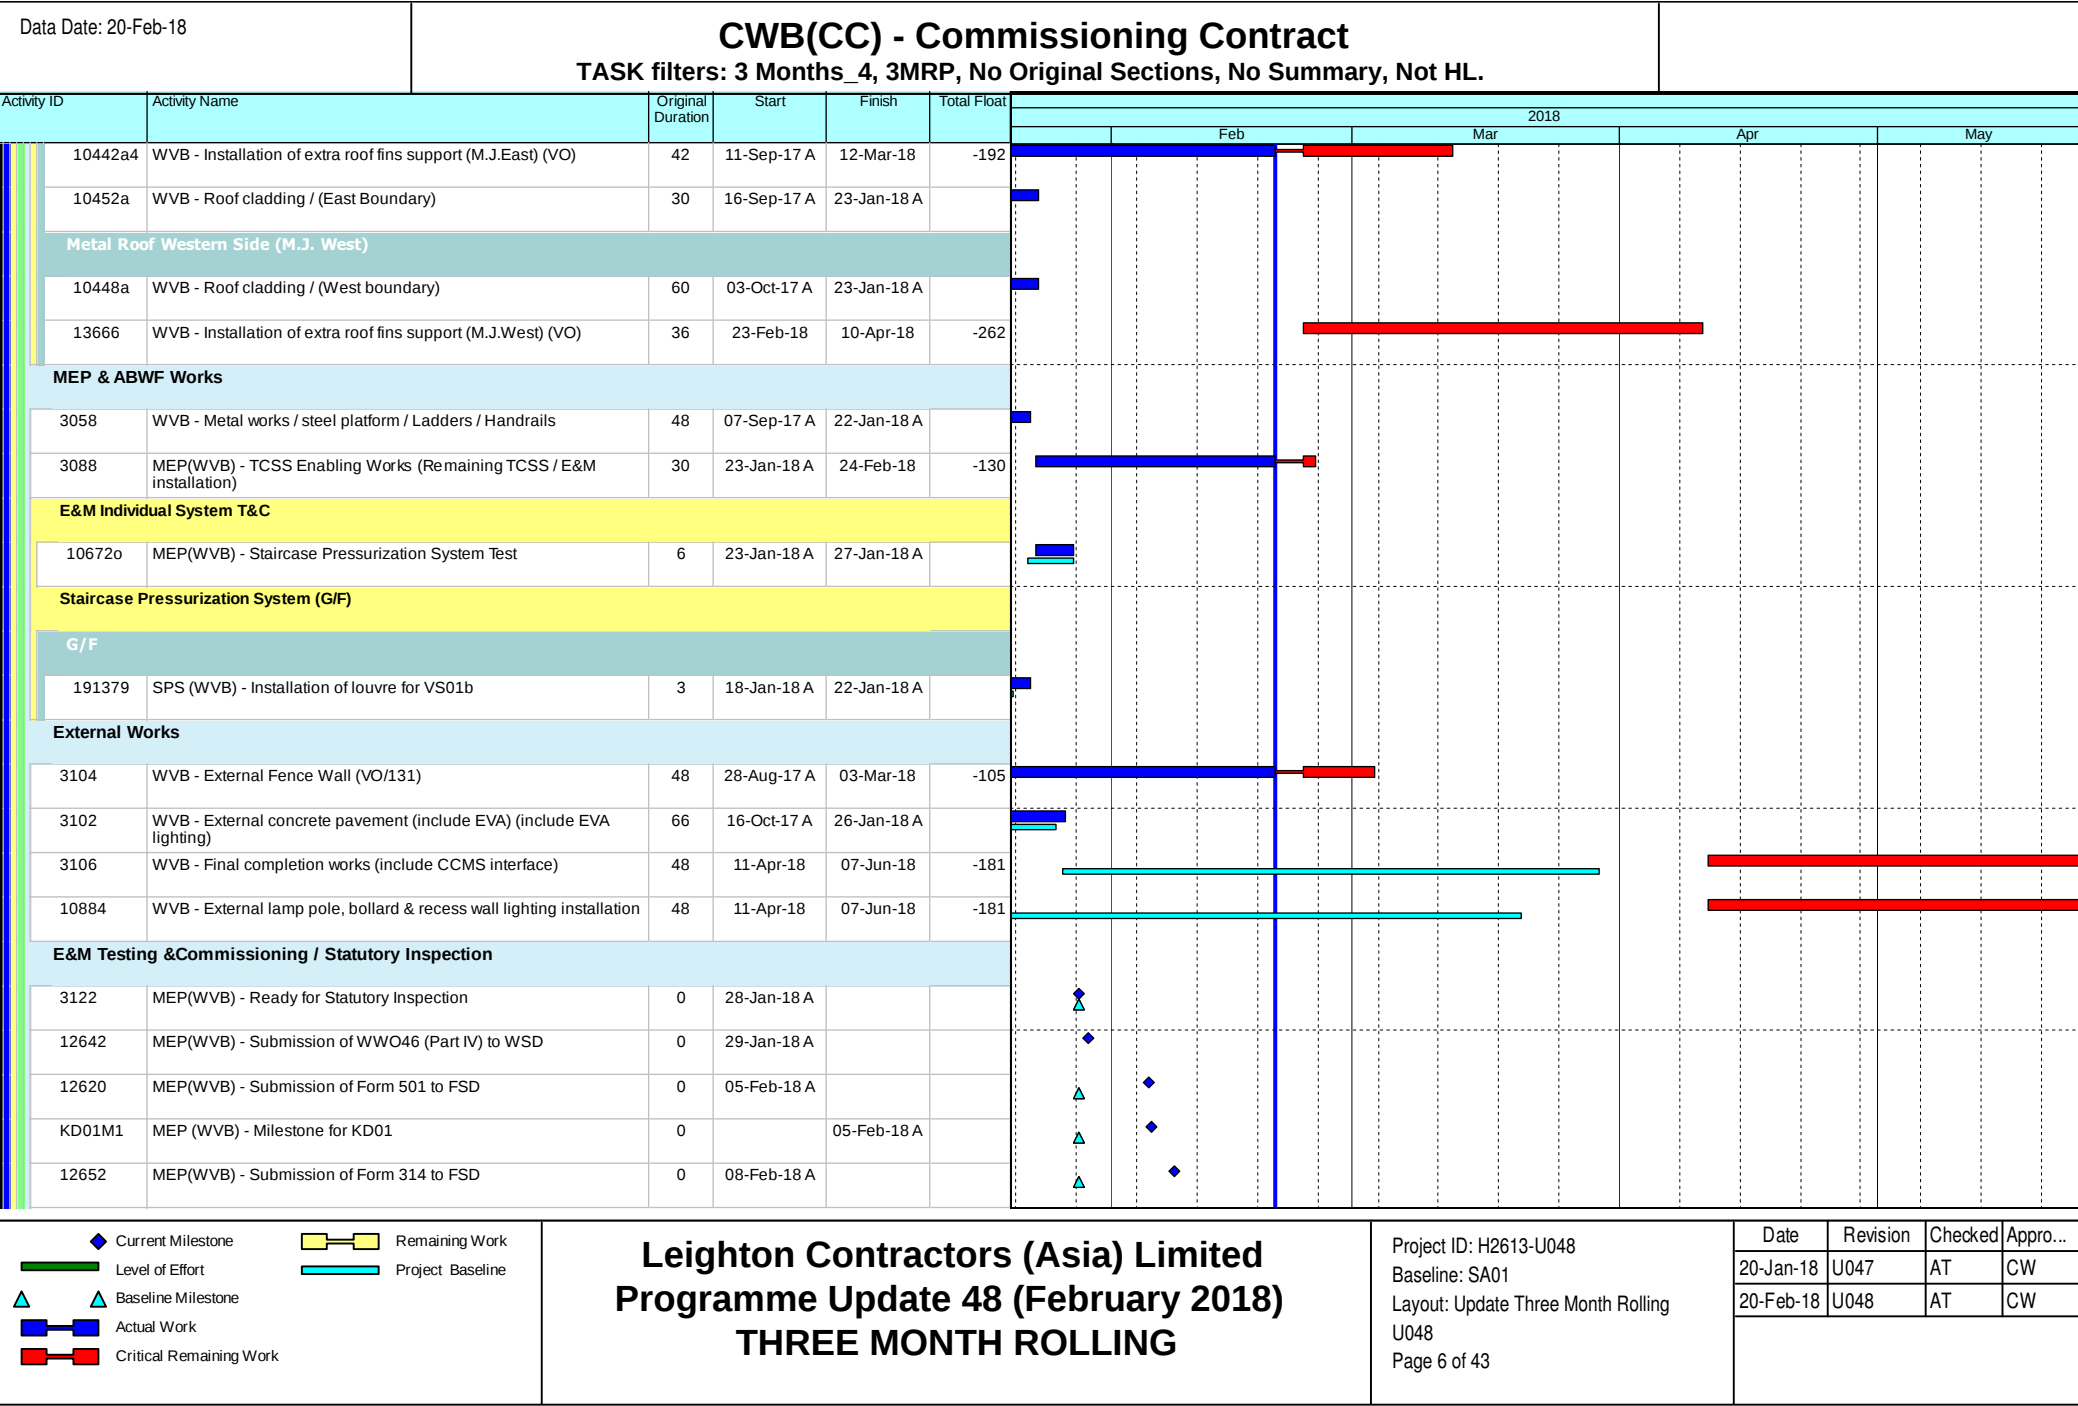

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

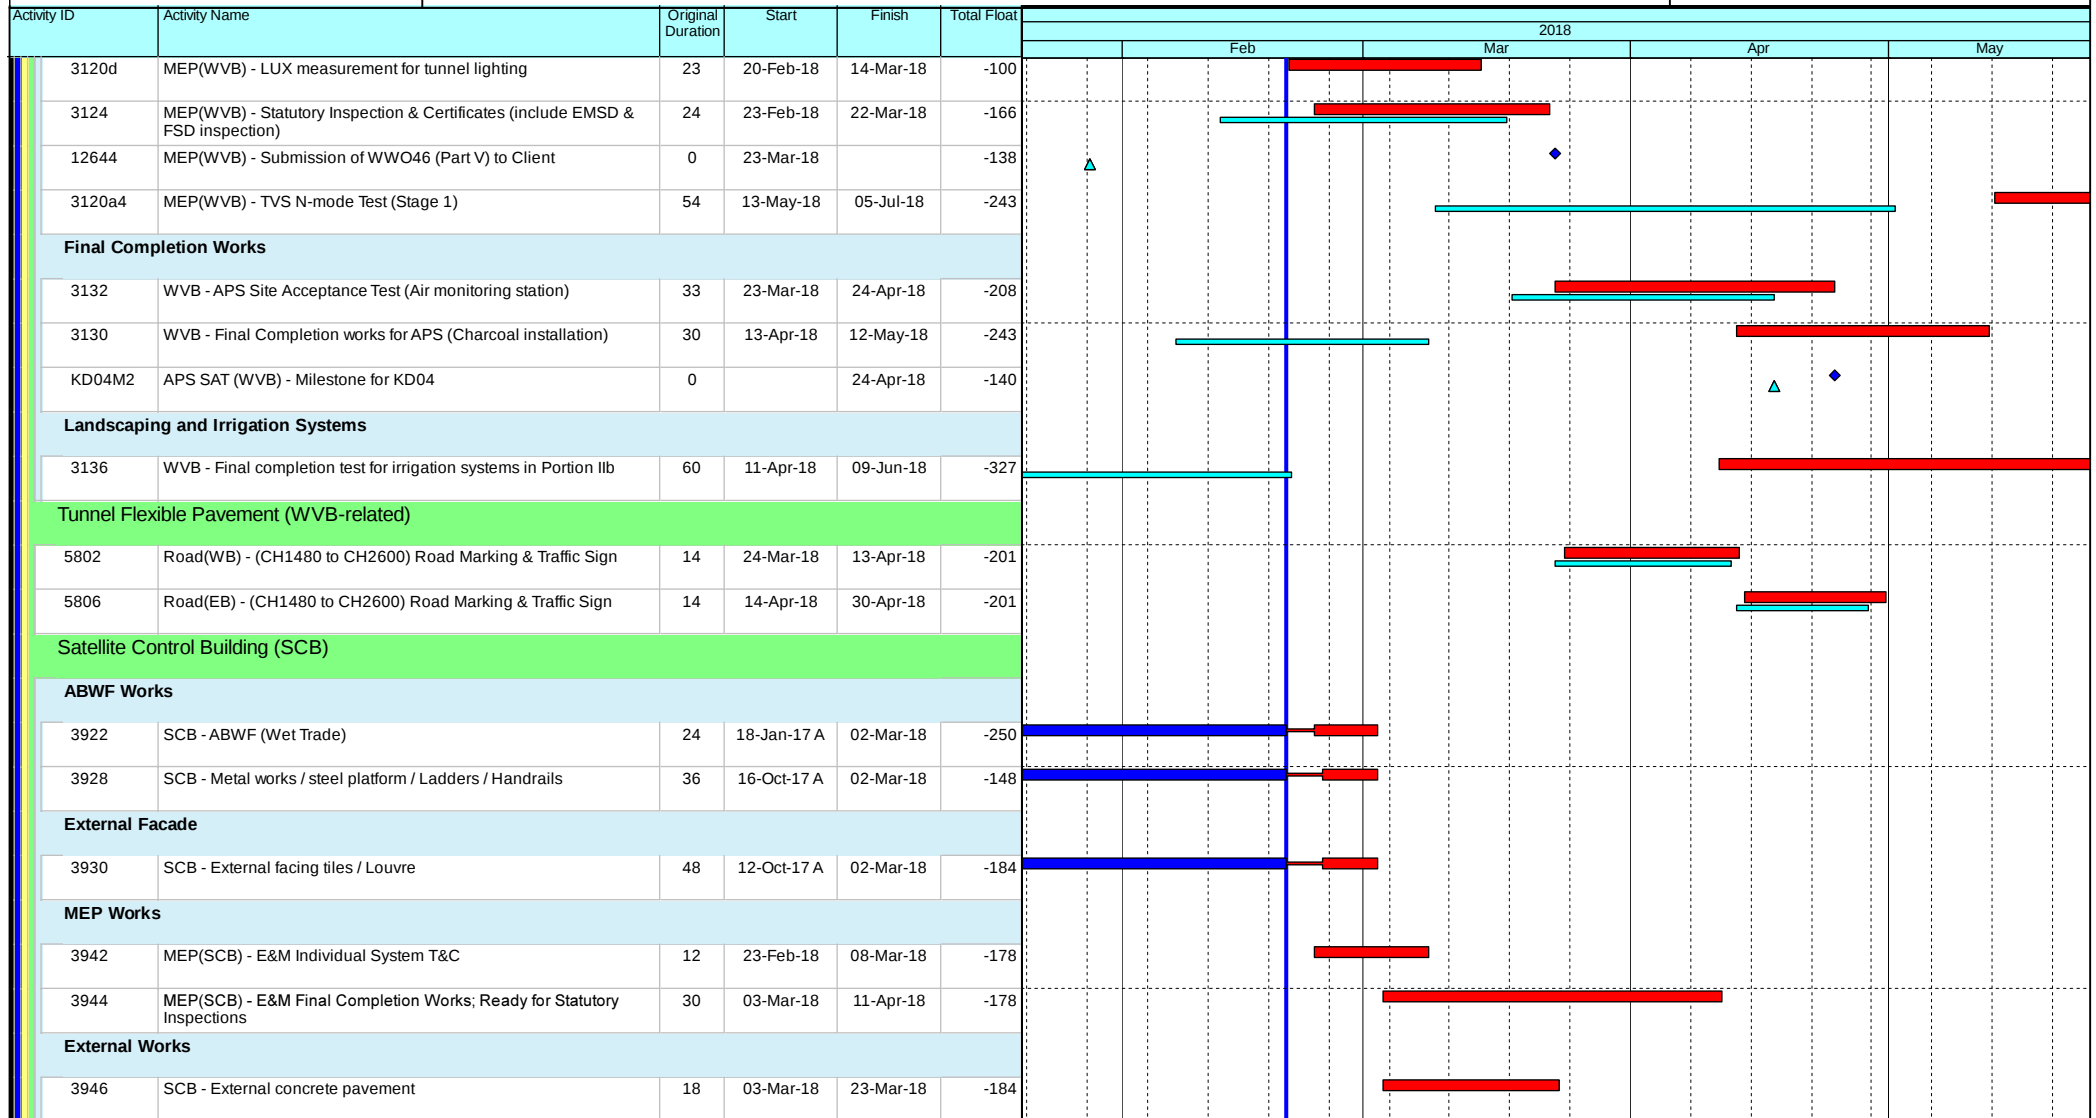


Leighton Contractors (Asia) Limited


Programme Update 48 (February 2018)


THREE MONTH ROLLING


Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 7 of 43


Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

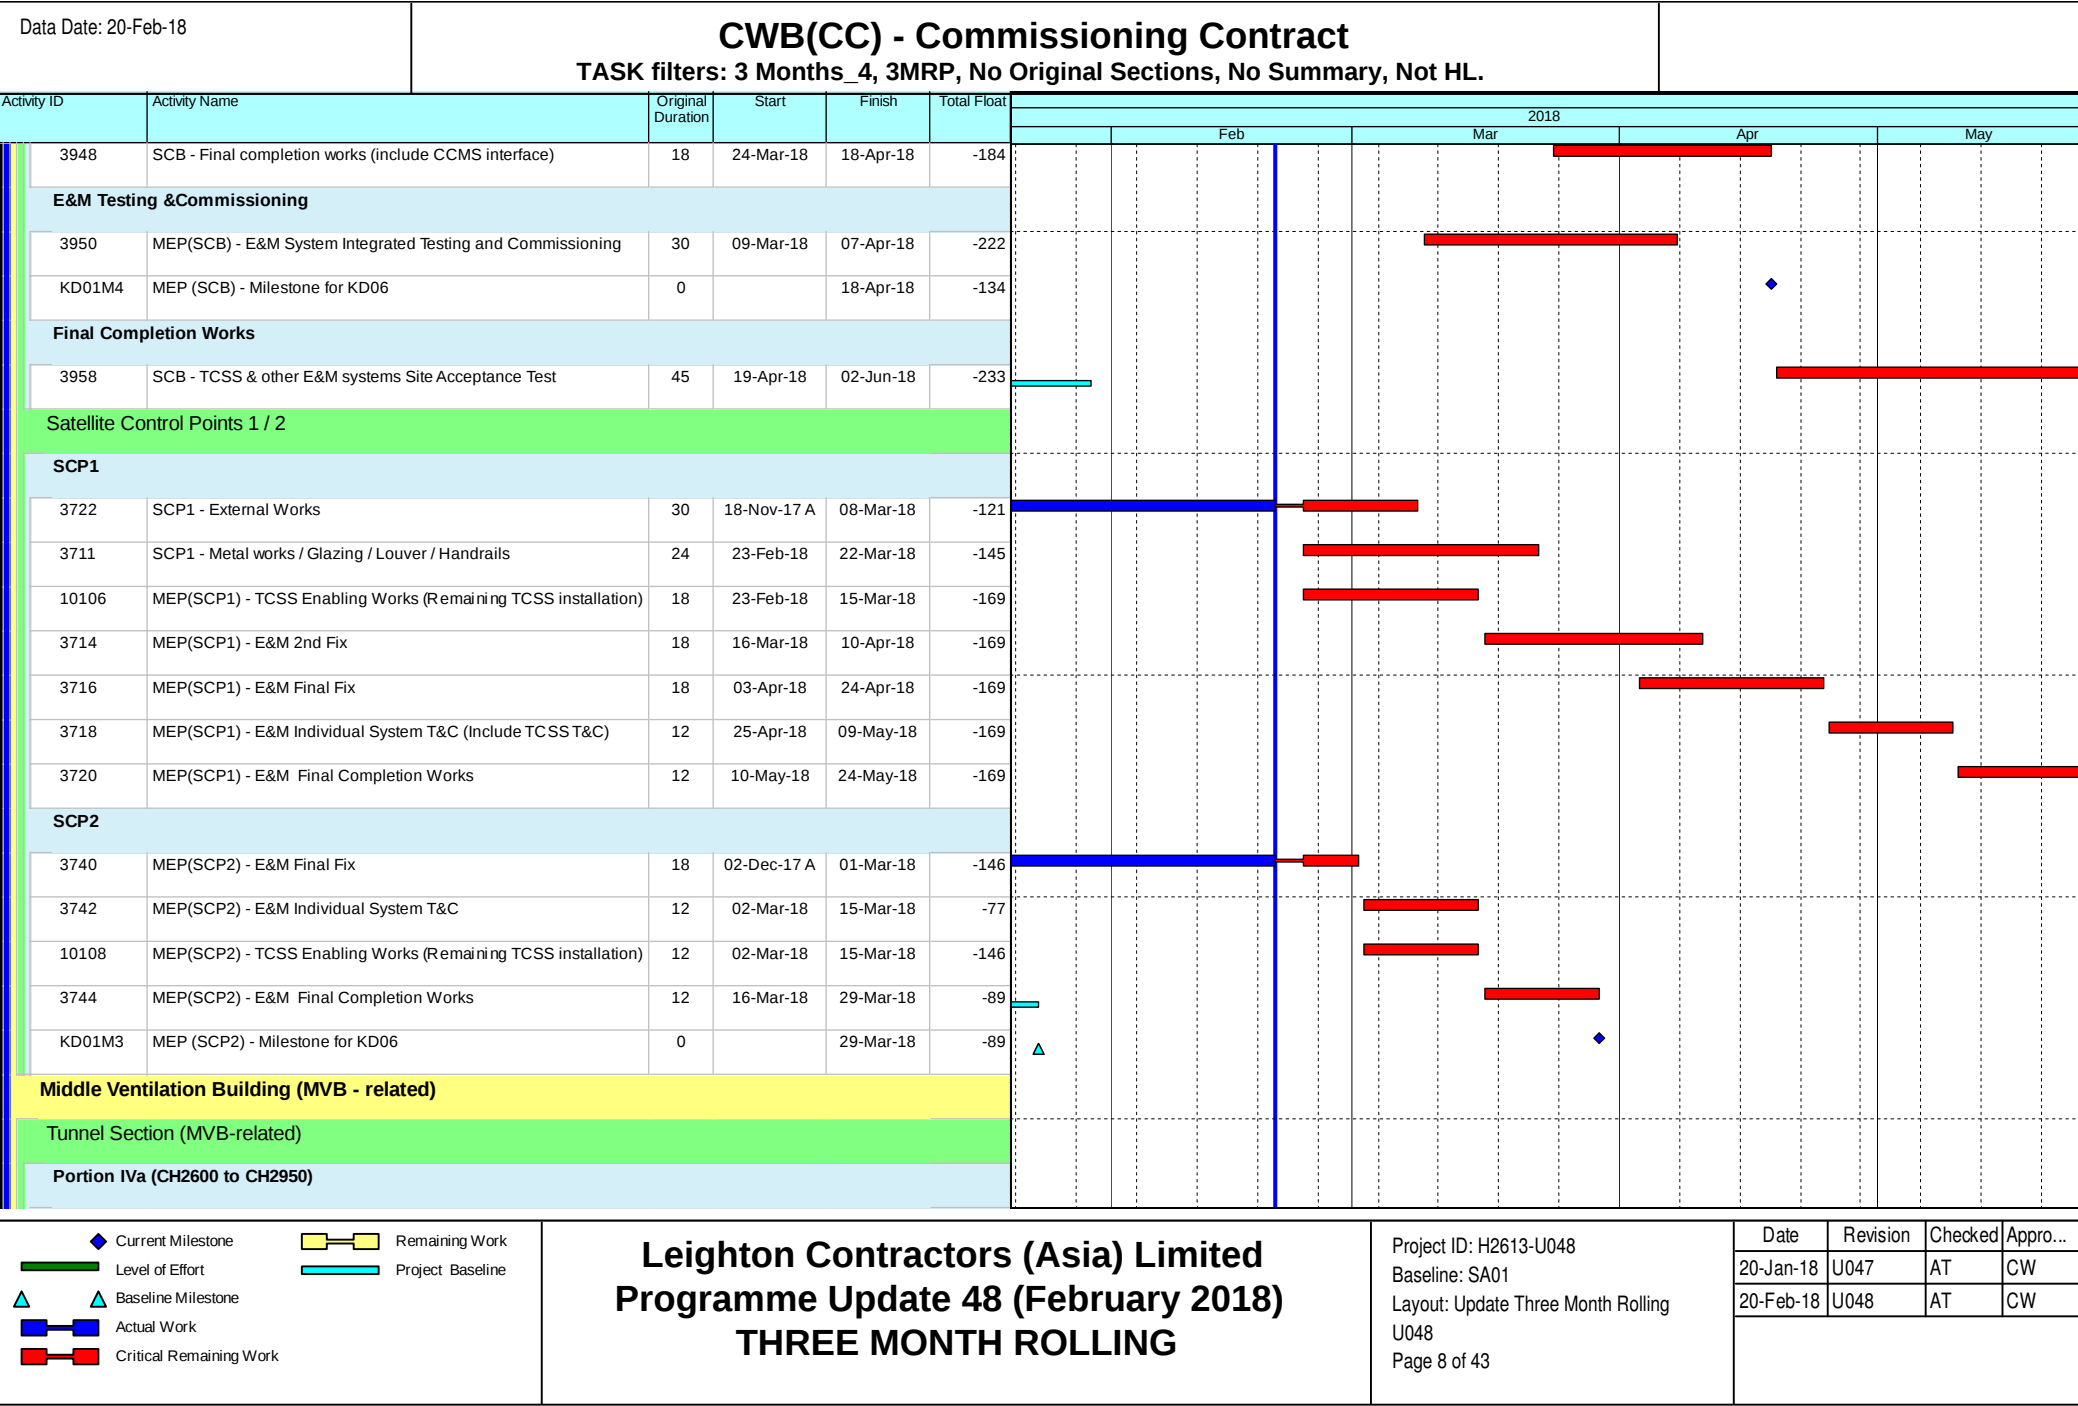

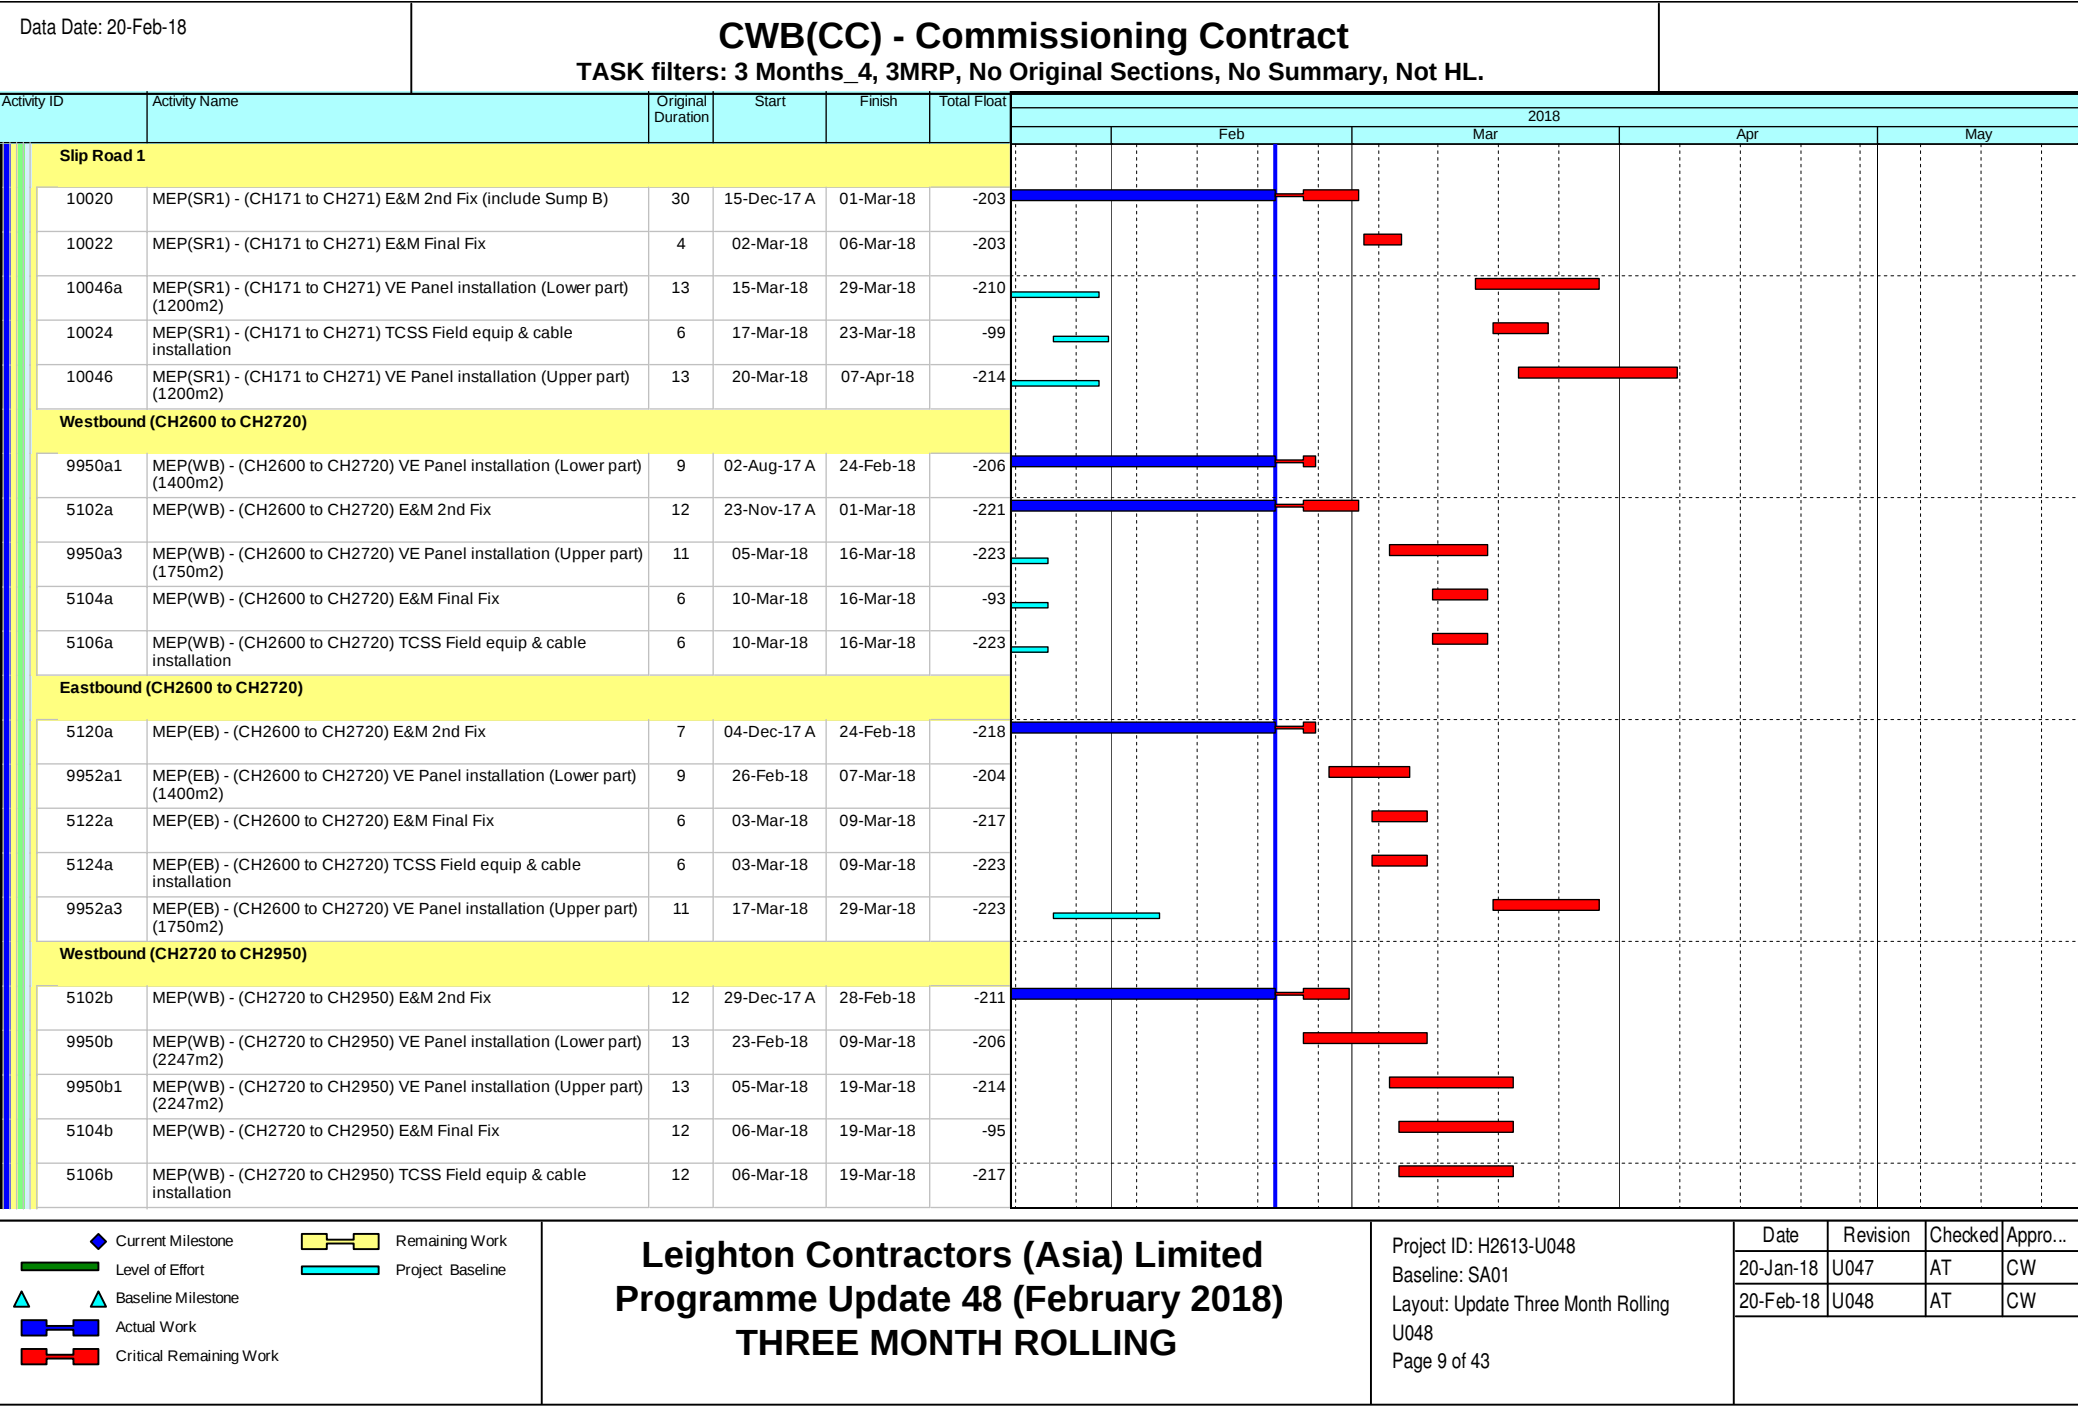

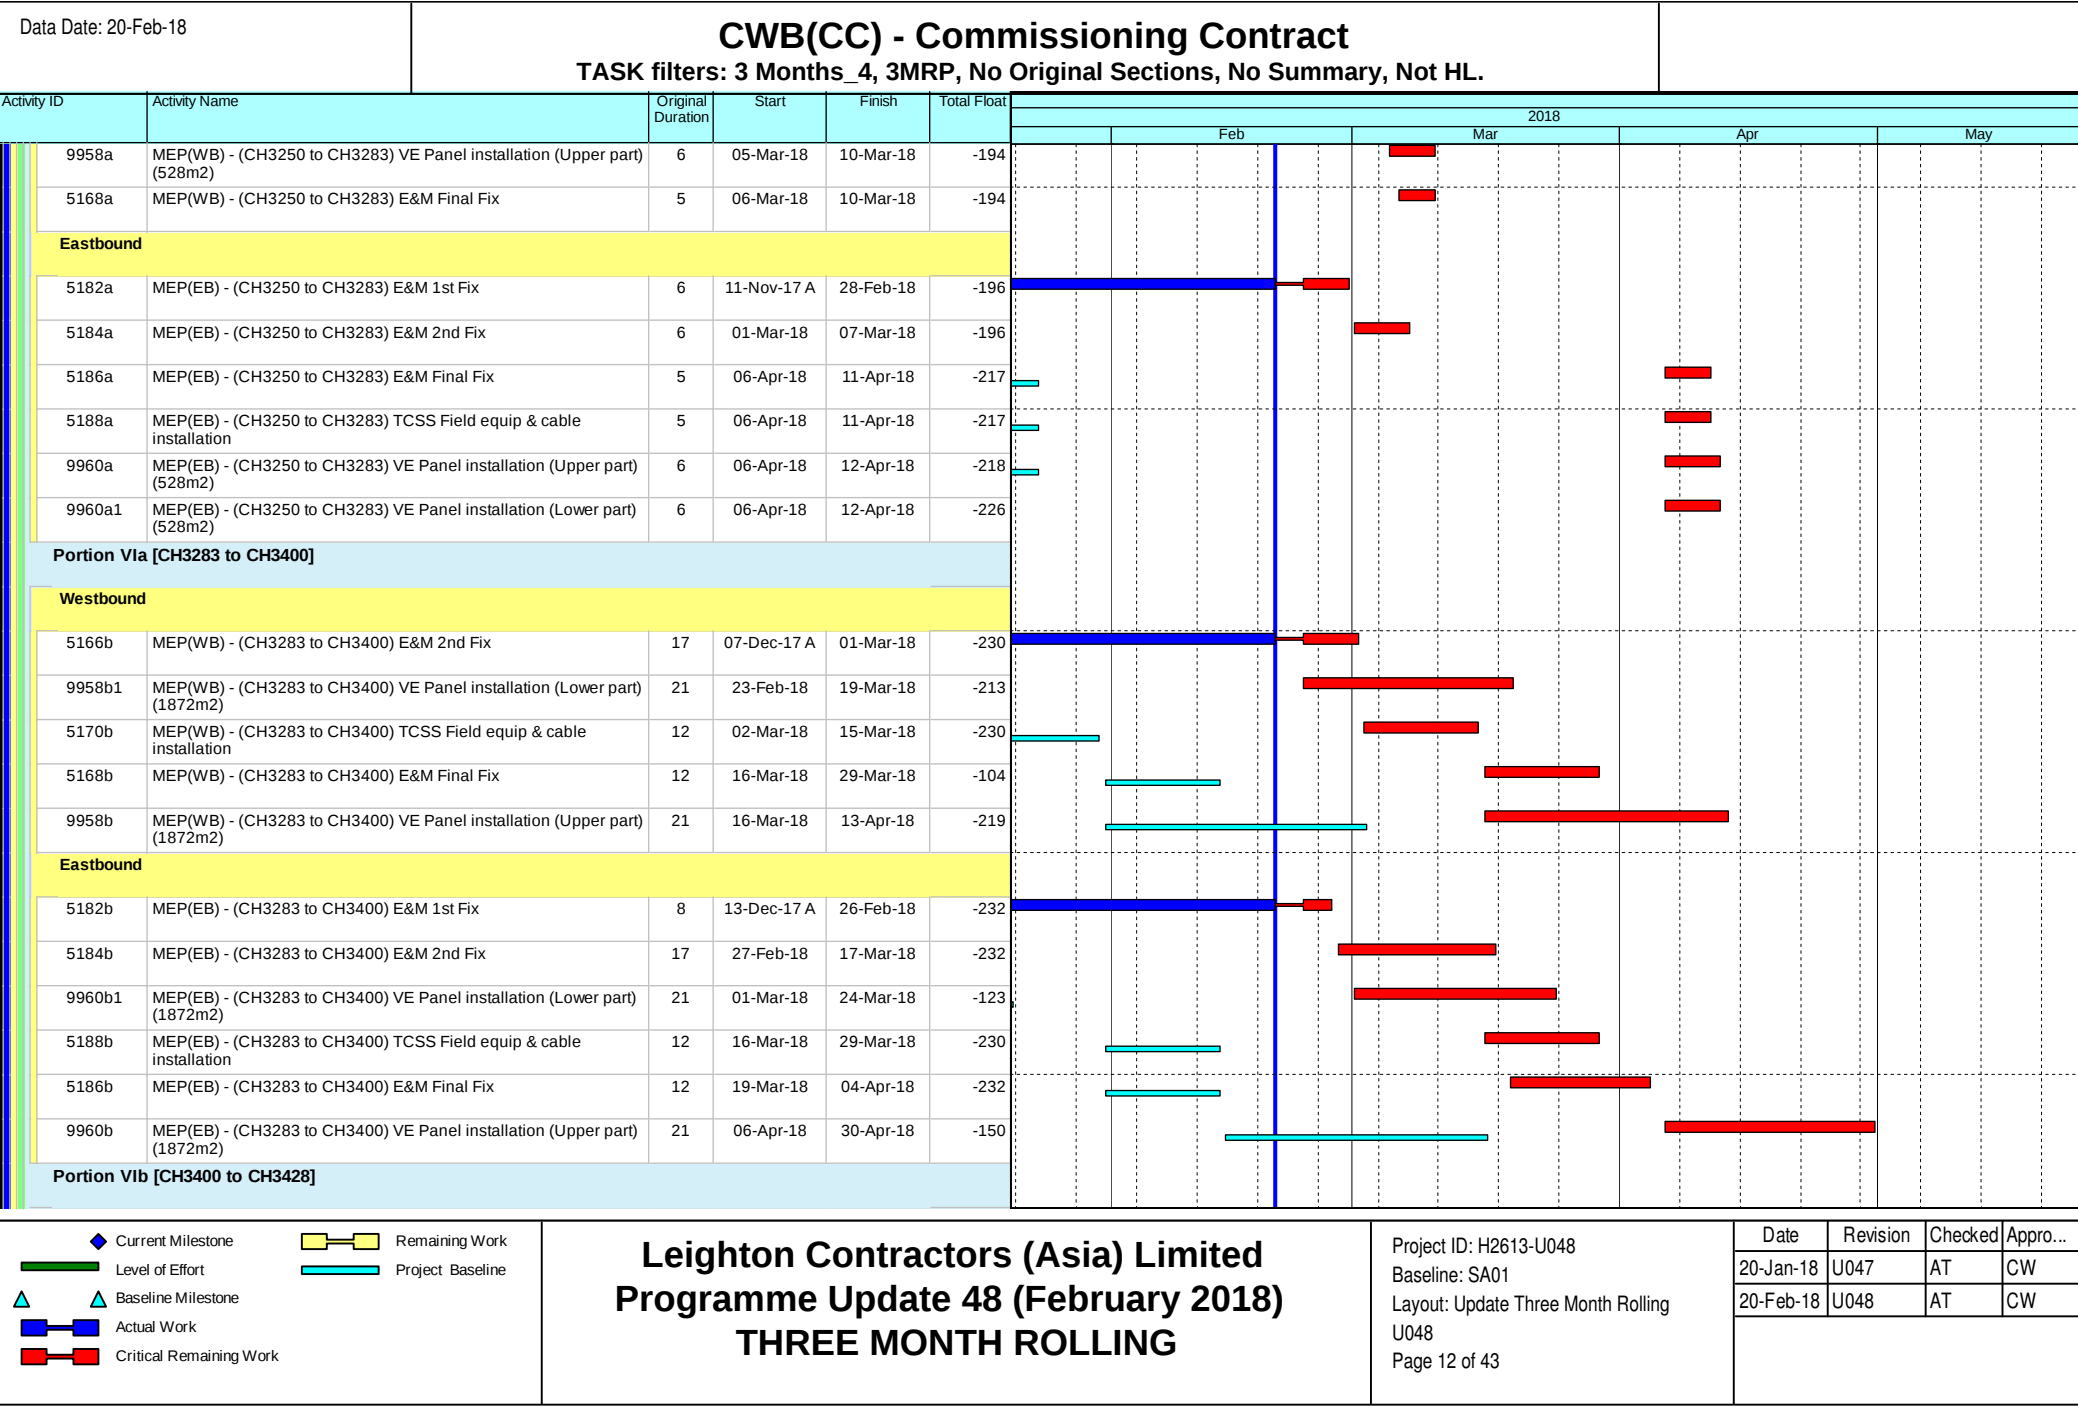


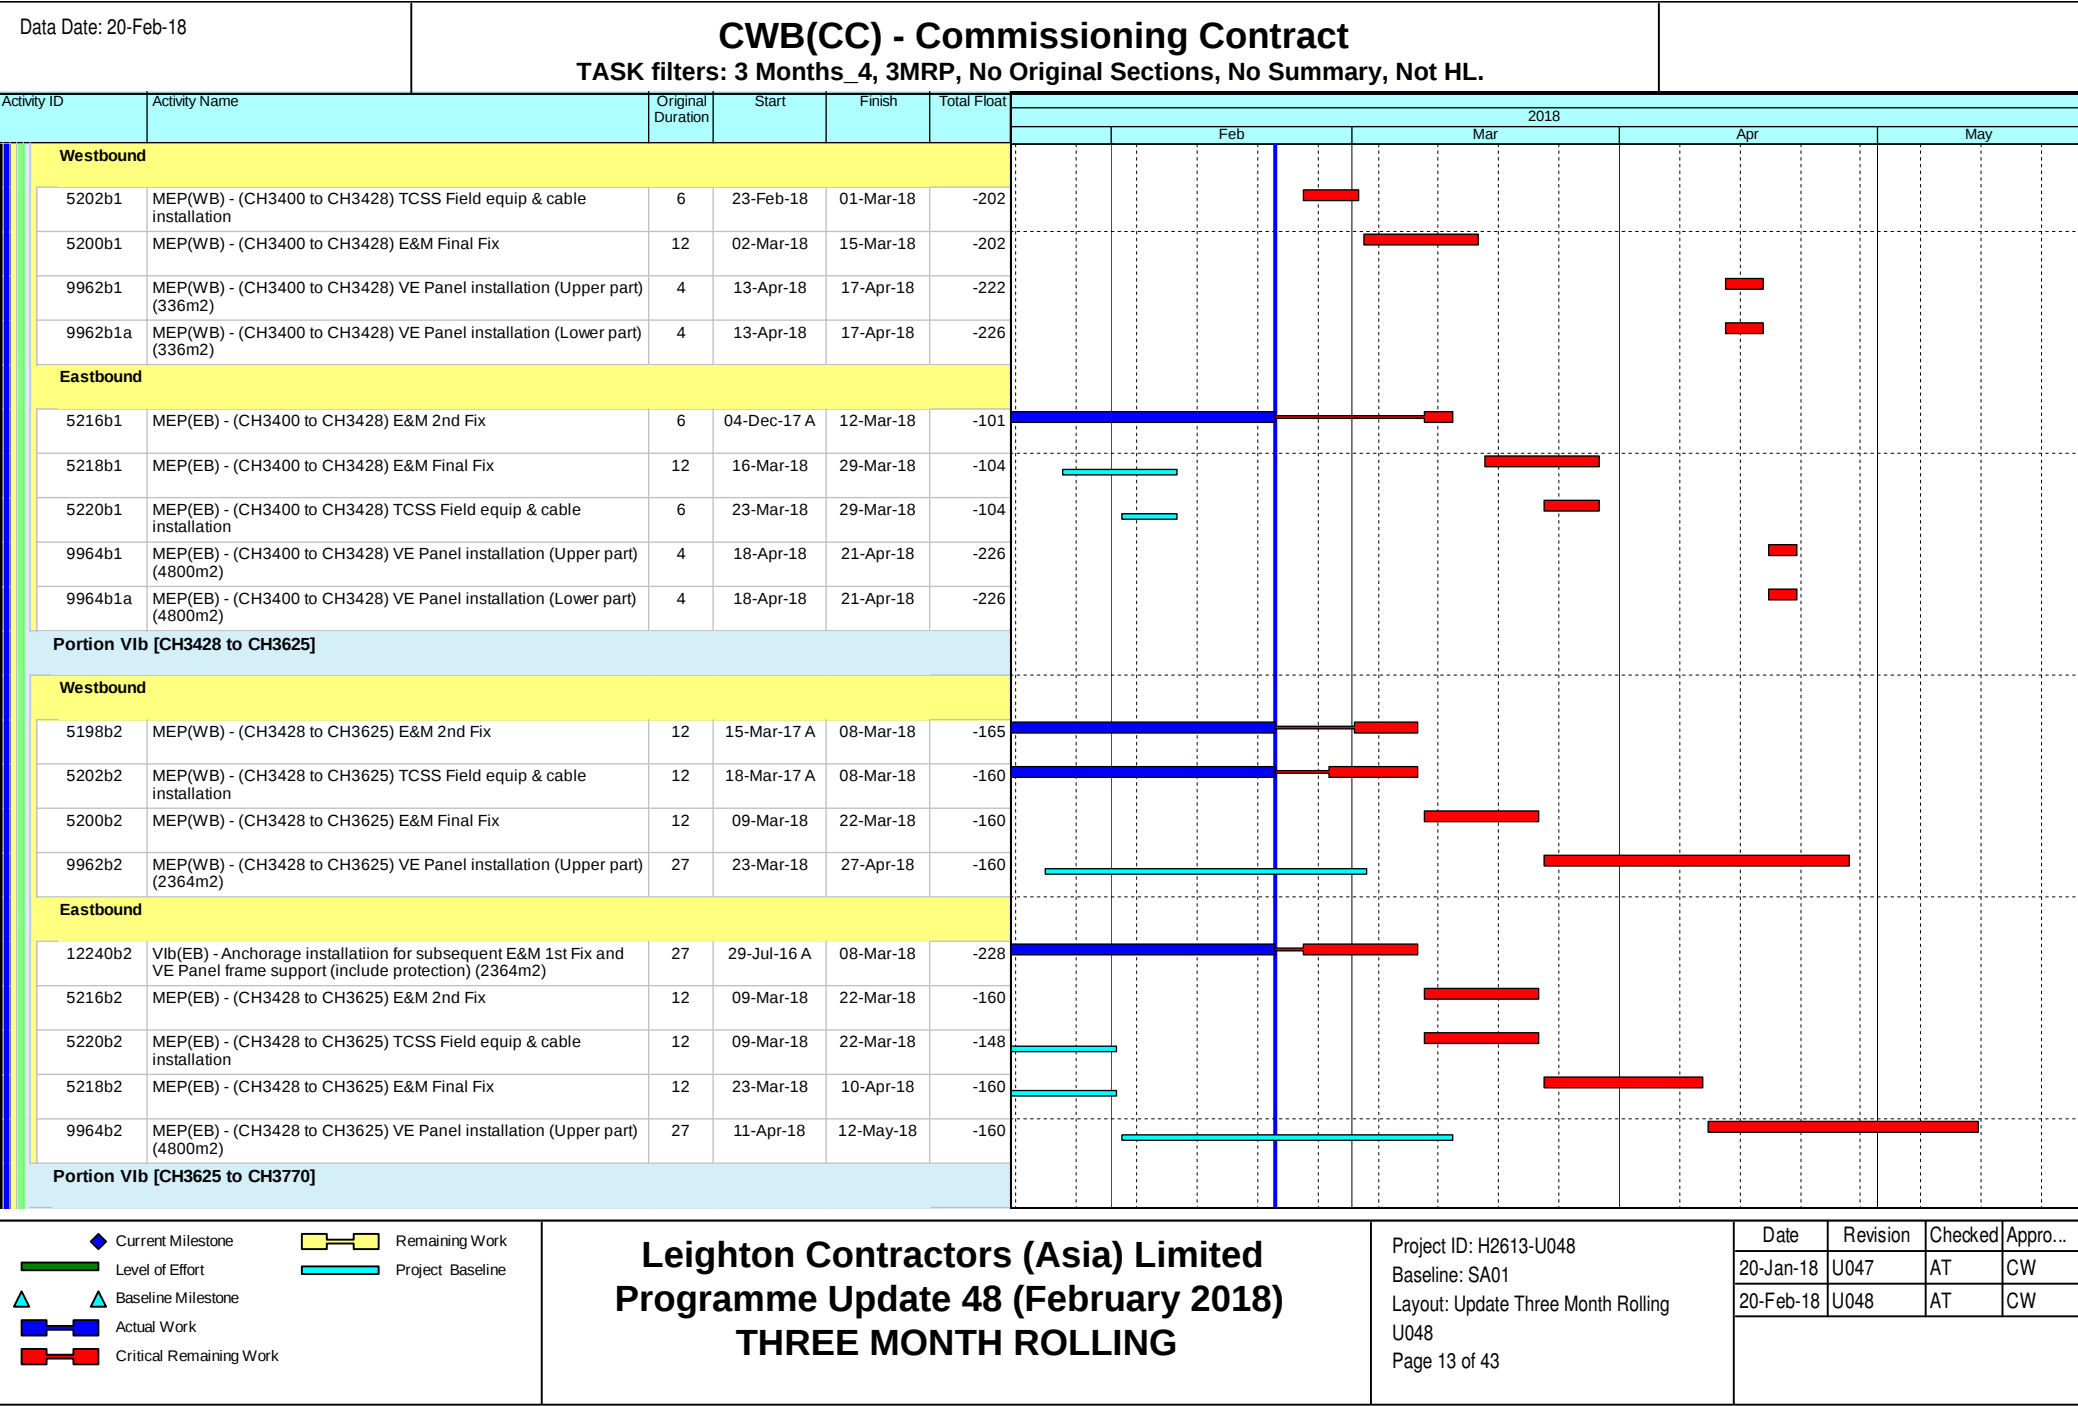


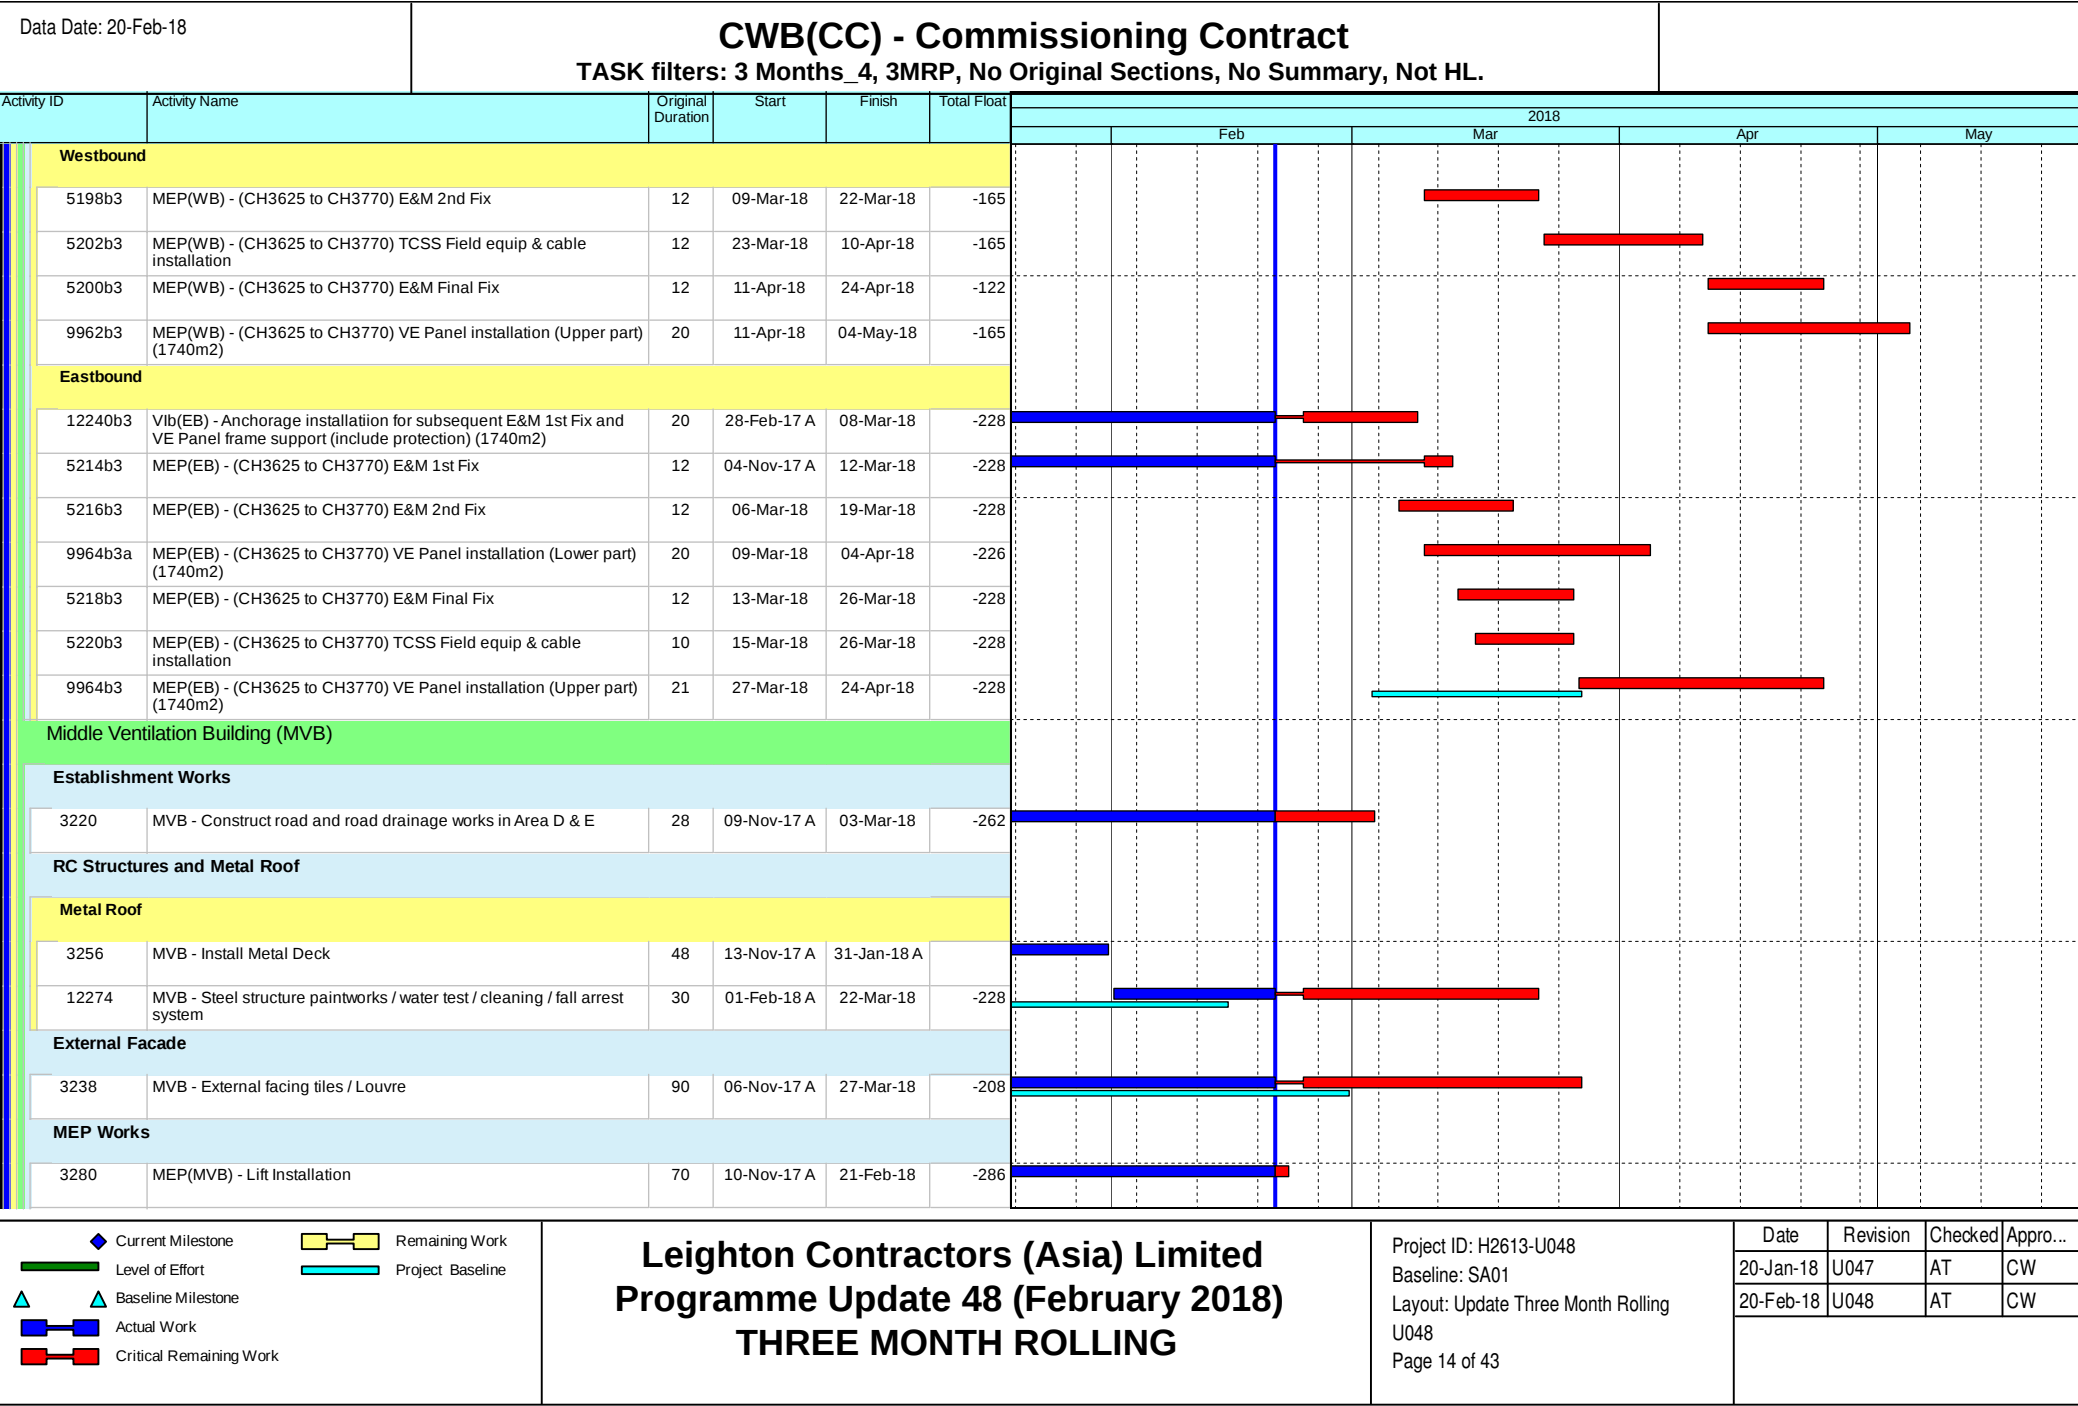

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

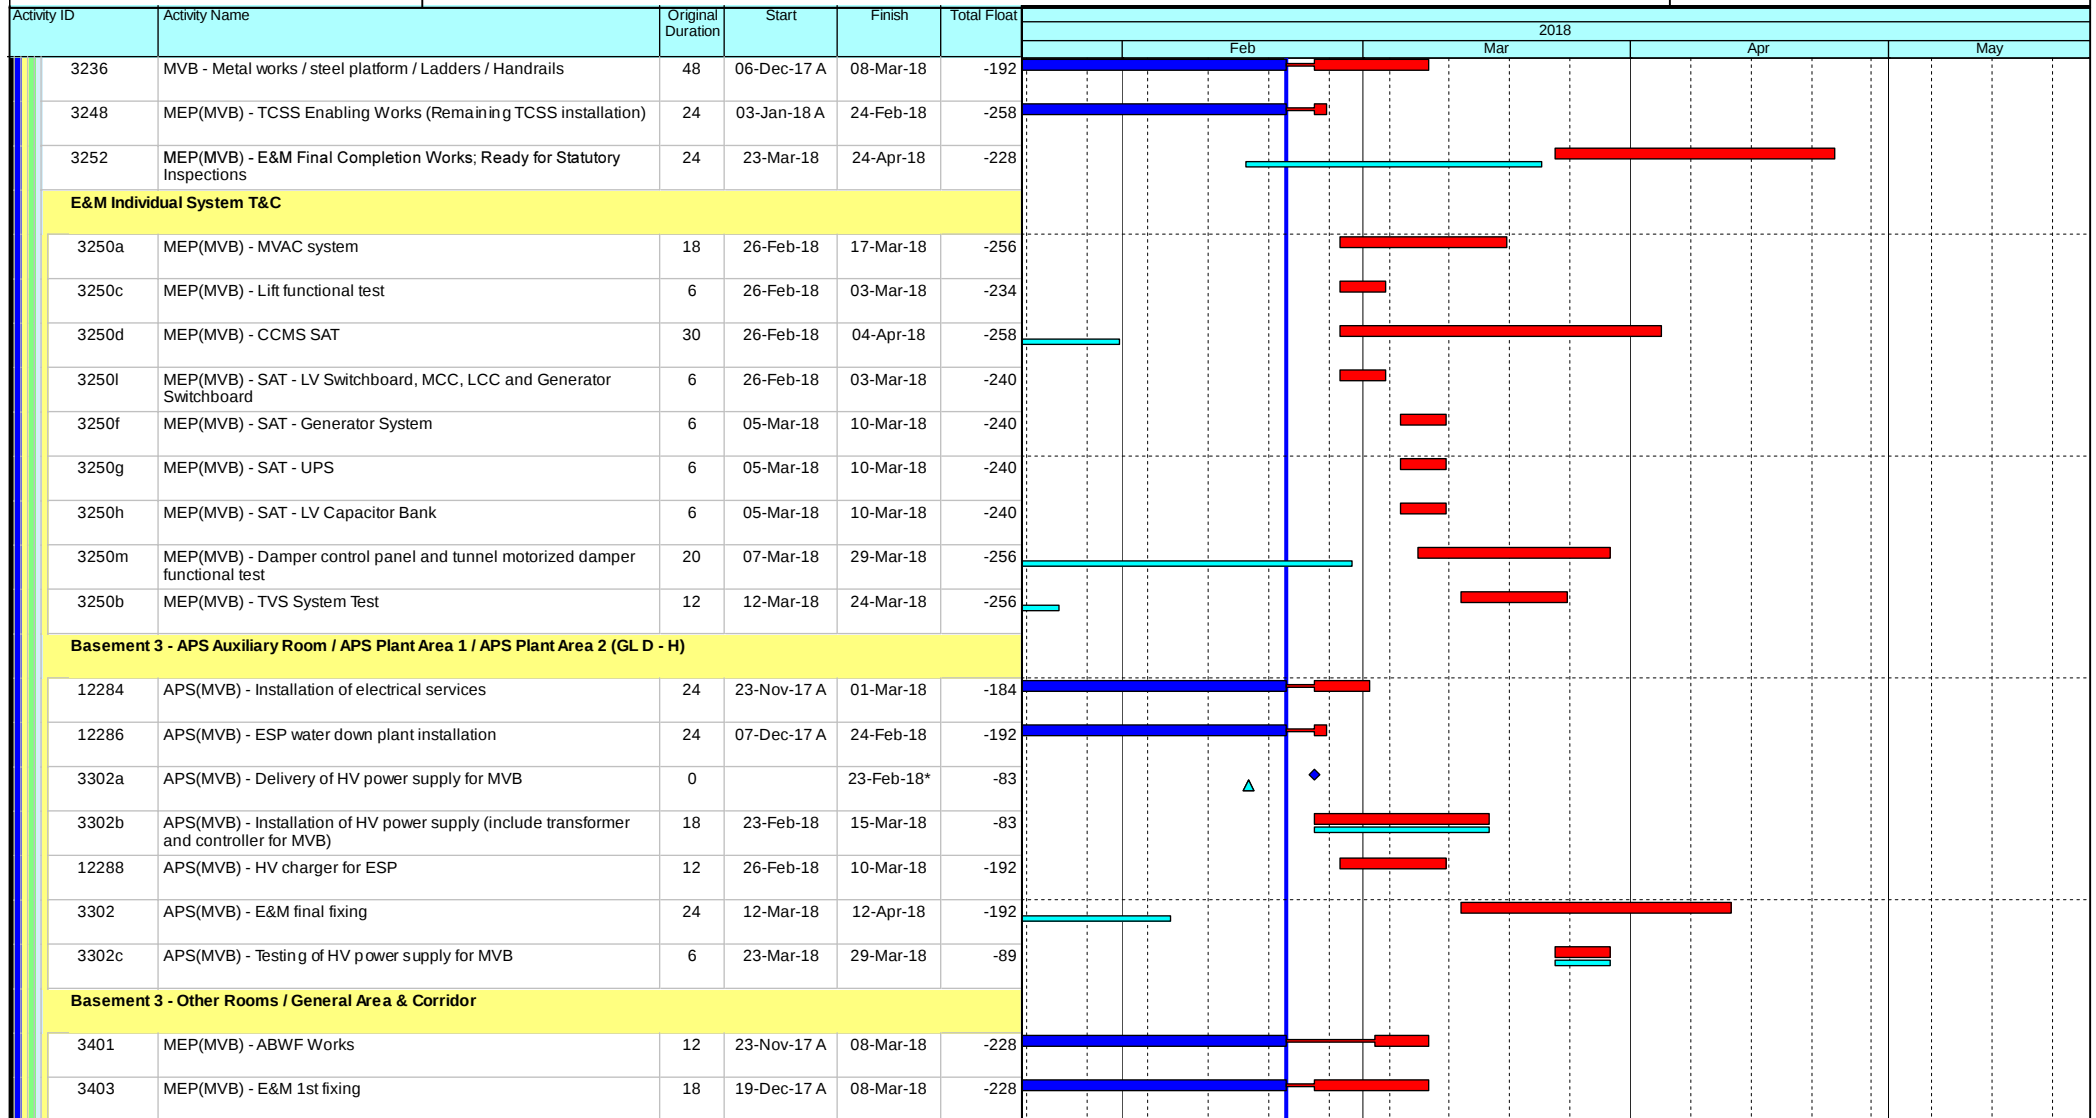


Leighton Contractors (Asia) Limited


Programme Update 48 (February 2018)


THREE MONTH ROLLING


Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 15 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

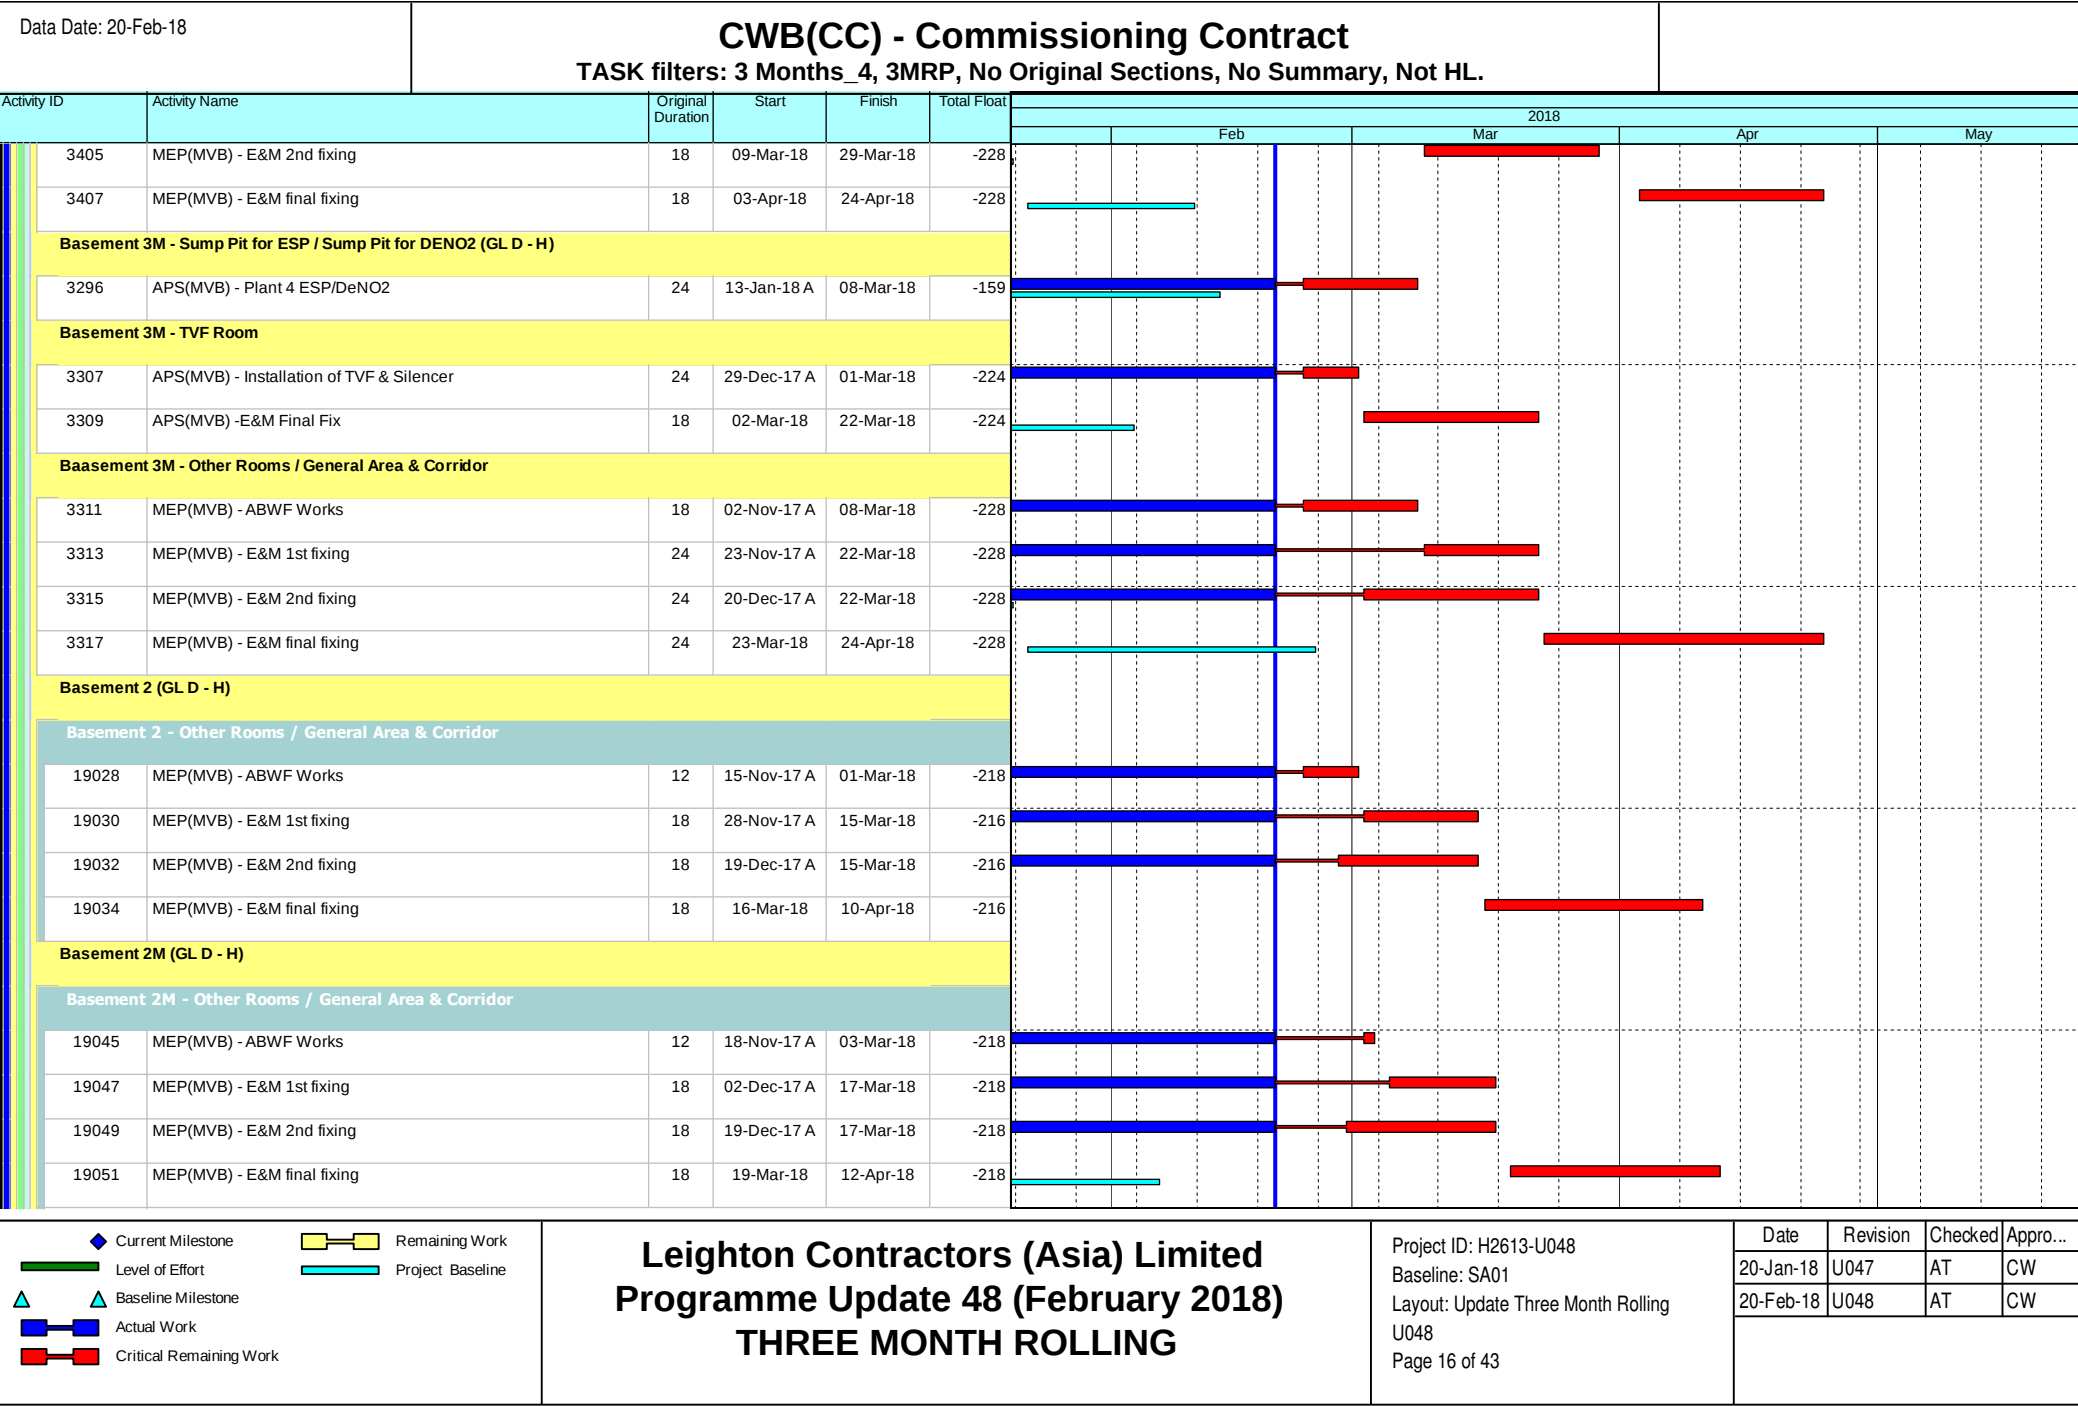

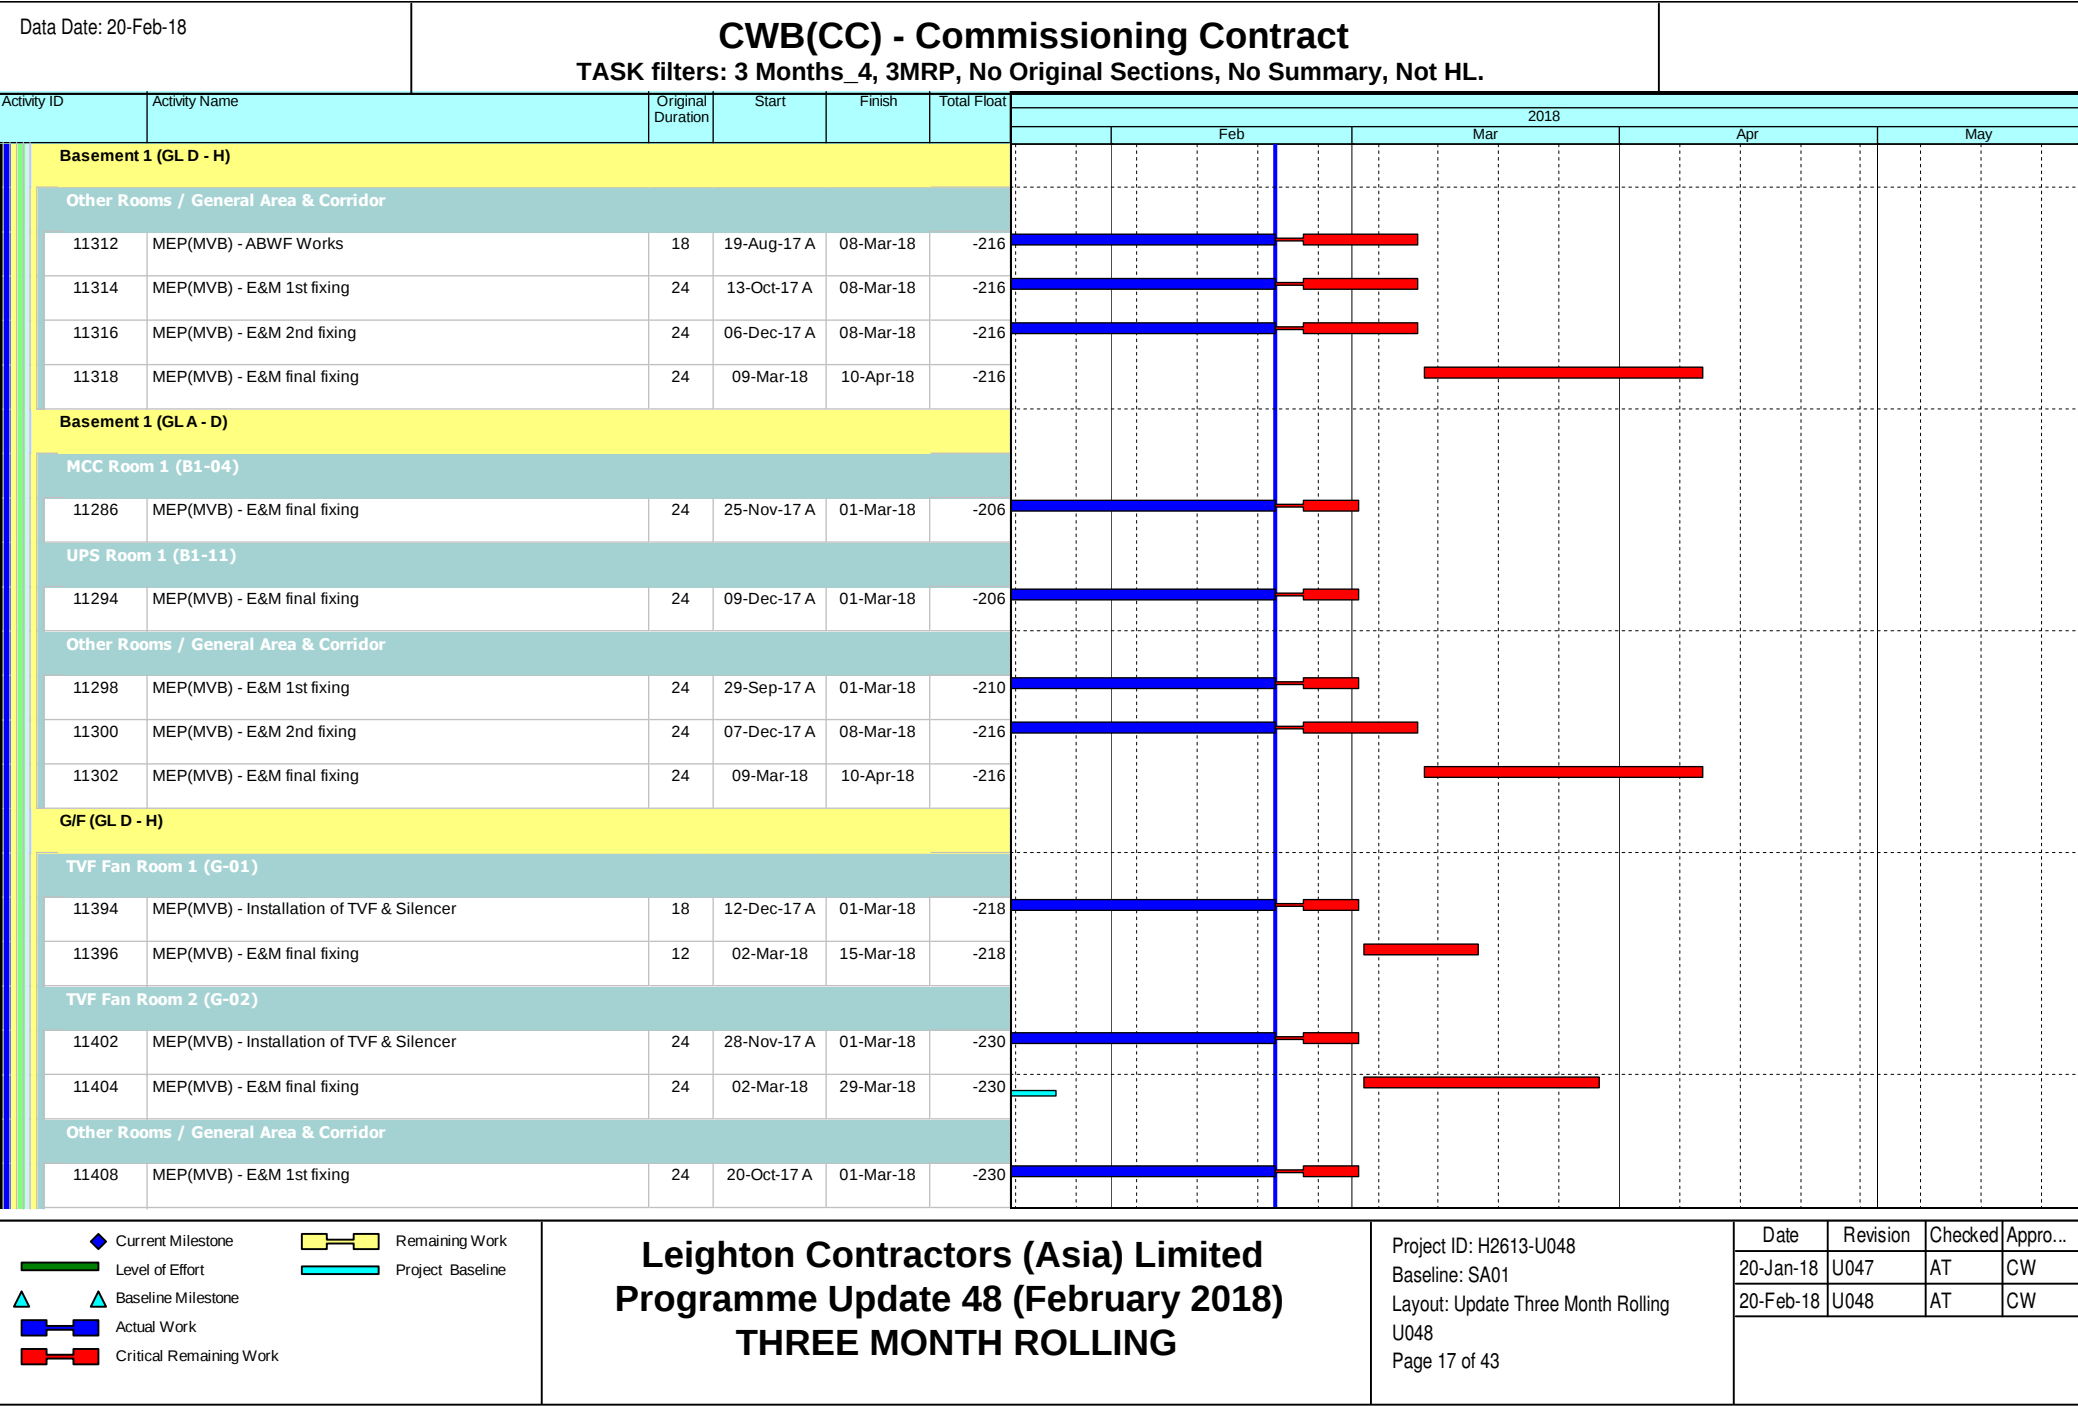


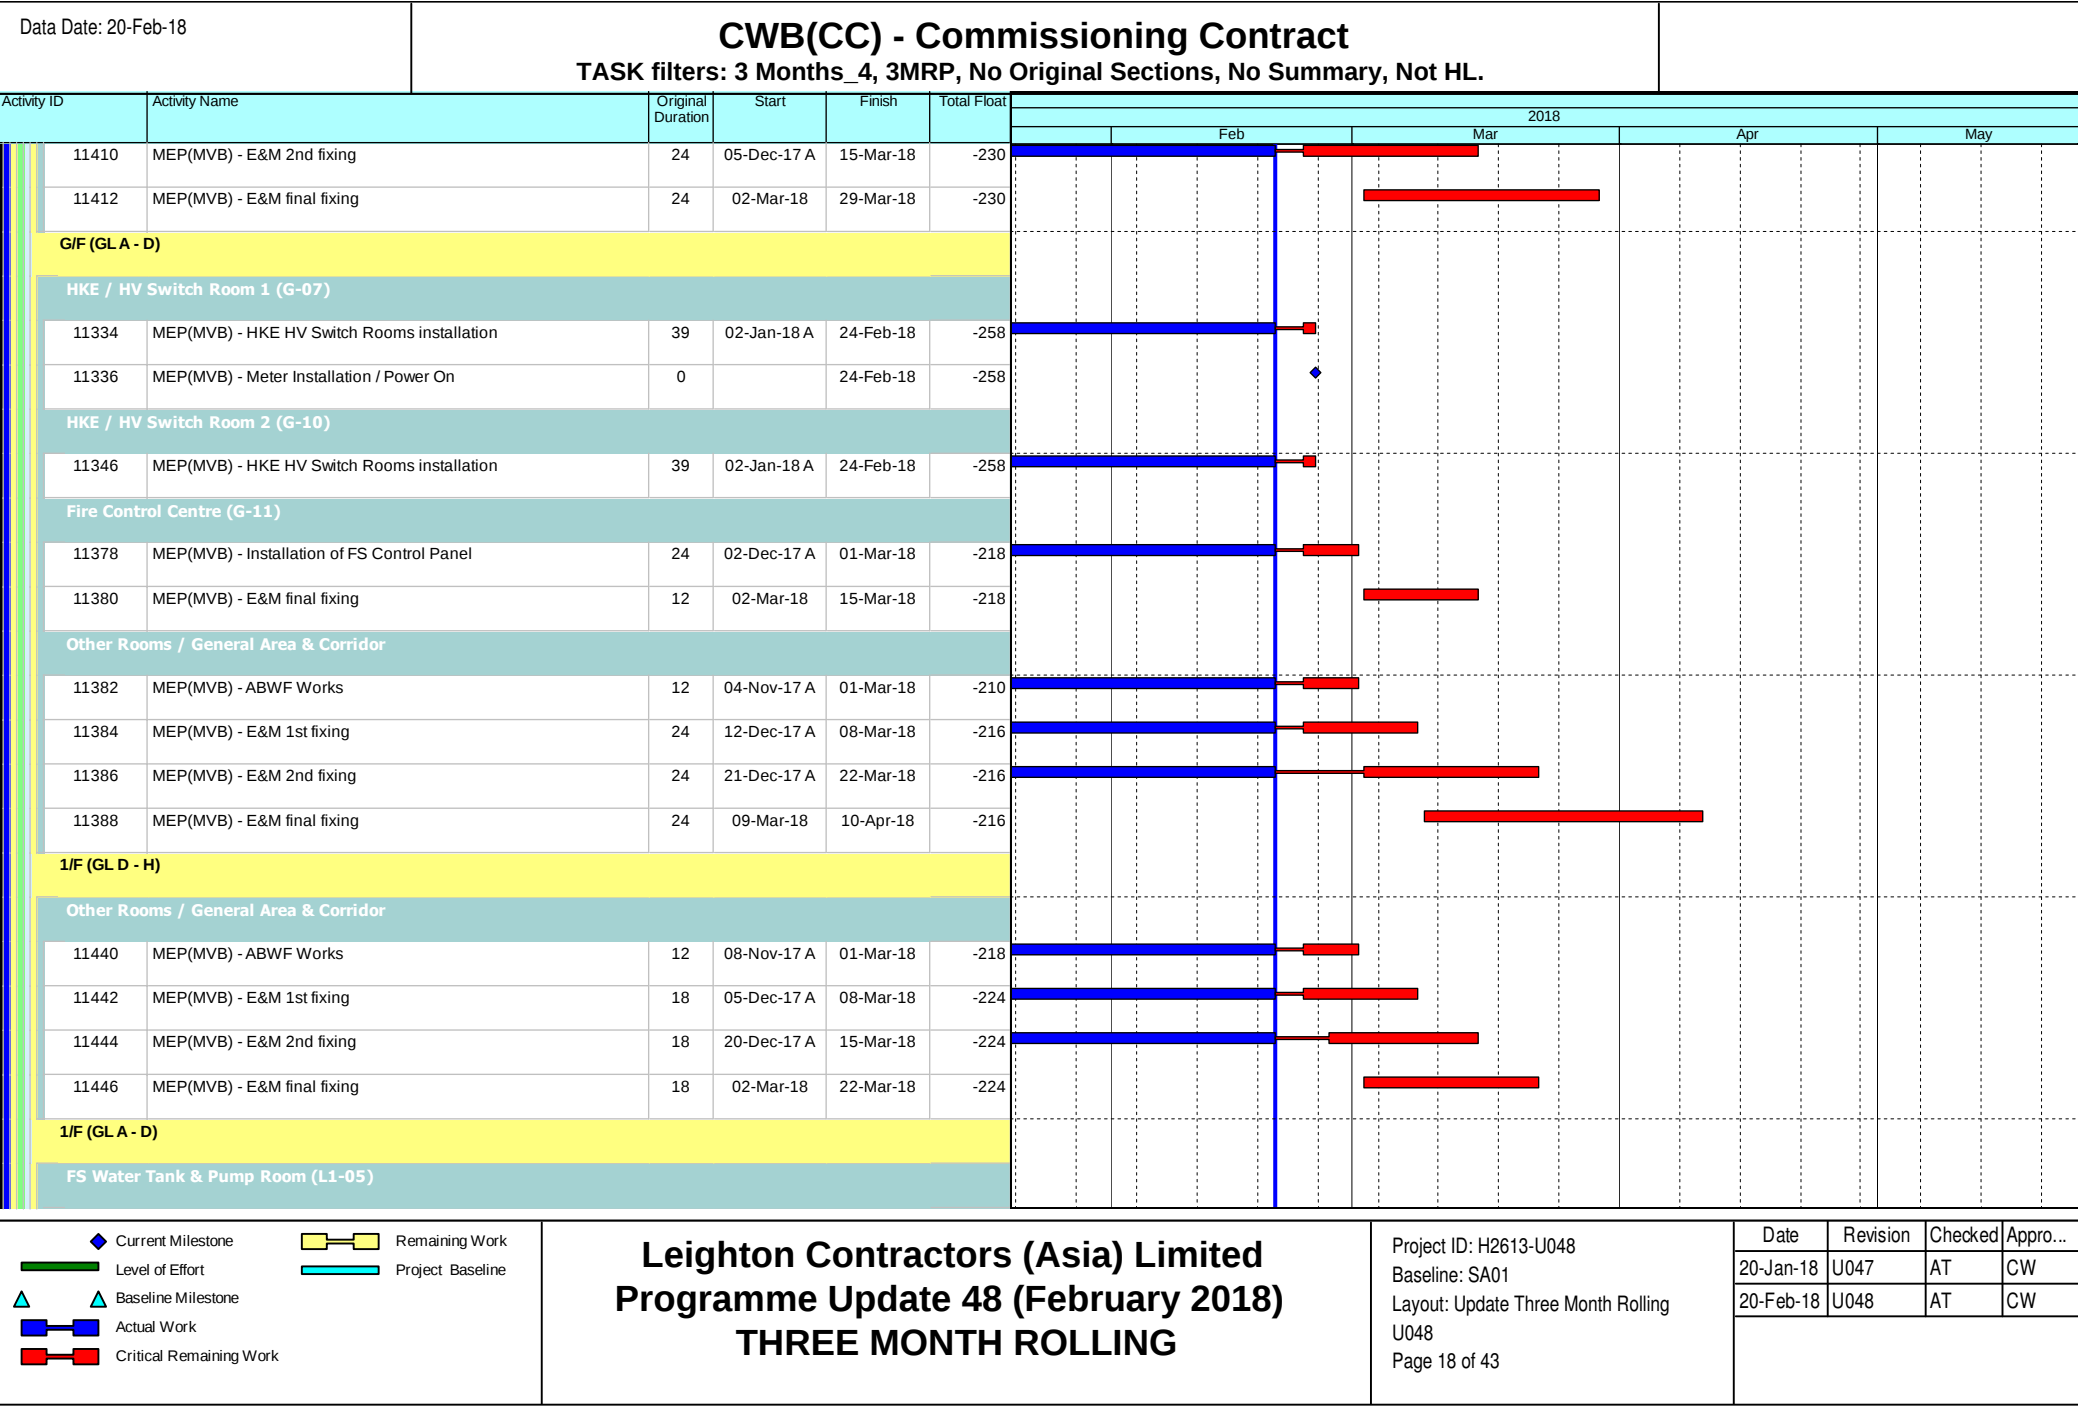


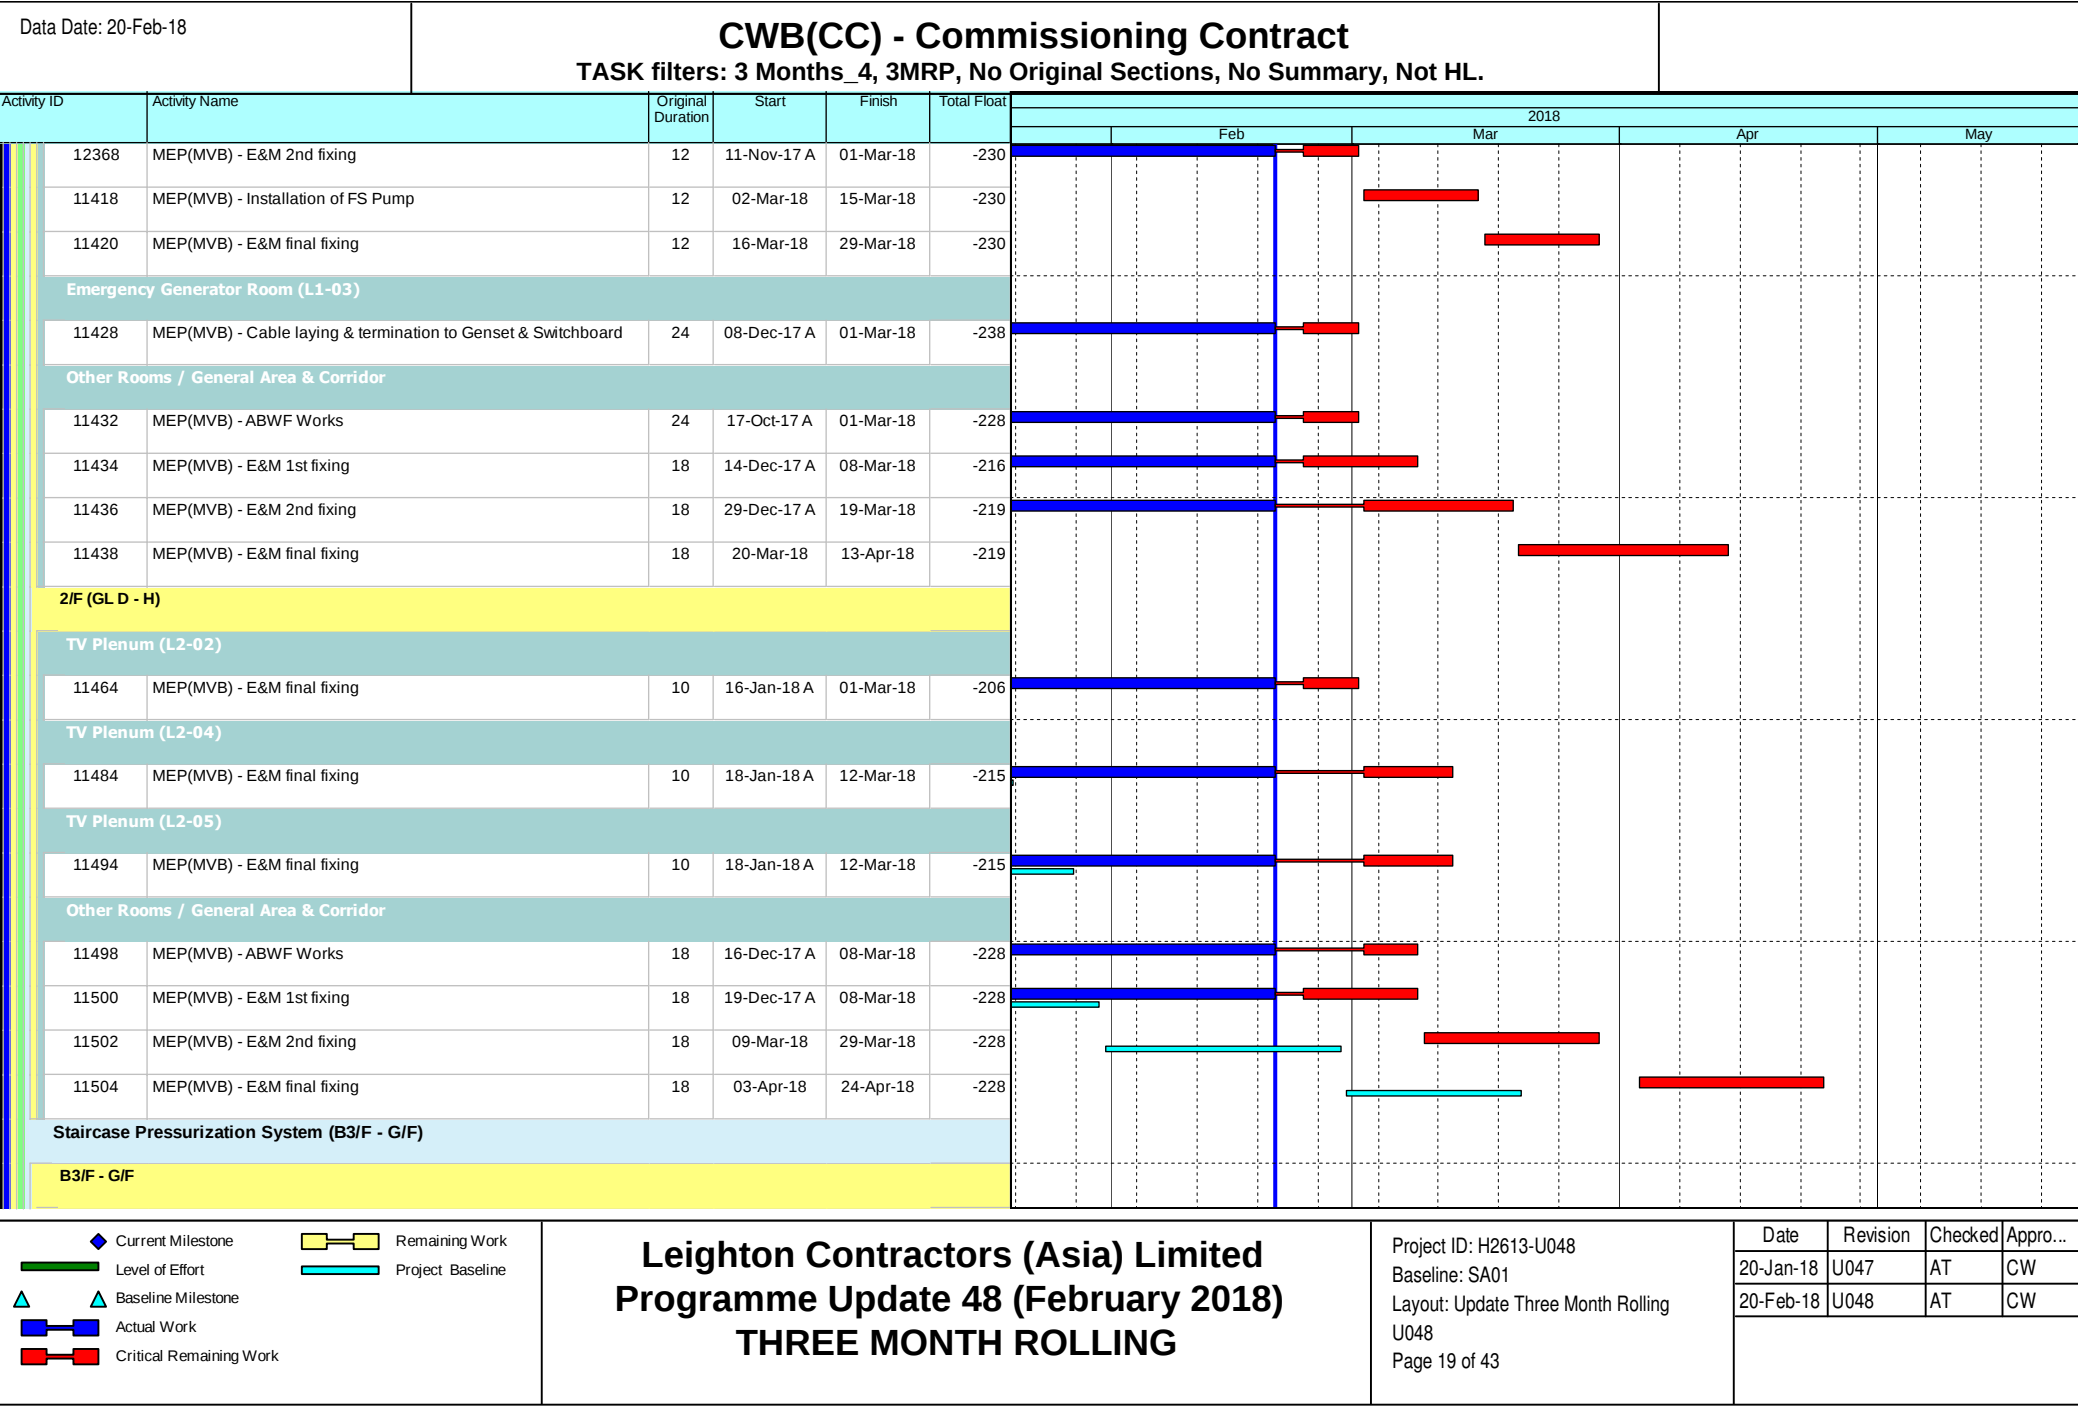

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

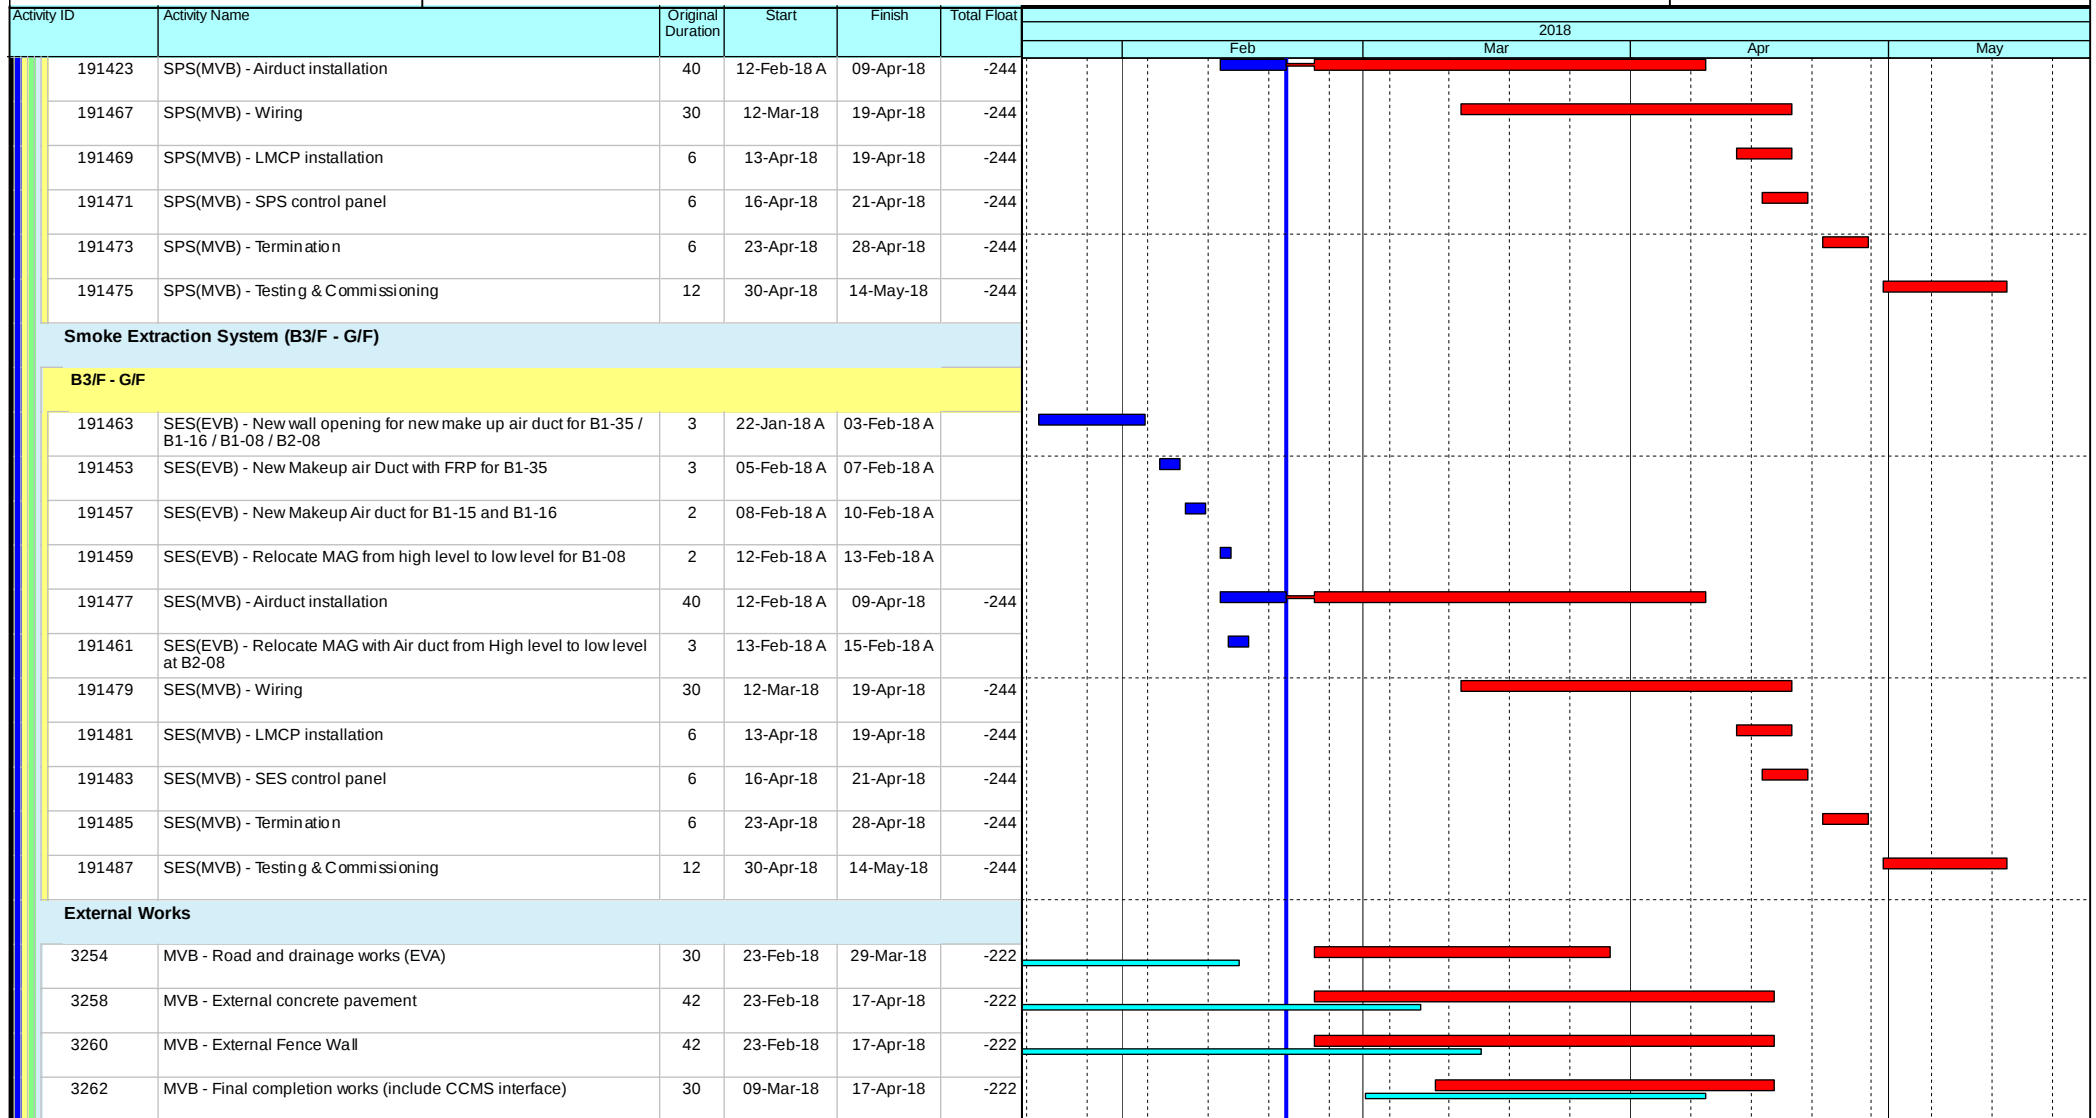

Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 20 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

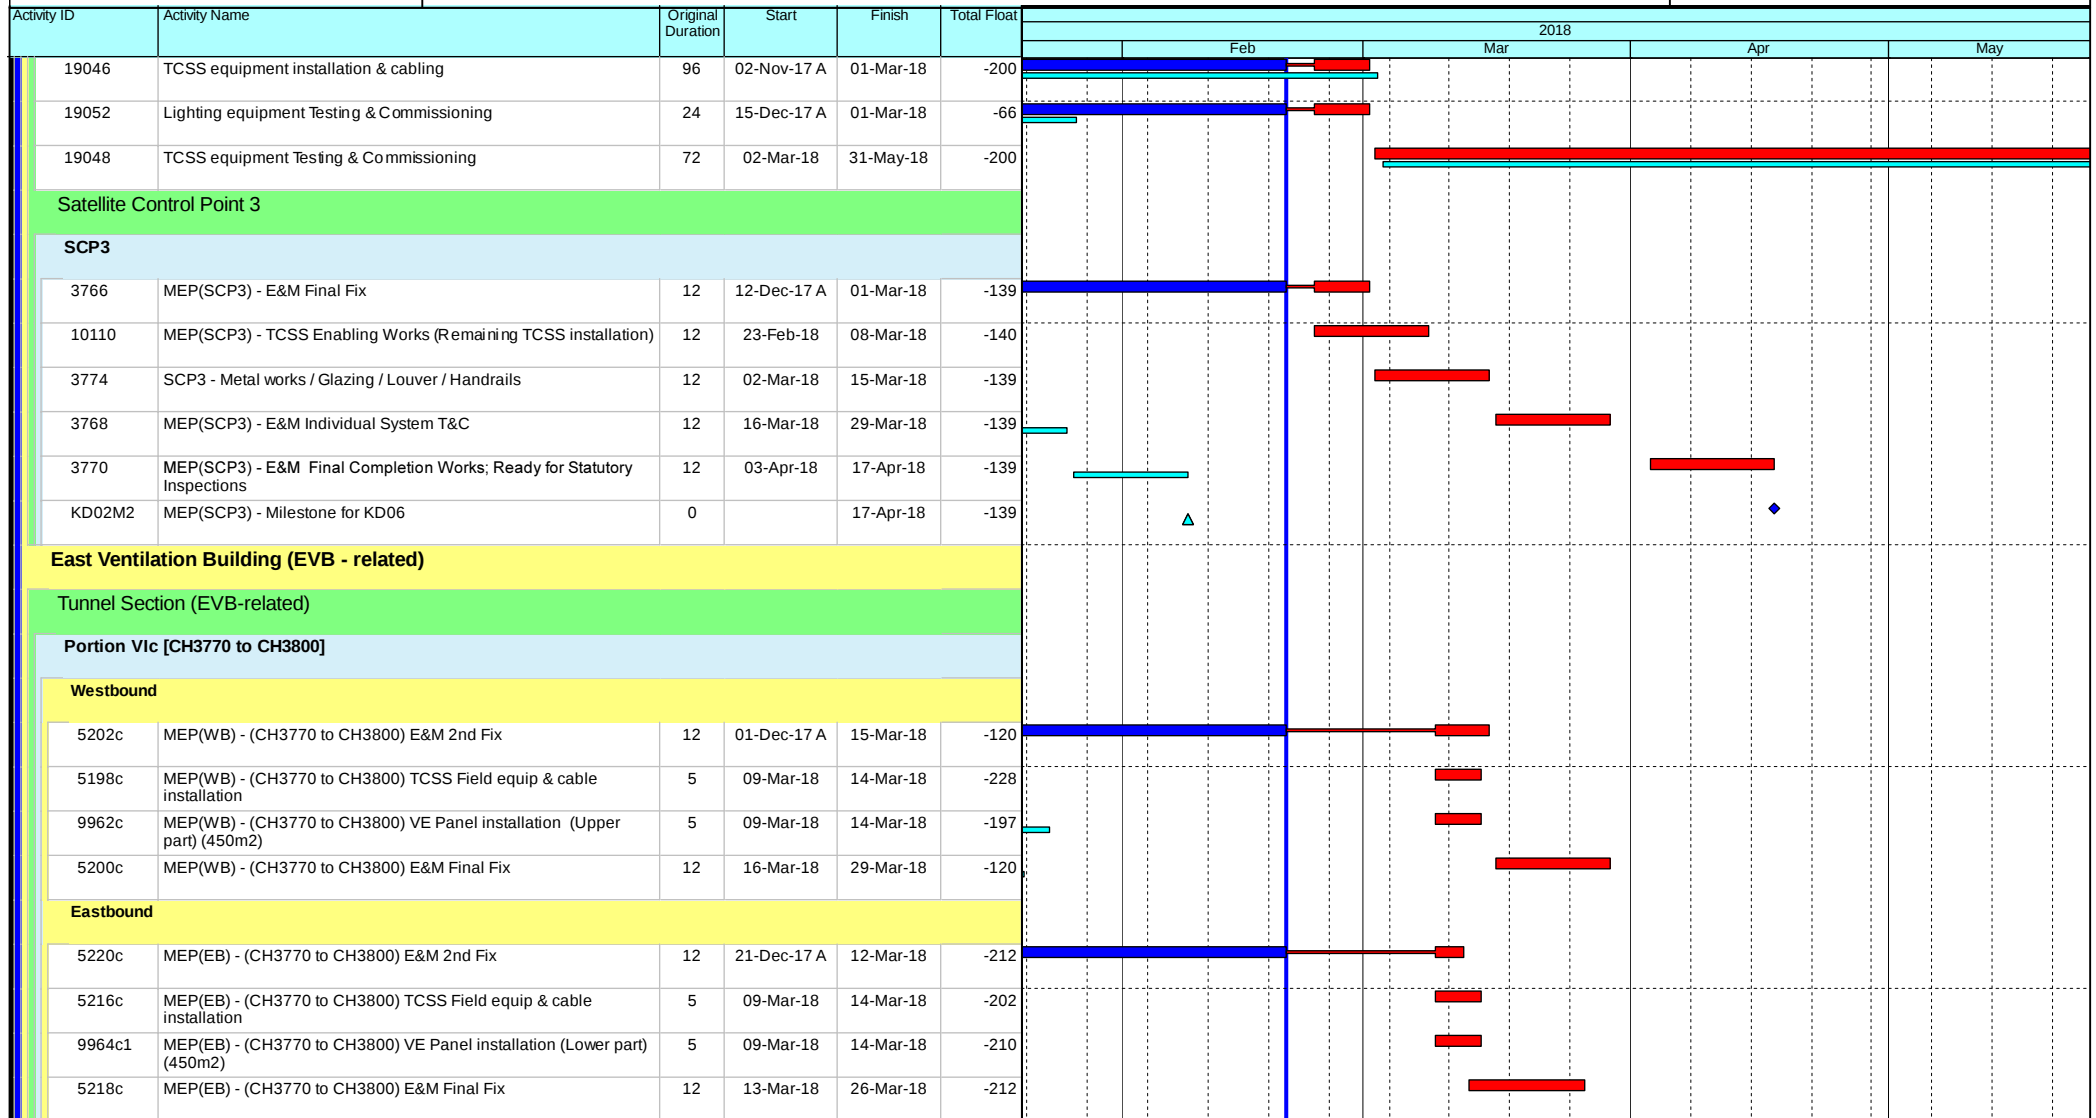

Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 22 of 43


Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

CWB(CC) - Commissioning Contract
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
9964c	MEP(EB) - (CH3770 to CH3800) VE Panel installation (Upper part) (450m2)	5	27-Mar-18	04-Apr-18	-212
Portion VII [CH3825 to CH4250] - Original Section in DWP Rev.2a					
5238	Possession of Portion VII	0	23-Feb-18		168
Portion VII [CH3800 to CH3911]					
Westbound					
9966a4a	MEP(WB) - (CH3800 to CH3911) VE Panel installation (Lower part) (1332m2)	15	04-Jul-17 A	02-Mar-18	-151
5230a4	MEP(WB) - (CH3800 to CH3911) E&M 2nd Fix	48	14-Aug-17 A	01-Mar-18	-154
5232a6	MEP(WB) - (CH3800 to CH3911) Niche installation	3	11-Sep-17 A	24-Feb-18	-204
5232a4	MEP(WB) - (CH3800 to CH3911) E&M Final Fix	16	26-Feb-18	15-Mar-18	-108
5234a4	MEP(WB) - (CH3800 to CH3911) TCSS Field equip & cable installation	12	02-Mar-18	15-Mar-18	-154
9966a4	MEP(WB) - (CH3800 to CH3911) VE Panel installation (Upper part) (1332m2)	15	16-Mar-18	06-Apr-18	-154
Eastbound					
5248a4	MEP(EB) - (CH3800 to CH3911) E&M 2nd Fix (inlcude Sump II)	12	15-Mar-17 A	01-Mar-18	-196
5252a4	MEP(EB) - (CH3800 to CH3911) TCSS Field equip & cable installation	12	17-Mar-17 A	07-Mar-18	-201
5250a4	MEP(EB) - (CH3800 to CH3911) E&M Final Fix	16	02-Mar-18	20-Mar-18	-157
9968a4a	MEP(EB) - (CH3800 to CH3911) VE Panel installation (Lower part) (1332m2)	14	15-Mar-18	03-Apr-18	-152
9968a4	MEP(EB) - (CH3800 to CH3911) VE Panel installation (Upper part) (1332m2)	14	21-Mar-18	10-Apr-18	-157
Portion VII [CH3911 to CH4250]					
Access Shaft Opening					
10120a1	VII(WB) - Shaft tunnel slab curing	6	20-Jan-18 A	26-Jan-18 A	
10120a5	VII(WB) - Cannot apply waterproofing due to water leaking	27	27-Jan-18 A	06-Mar-18	-165
10120a2	VII(WB) - Waterproofing on Shaft tunnel slab	18	07-Mar-18	27-Mar-18	-165
10120a3	VII(WB) - Backfilling (78 layers; 1 day/layer)	78	28-Mar-18	05-Jul-18	-165
Westbound					





**Leighton Contractors (Asia) Limited
Programme Update 48 (February 2018)
THREE MONTH ROLLING**

Project ID: H2613-U048
Baseline: SA01
Layout: Update Three Month Rolling
U048
Page 23 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

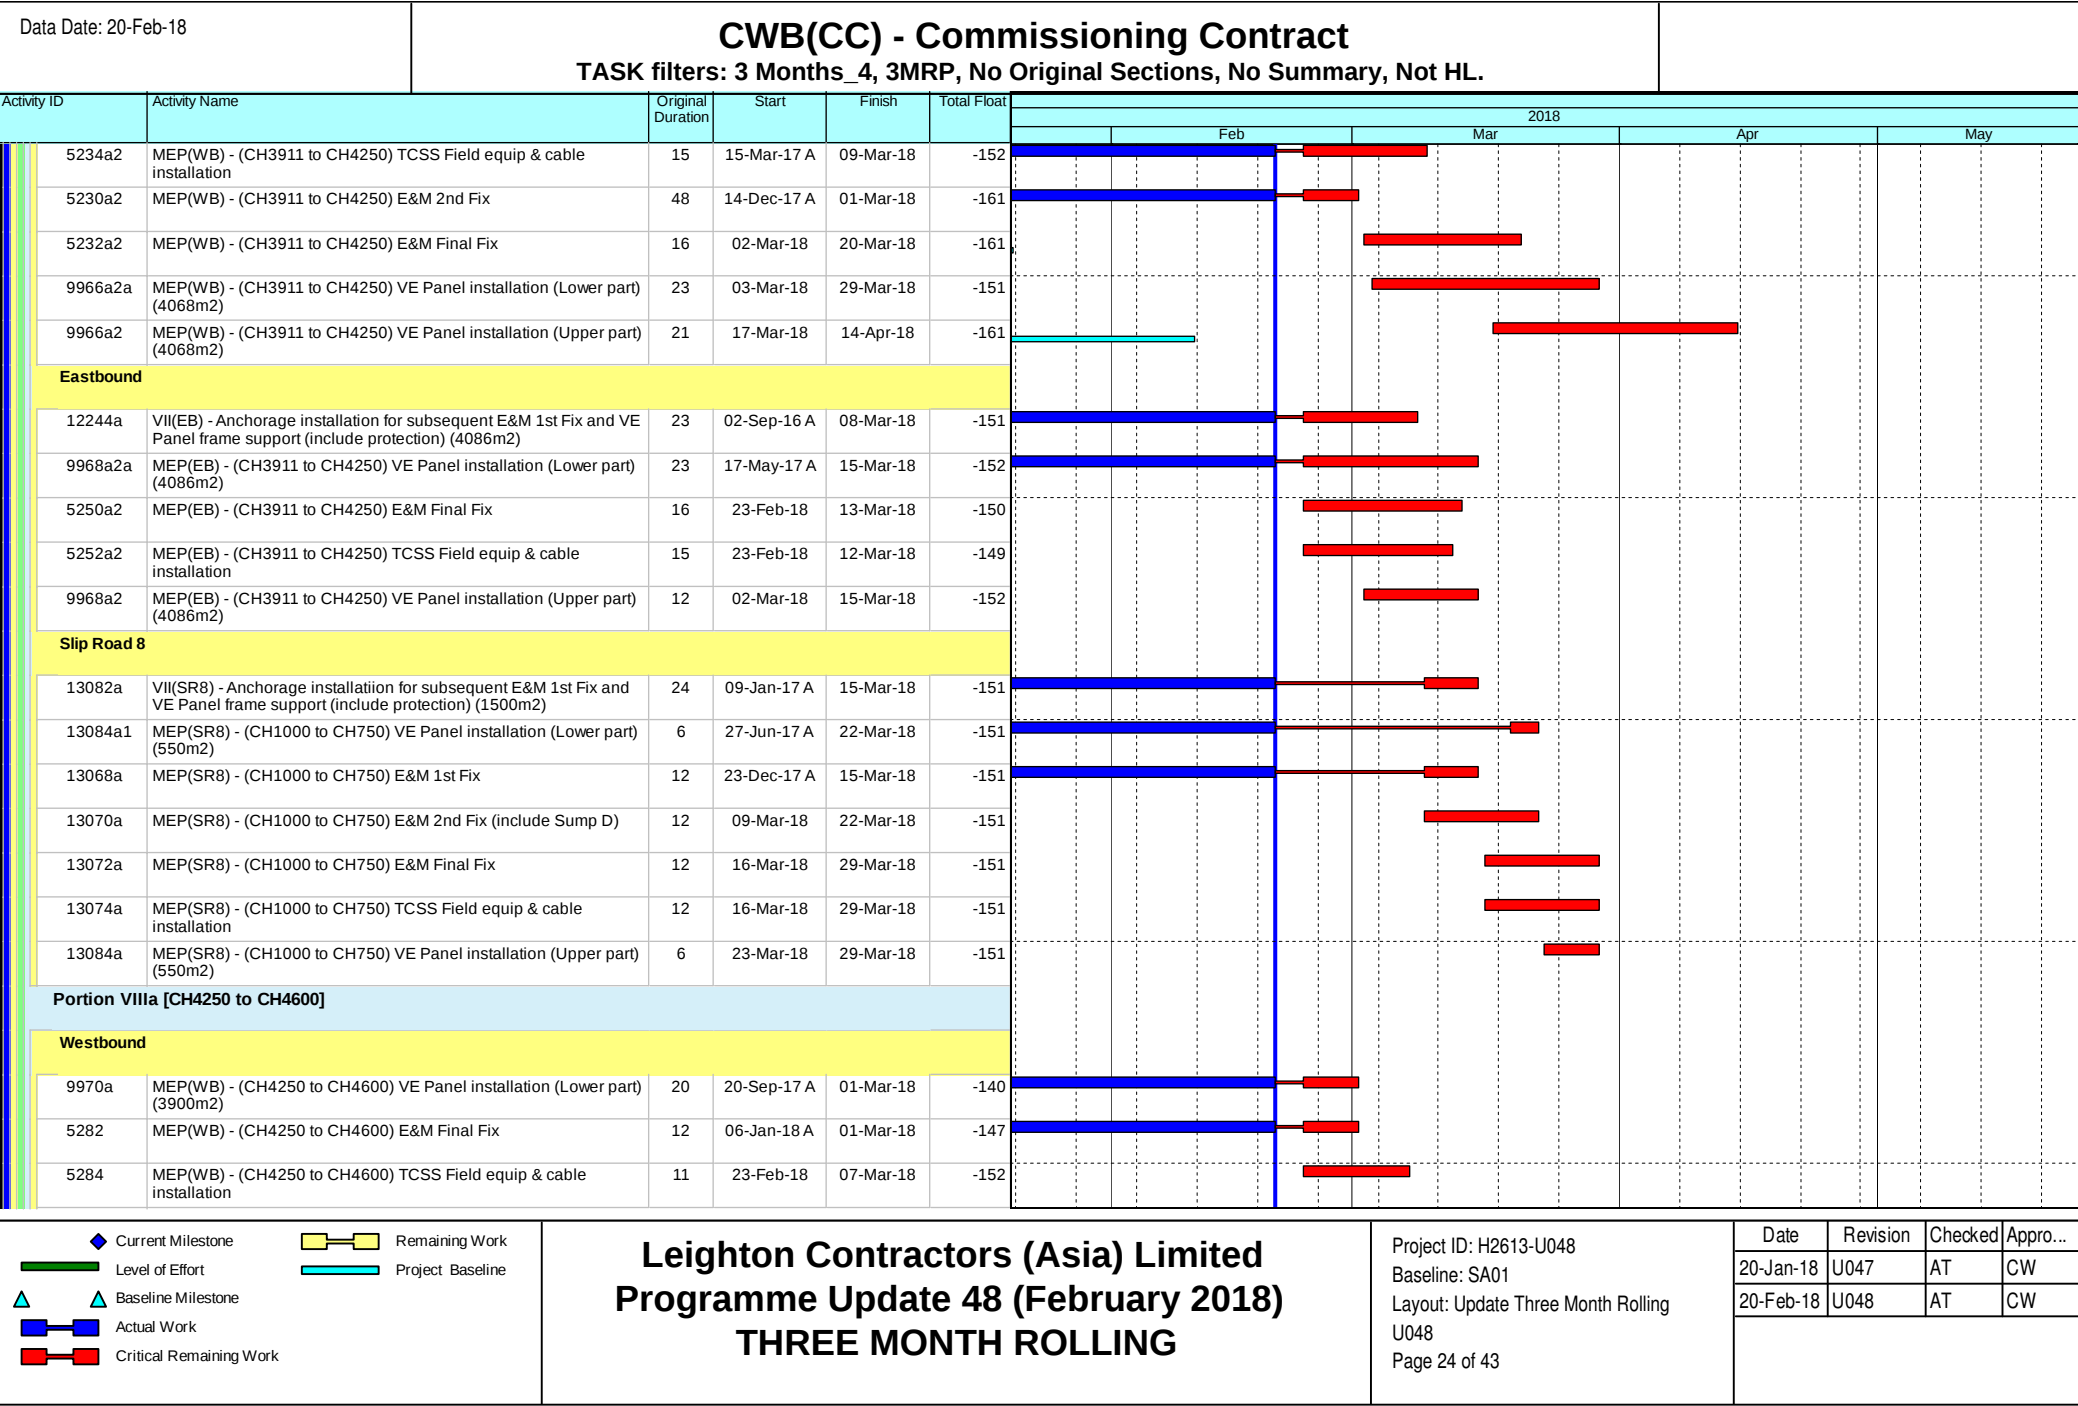


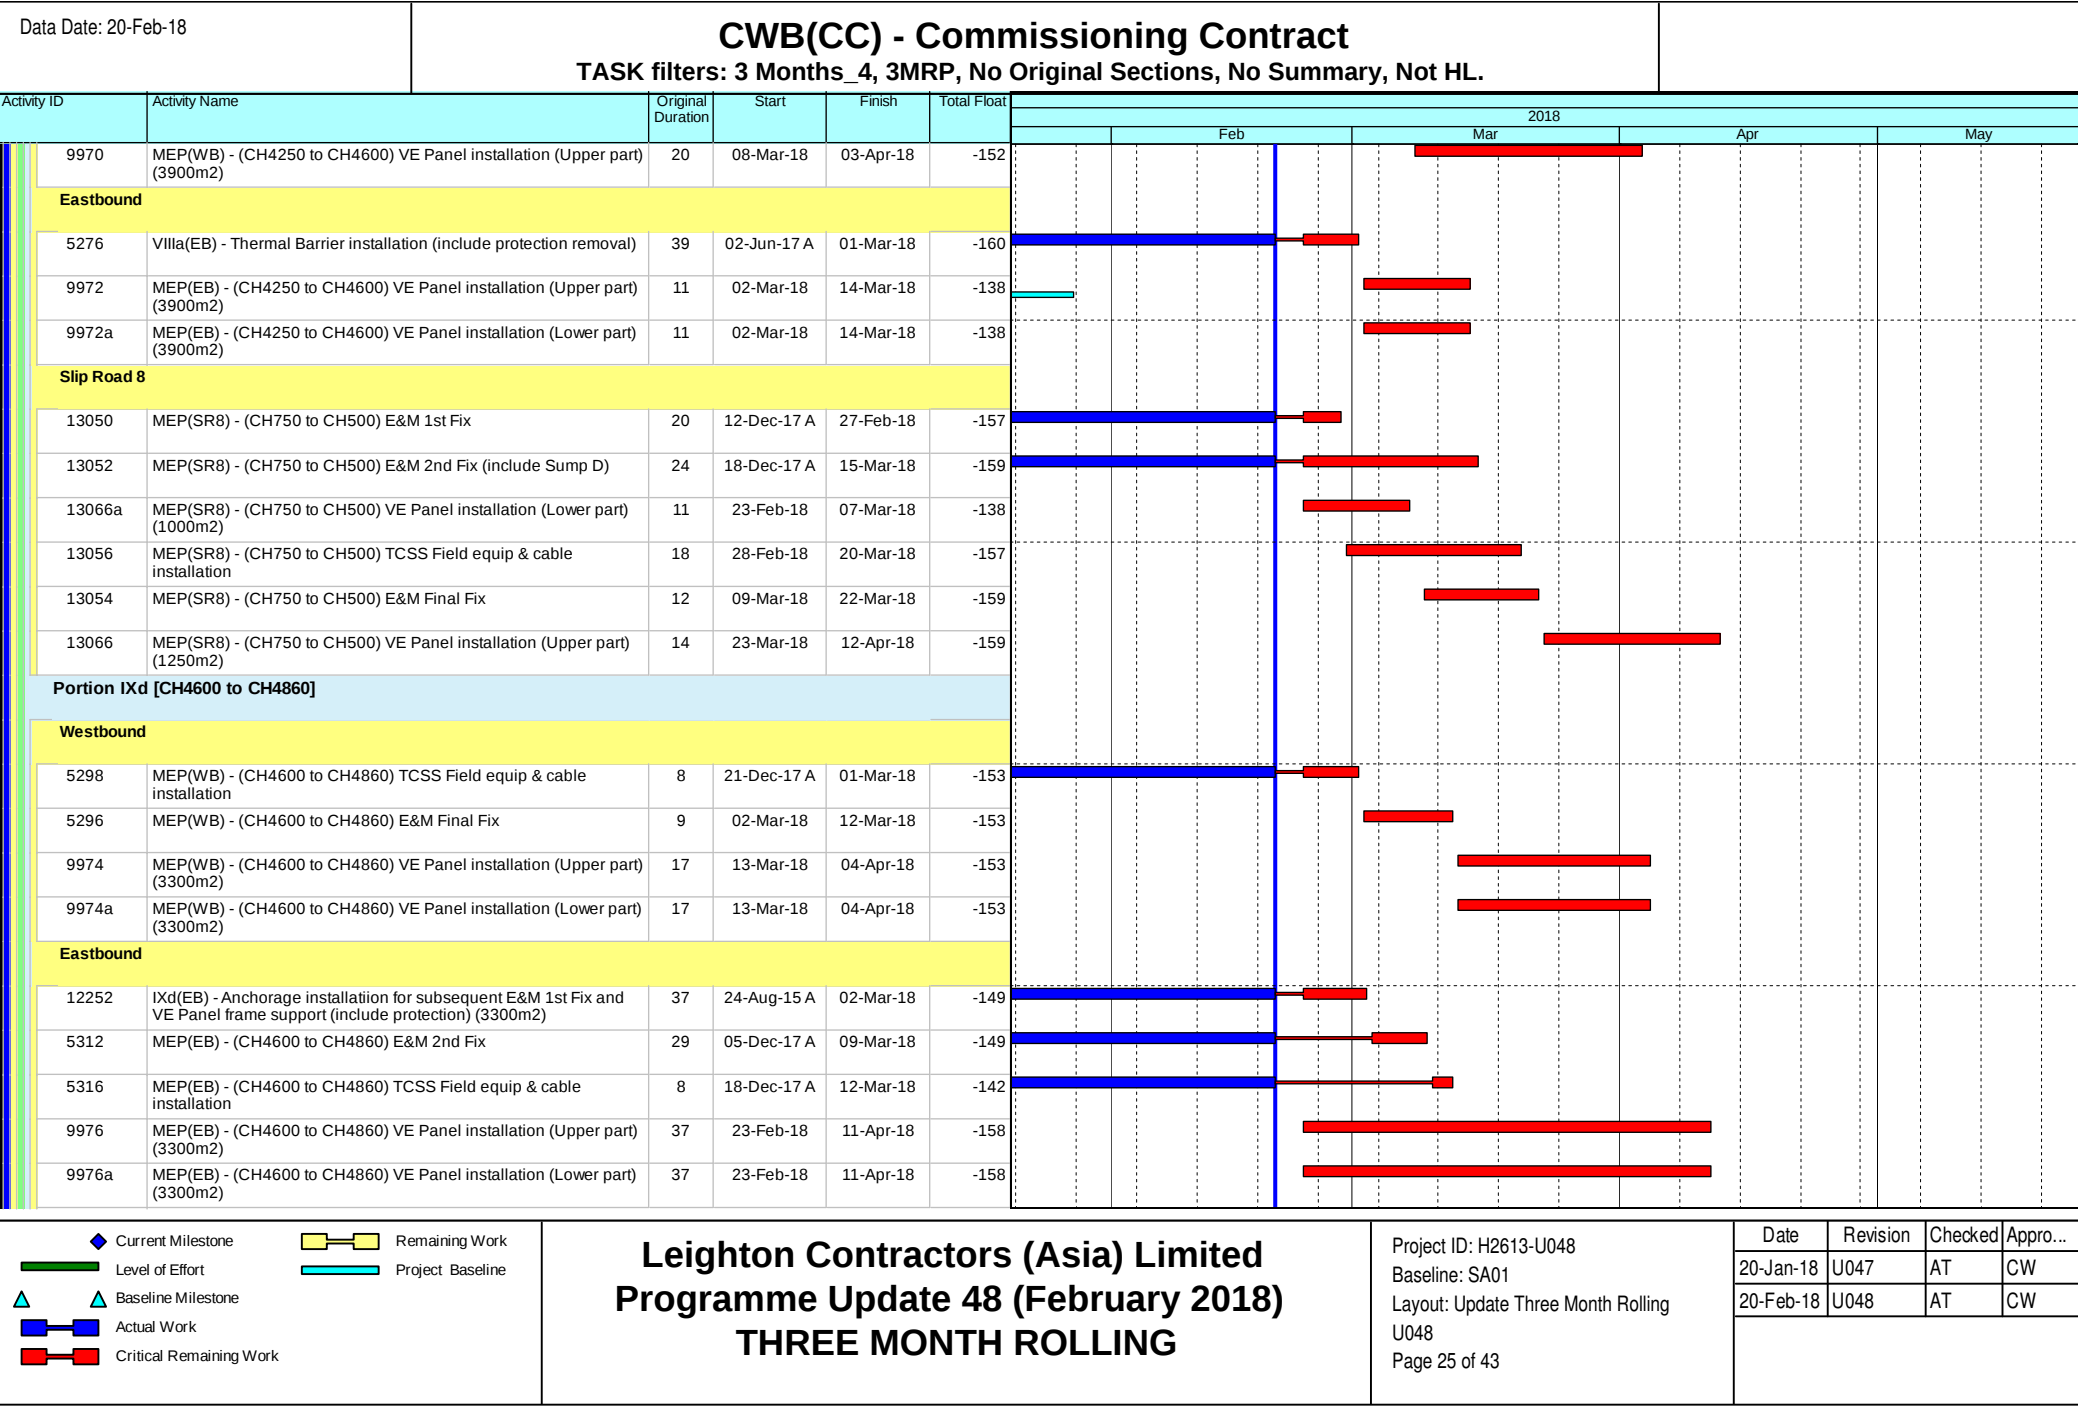


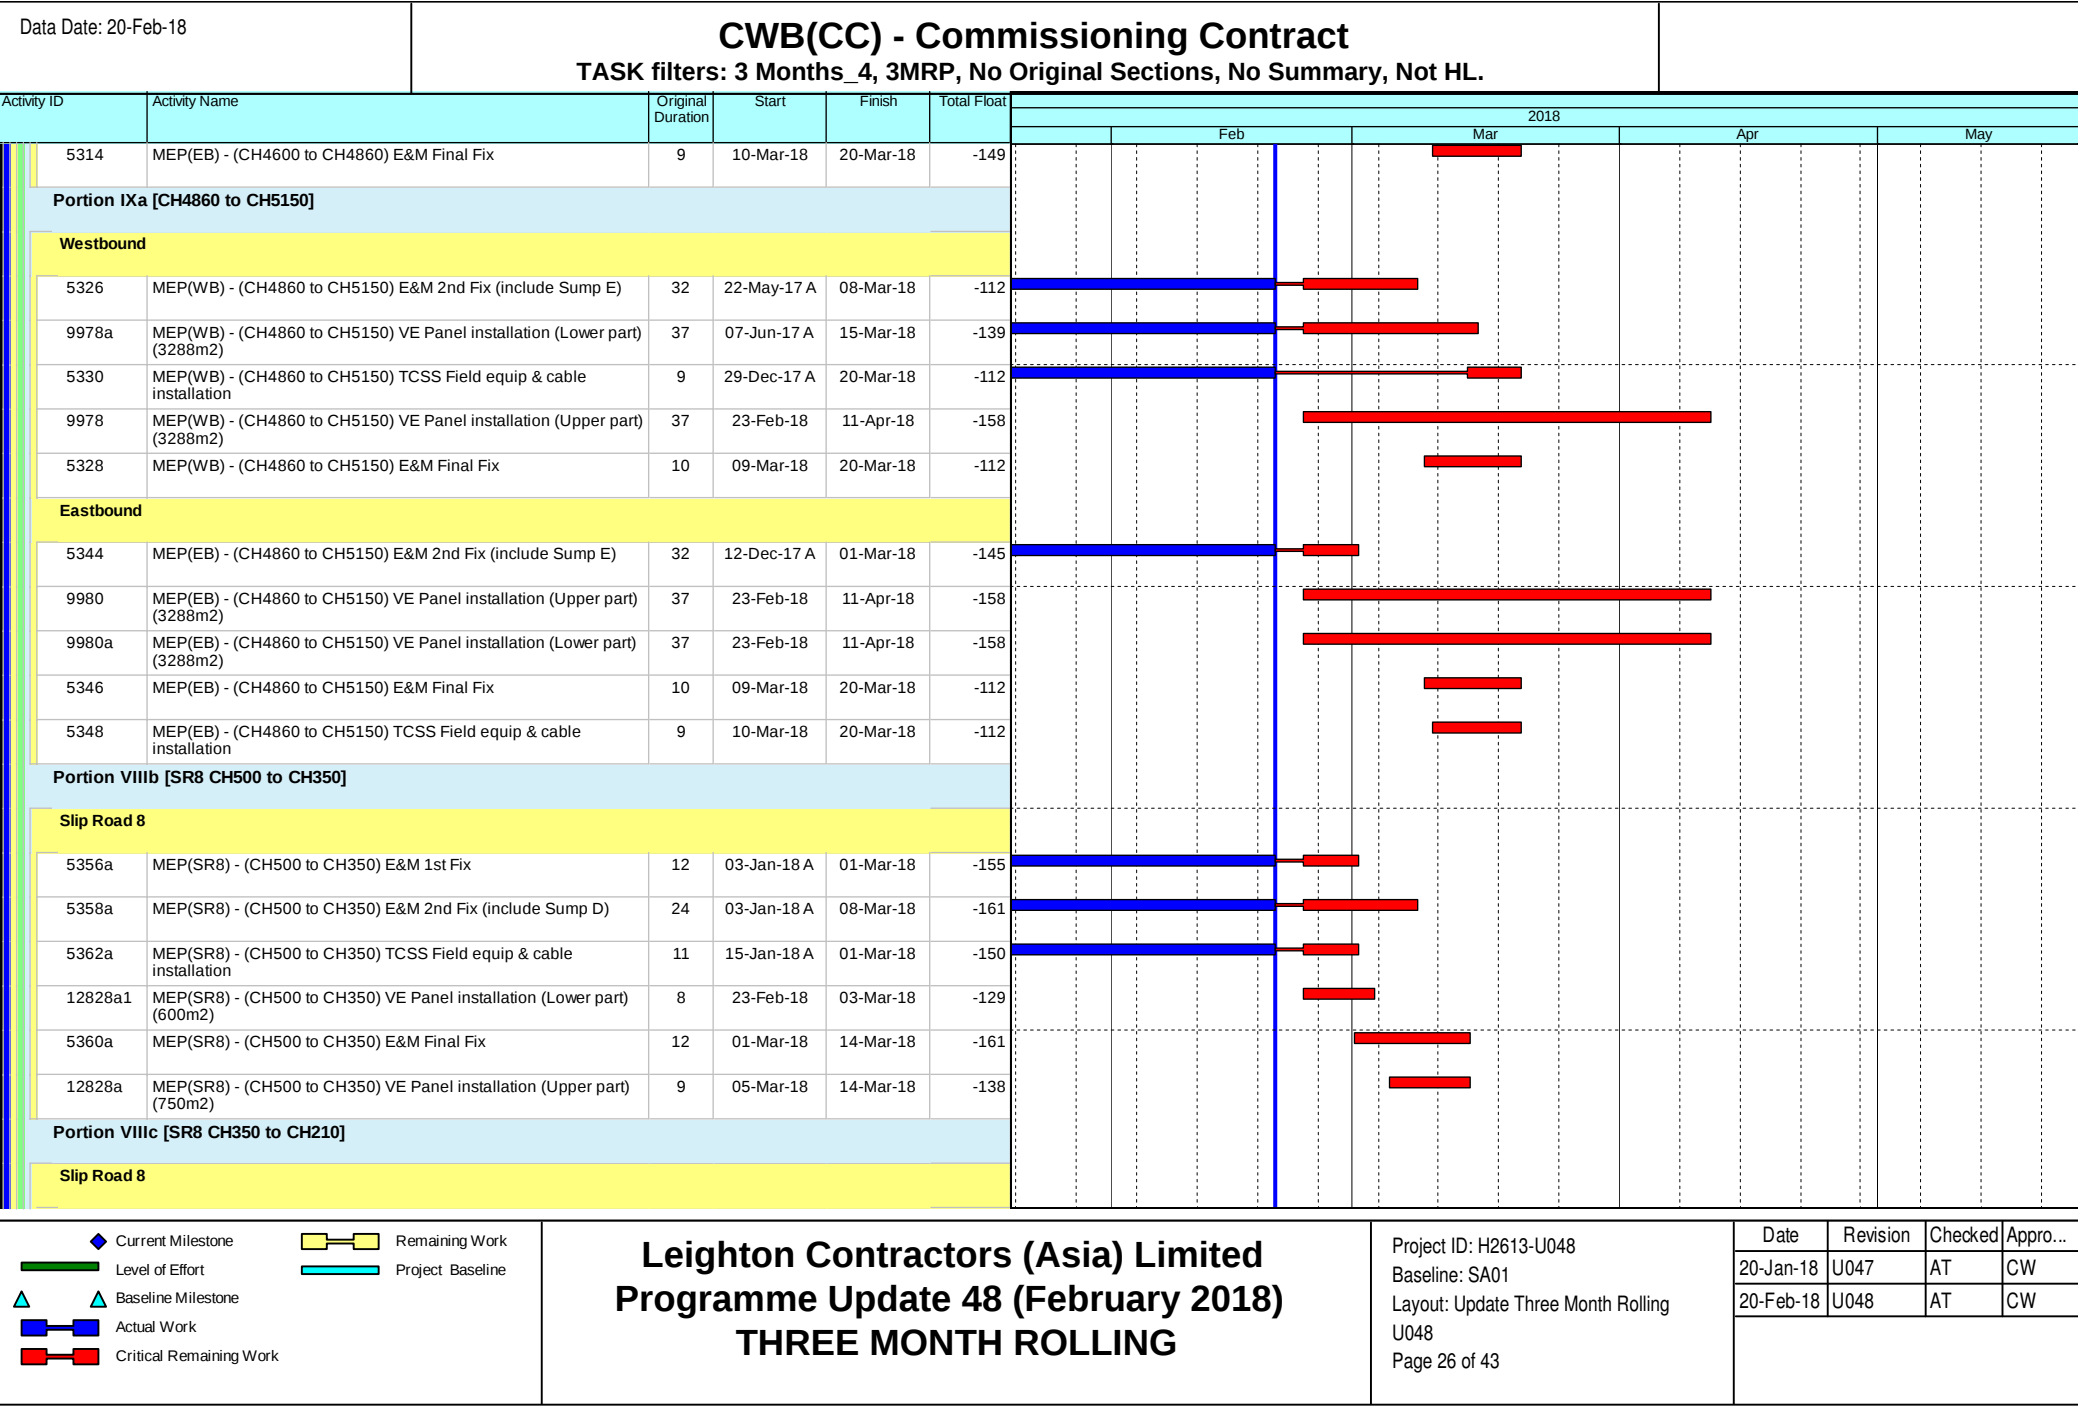

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

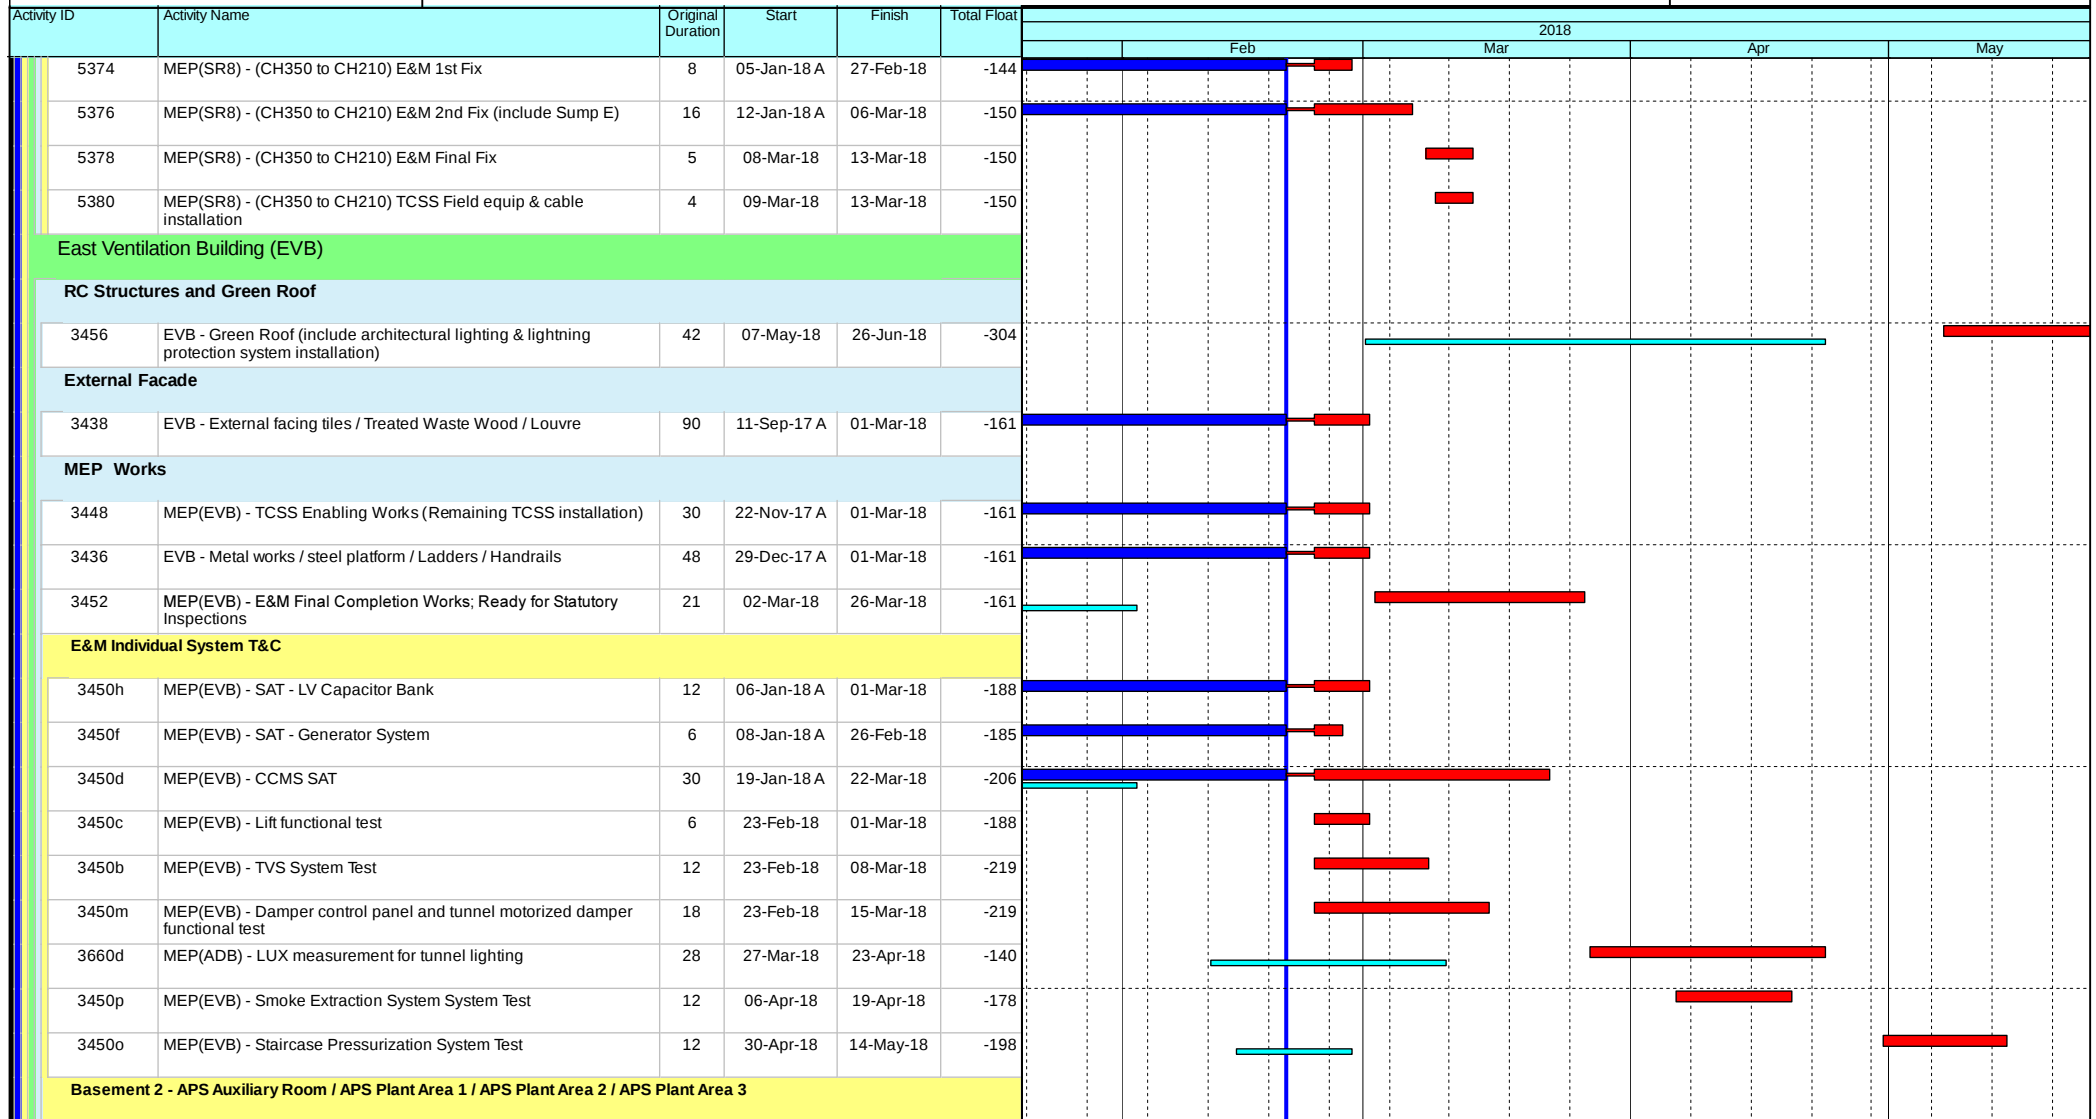


Leighton Contractors (Asia) Limited


Programme Update 48 (February 2018)

THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 27 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW


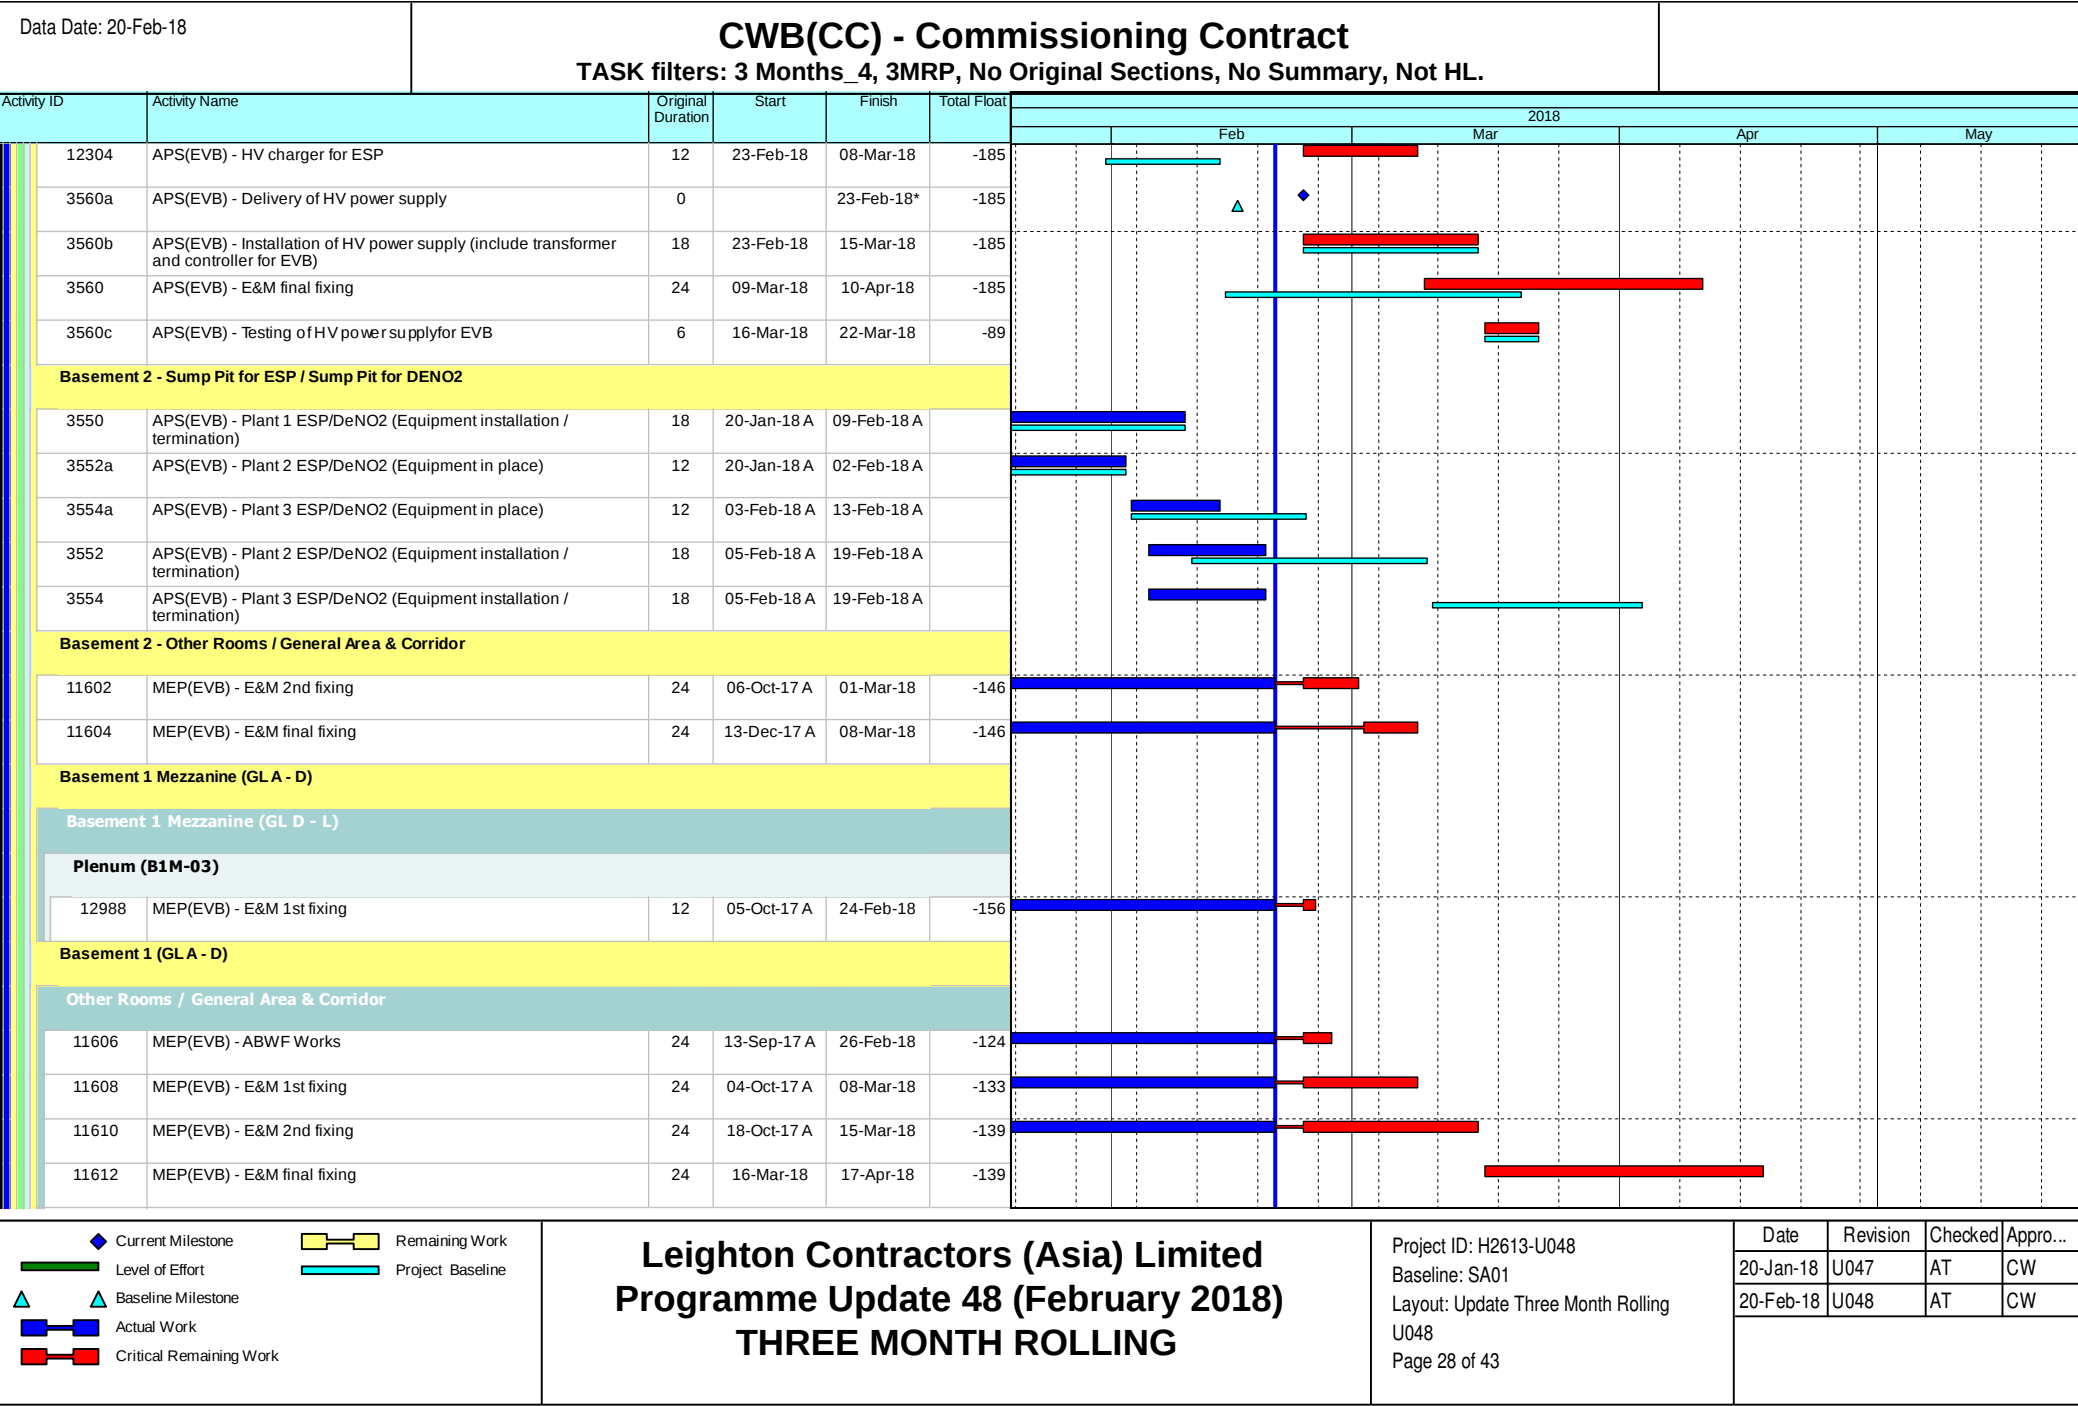


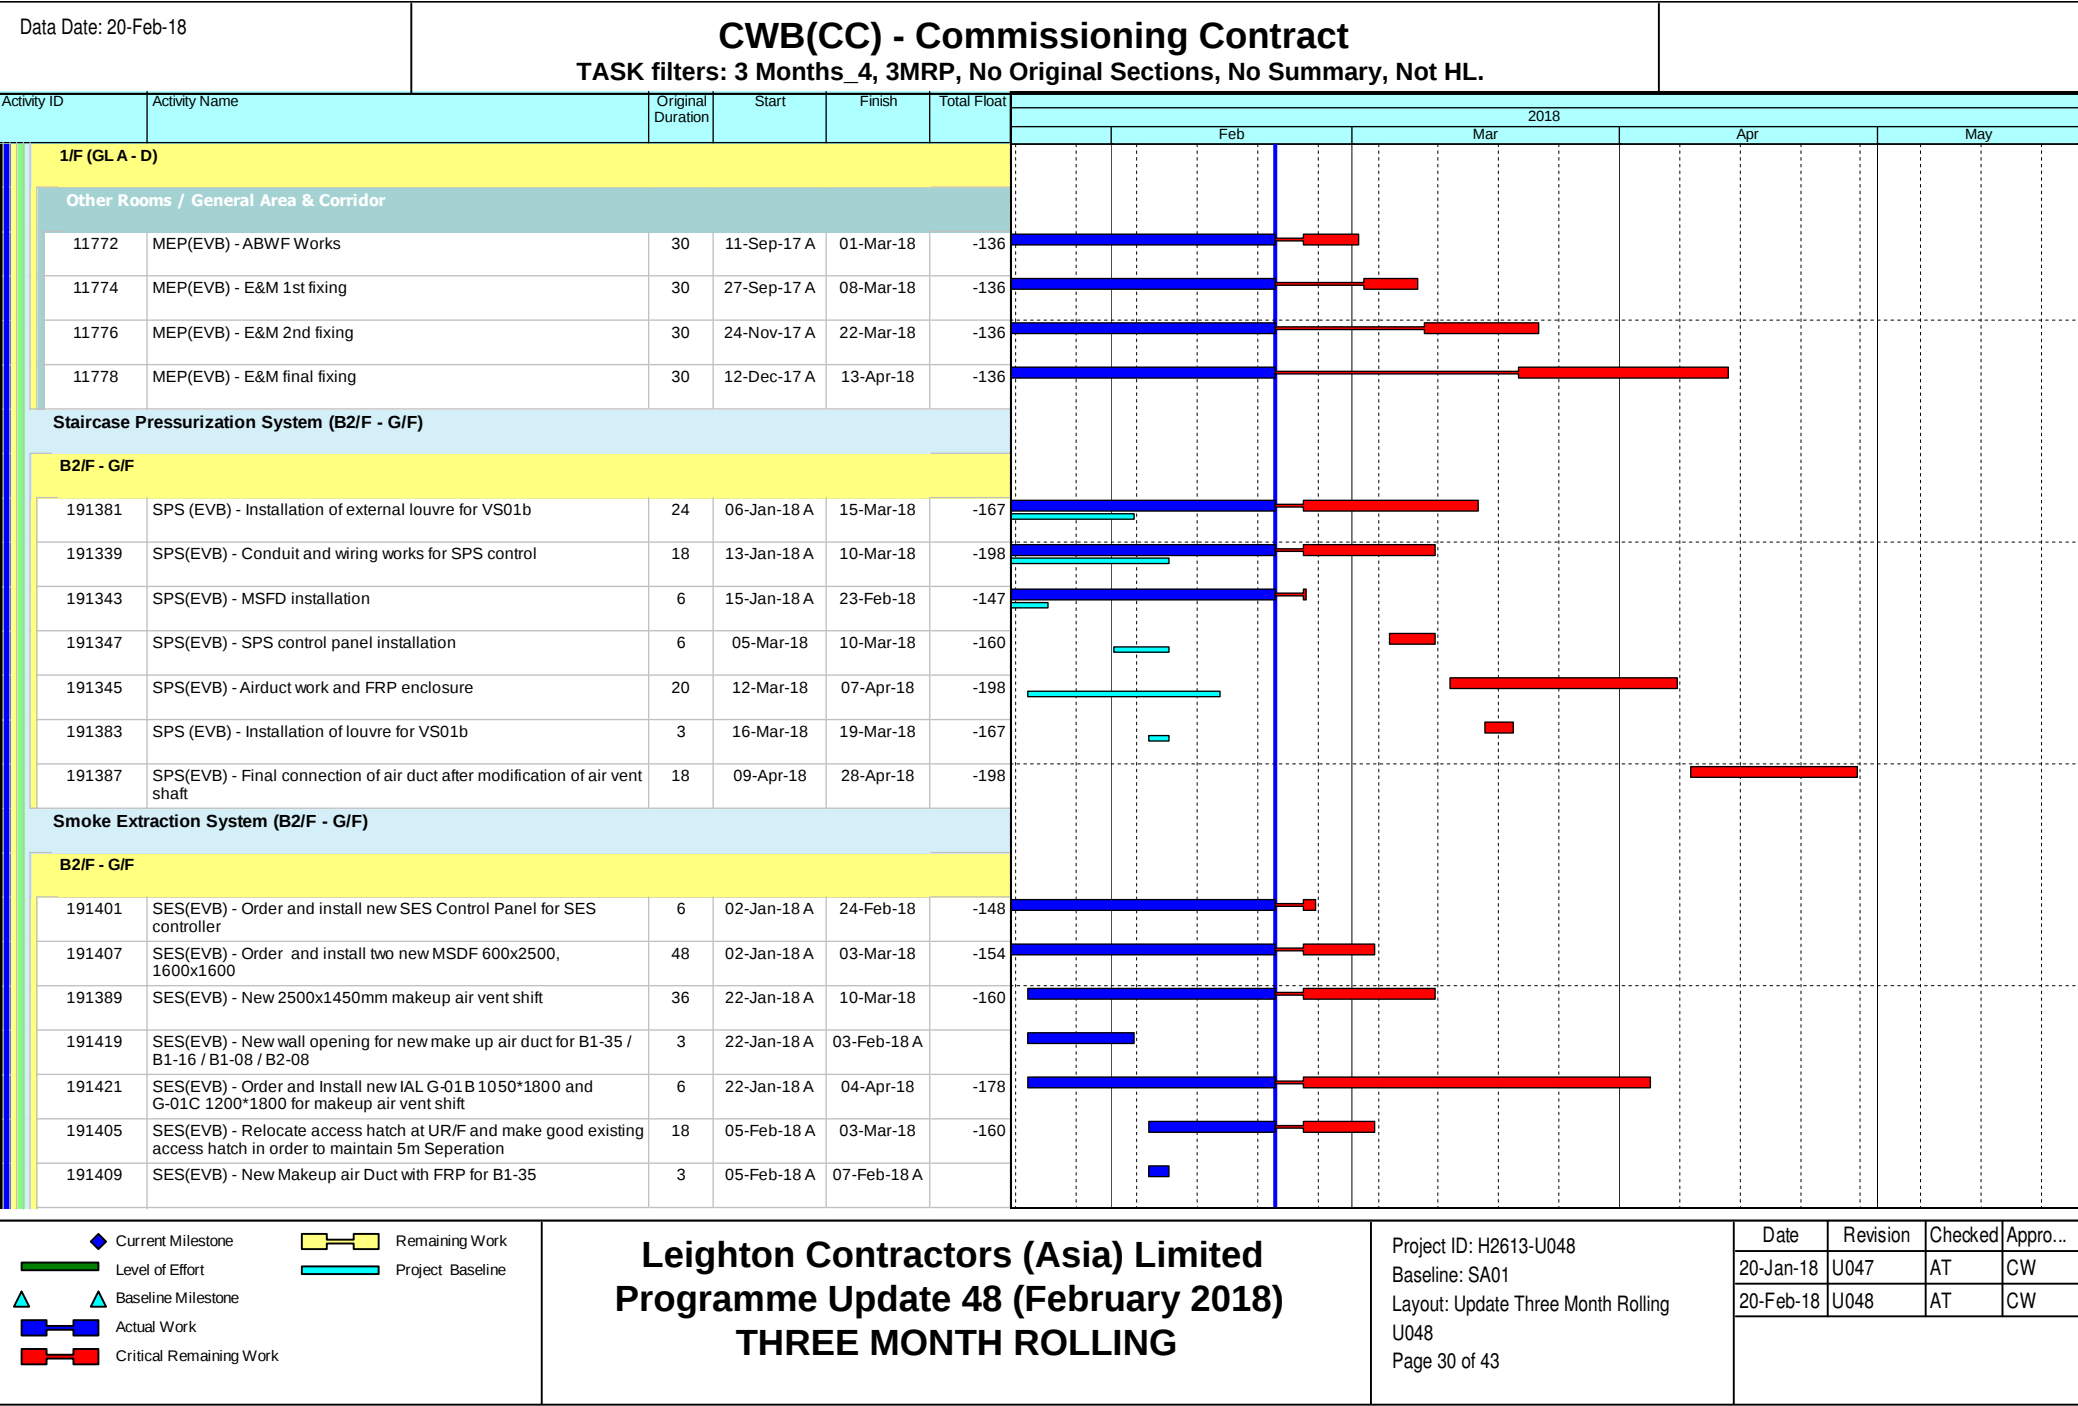

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

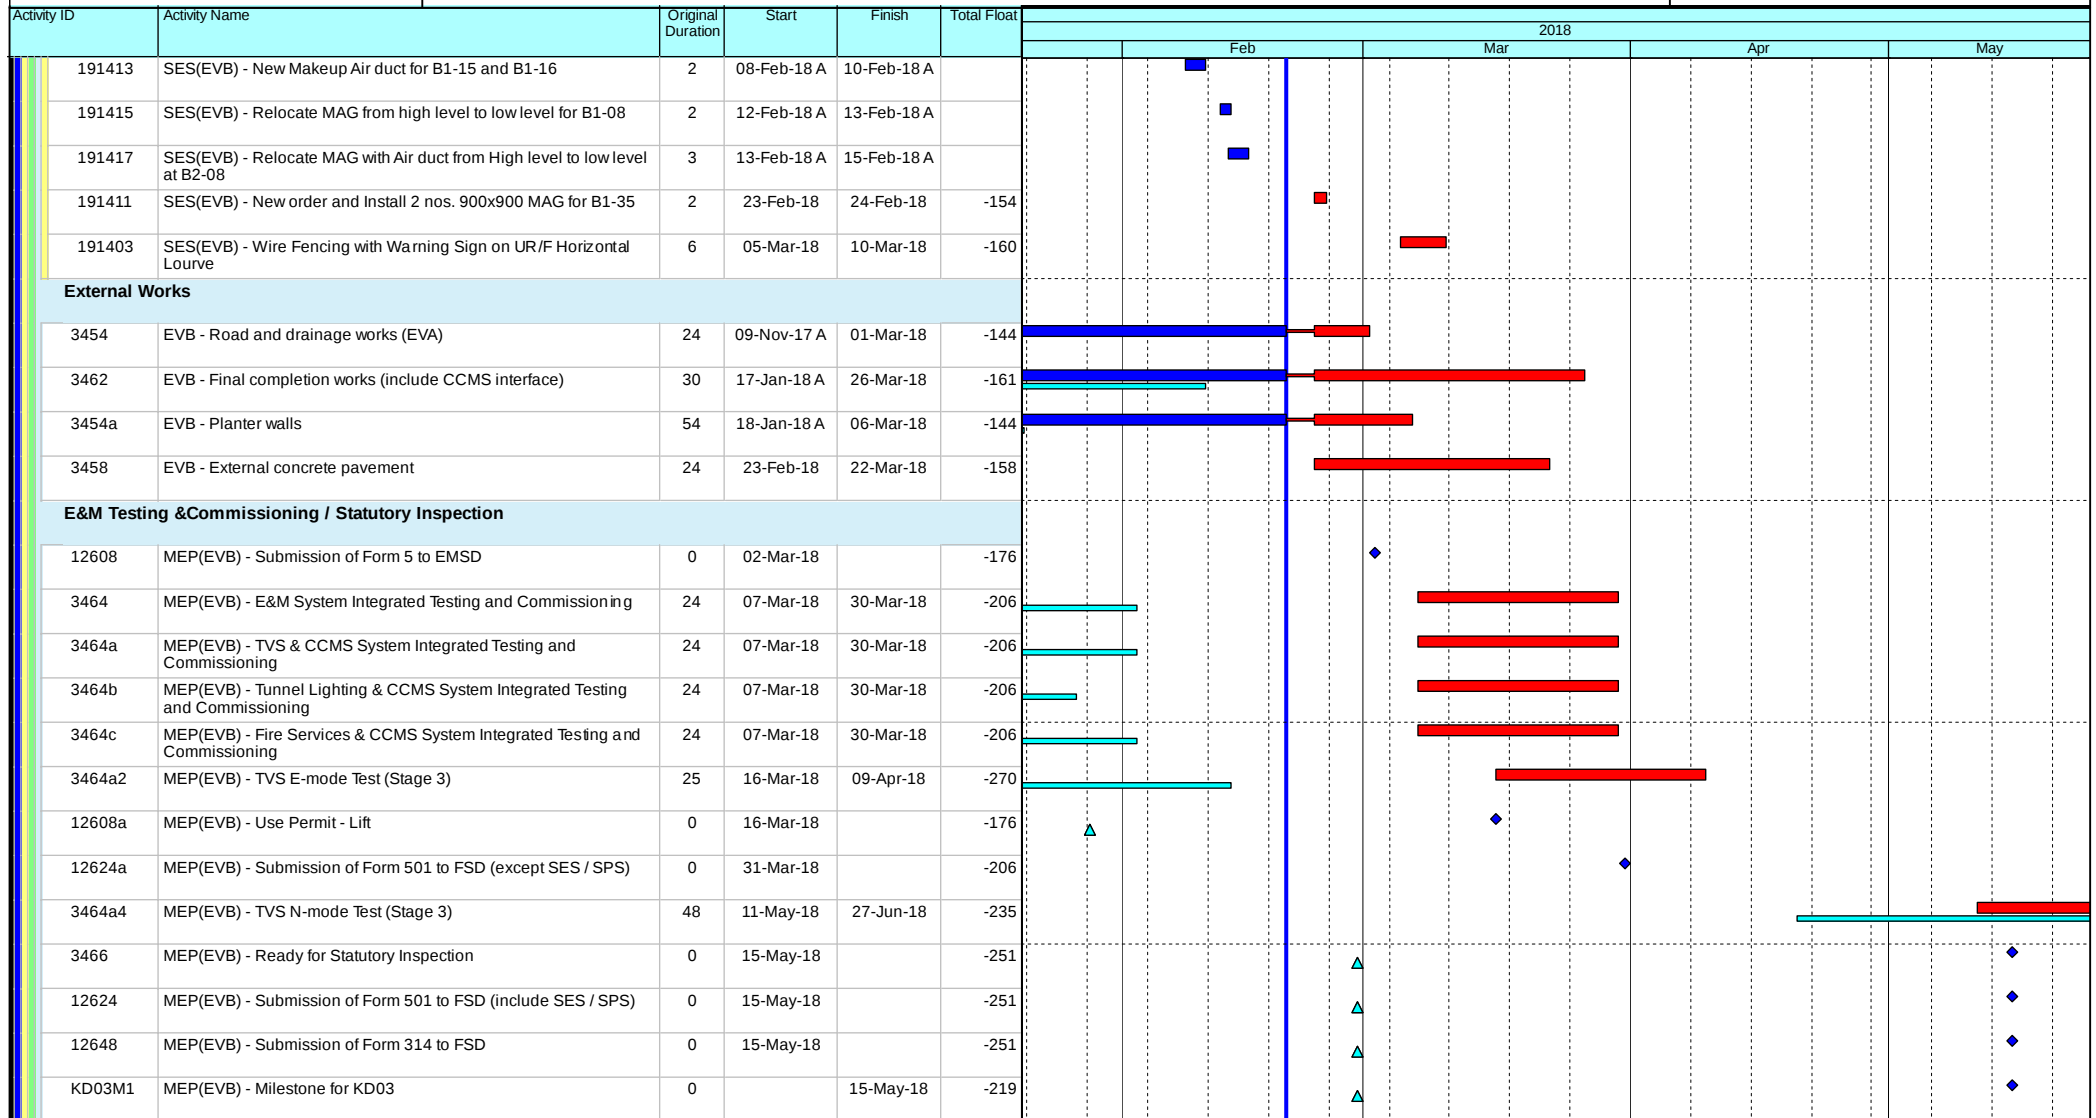

Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 31 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

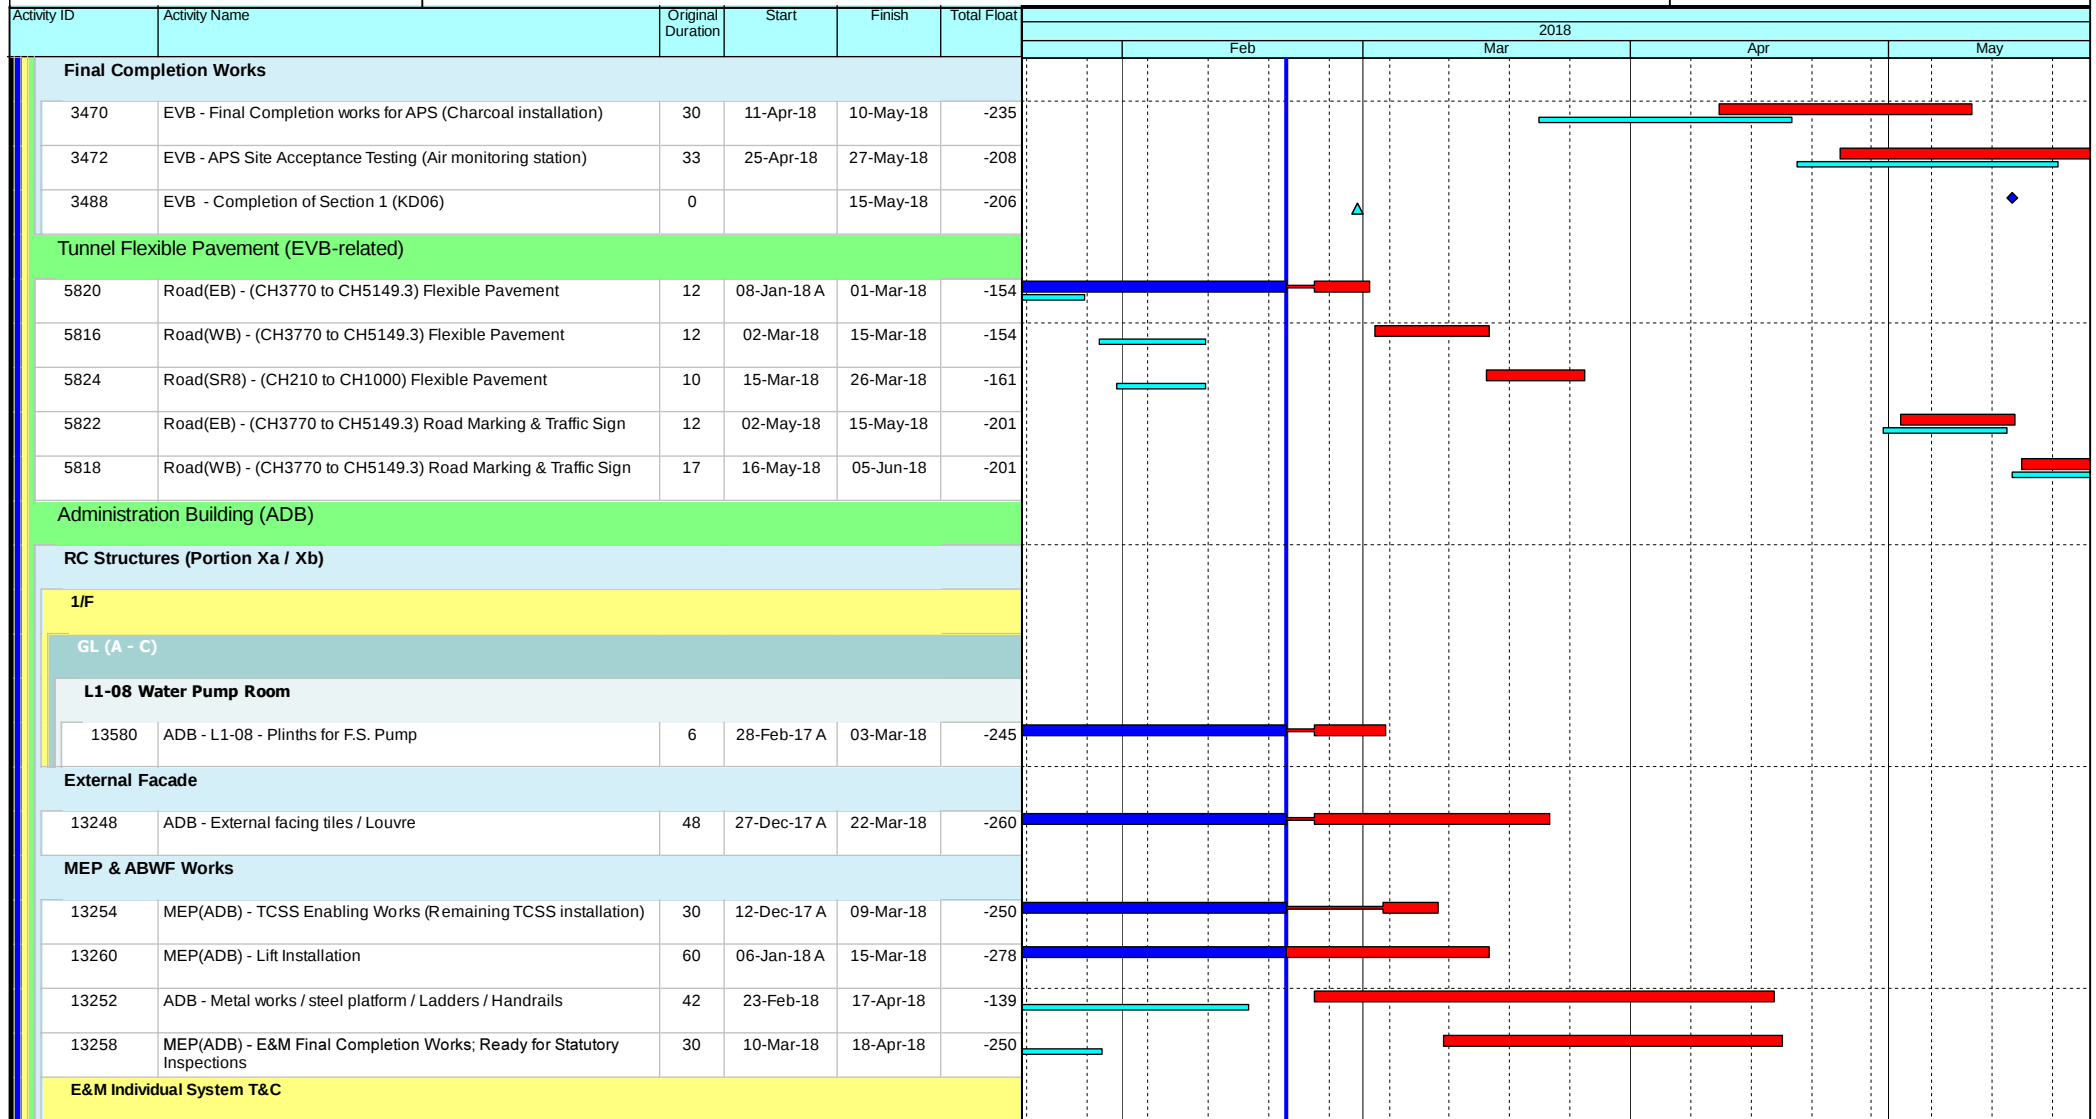

Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 32 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

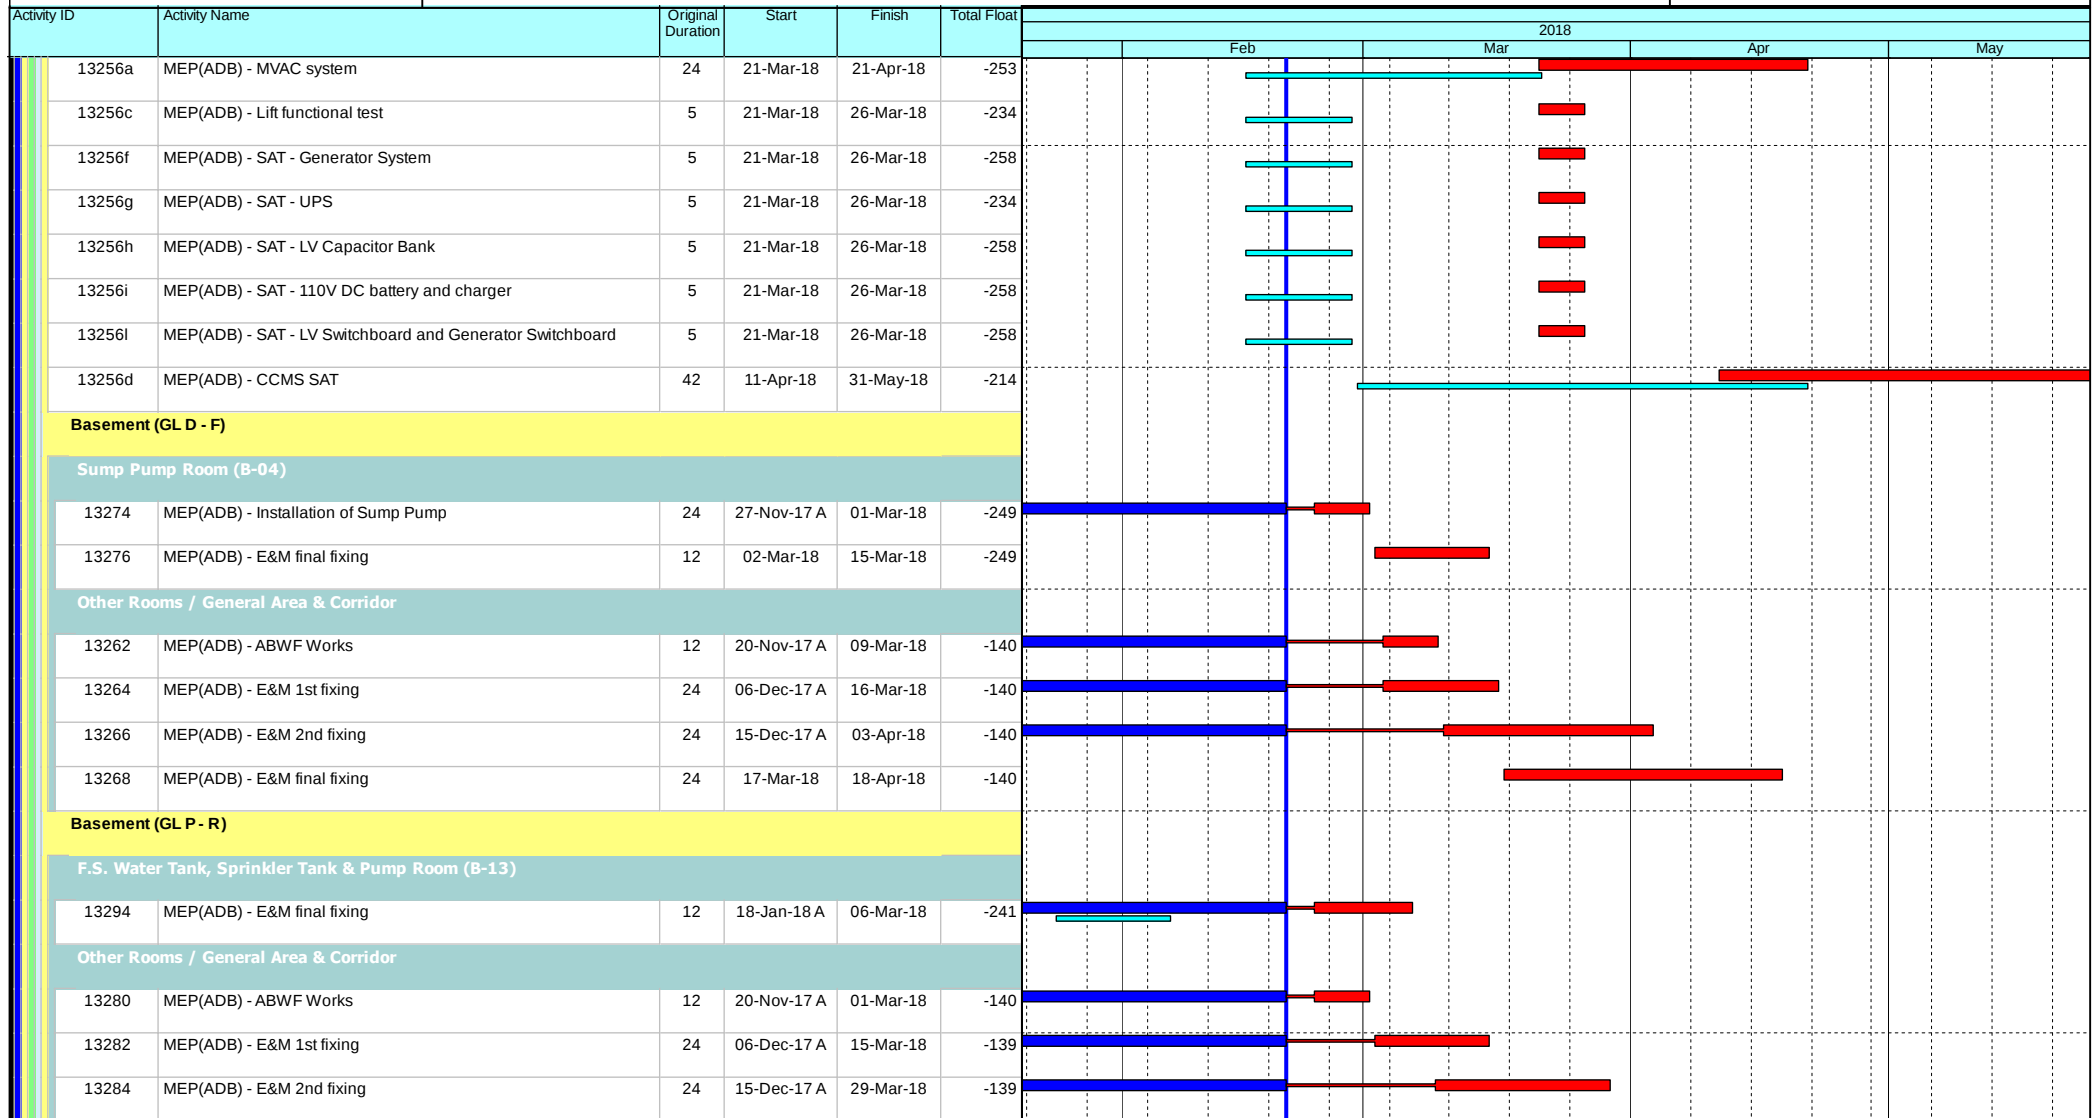

Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 33 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

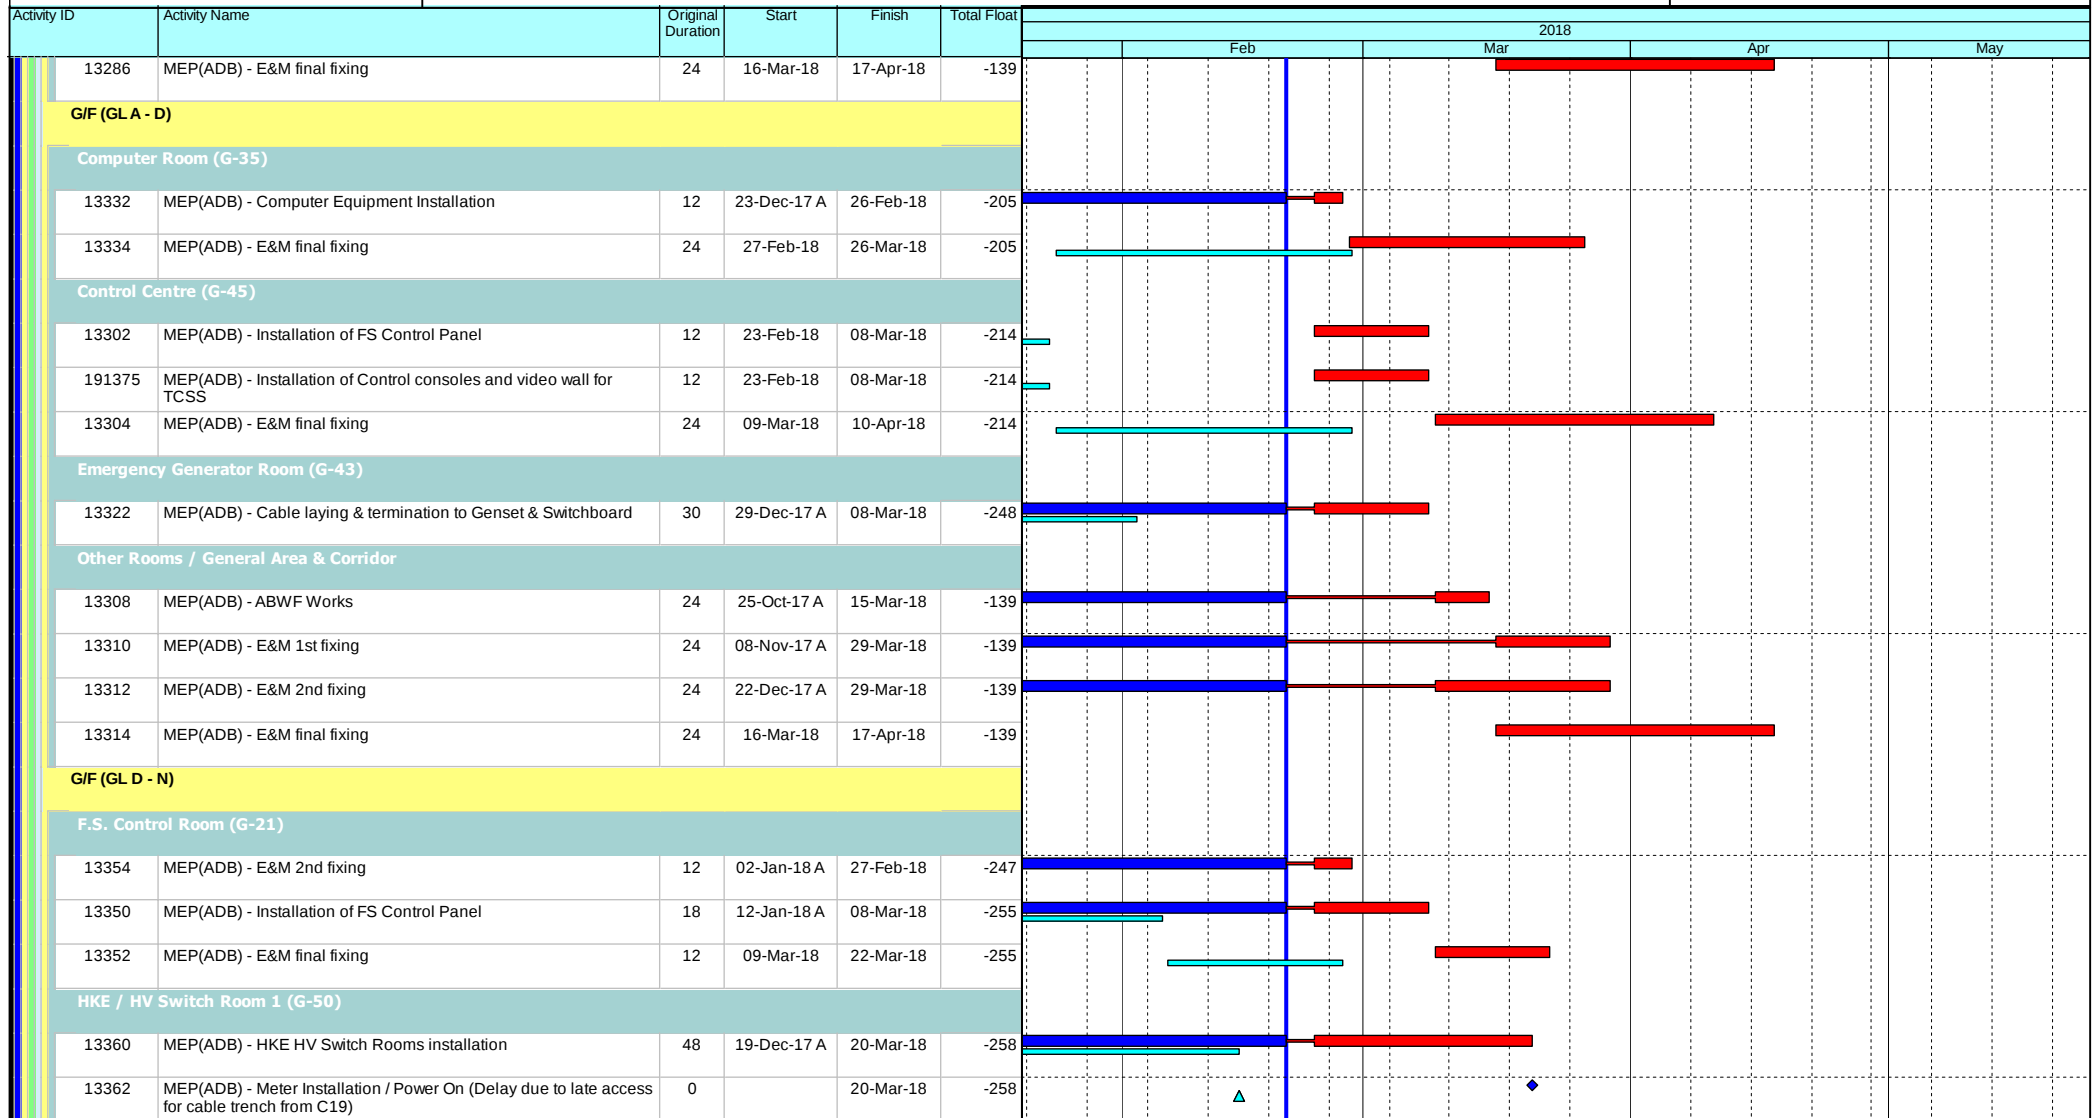

Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 34 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

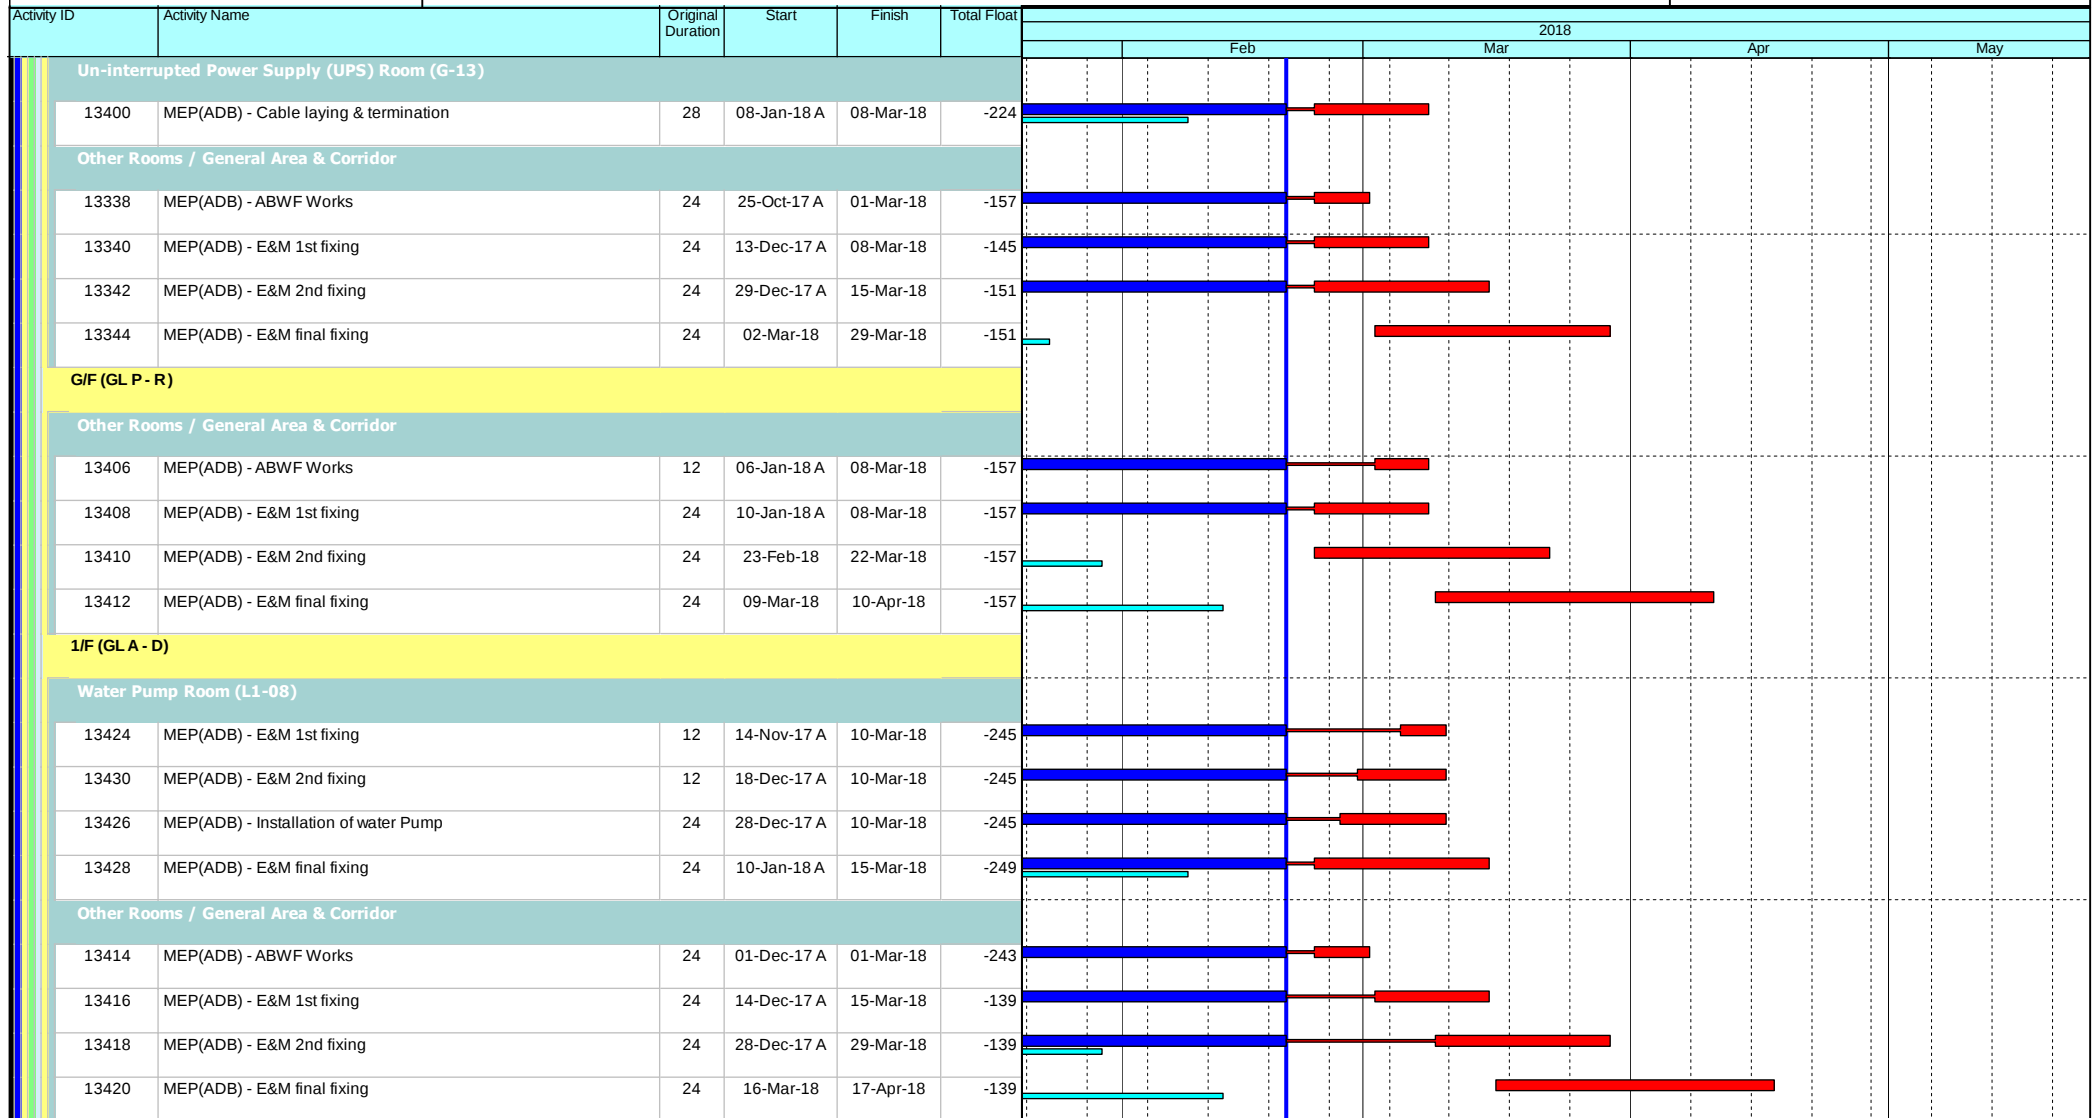

Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING



Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 35 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

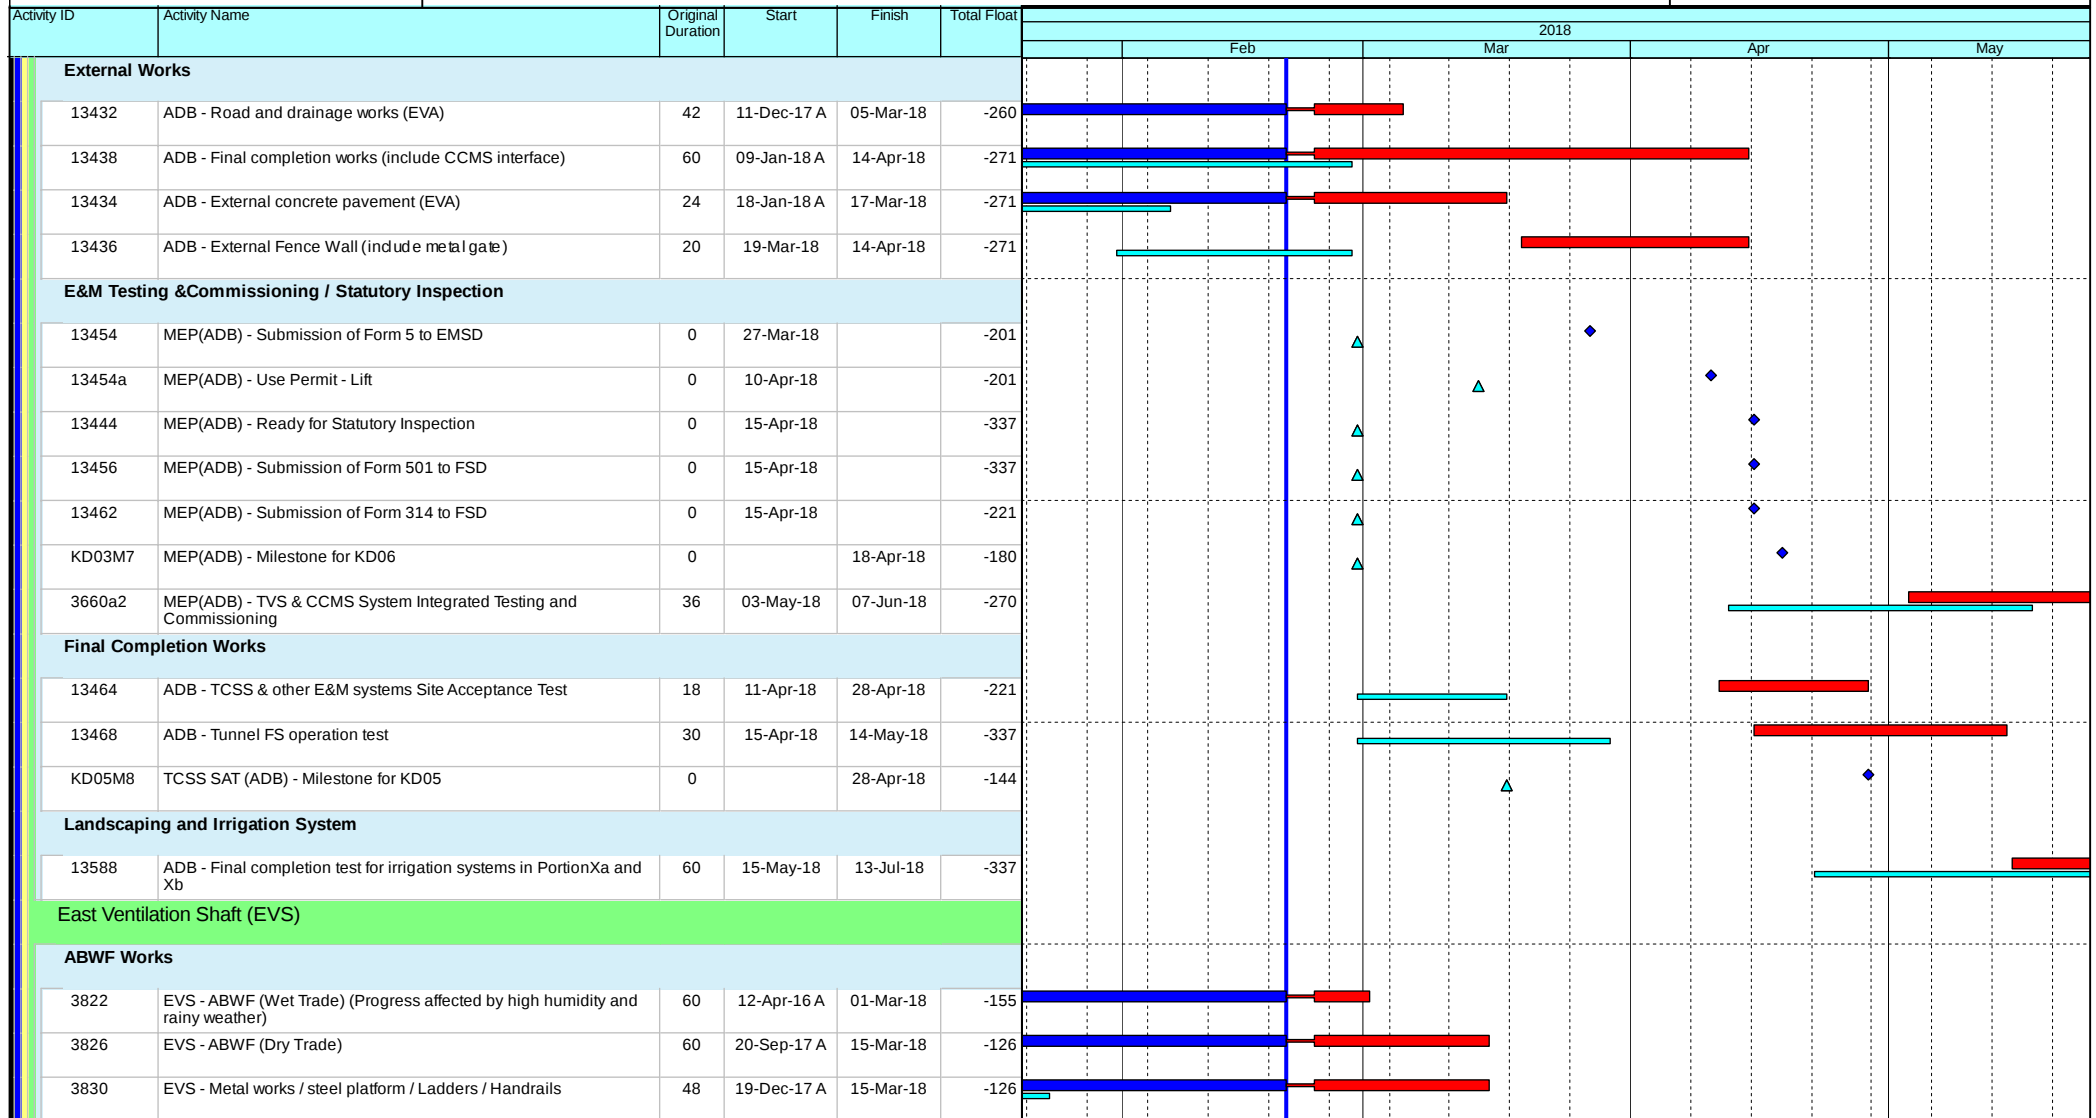


Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 36 of 43



Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

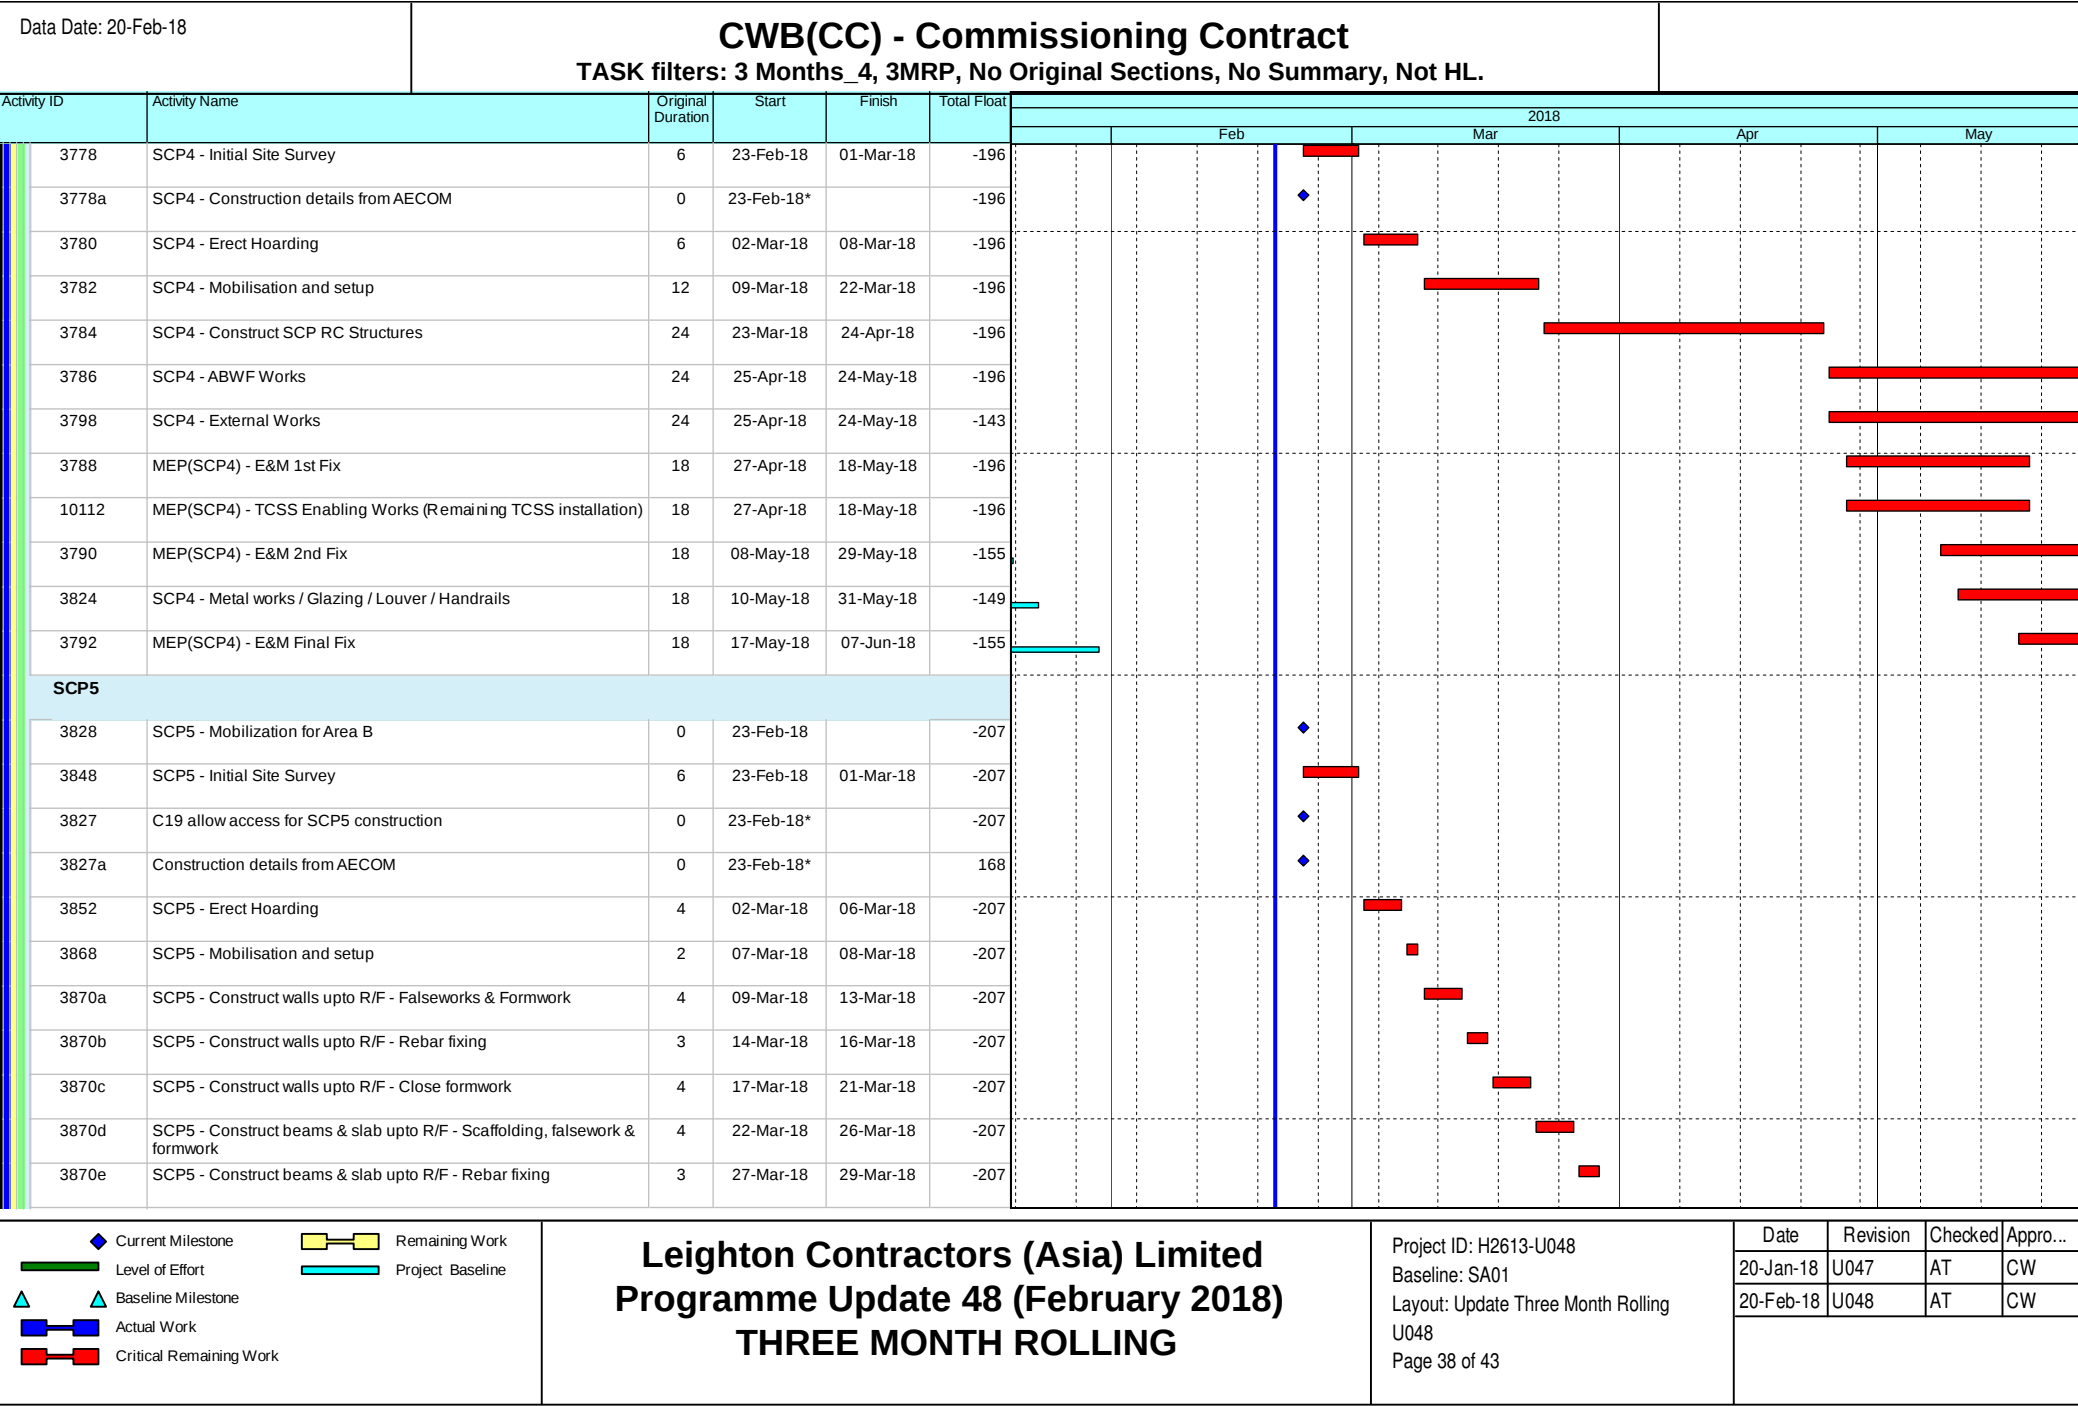

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

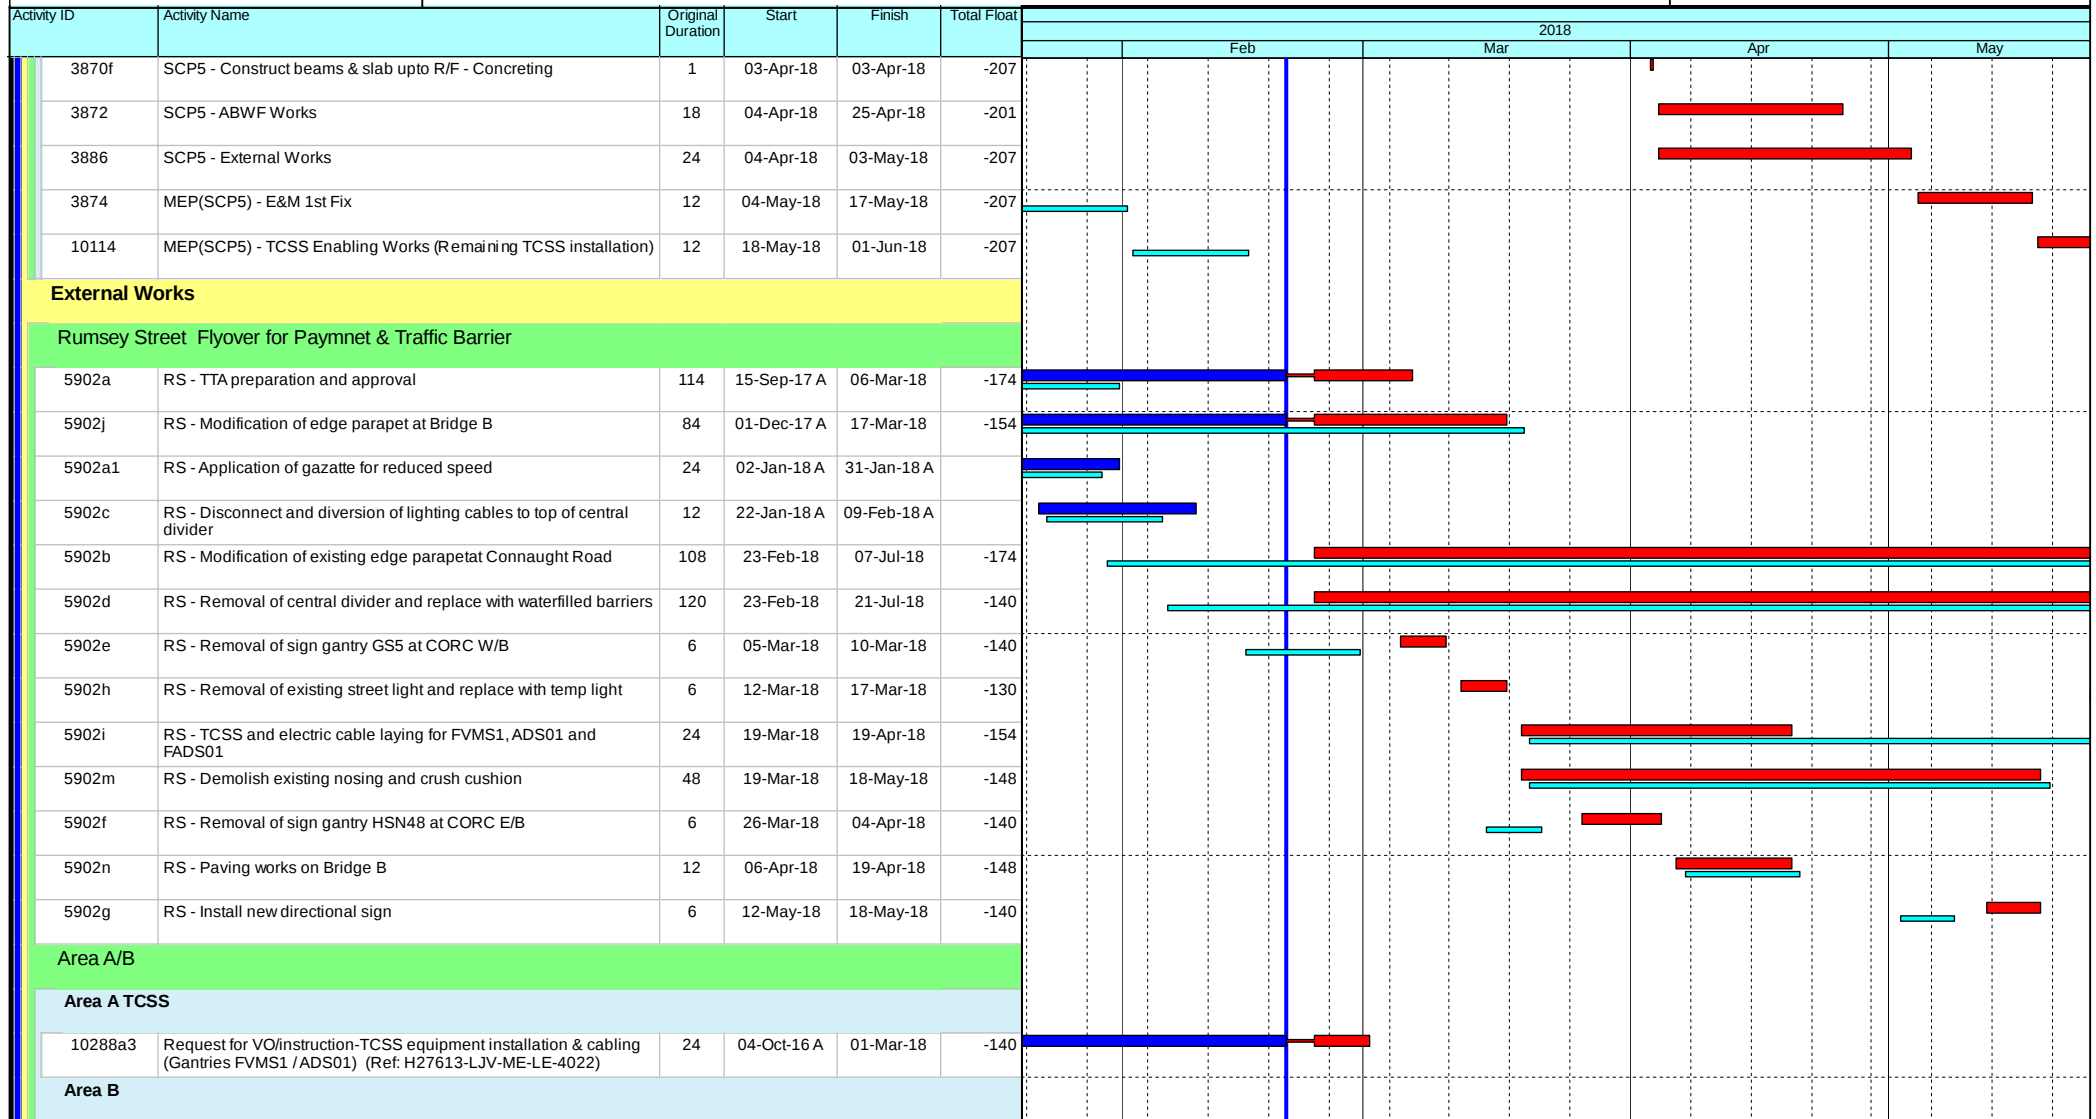


Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 39 of 43



Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

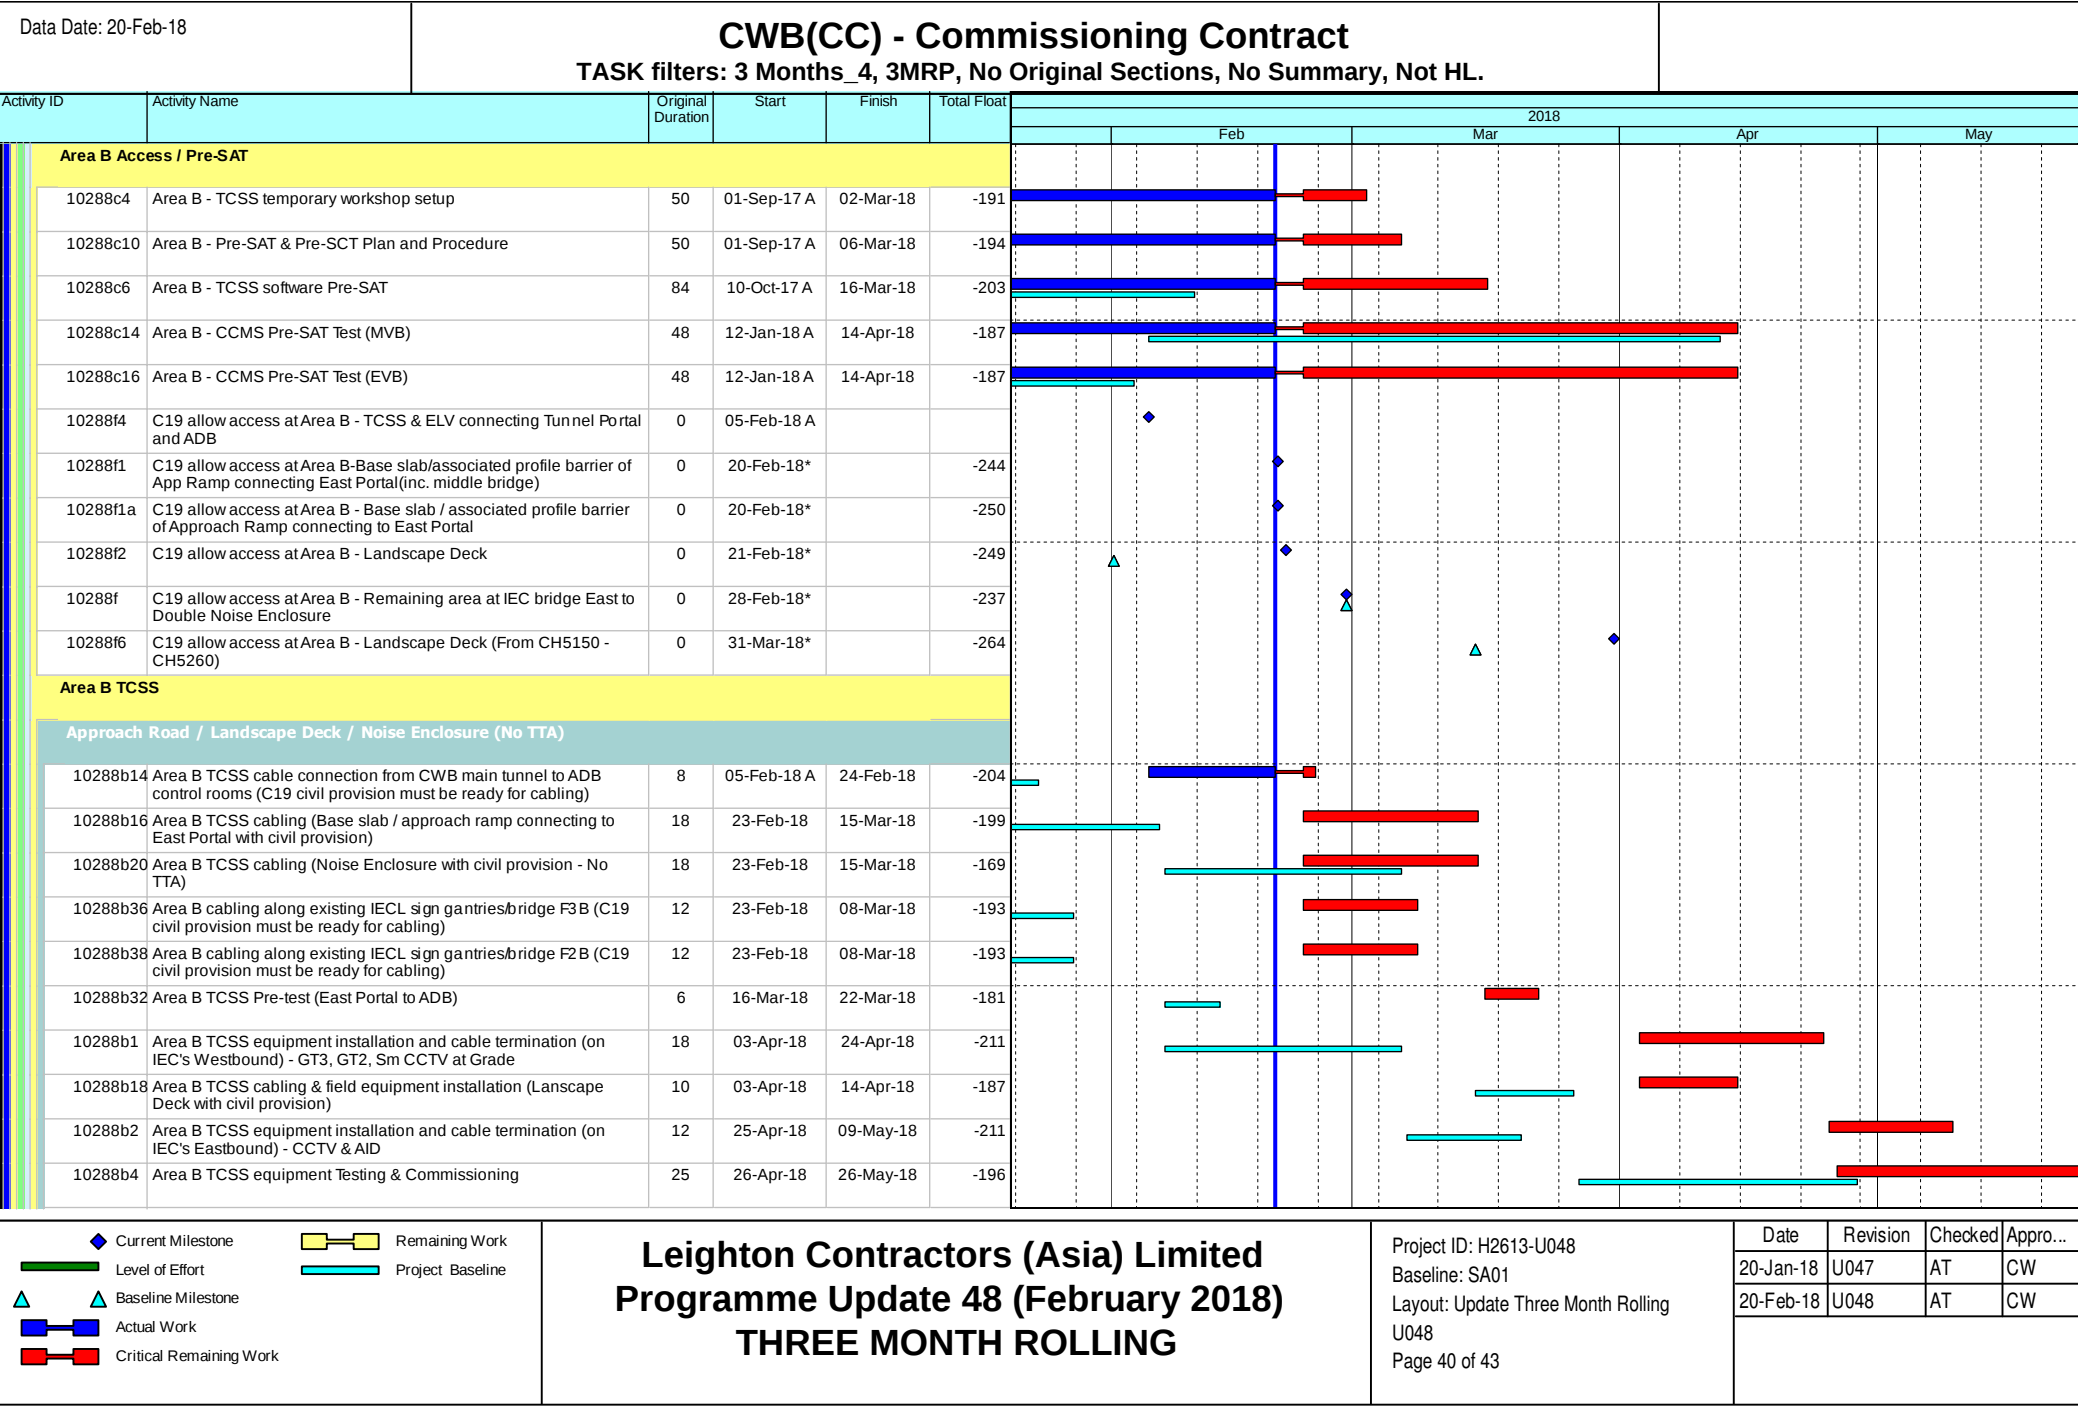

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

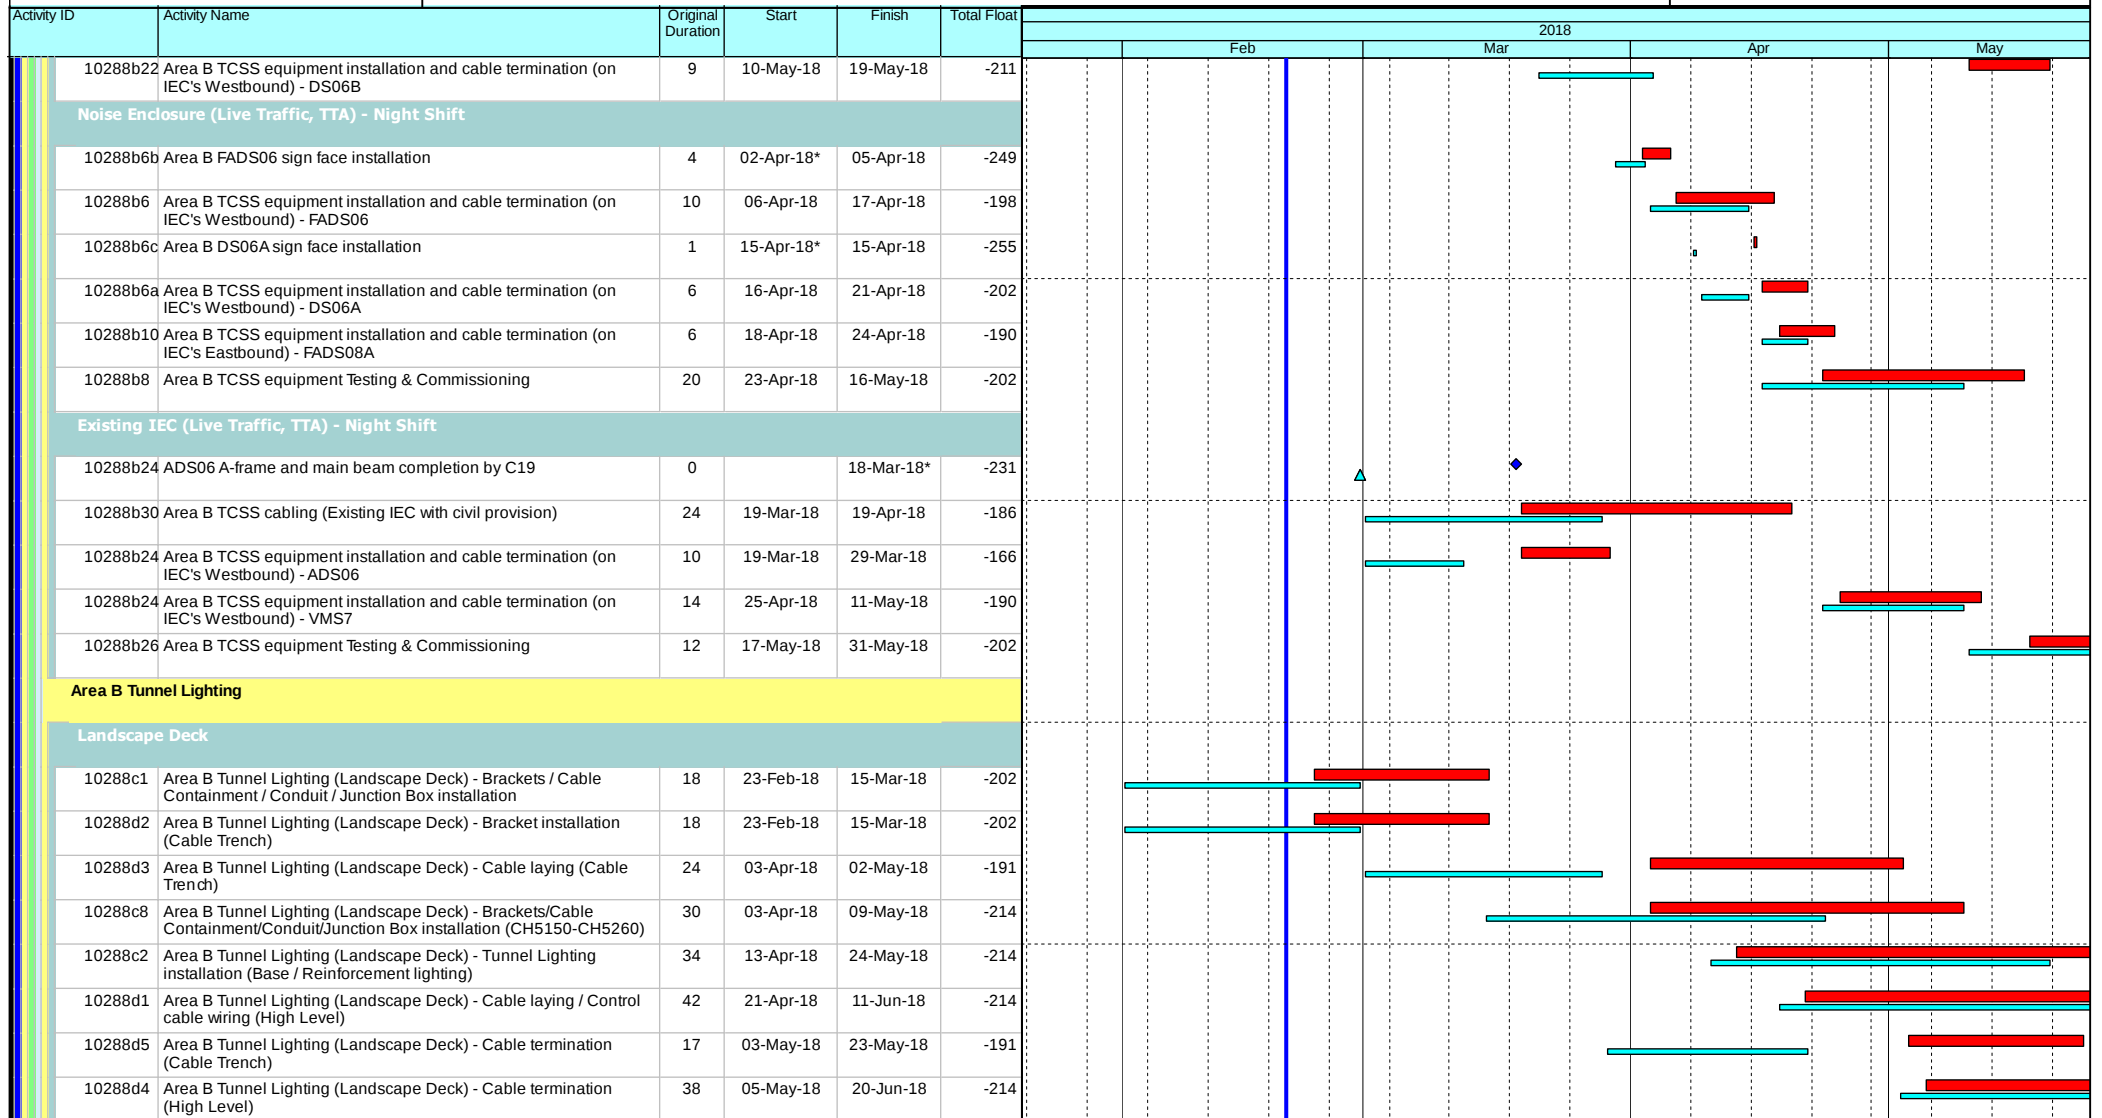


Leighton Contractors (Asia) Limited

Programme Update 48 (February 2018)

THREE MONTH ROLLING

Project ID: H2613-U048
 Baseline: SA01
 Layout: Update Three Month Rolling
 U048
 Page 41 of 43


Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

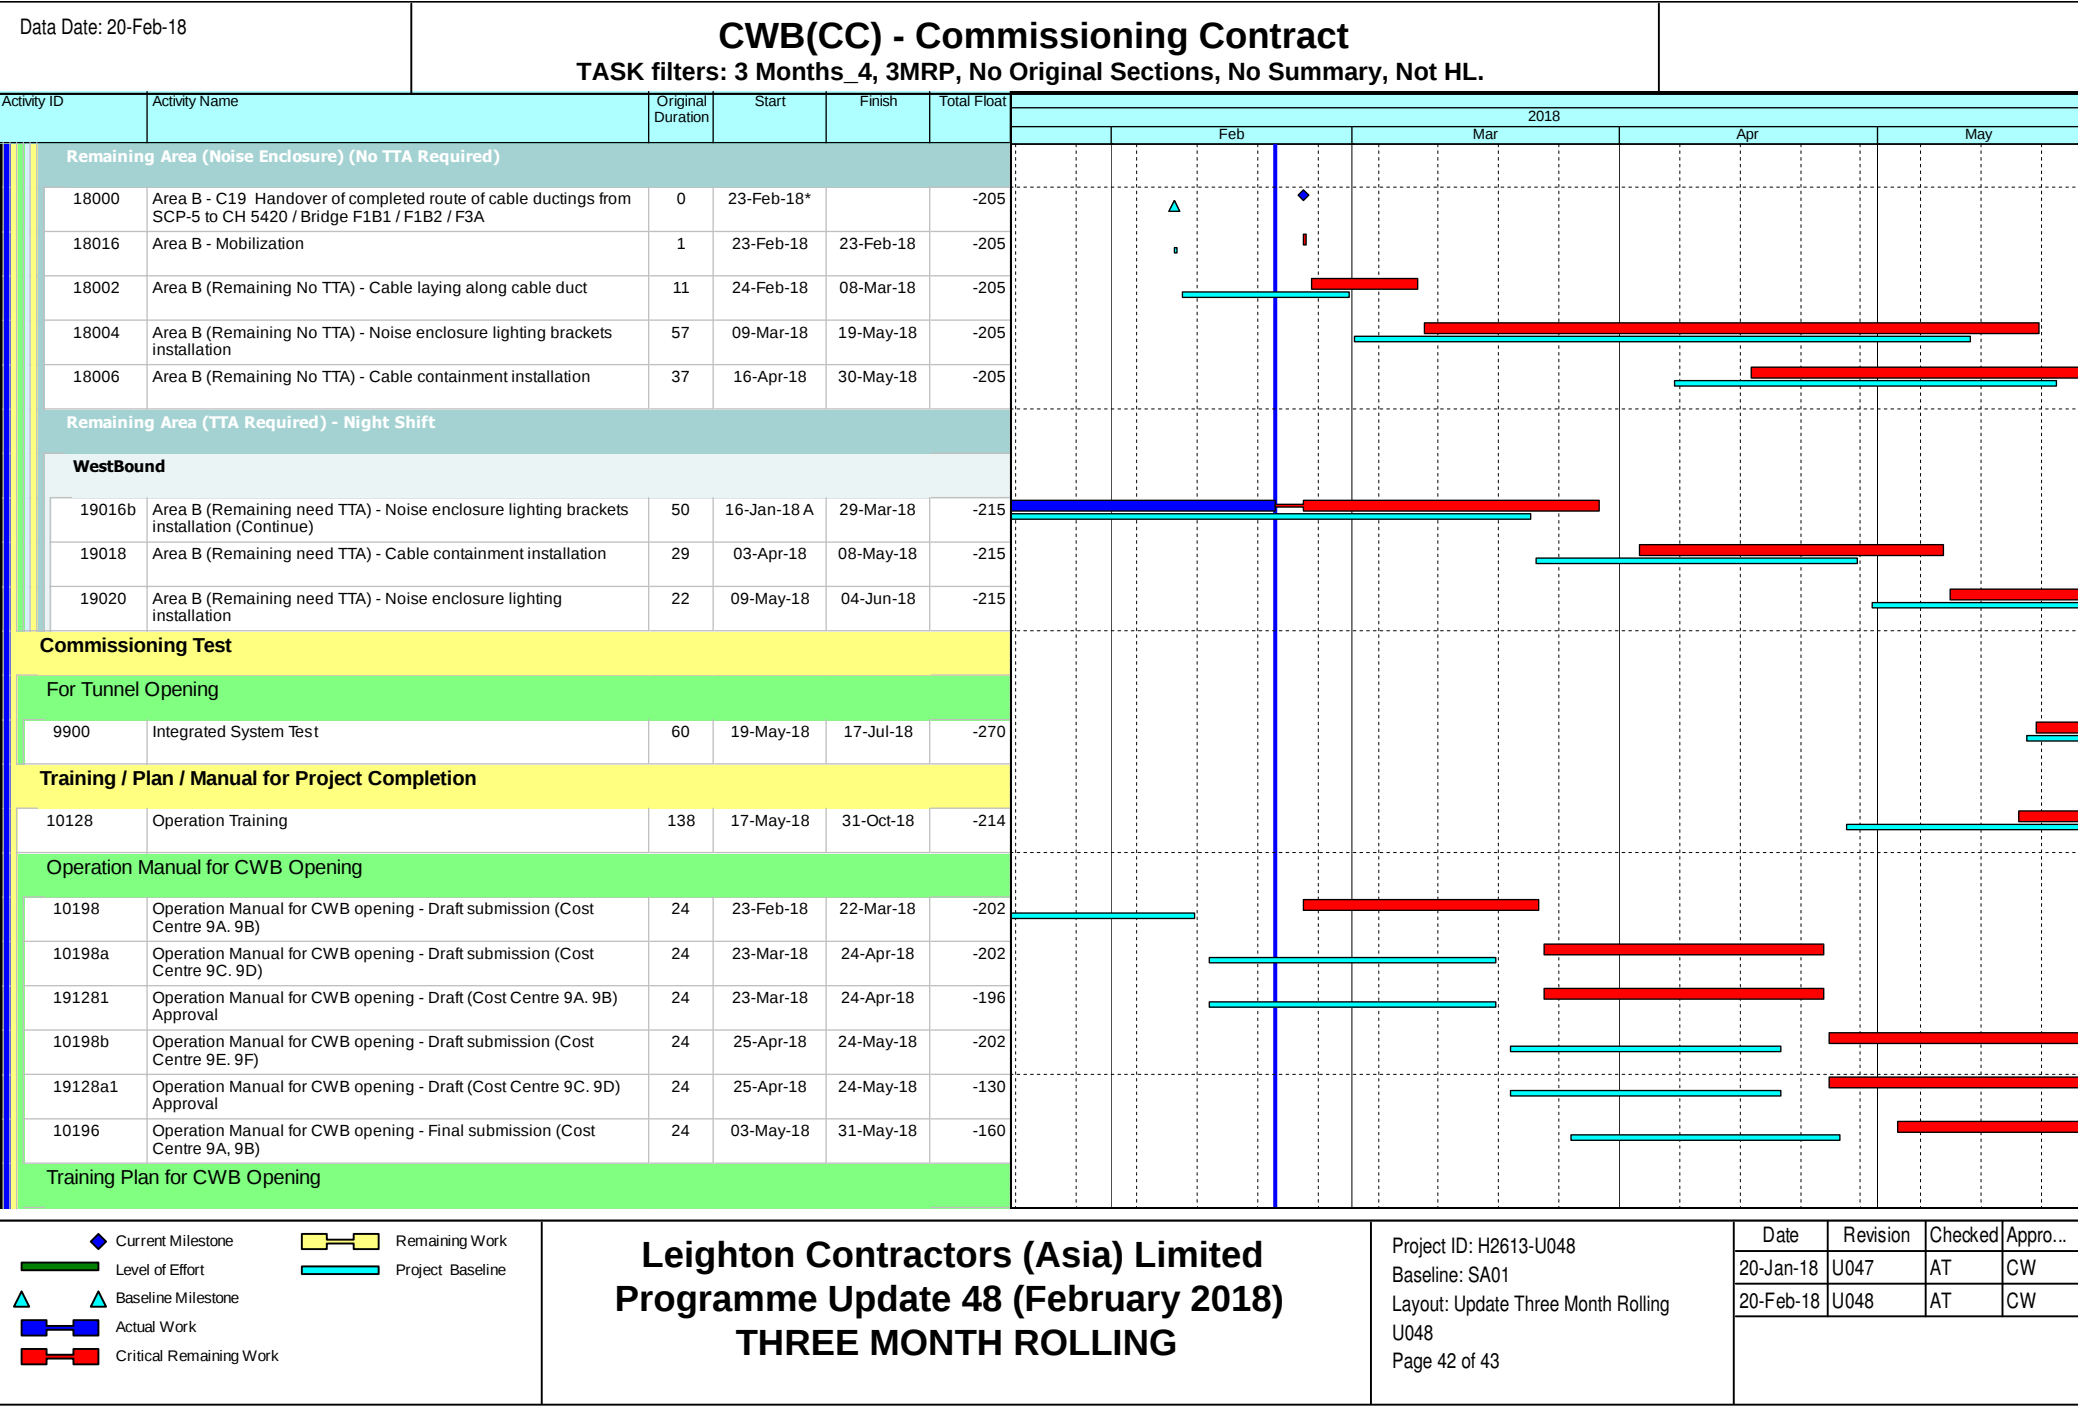

Data Date: 20-Feb-18

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

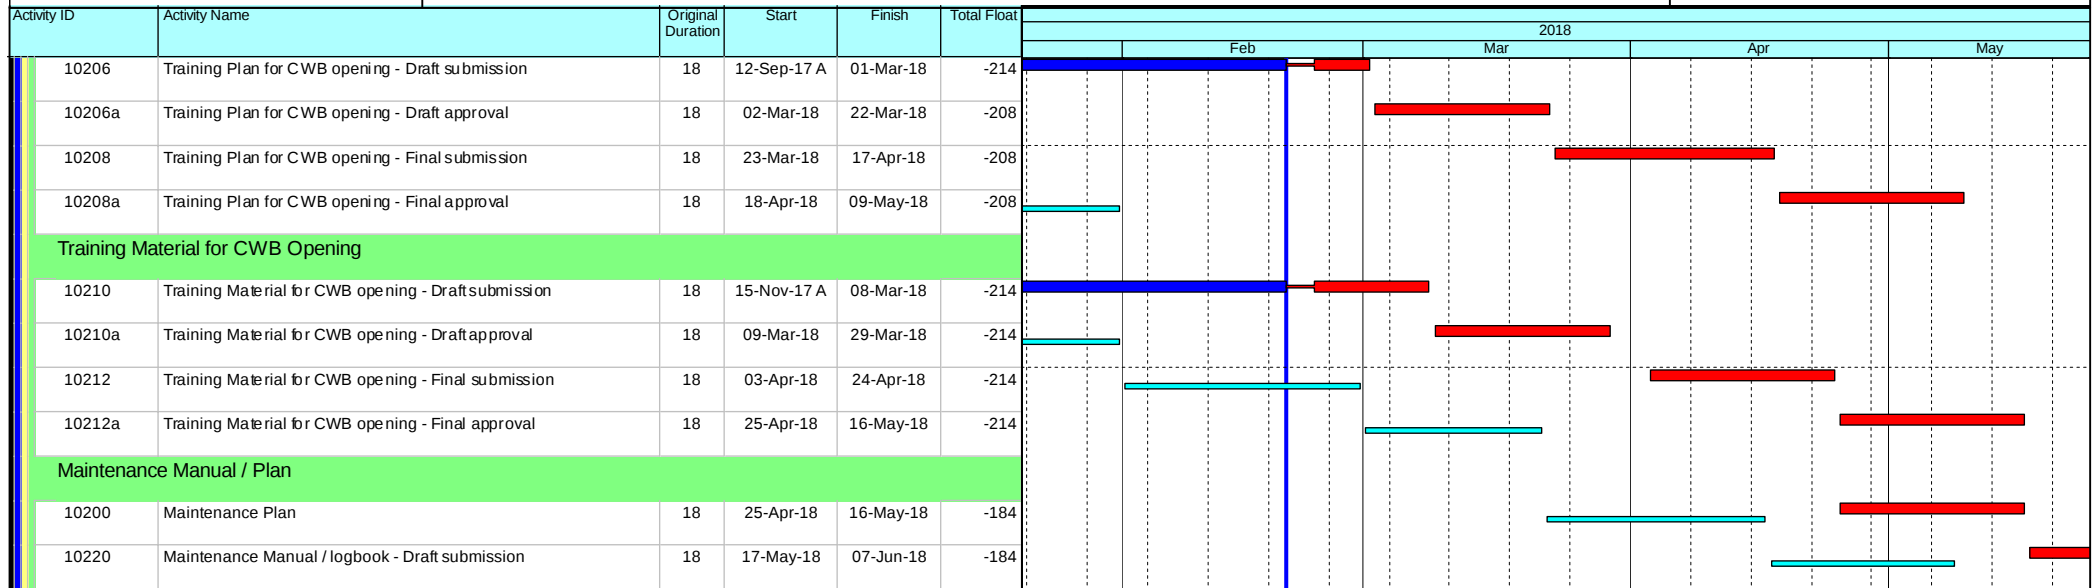

- Current Milestone
- Level of Effort
- Baseline Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Project Baseline

Leighton Contractors (Asia) Limited Programme Update 48 (February 2018) THREE MONTH ROLLING

Project ID: H2613-U048
Baseline: SA01
Layout: Update Three Month Rolling
U048
Page 43 of 43

Date	Revision	Checked	Appro...
20-Jan-18	U047	AT	CW
20-Feb-18	U048	AT	CW

Data Date: 20-Mar-18		CWB(CC) - Commissioning Contract																
		TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018												
						Mar			Apr			May			Jun			
PO-VII_a2	Possession of Portion VII (Day 762) - CH3800-3911 (below -6.0mPD)	567	31-Mar-16 A	17-Apr-18	-213													
PO-IXc_1	Possession of Portion IXc (Day 712) - EVB above 3.6mPD - Relinquished on 12 Apr 2016	445	29-Jul-16 A	17-Apr-18	-293													
PO-IXb_1	Possession of Portion IXb (Day 712) - EVB (below +3.6mPD to tunnel top slab) - Relinquished on 12 Apr 2016	445	05-Aug-16 A	17-Apr-18	-293													
PO-VIa_a	Possession of Portion VIa (Day 823) - CH3250-3283	425	15-Aug-16 A	17-Apr-18	-182													
PO-Vb2_a	Possession of Portion V (Day 607) - SR2	456	15-Aug-16 A	17-Apr-18	-206													
PO-VIc_a	Possession of Portion VIc (Day 761) - CH3770-3800 (Access Shaft Opening)	391	23-Sep-16 A	17-Apr-18	-199													
PO-VIb_c	Possession of Portion VIb (Day 761) - CH3625-3770	391	23-Sep-16 A	17-Apr-18	-199													
PO-IVa1	Possession of Portion IVa (Day 930) - CH2600-2720	323	30-Nov-16 A	17-Apr-18	-220													
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GL D-H)	233	28-Feb-17 A	17-Apr-18	-330													
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - CH4530-4591 W/B	233	28-Feb-17 A	17-Apr-18	-273													
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600 (Remaining)	241	12-Mar-17 A	17-Apr-18	-273													
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)	233	12-Mar-17 A	17-Apr-18	-193													
PO-VIIIc	Possession of Portion VIIIc (Day 1039) - SR8 (CH350-310) / SCP4	233	12-Mar-17 A	17-Apr-18	-204													
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH2720-2950	241	12-Mar-17 A	17-Apr-18	-220													
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GL A-C)	239	14-Mar-17 A	17-Apr-18	-330													
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	17-Apr-18	-220													
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	03-Jul-17 A	17-Apr-18	-206													
PO-VIb_a	Possession of Portion VIb (Day 761) - CH3400-3428	80	31-Jul-17 A	17-Apr-18	-155													
PO-VIa_b	Possession of Portion VIa (Day 823) - CH3283-3400	80	31-Jul-17 A	17-Apr-18	-273													
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	20-Mar-18	08-Jul-18	-275													
Submissions and Approvals																		
Initial General Submission																		
10168	Submission of CMC 3DVR	30	20-Mar-18	18-Apr-18	-74													
DETAILED DESIGN OF WORKS																		

◆

Current Milestone

▬

Level of Effort

▲

Baseline Milestone

▬

Actual Work

▬

Critical Remaining Work

▬

Remaining Work

▬

Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 49 (March 2018)

THREE MONTH ROLLING


Project ID: H2613-U049


Baseline: SA01


Layout: Update Three Month Rolling U049


Page 2 of 39


Date	Revision	Checked	Appro...
20-Feb-18	U048	AT	CW
20-Mar-18	U049	AT	CW

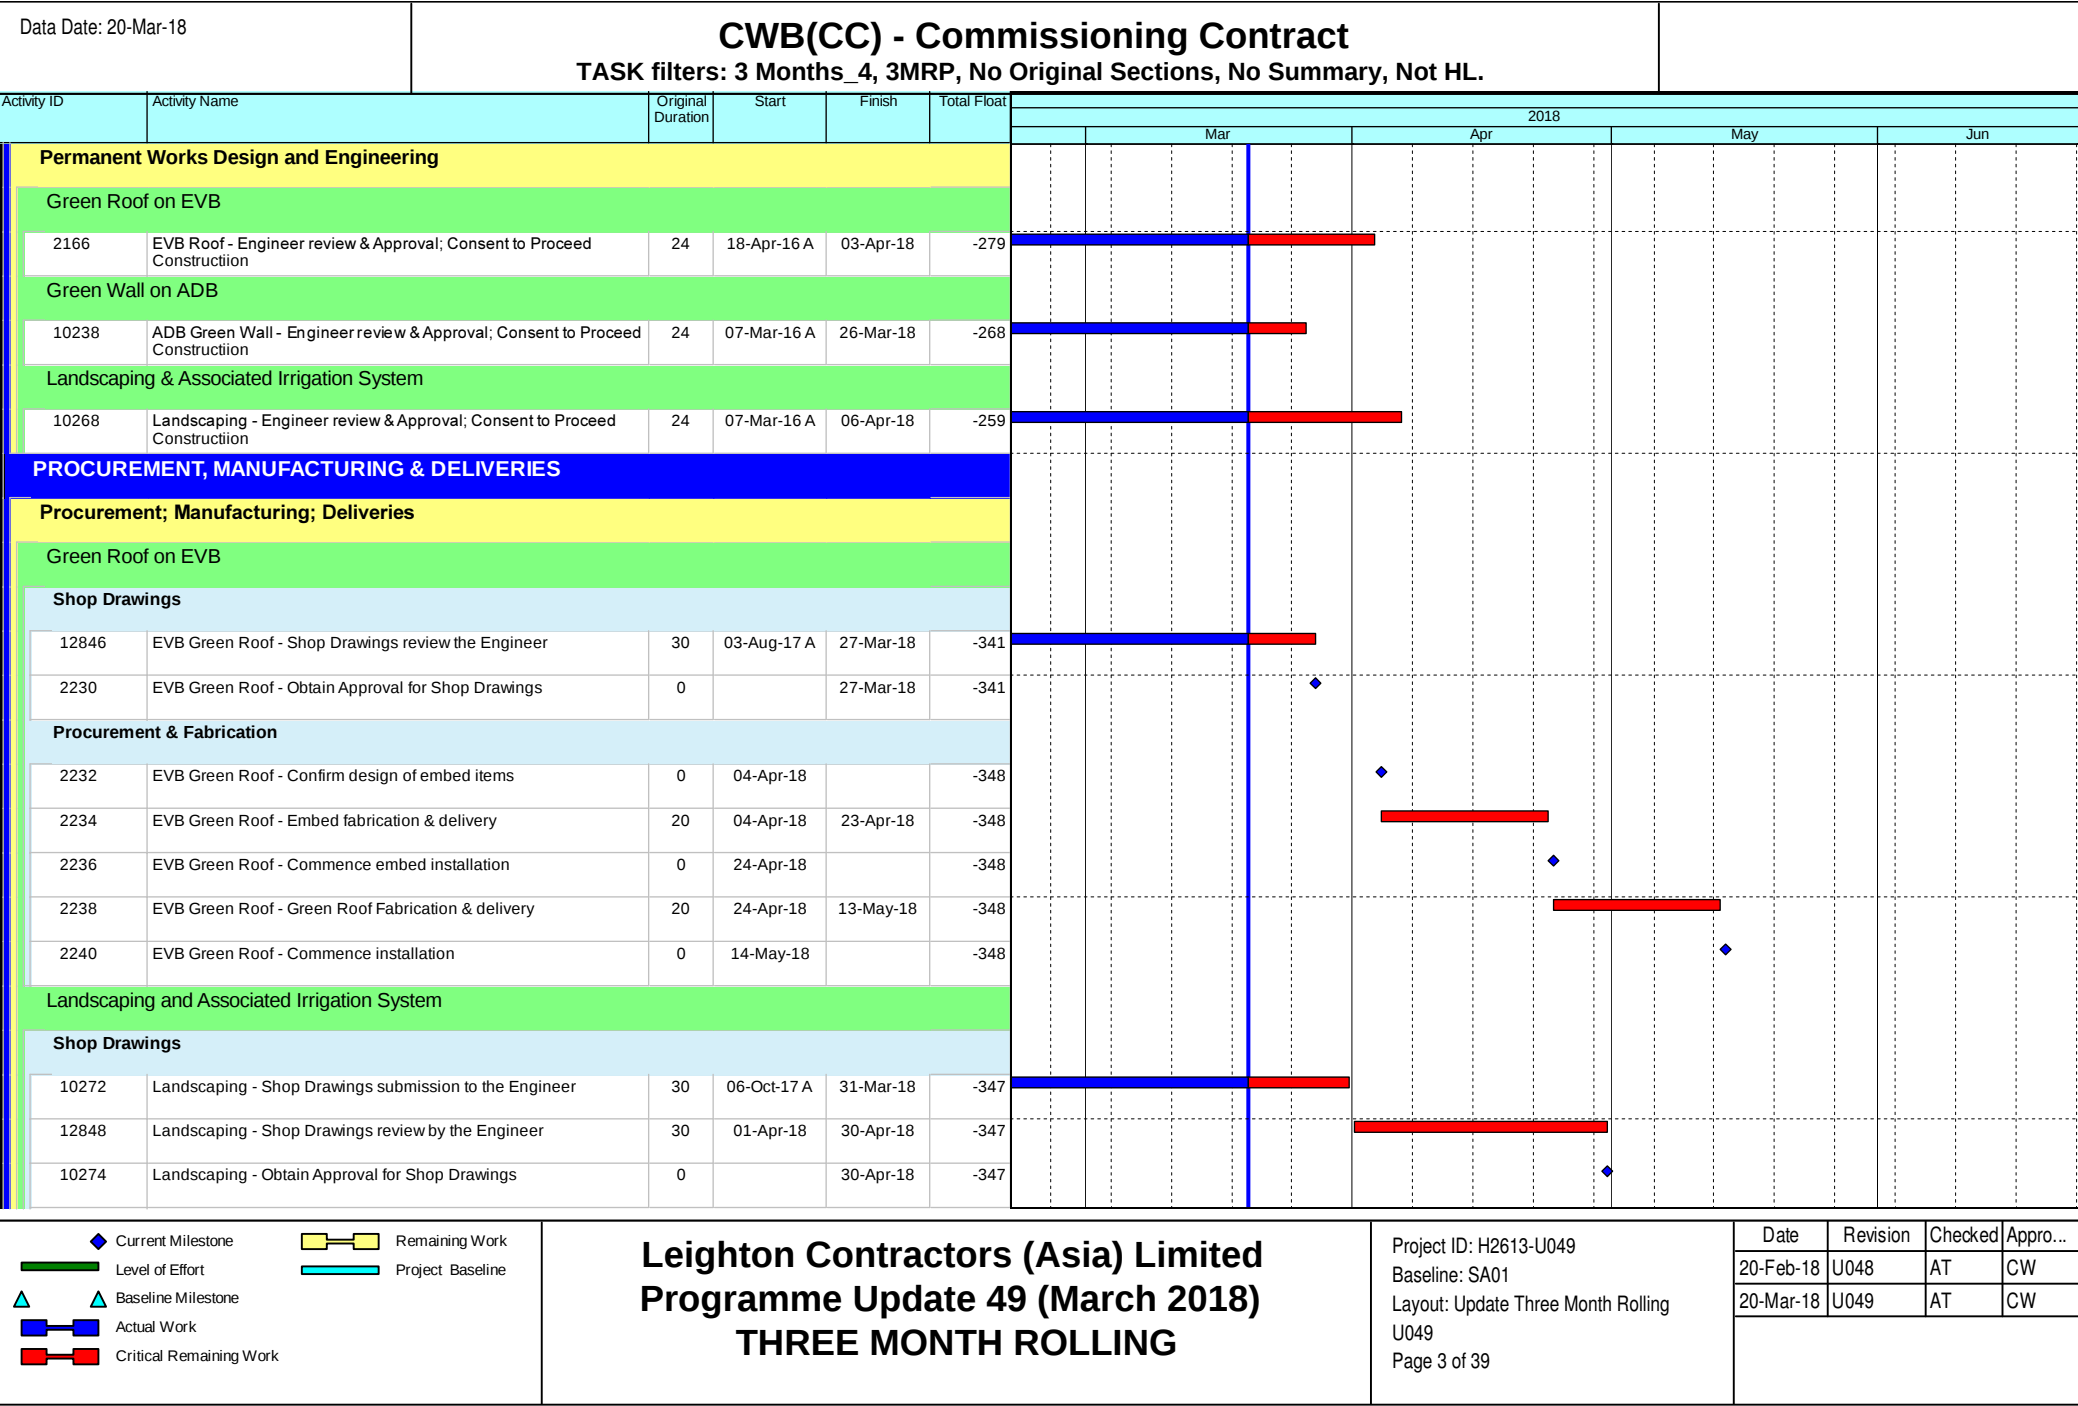


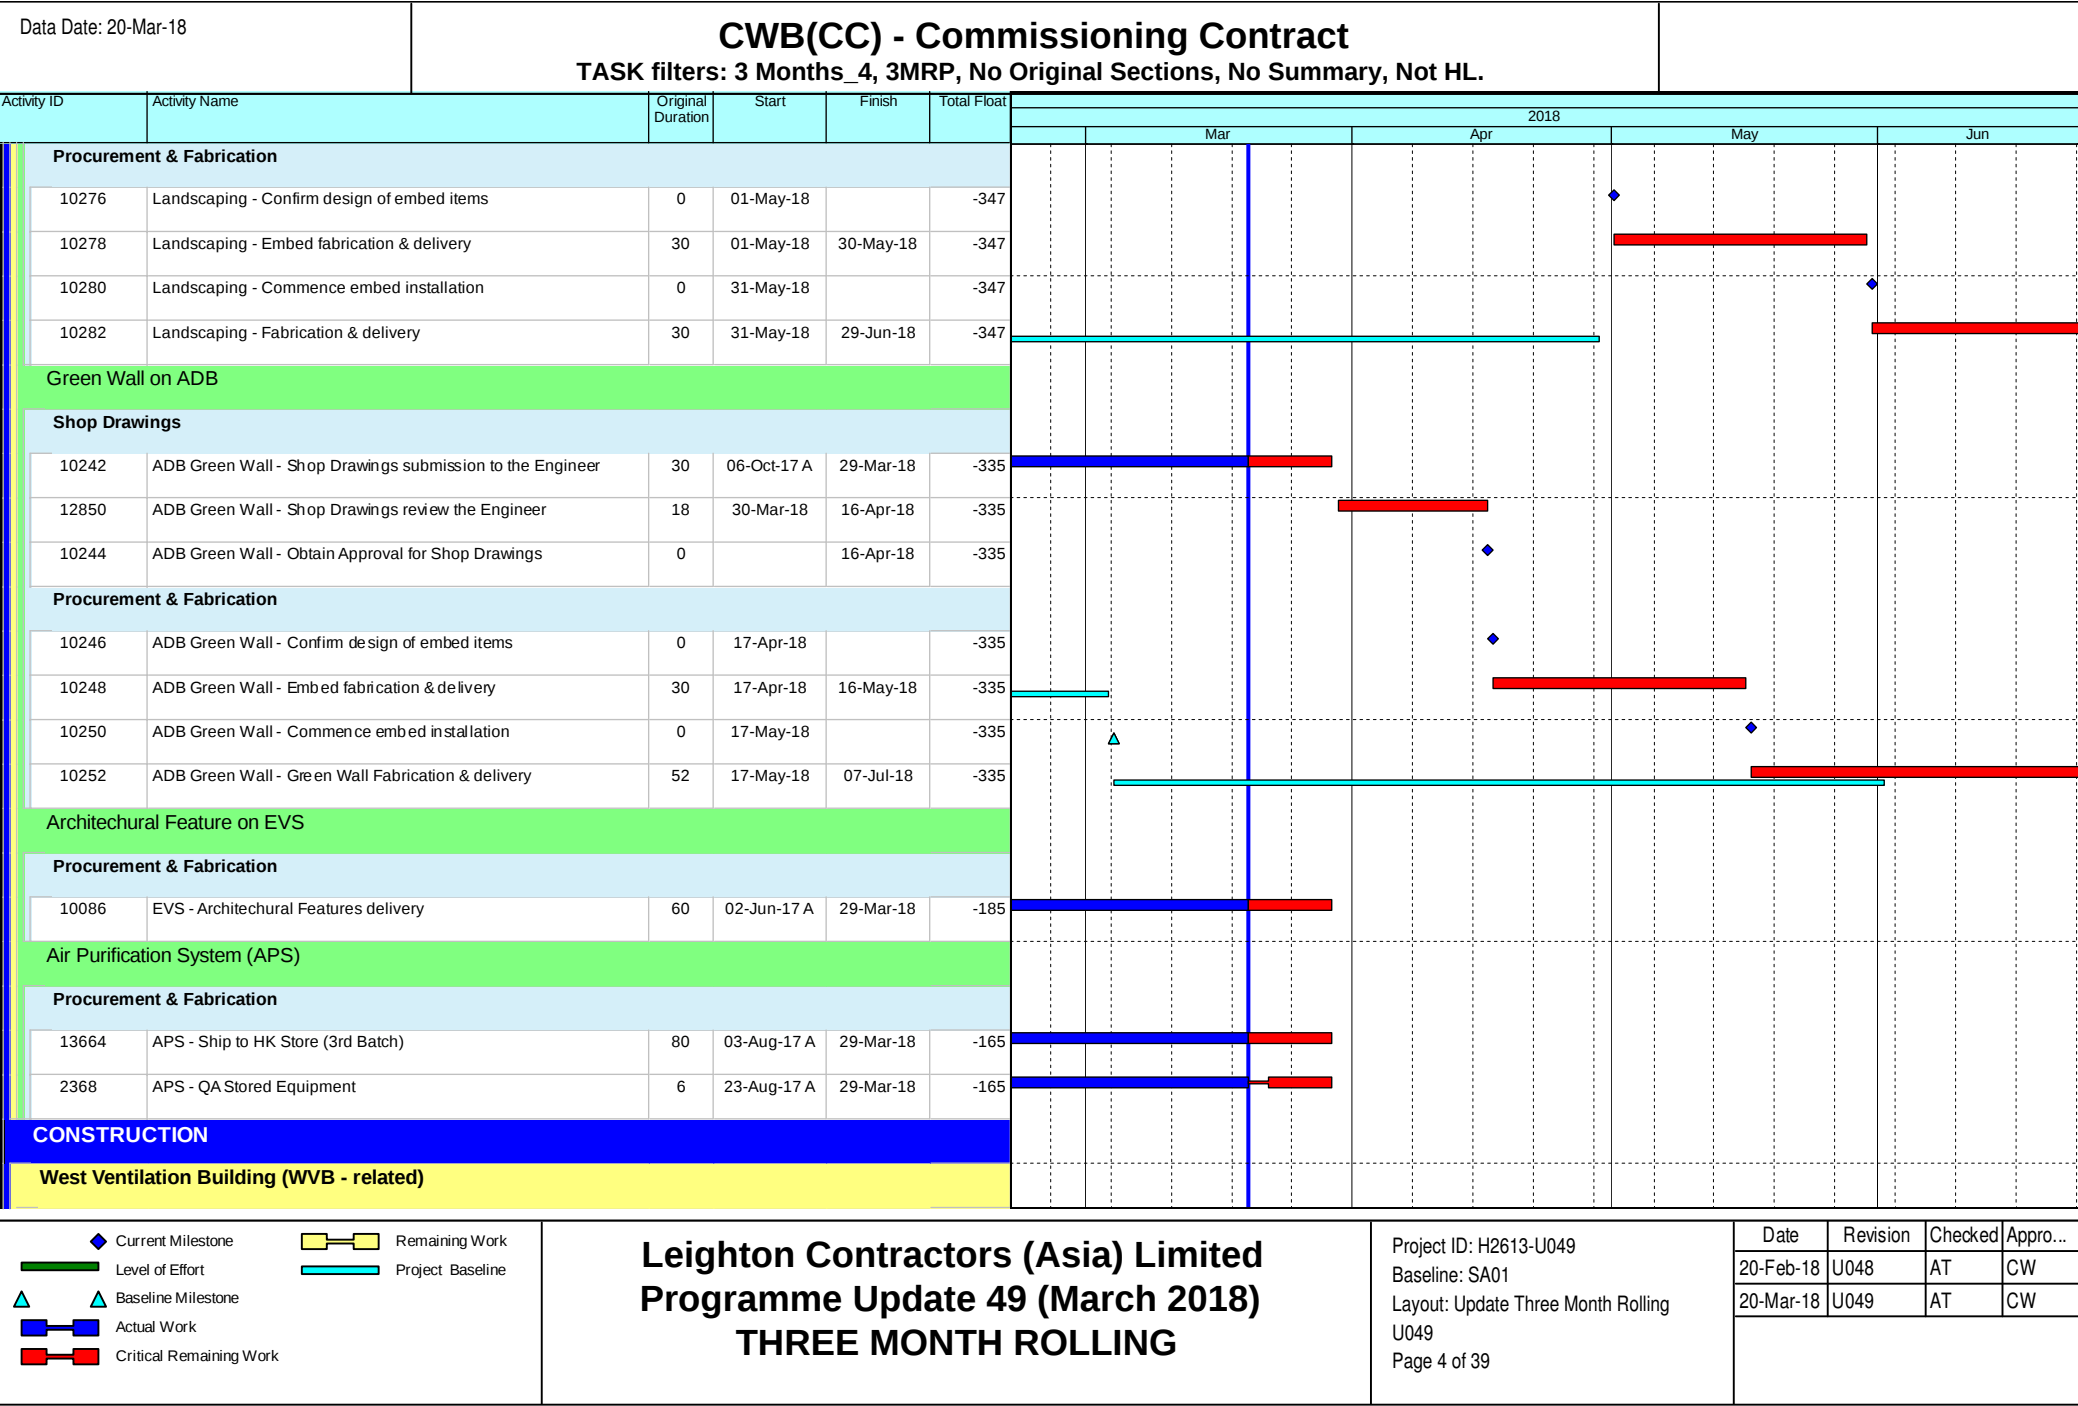


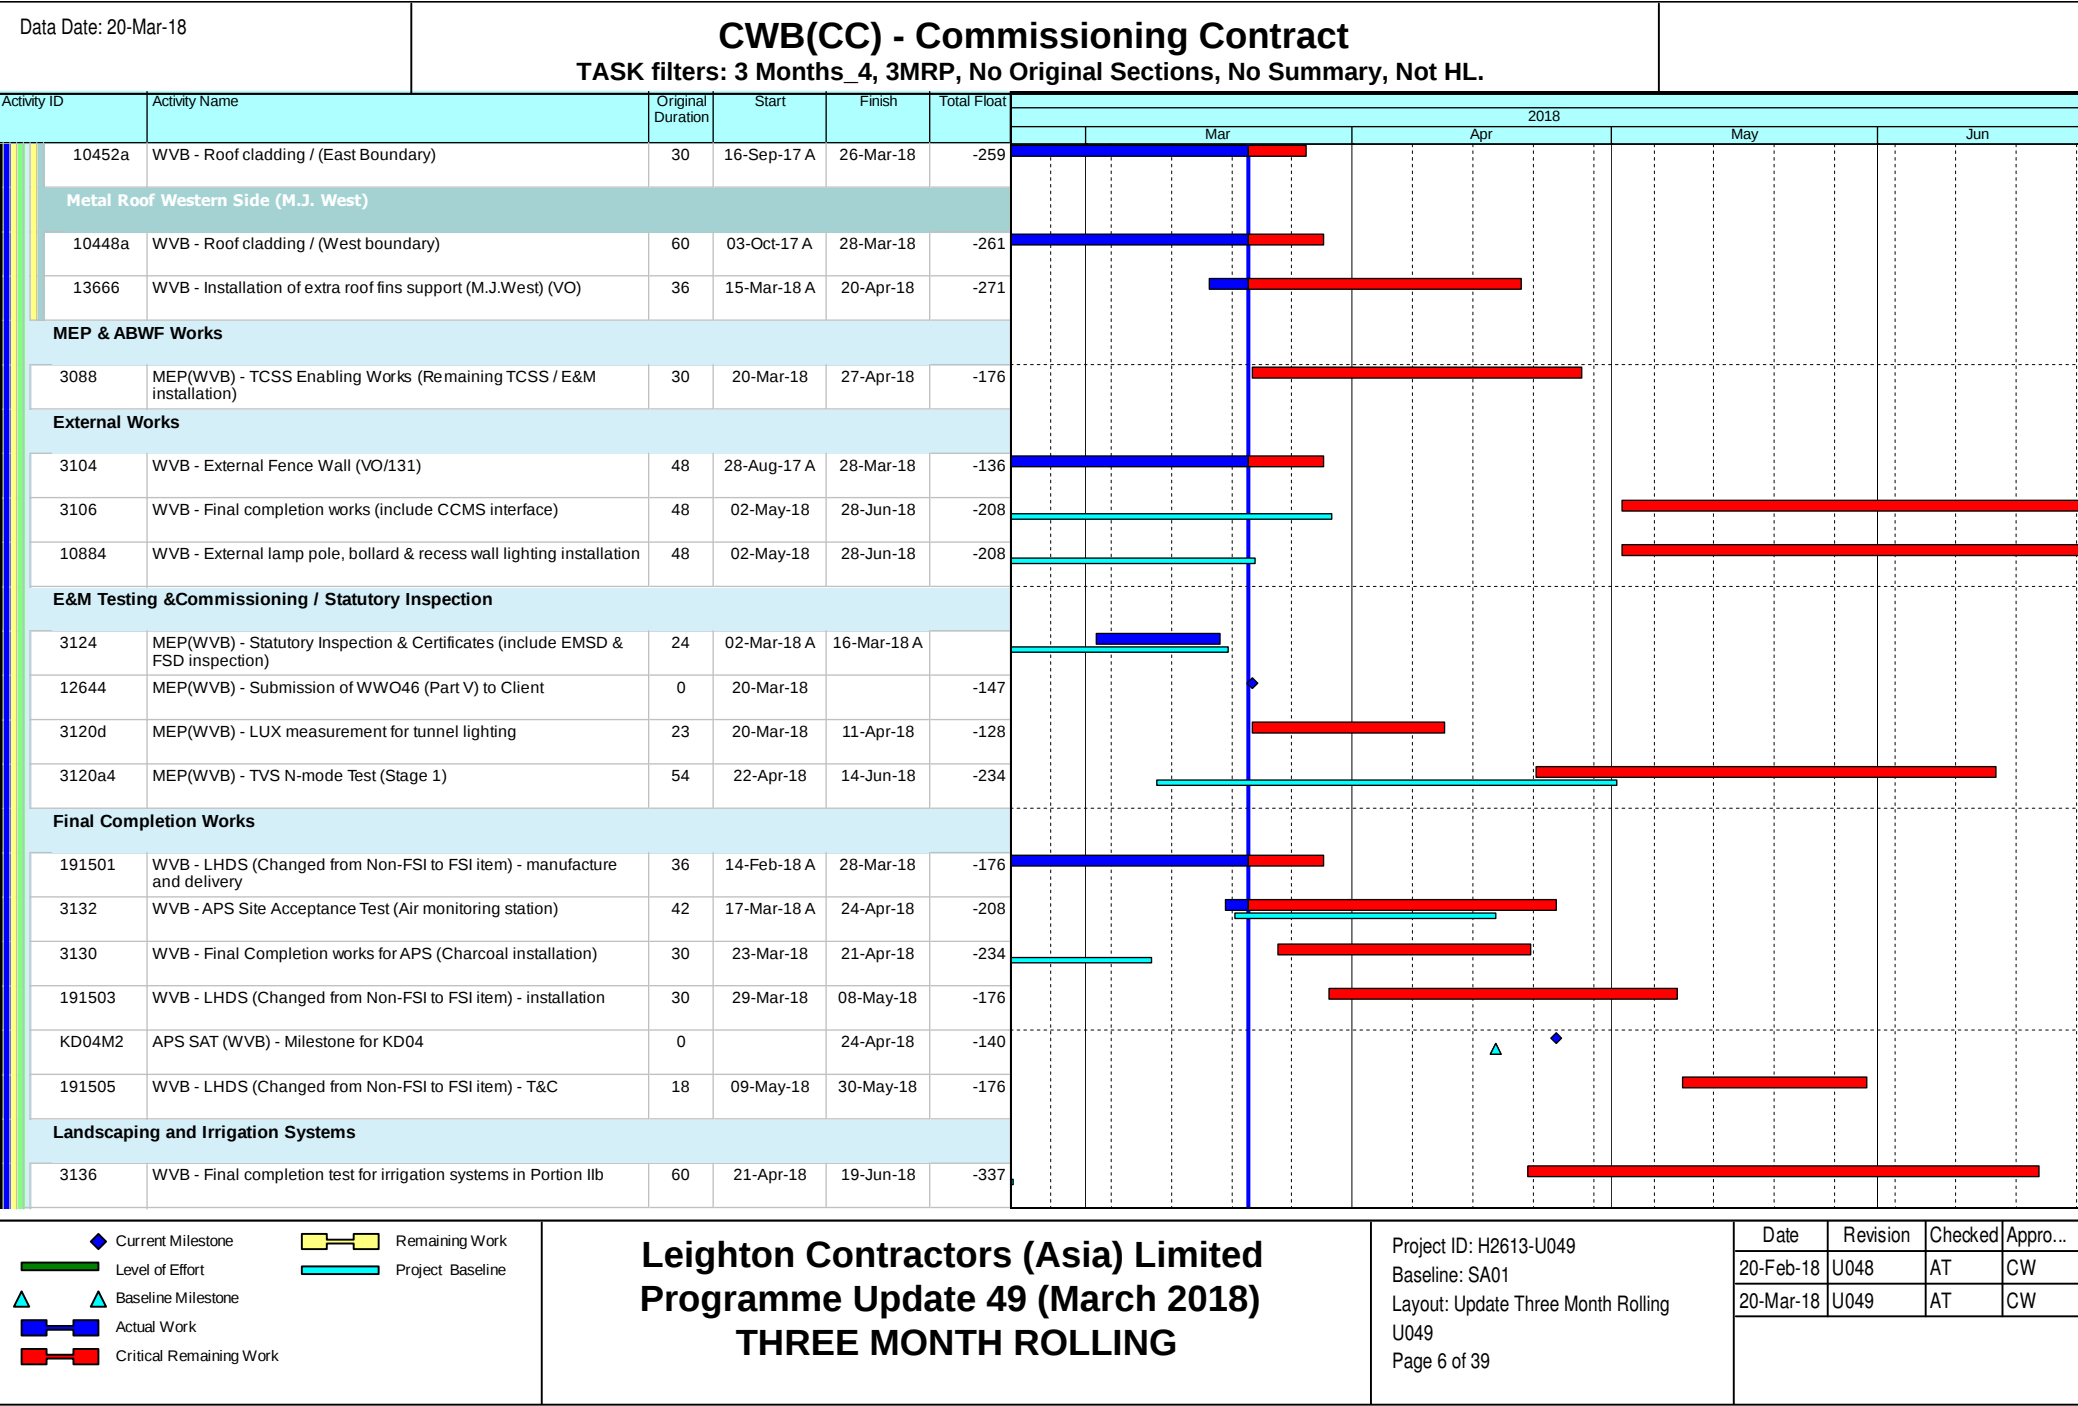


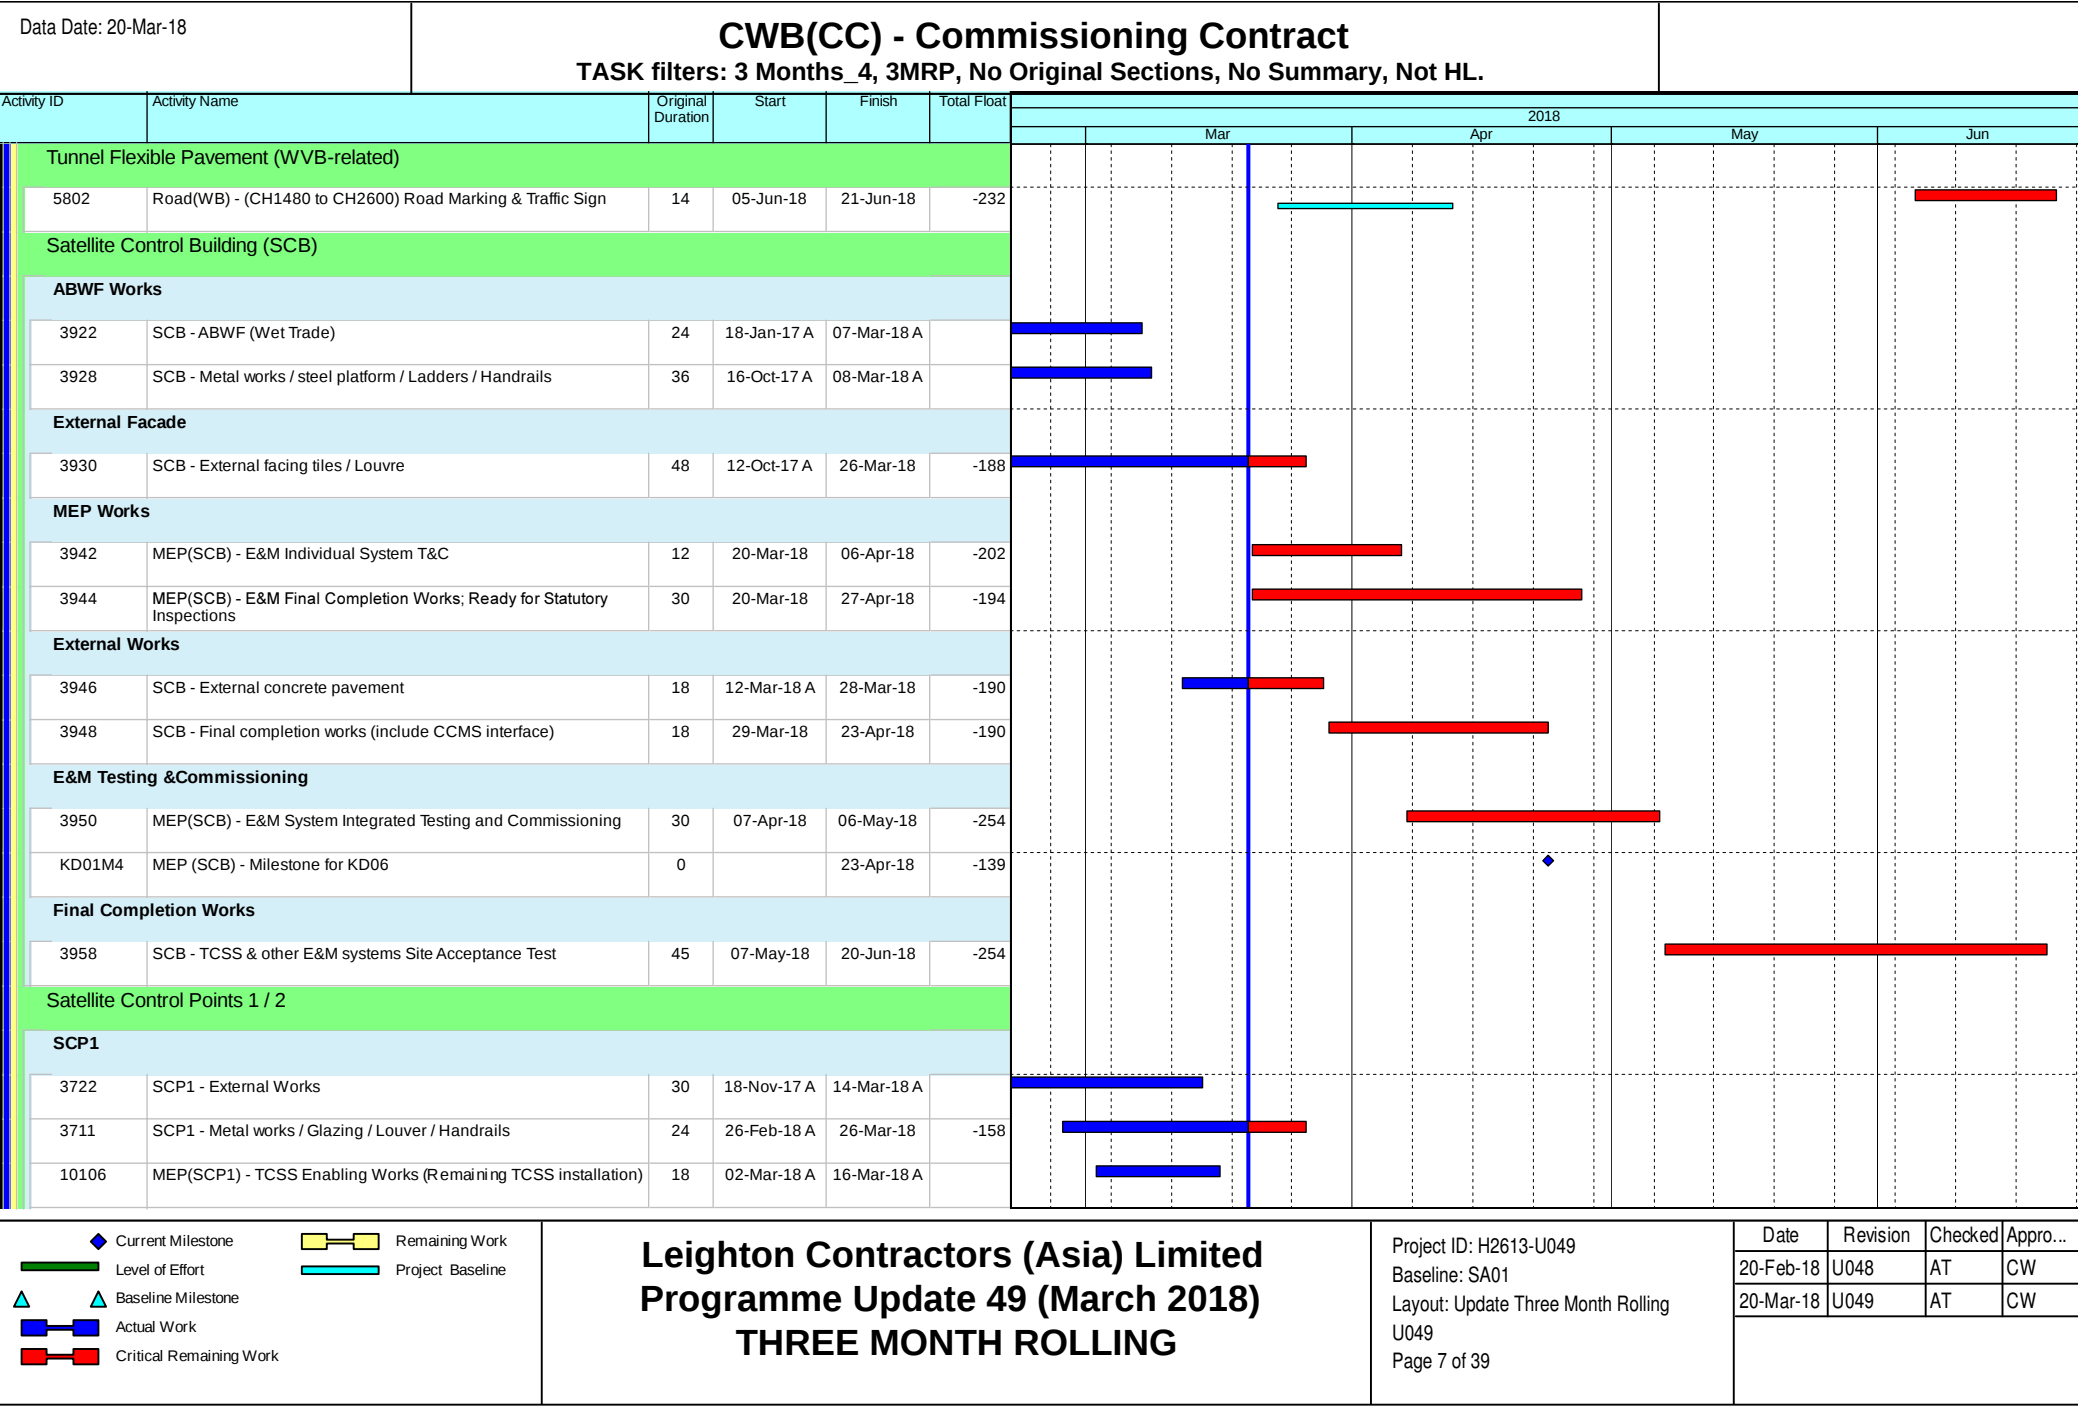


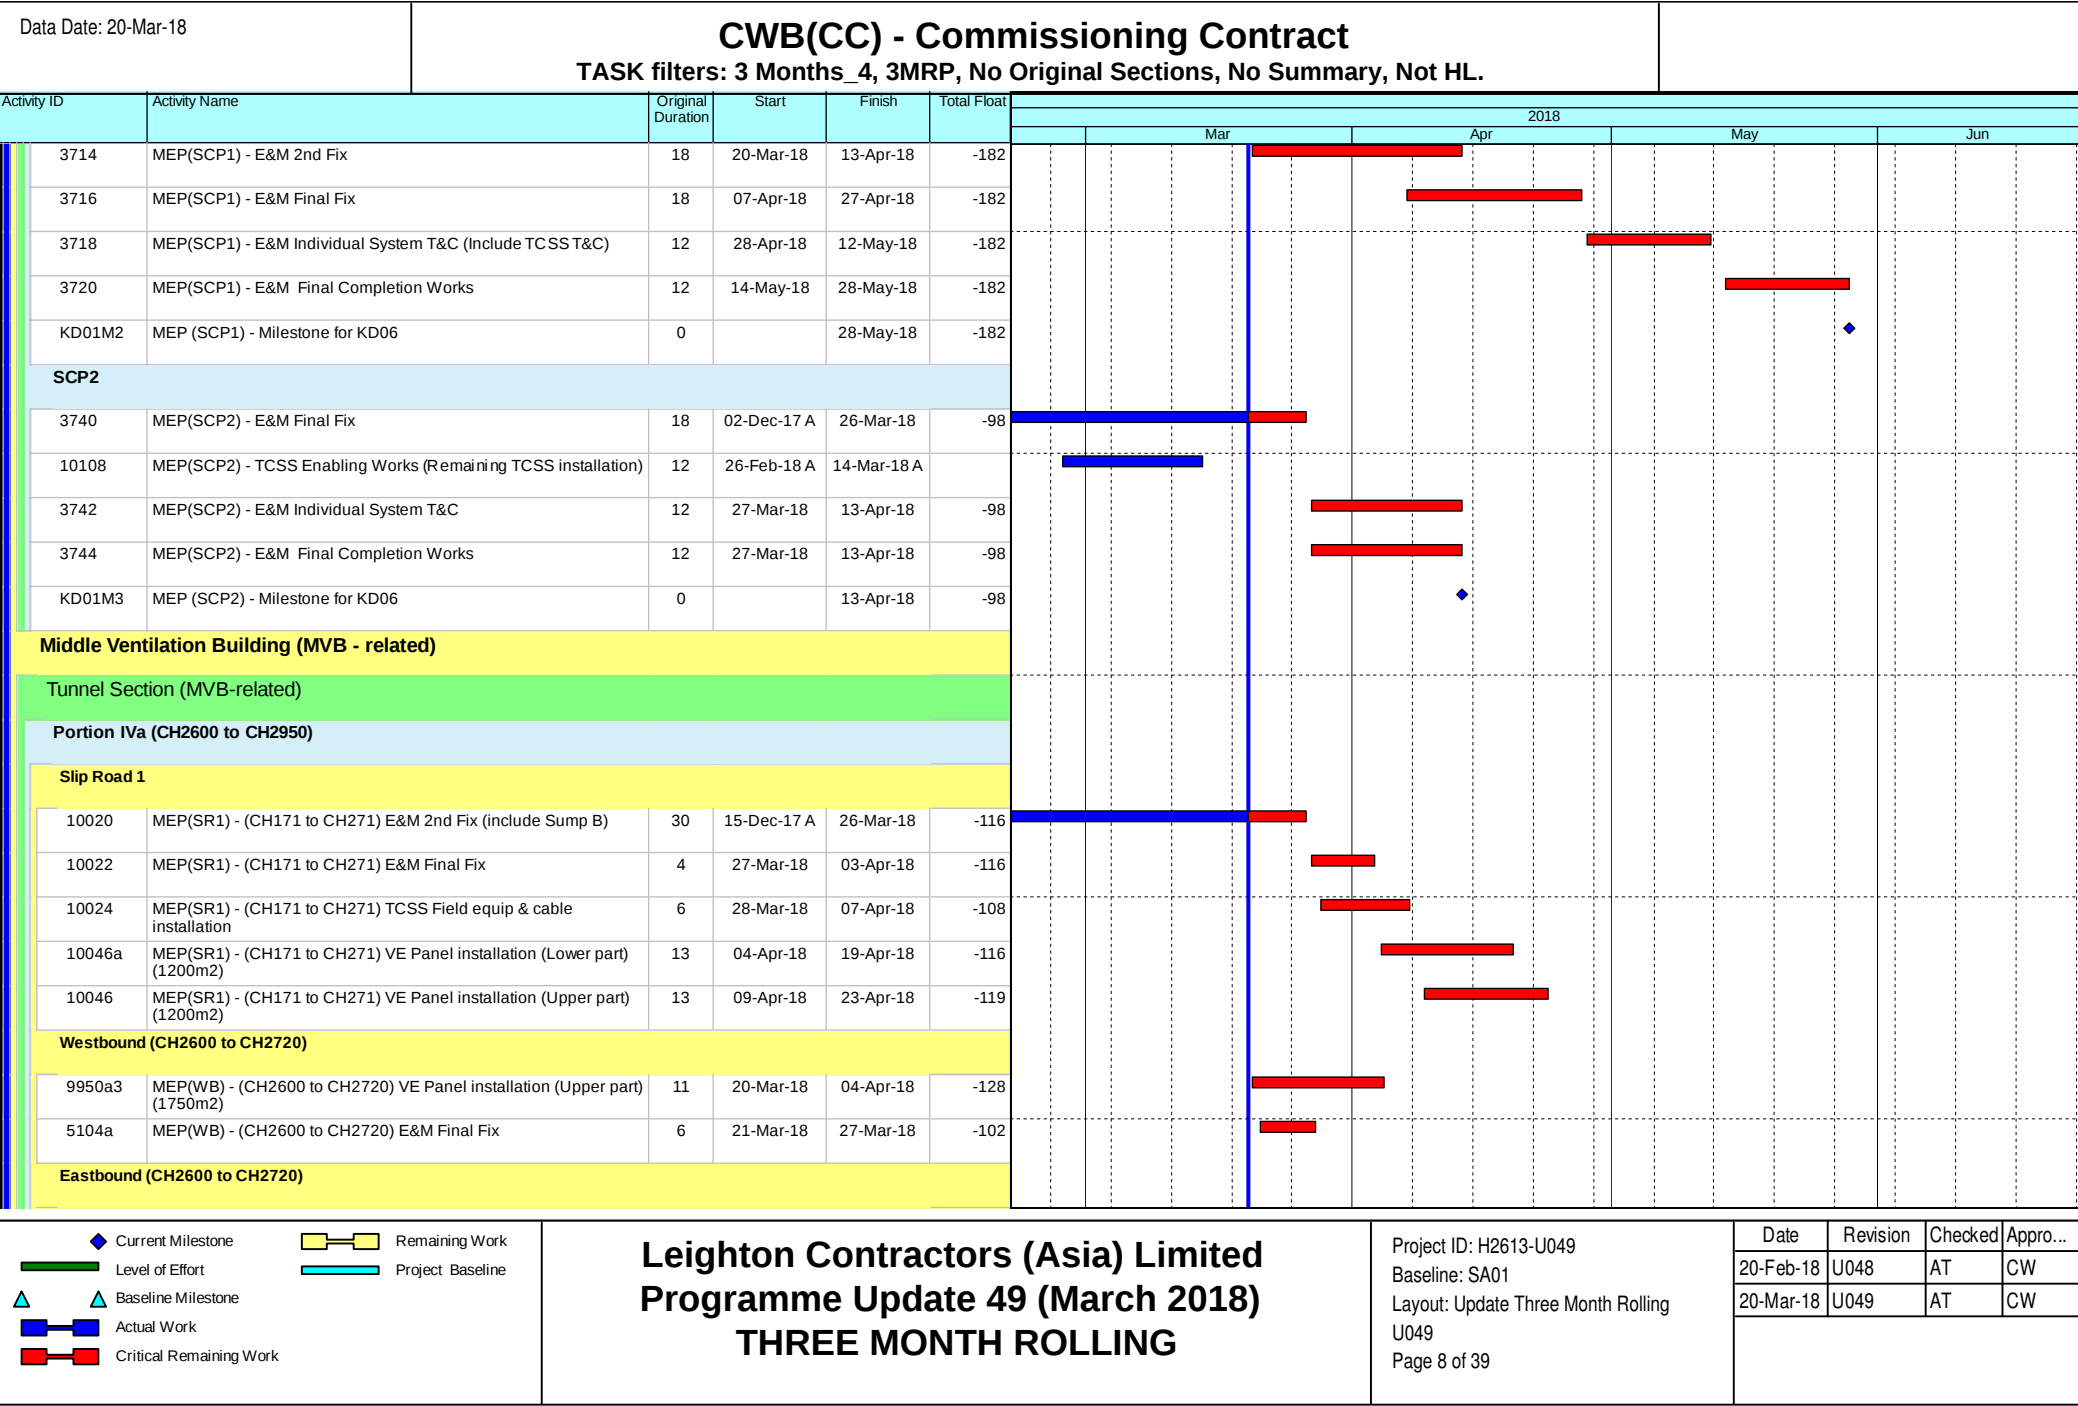


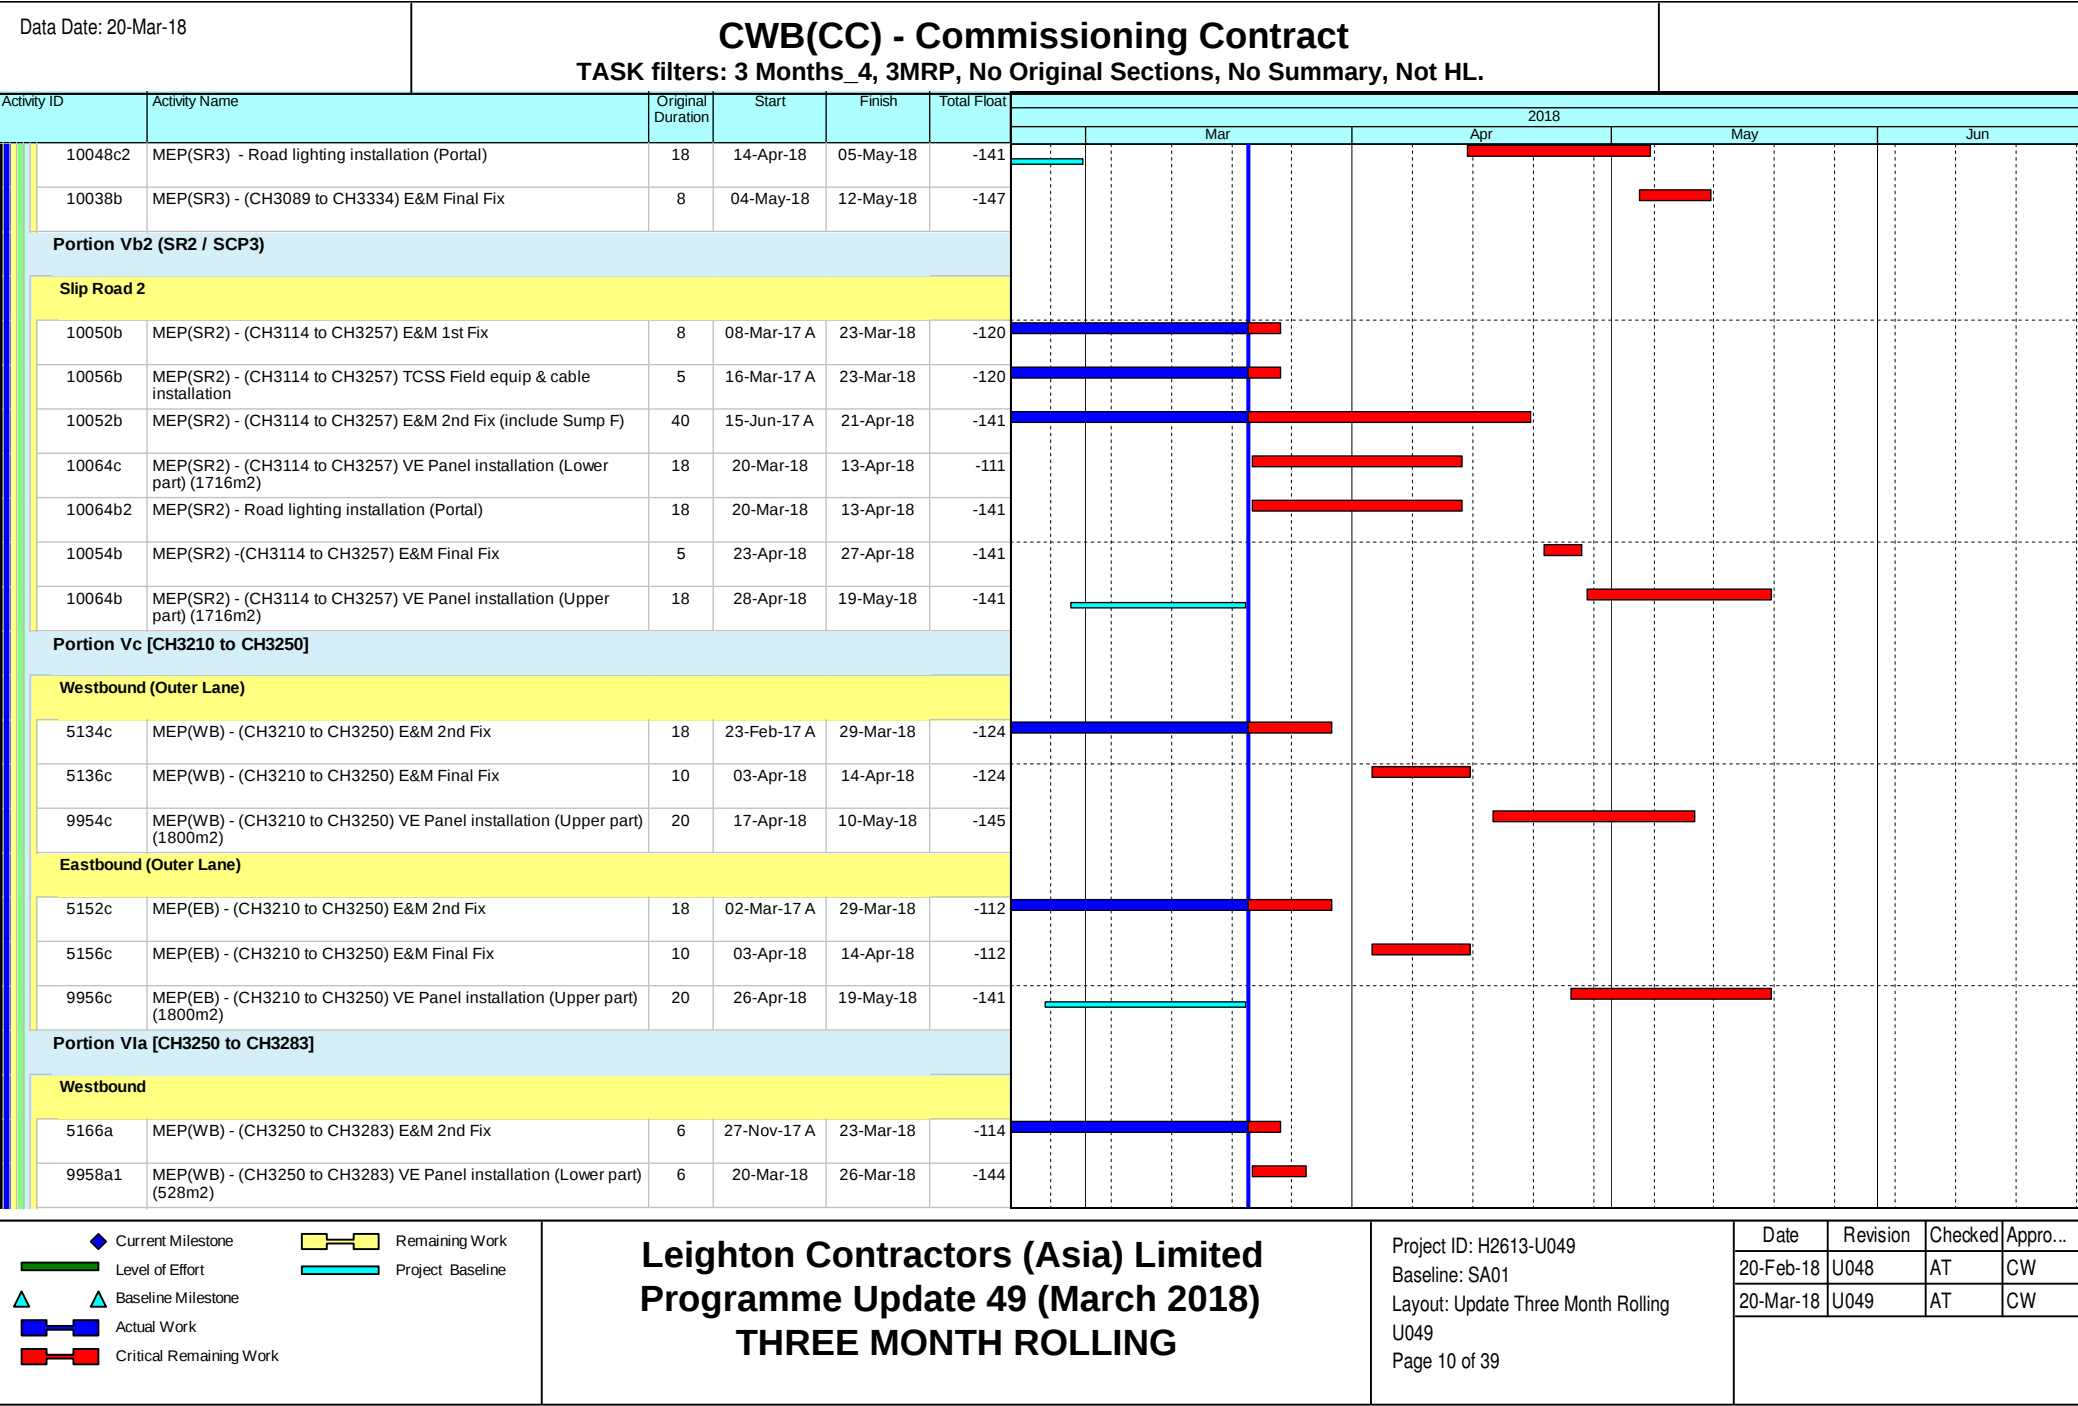


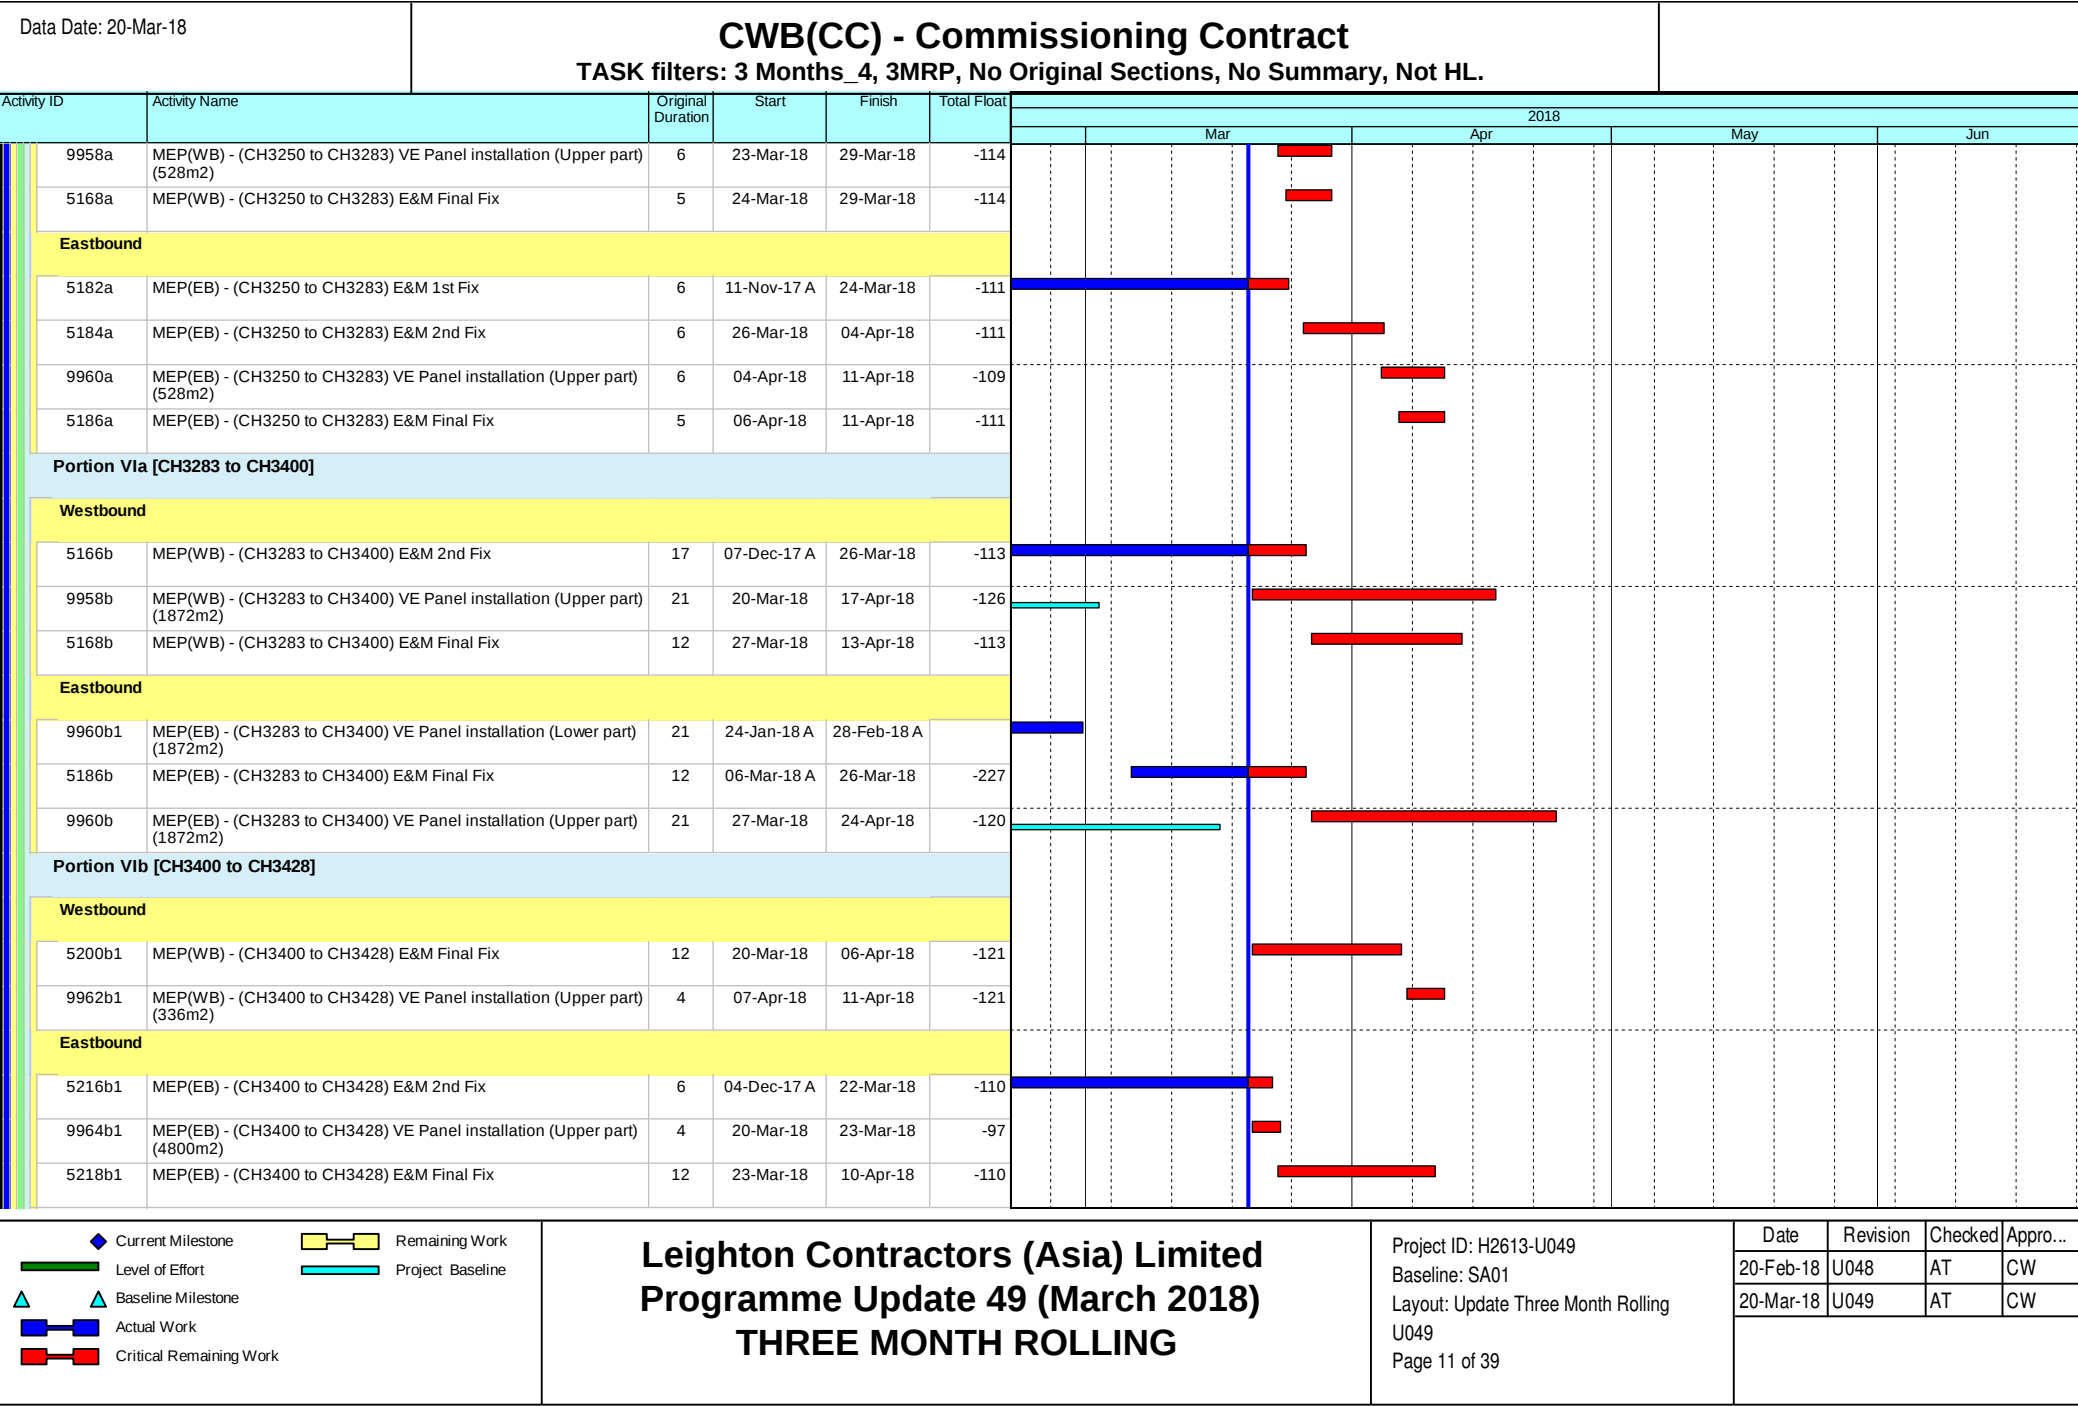


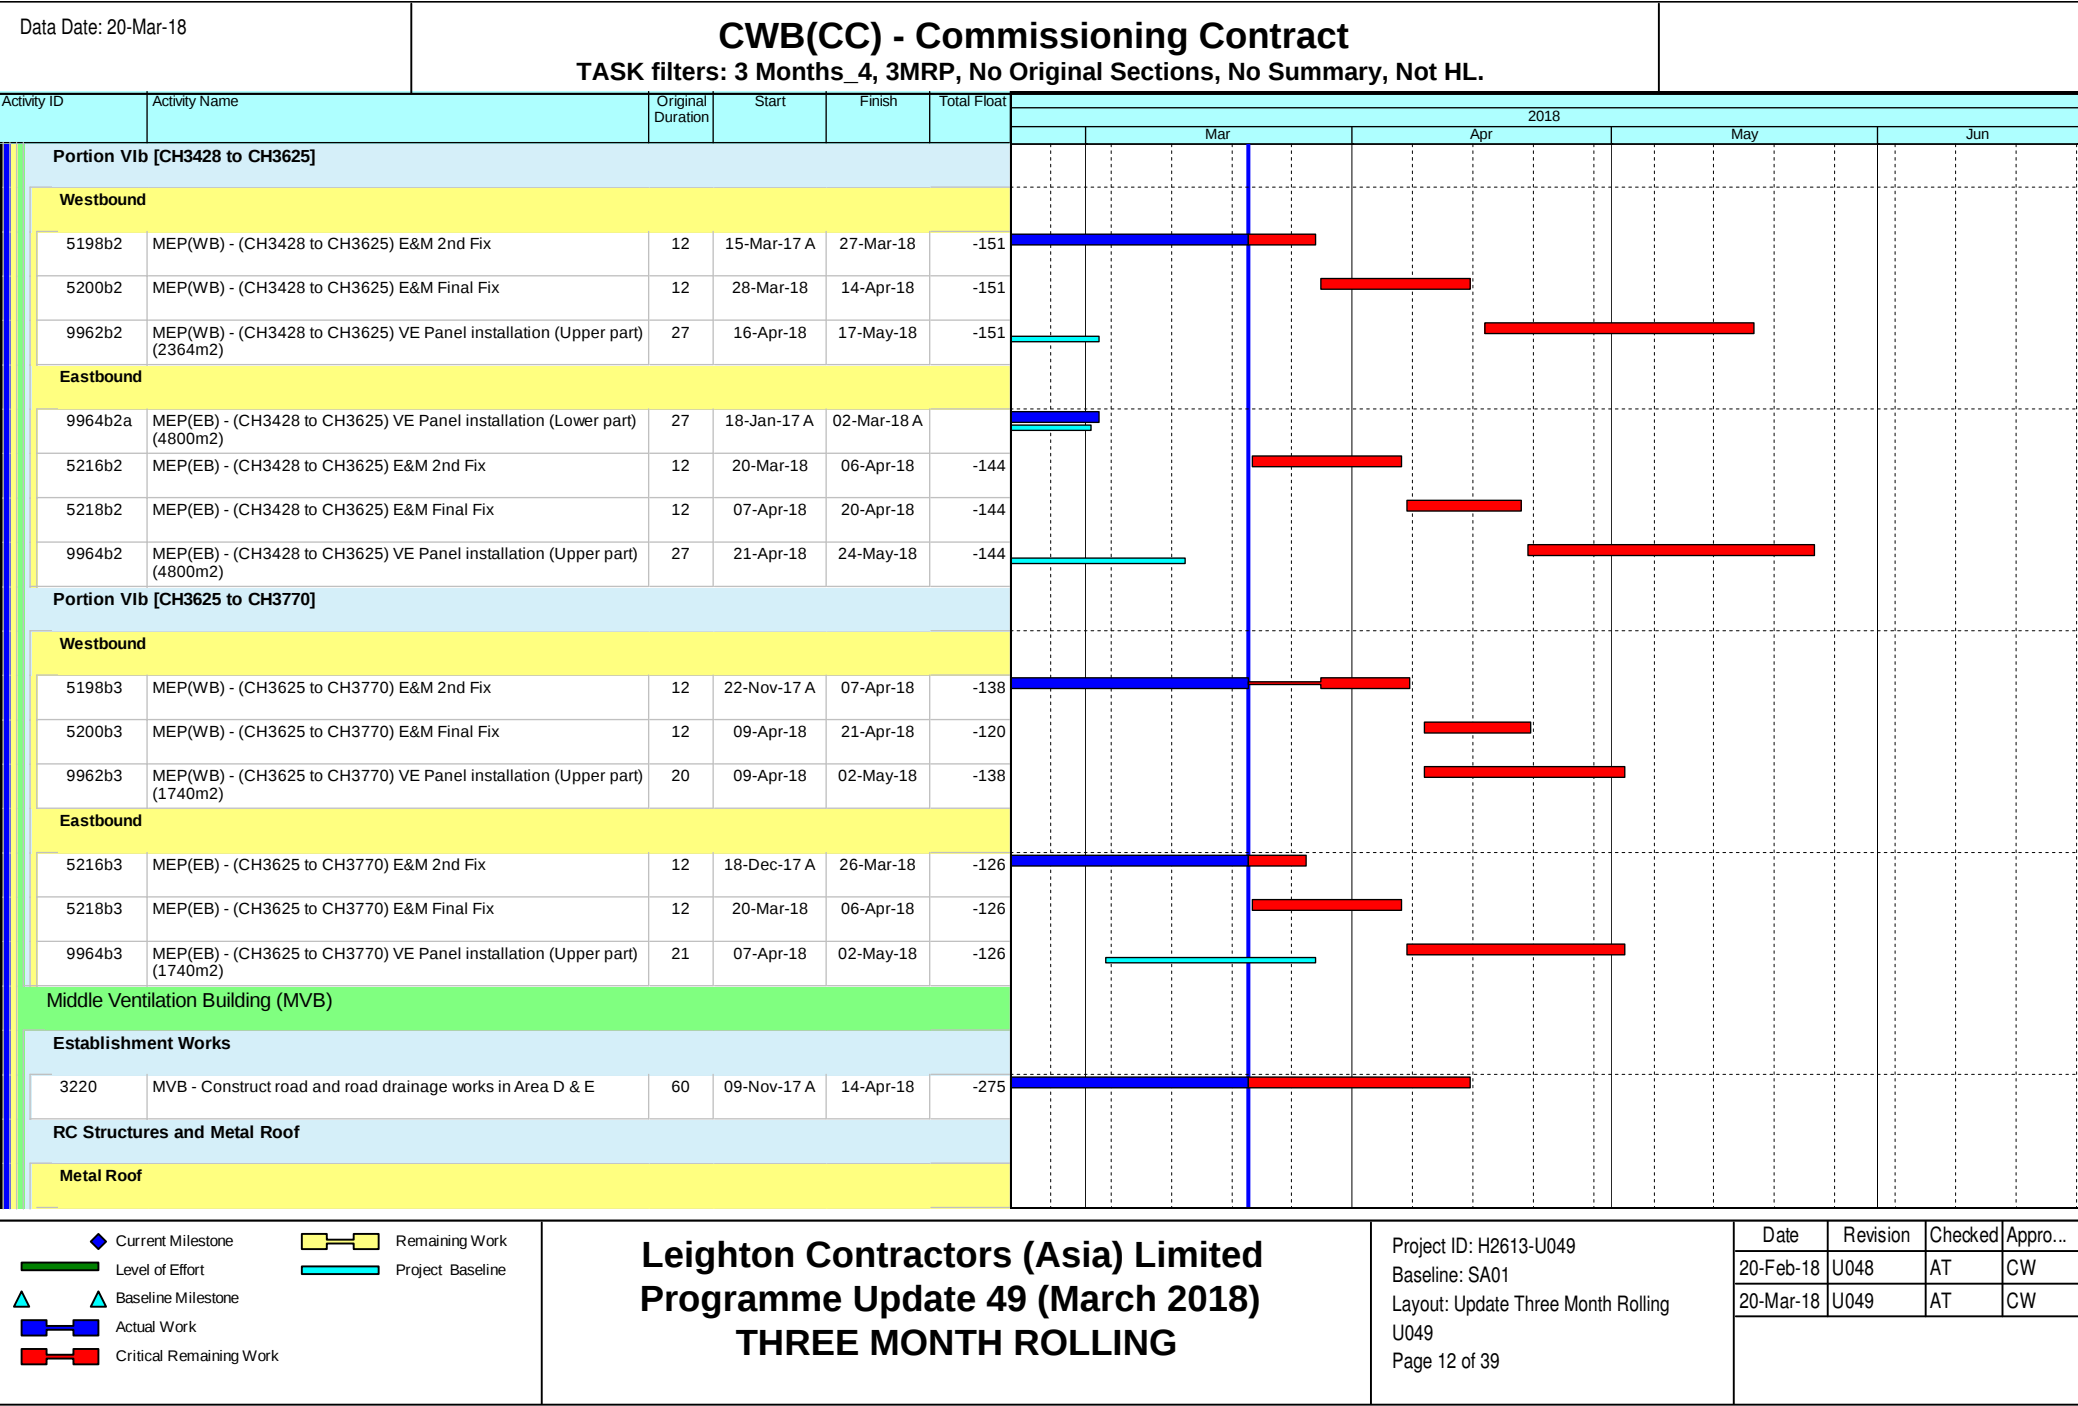


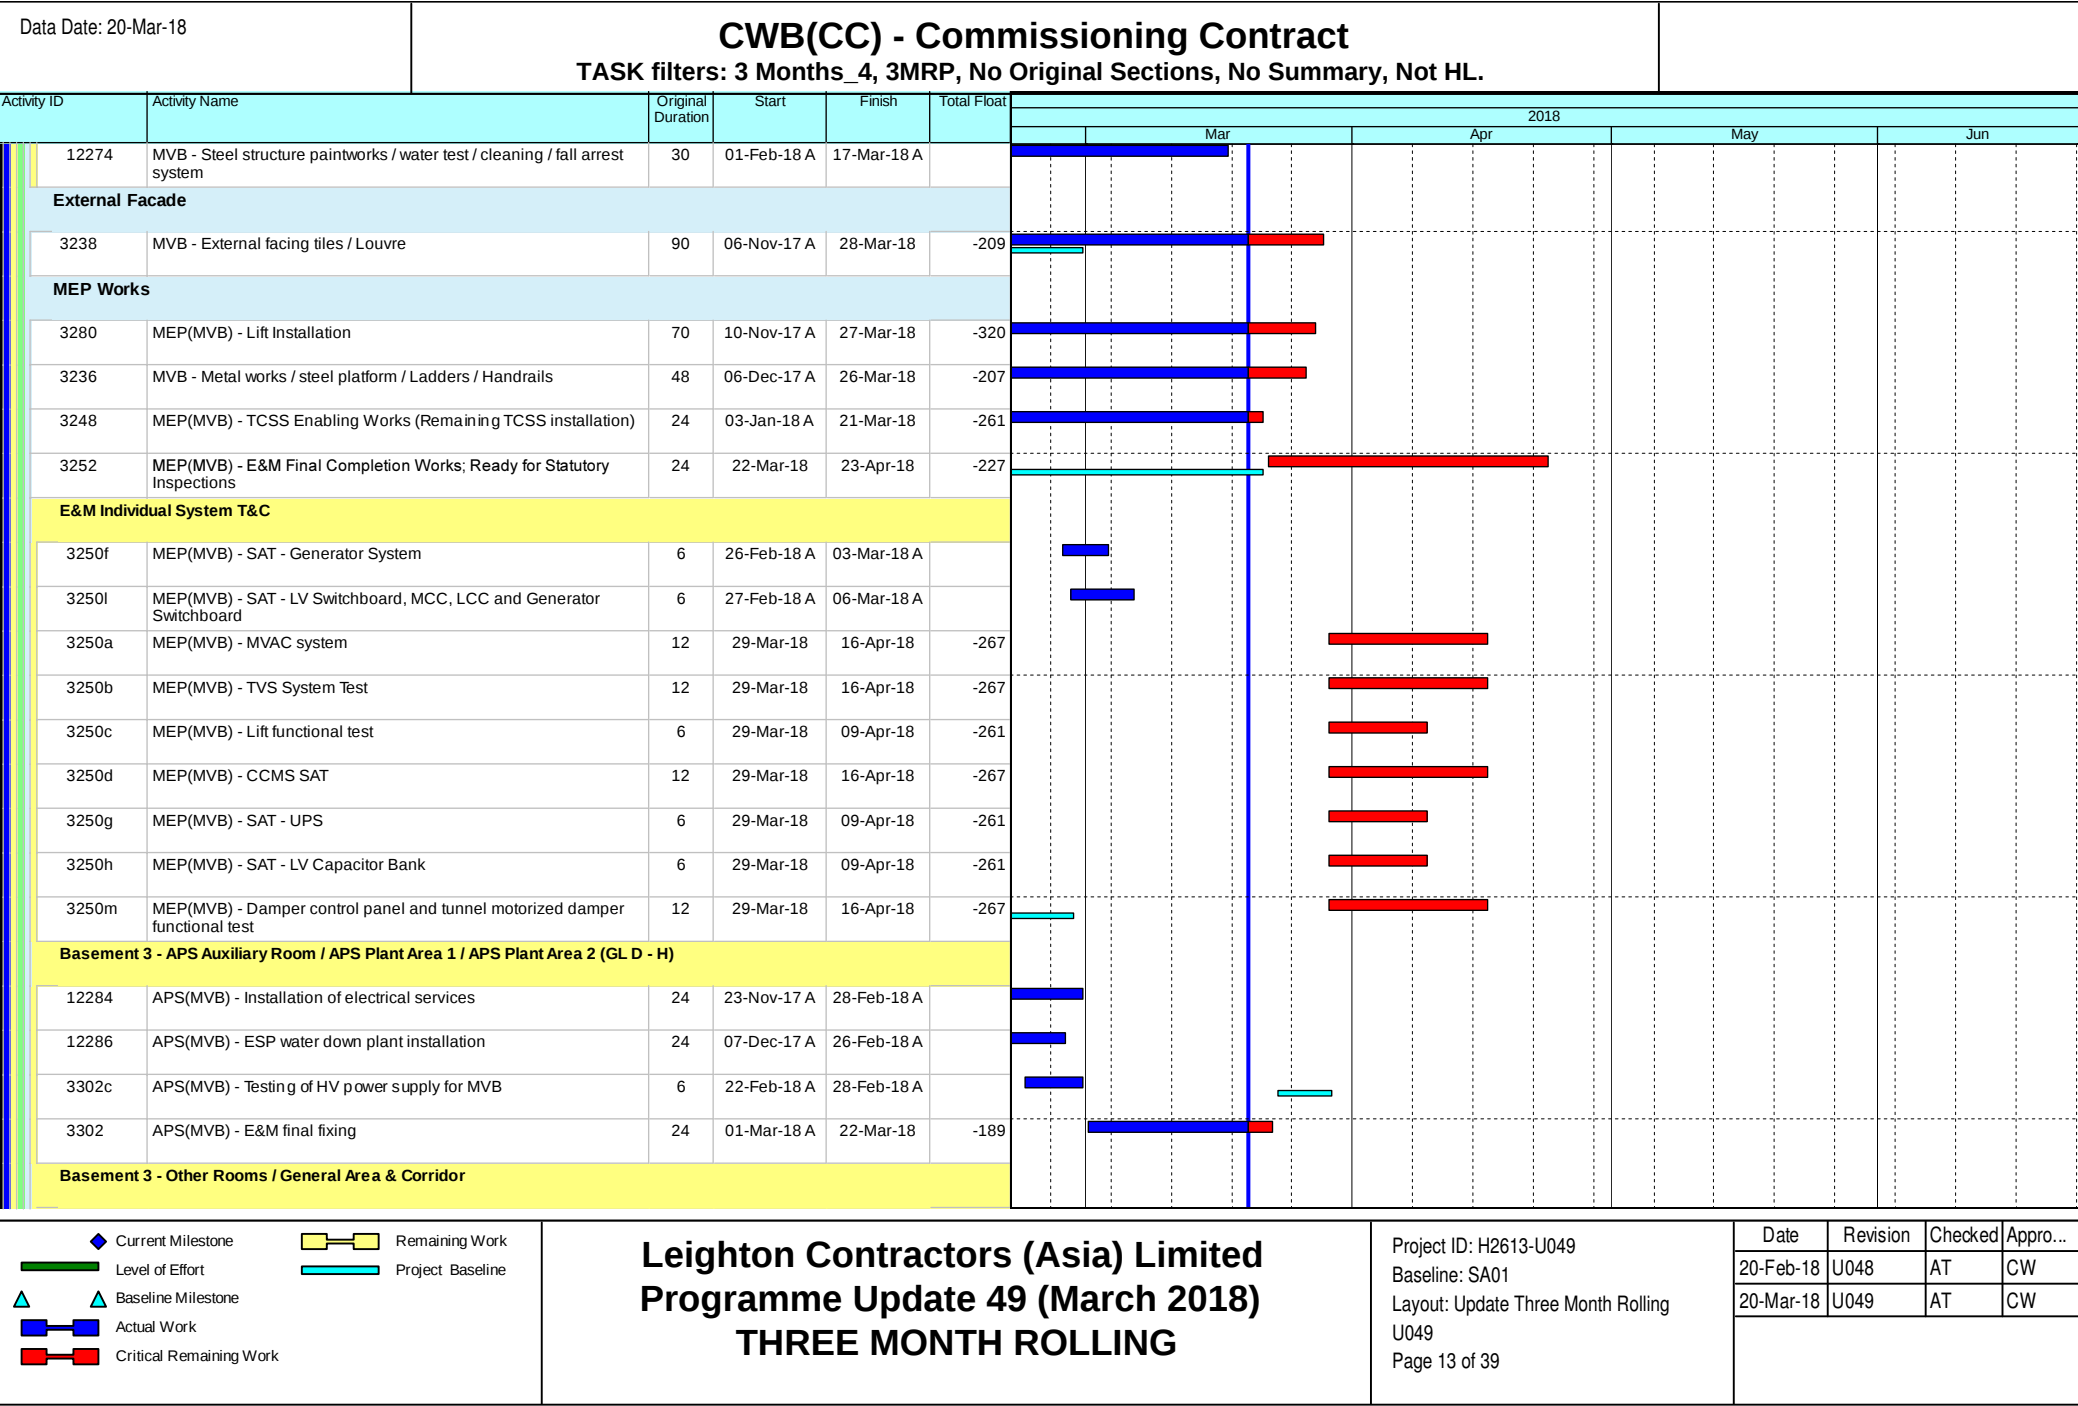


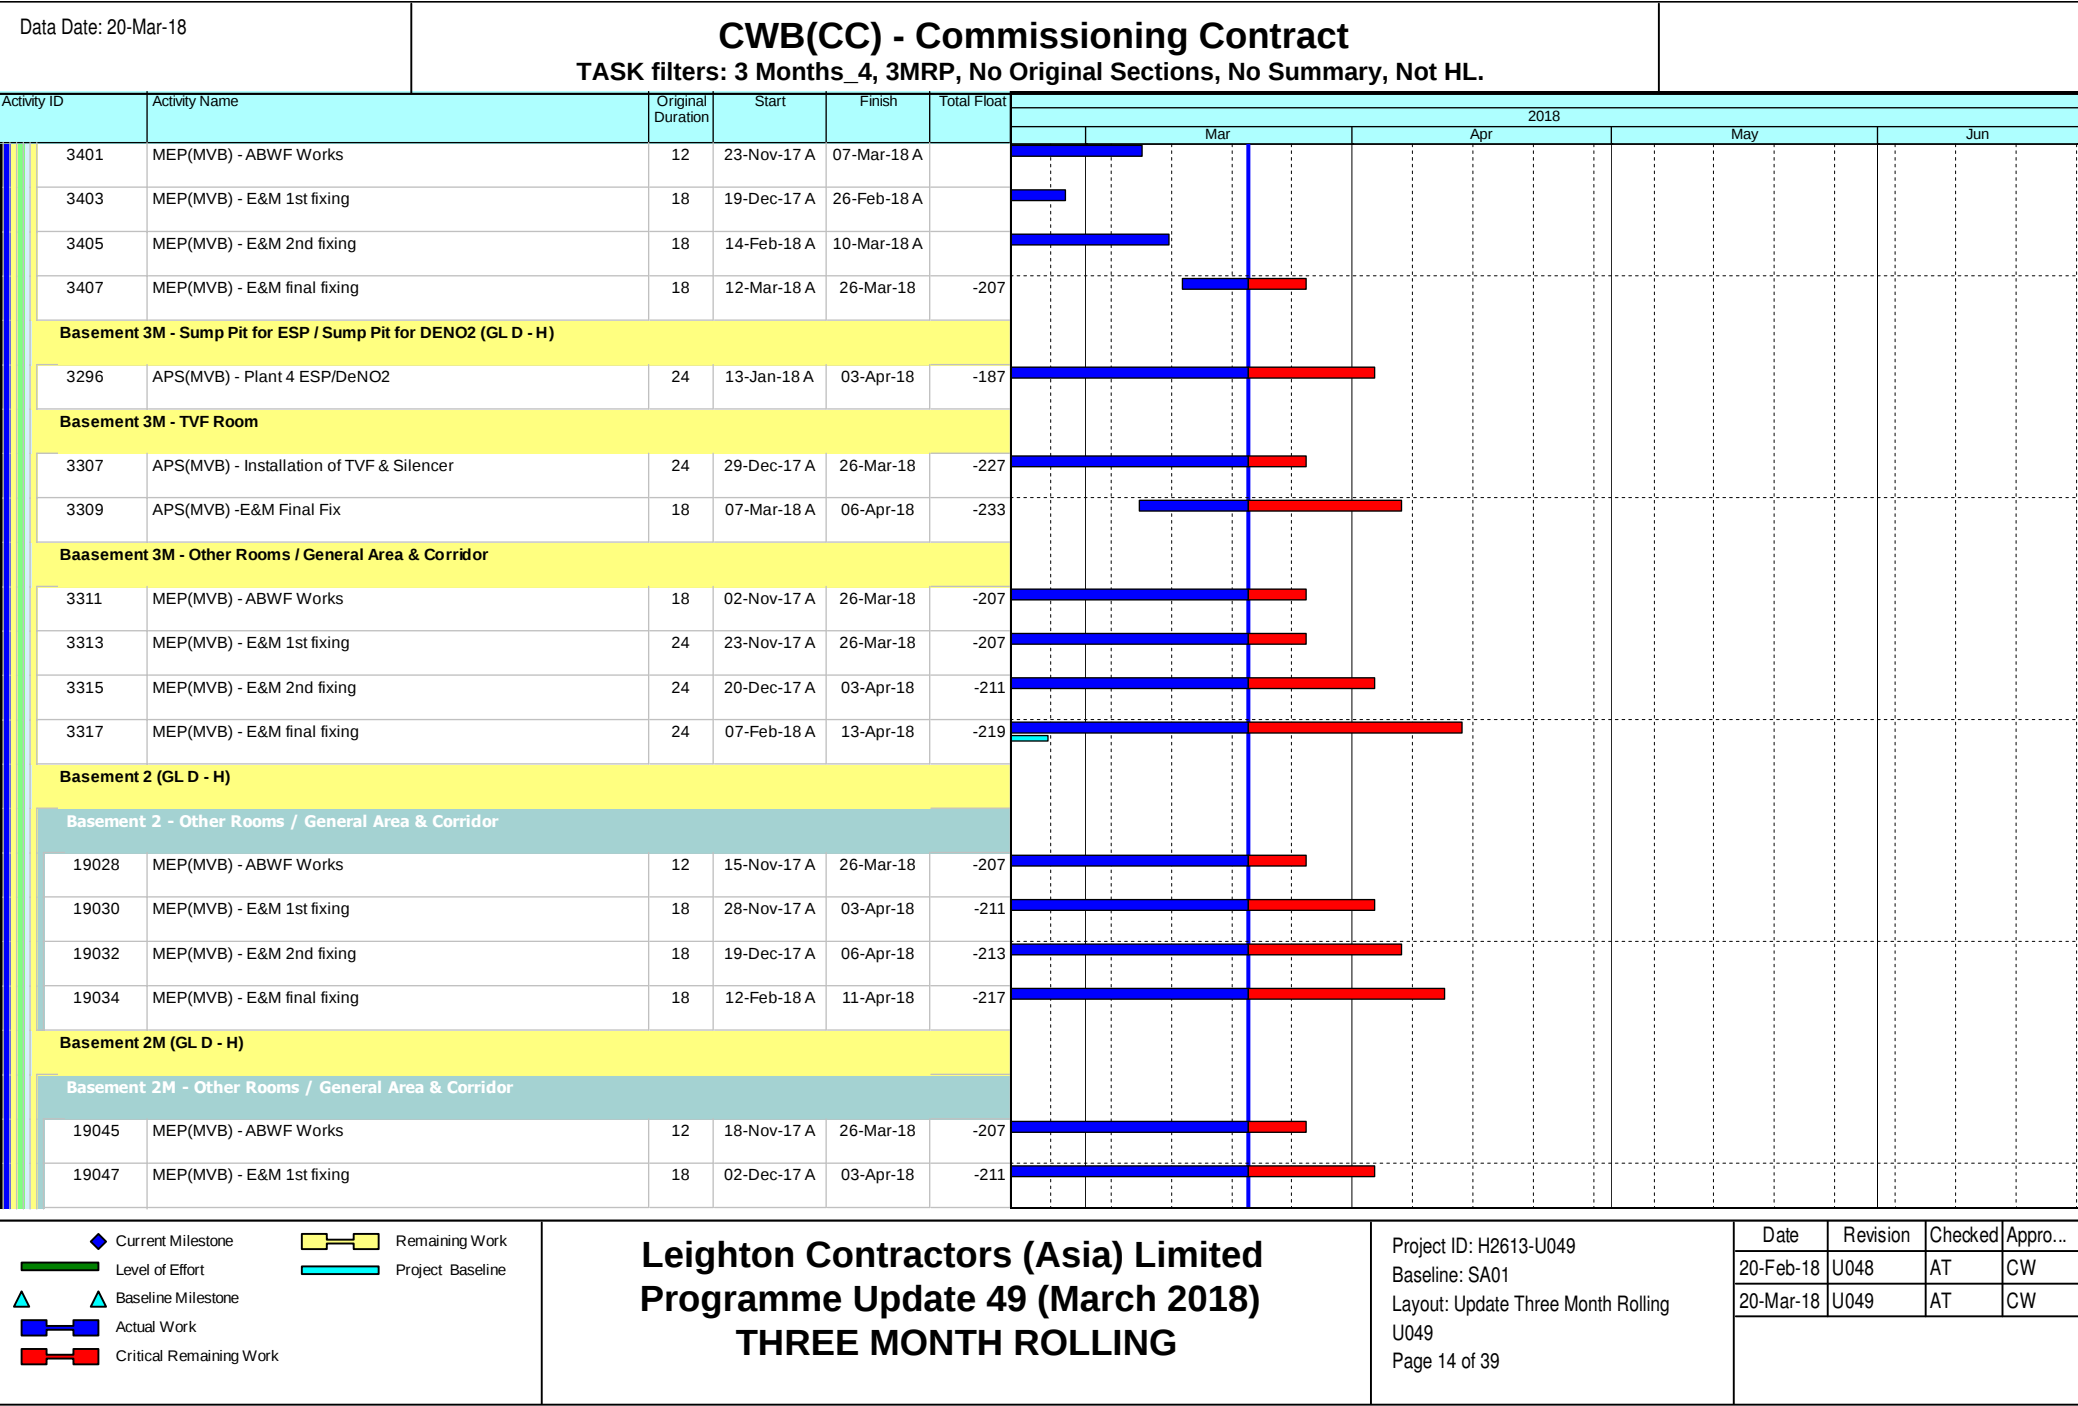


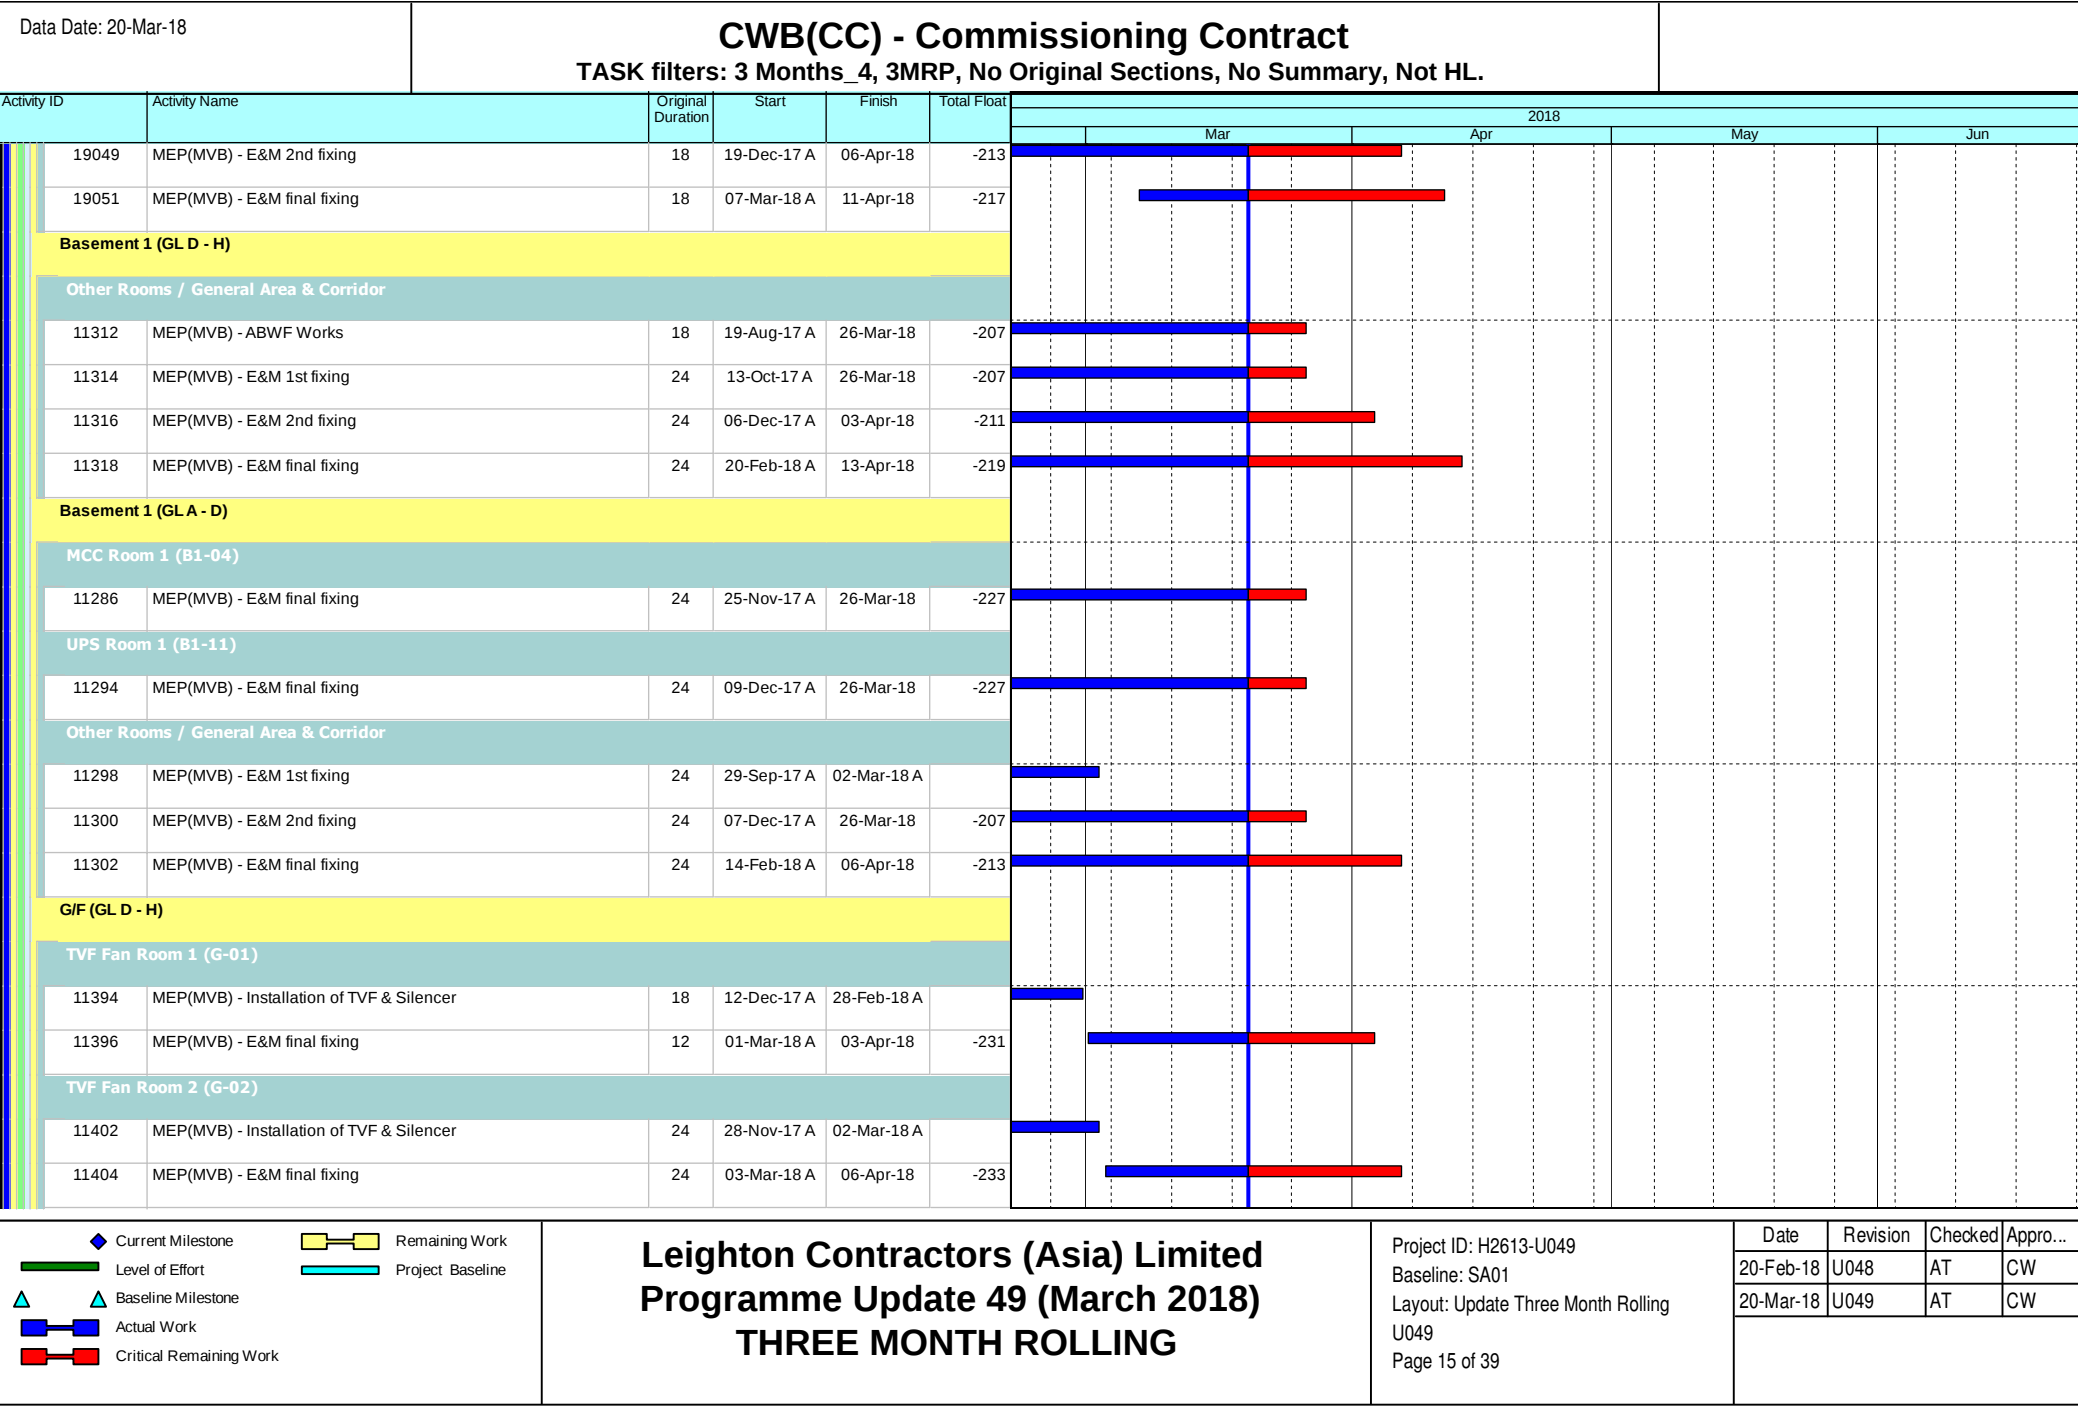

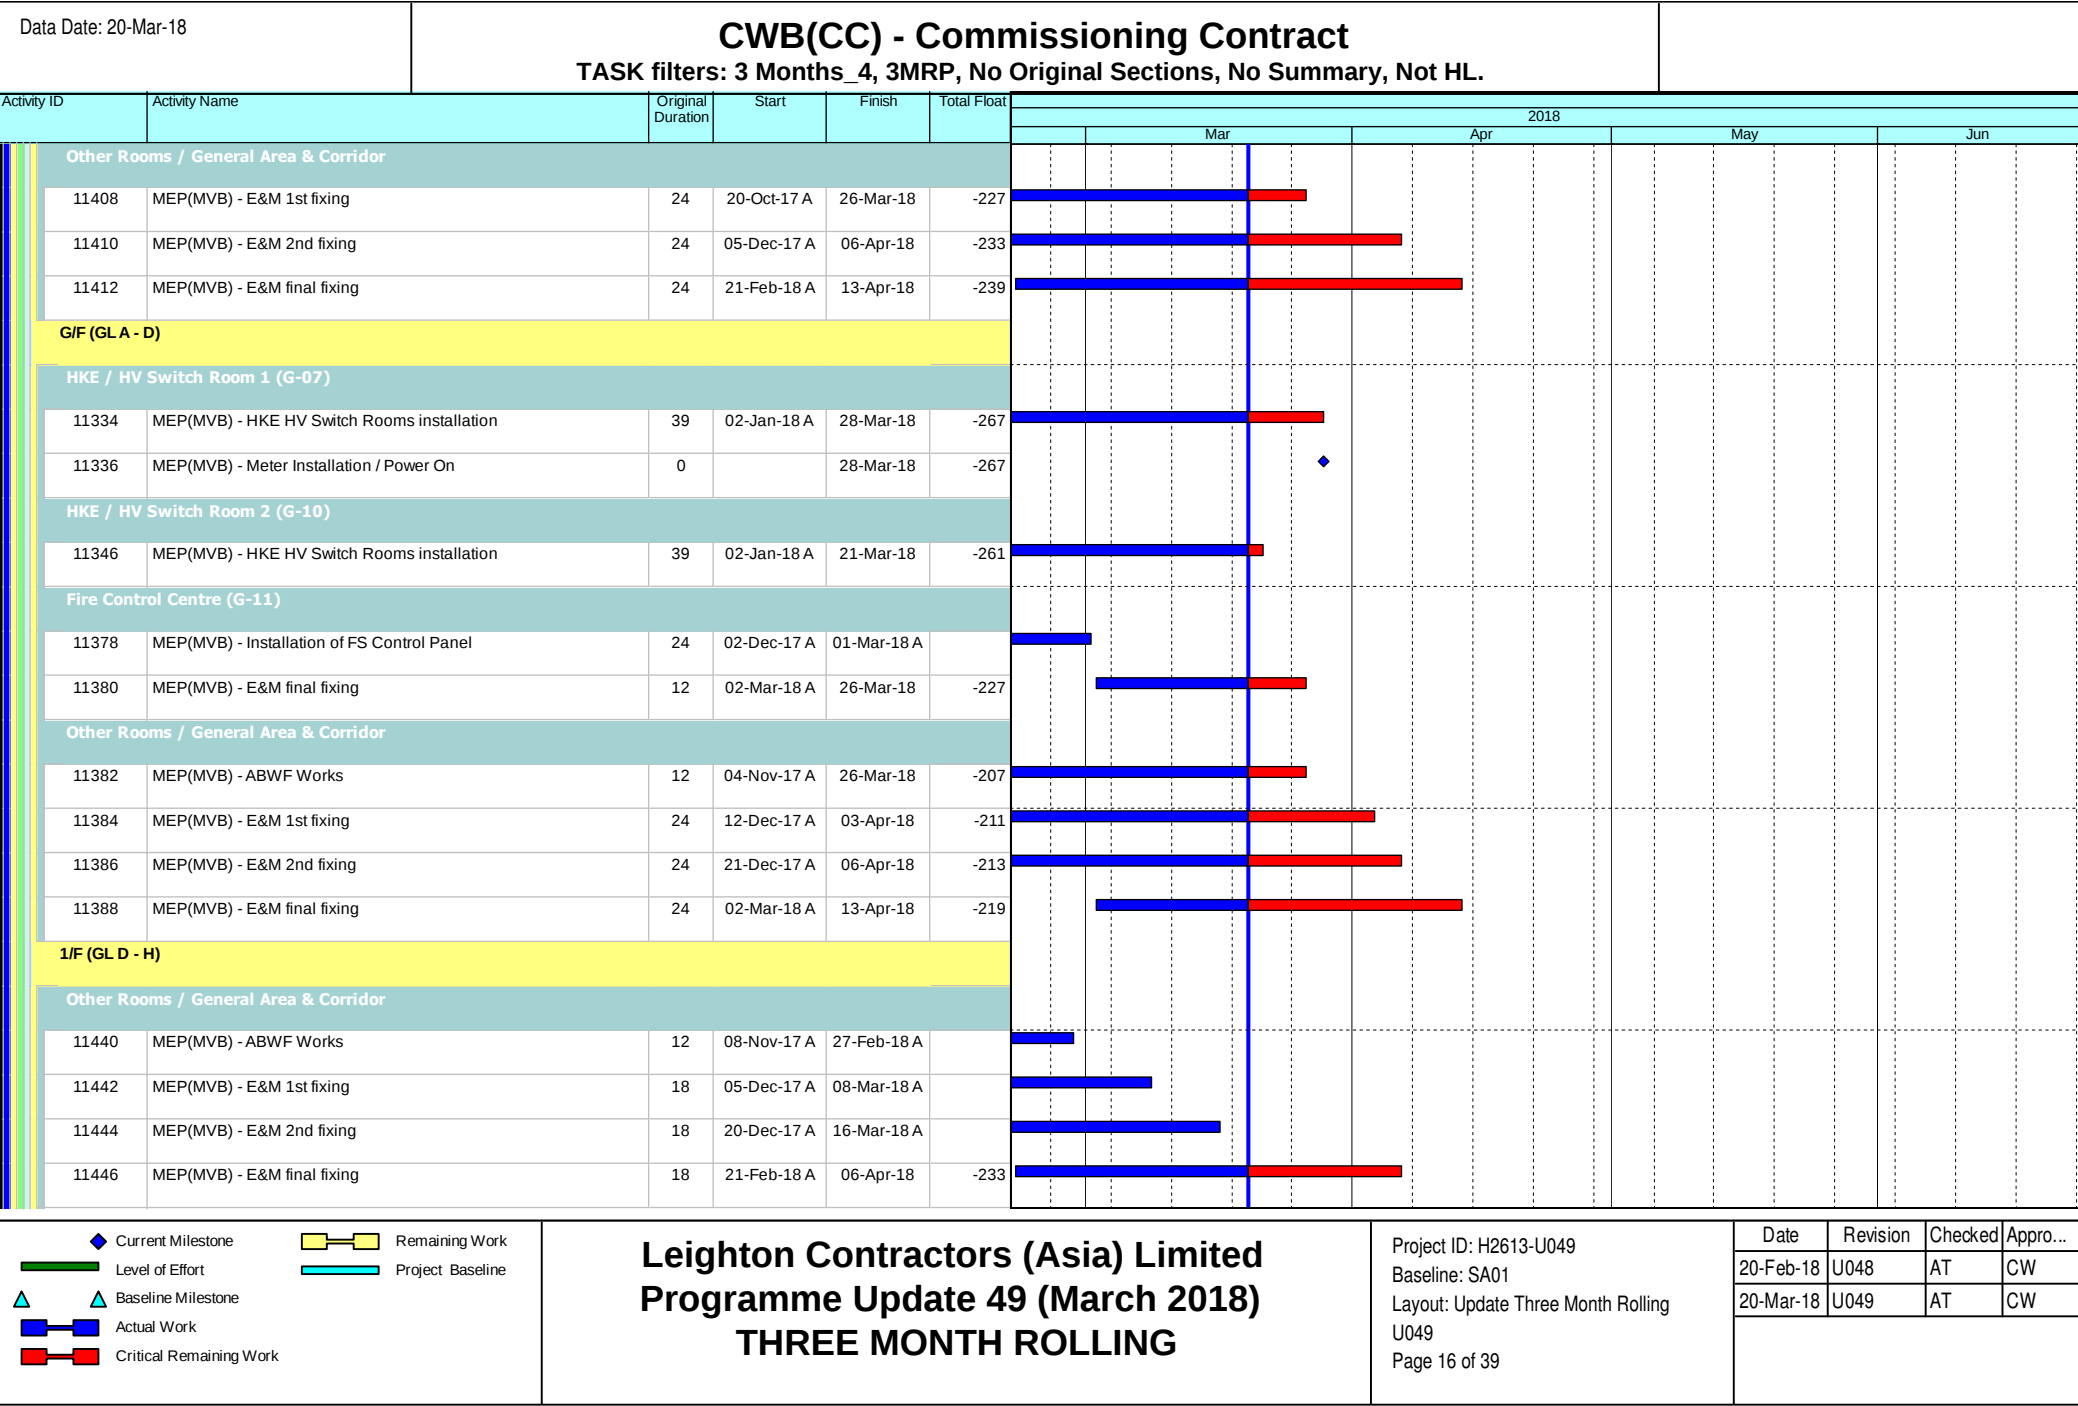

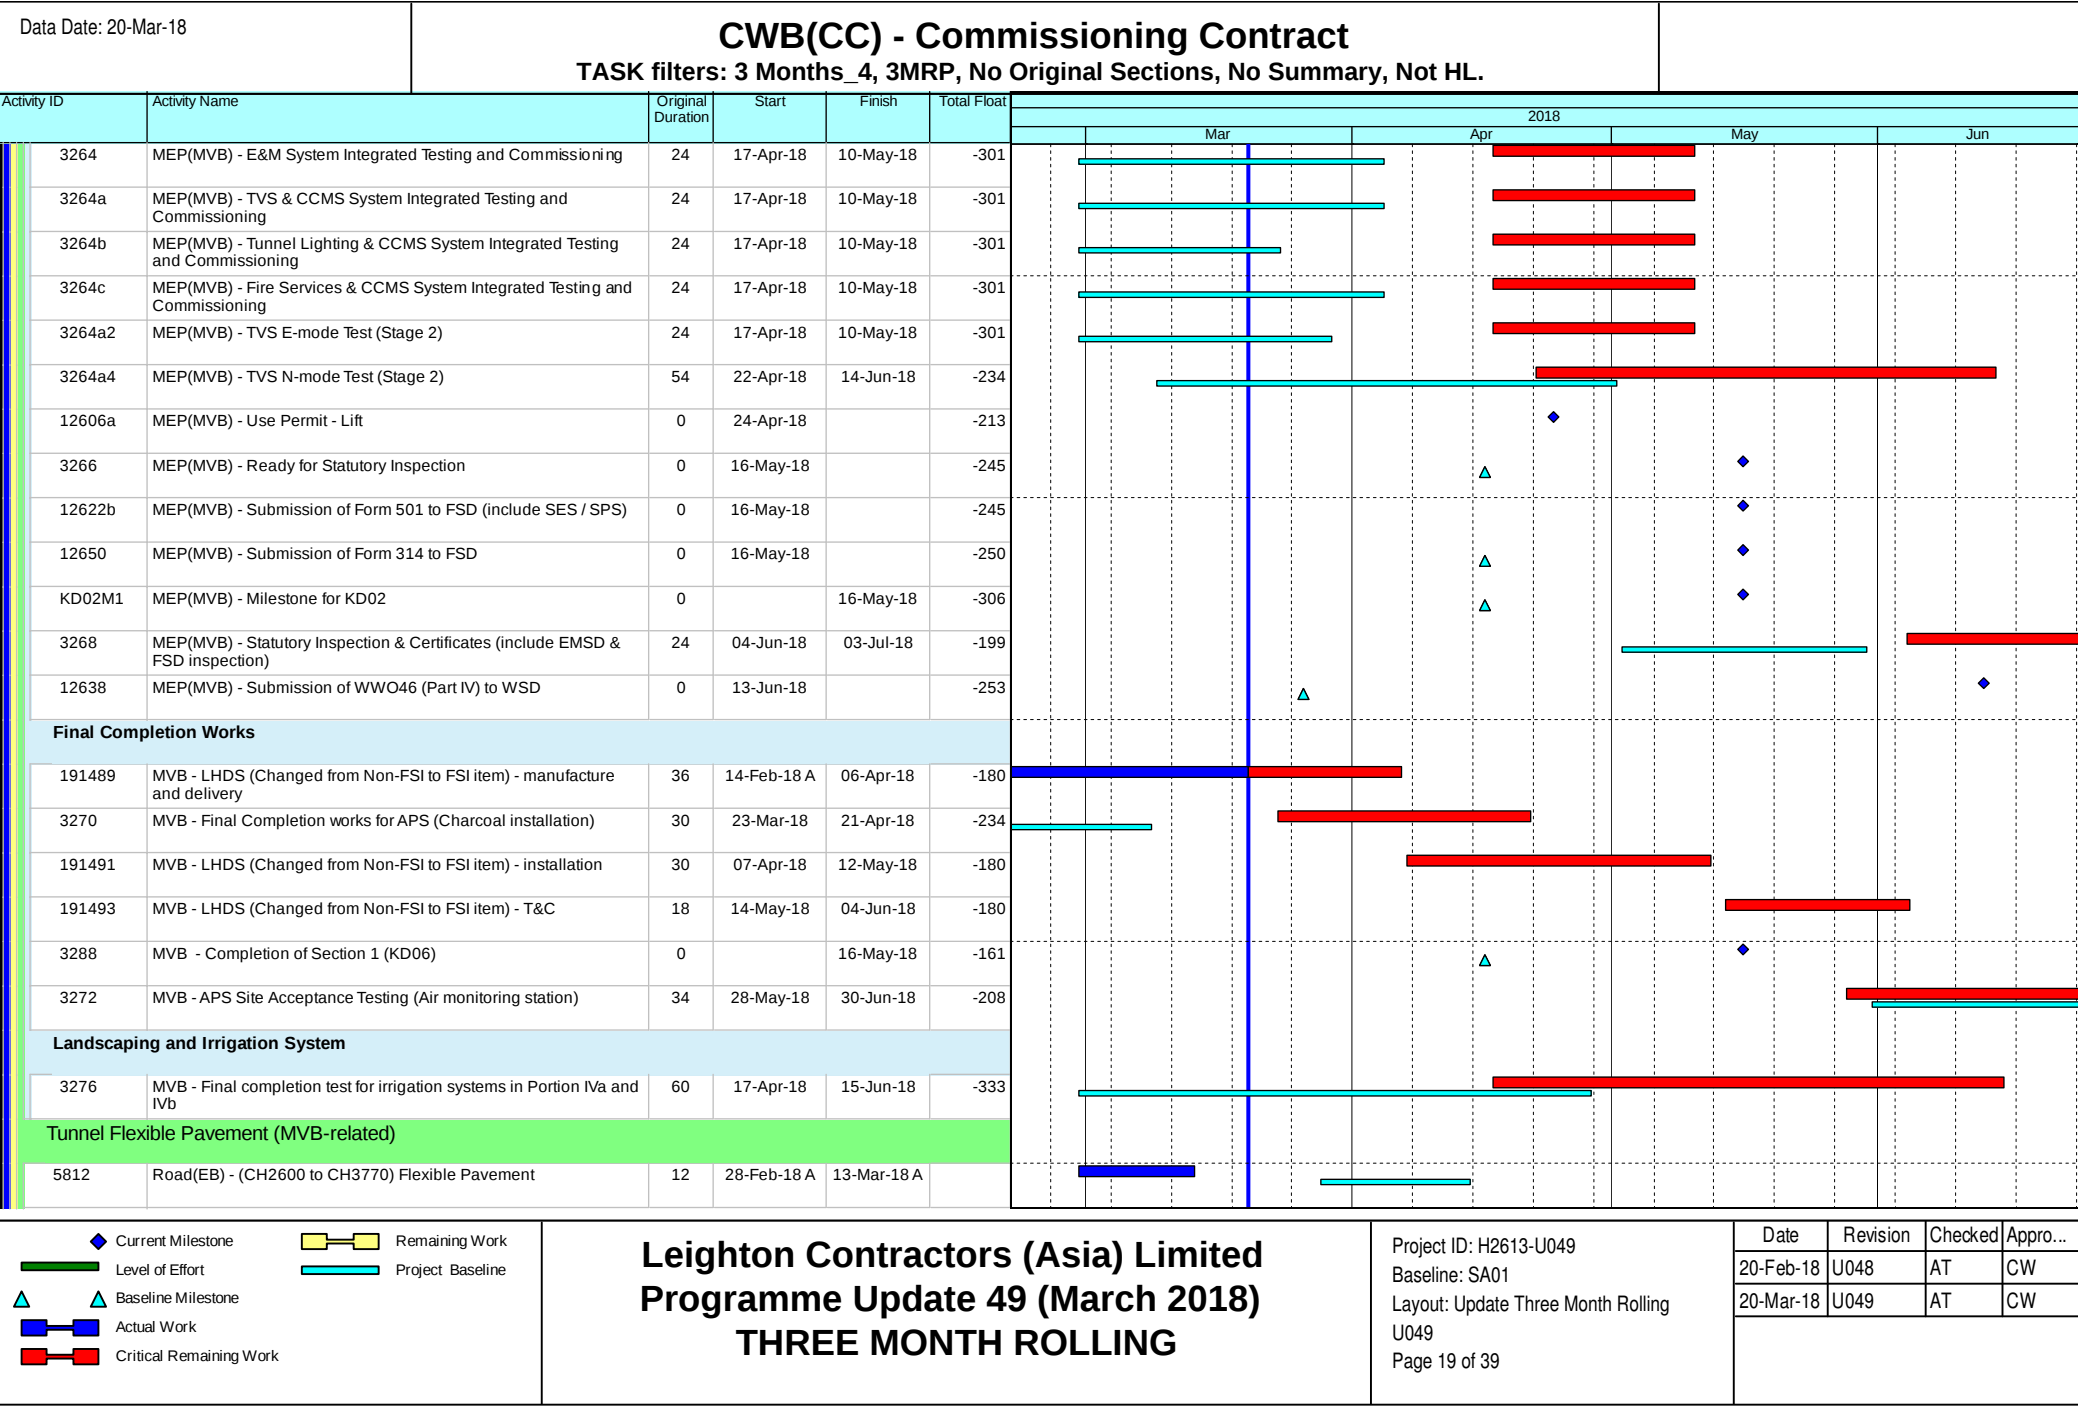

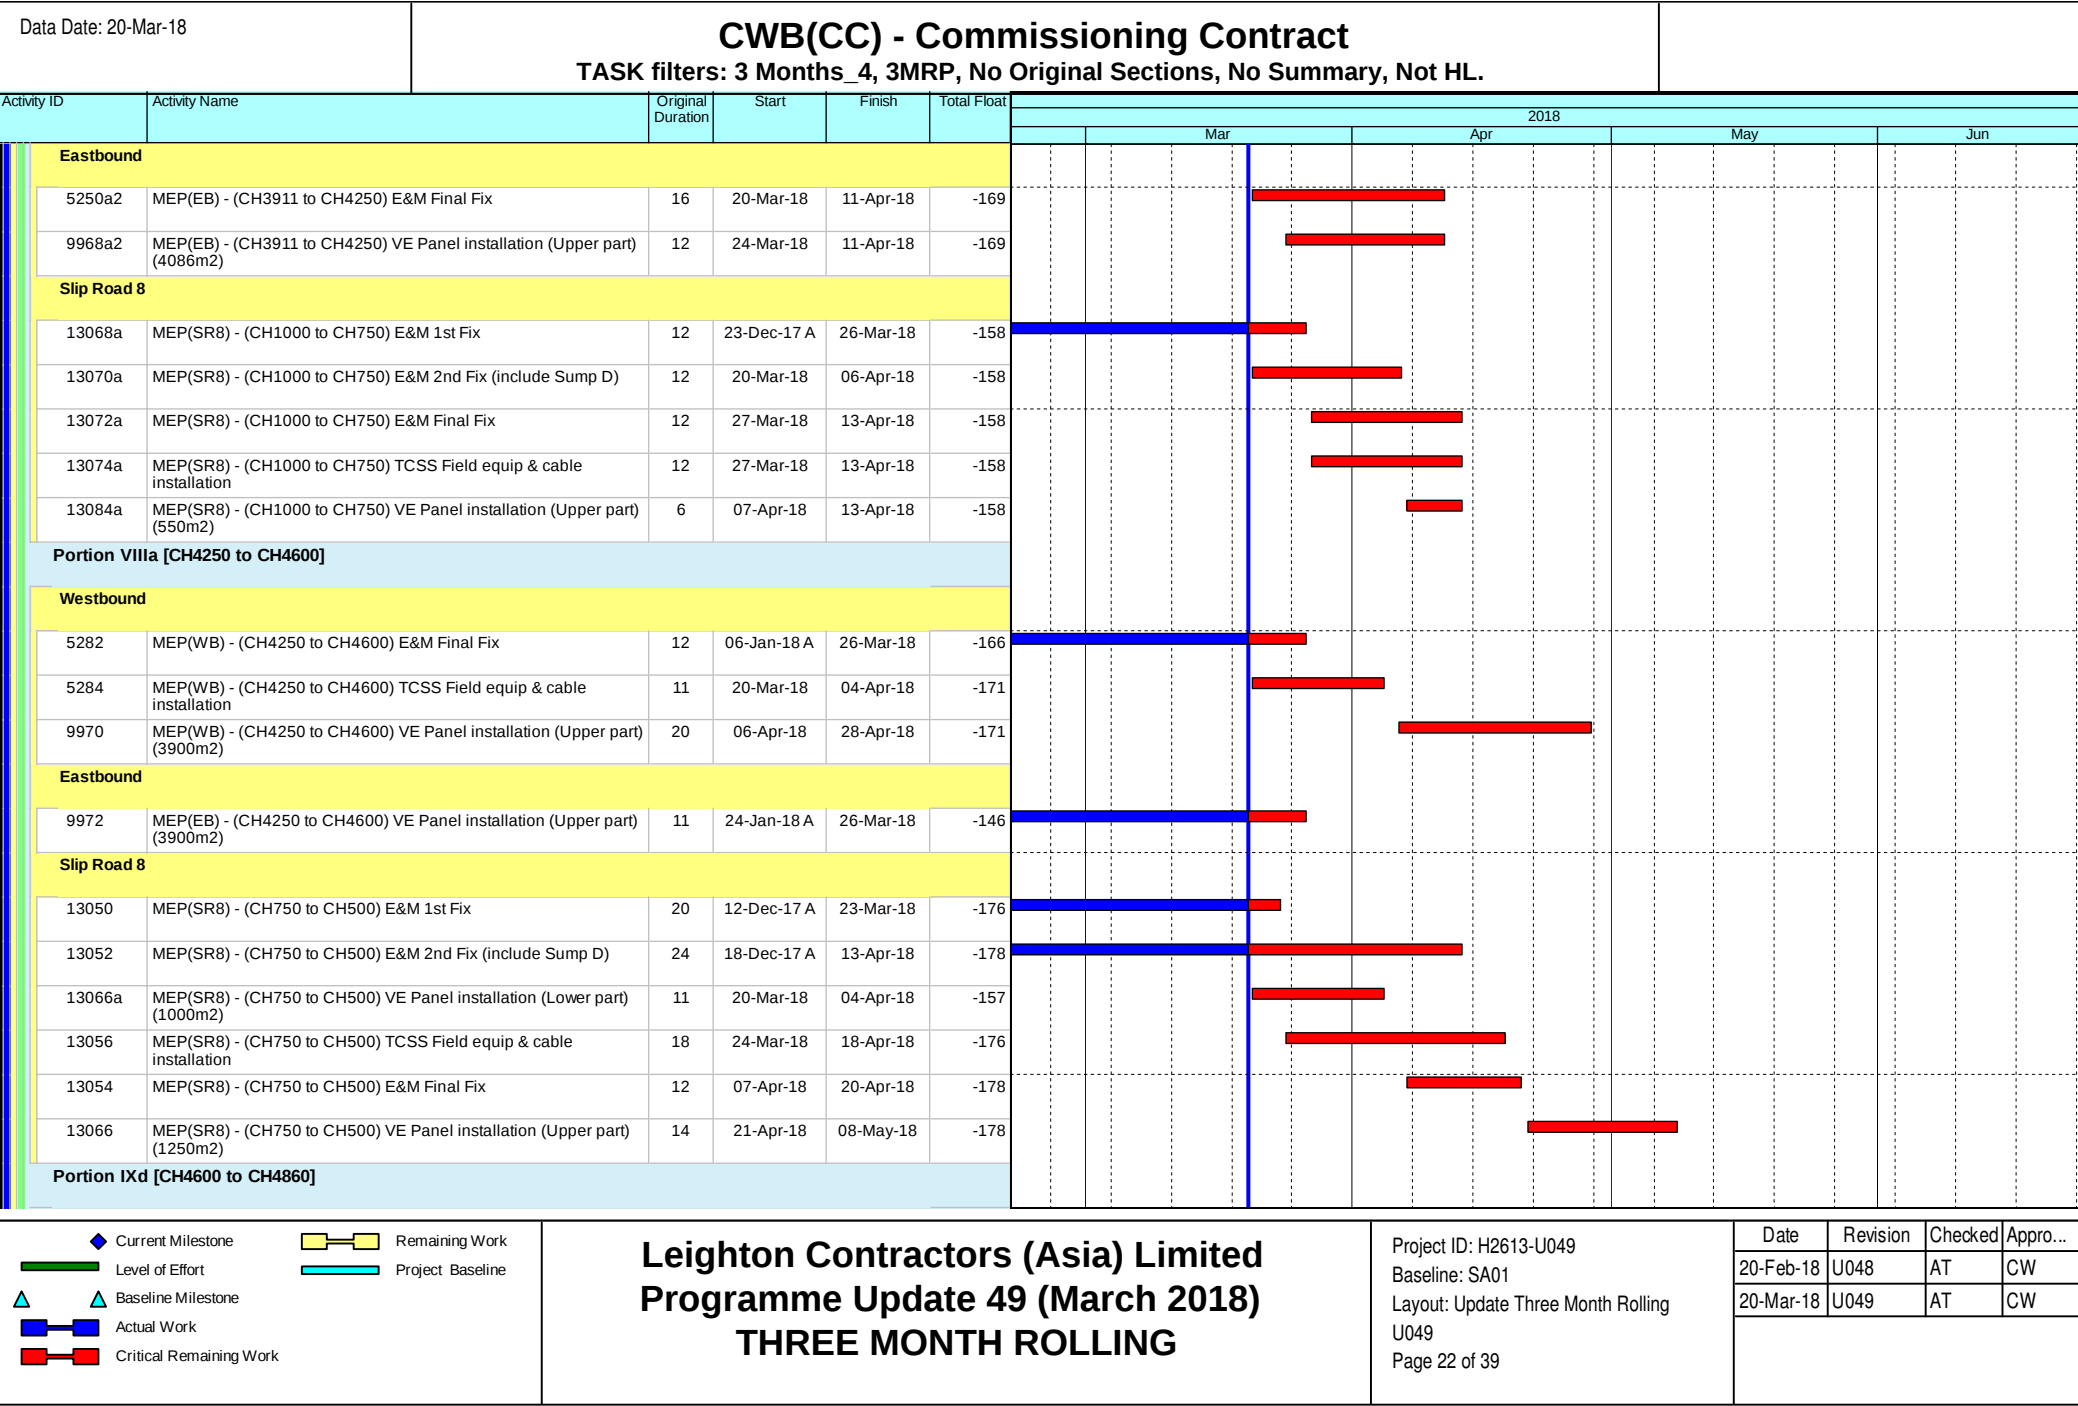

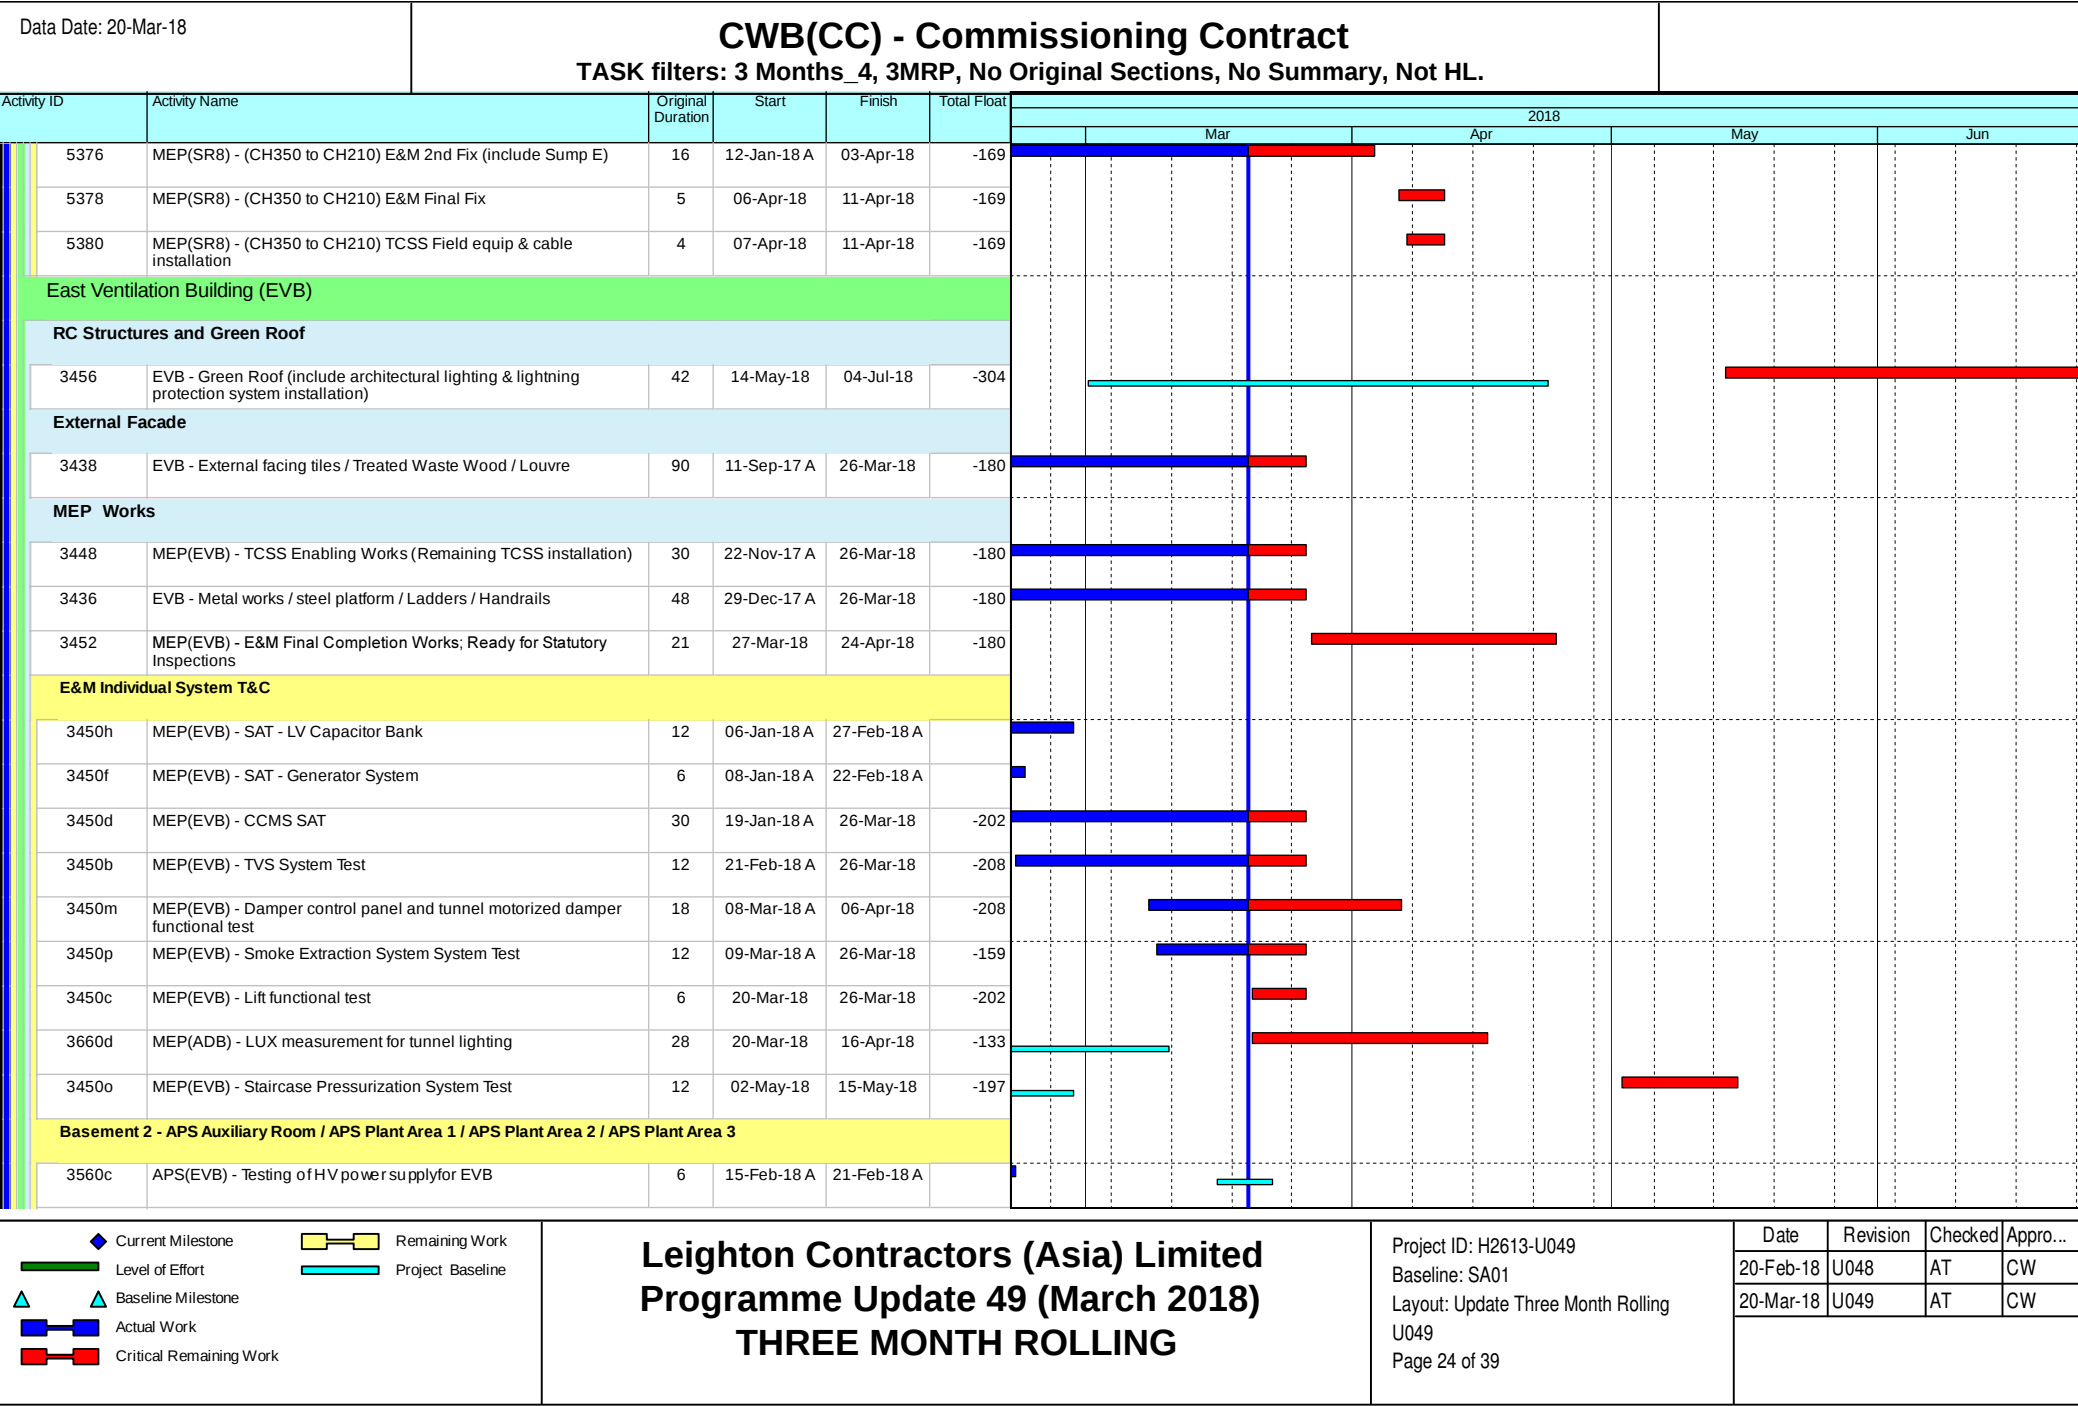

Data Date: 20-Mar-18		CWB(CC) - Commissioning Contract																
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																		
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2018												
						Mar			Apr			May			Jun			
11658	MEP(EVB) - E&M 2nd fixing	24	16-Oct-17 A	20-Feb-18 A														
11660	MEP(EVB) - E&M final fixing	24	07-Feb-18 A	08-Mar-18 A														
Basement 1 (GL L - O)																		
Tunnel F.S.Water Tank & Pump Room (B1-02)																		
11644	MEP(EVB) - E&M final fixing	24	05-Dec-17 A	03-Mar-18 A														
F.S.Water Tank & Pump Room (B1-03)																		
11652	MEP(EVB) - E&M final fixing	24	28-Nov-17 A	22-Feb-18 A														
Other Rooms / General Area & Corridor																		
11678	MEP(EVB) - E&M final fixing	24	18-Dec-17 A	27-Feb-18 A														
G/F (GL A - D)																		
Other Rooms / General Area & Corridor																		
11738	MEP(EVB) - E&M final fixing	24	17-Jan-18 A	28-Feb-18 A														
1/F (GL A - D)																		
Other Rooms / General Area & Corridor																		
11774	MEP(EVB) - E&M 1st fixing	30	27-Sep-17 A	21-Feb-18 A														
11776	MEP(EVB) - E&M 2nd fixing	30	24-Nov-17 A	26-Mar-18	-122													
11778	MEP(EVB) - E&M final fixing	30	12-Dec-17 A	03-Apr-18	-126													
Staircase Pressurization System (B2/F - G/F)																		
B2/F - G/F																		
191381	SPS (EVB) - Installation of external louvre for VS01b	24	06-Jan-18 A	15-Mar-18 A														
191339	SPS(EVB) - Conduit and wiring works for SPS control	20	13-Jan-18 A	14-Mar-18 A														
191343	SPS(EVB) - MSFD installation	6	15-Jan-18 A	23-Feb-18 A														
191347	SPS(EVB) - SPS control panel installation	6	07-Mar-18 A	14-Mar-18 A														
191345	SPS(EVB) - Airduct work and FRP enclosure	20	15-Mar-18 A	09-Apr-18	-197													

Current Milestone

Level of Effort

Baseline Milestone

Actual Work

Critical Remaining Work

Remaining Work

Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 49 (March 2018)

THREE MONTH ROLLING

Project ID: H2613-U049

Baseline: SA01

Layout: Update Three Month Rolling

U049

Page 26 of 39

Date	Revision	Checked	Appro...
20-Feb-18	U048	AT	CW
20-Mar-18	U049	AT	CW

◆ Current Milestone

▬ Level of Effort

▲ Baseline Milestone

▬ Actual Work

▬ Critical Remaining Work

▬ Remaining Work

▬ Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 49 (March 2018)

THREE MONTH ROLLING

Project ID: H2613-U049


Baseline: SA01


Layout: Update Three Month Rolling


U049


Page 26 of 39


Date	Revision	Checked	Appro...
20-Feb-18	U048	AT	CW
20-Mar-18	U049	AT	CW

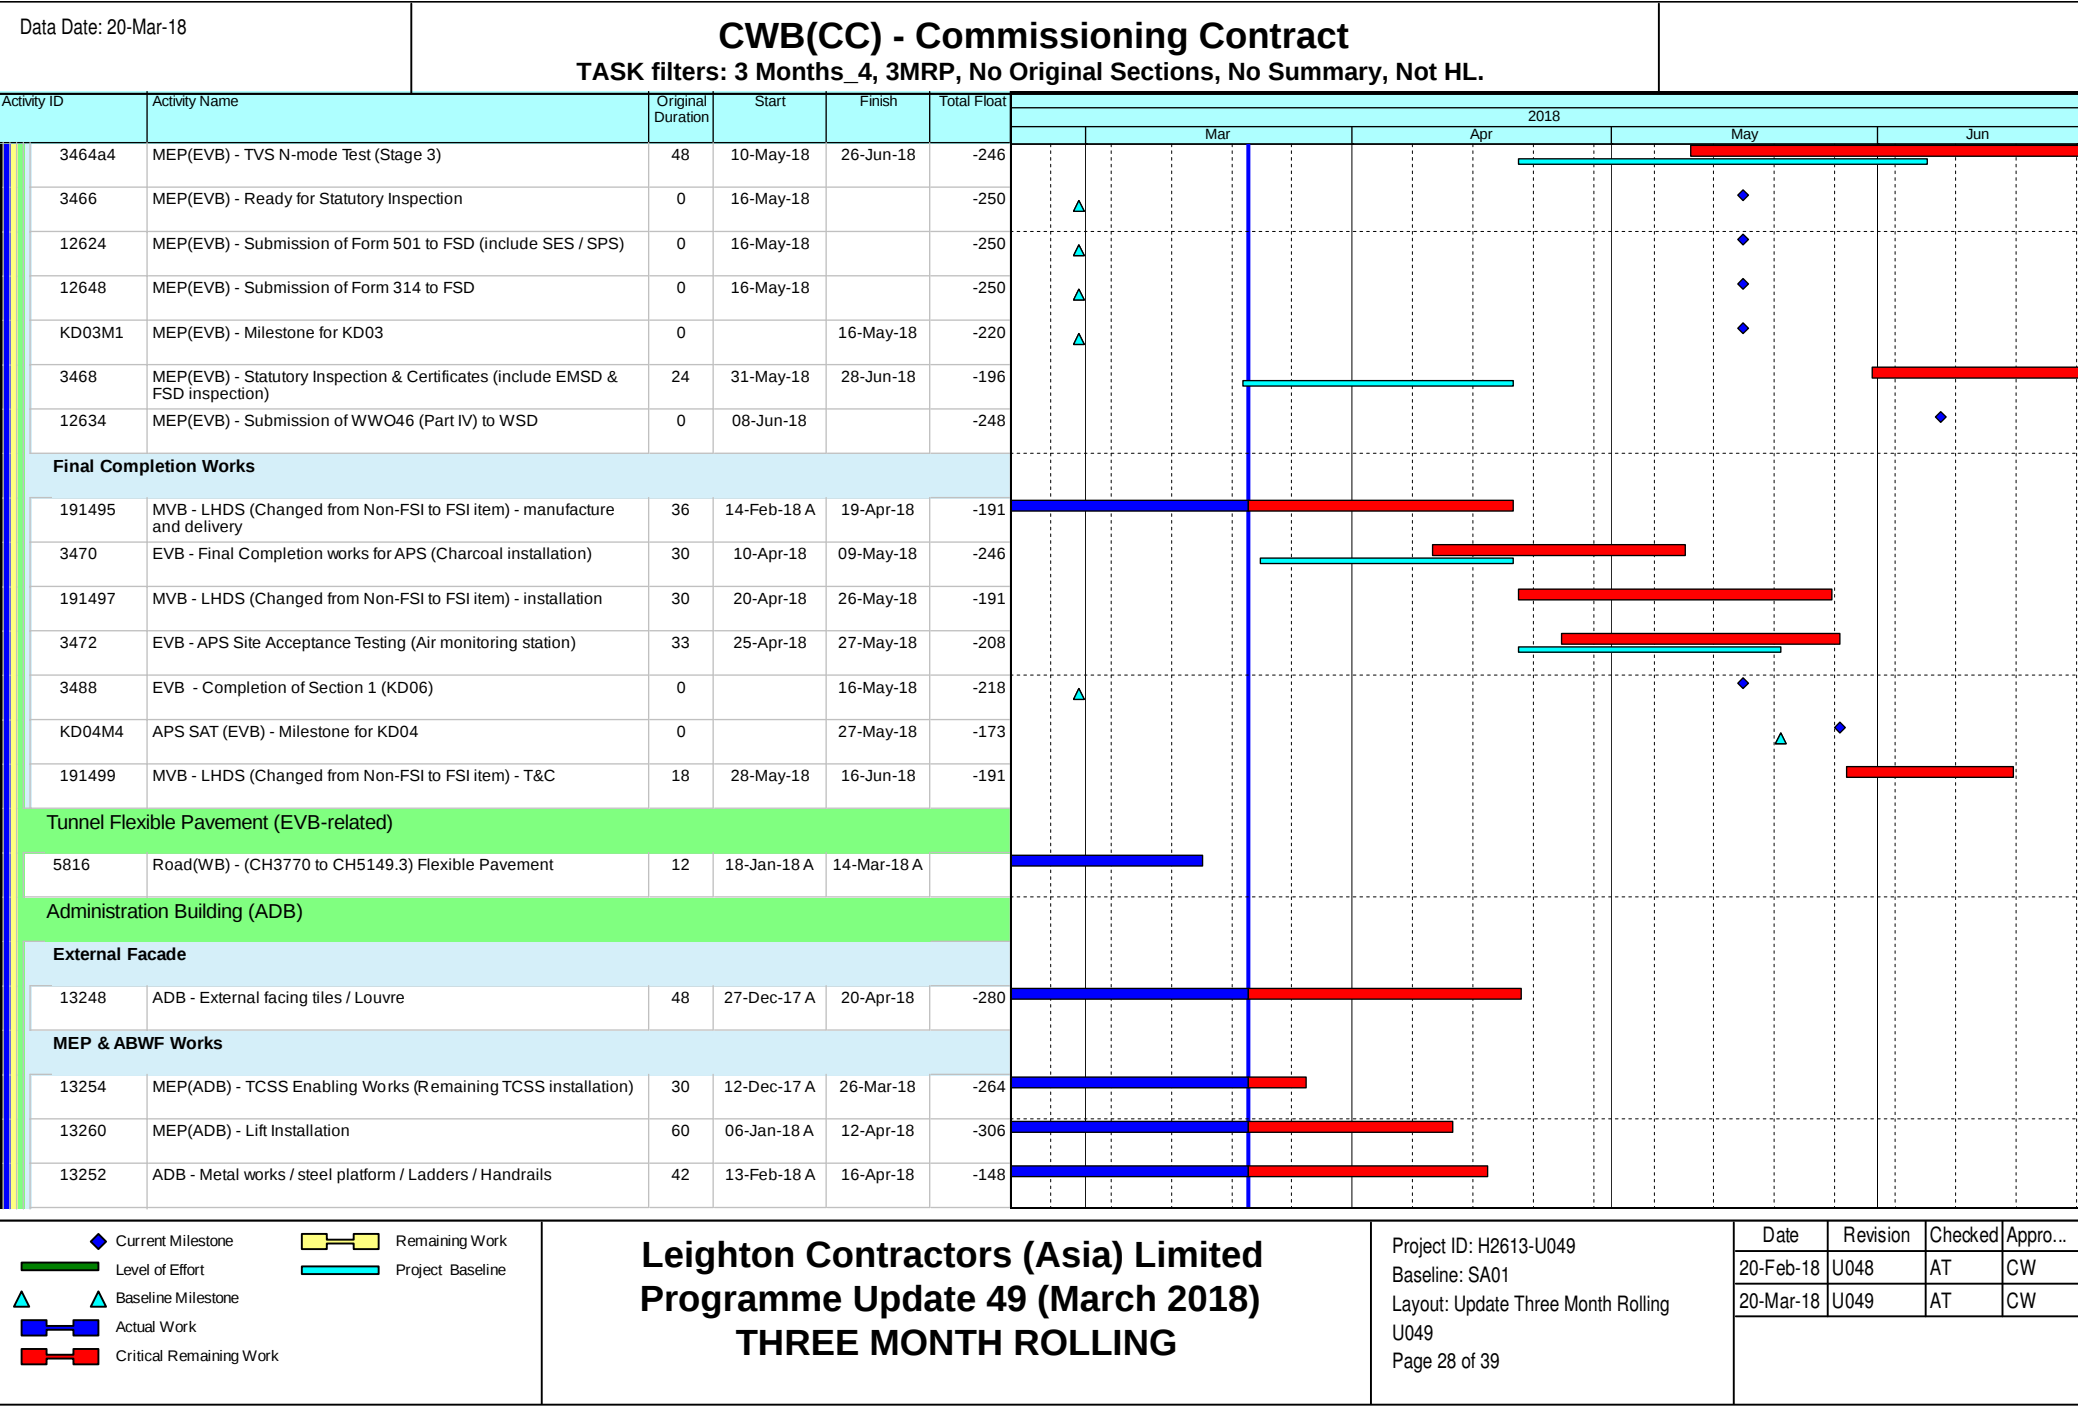


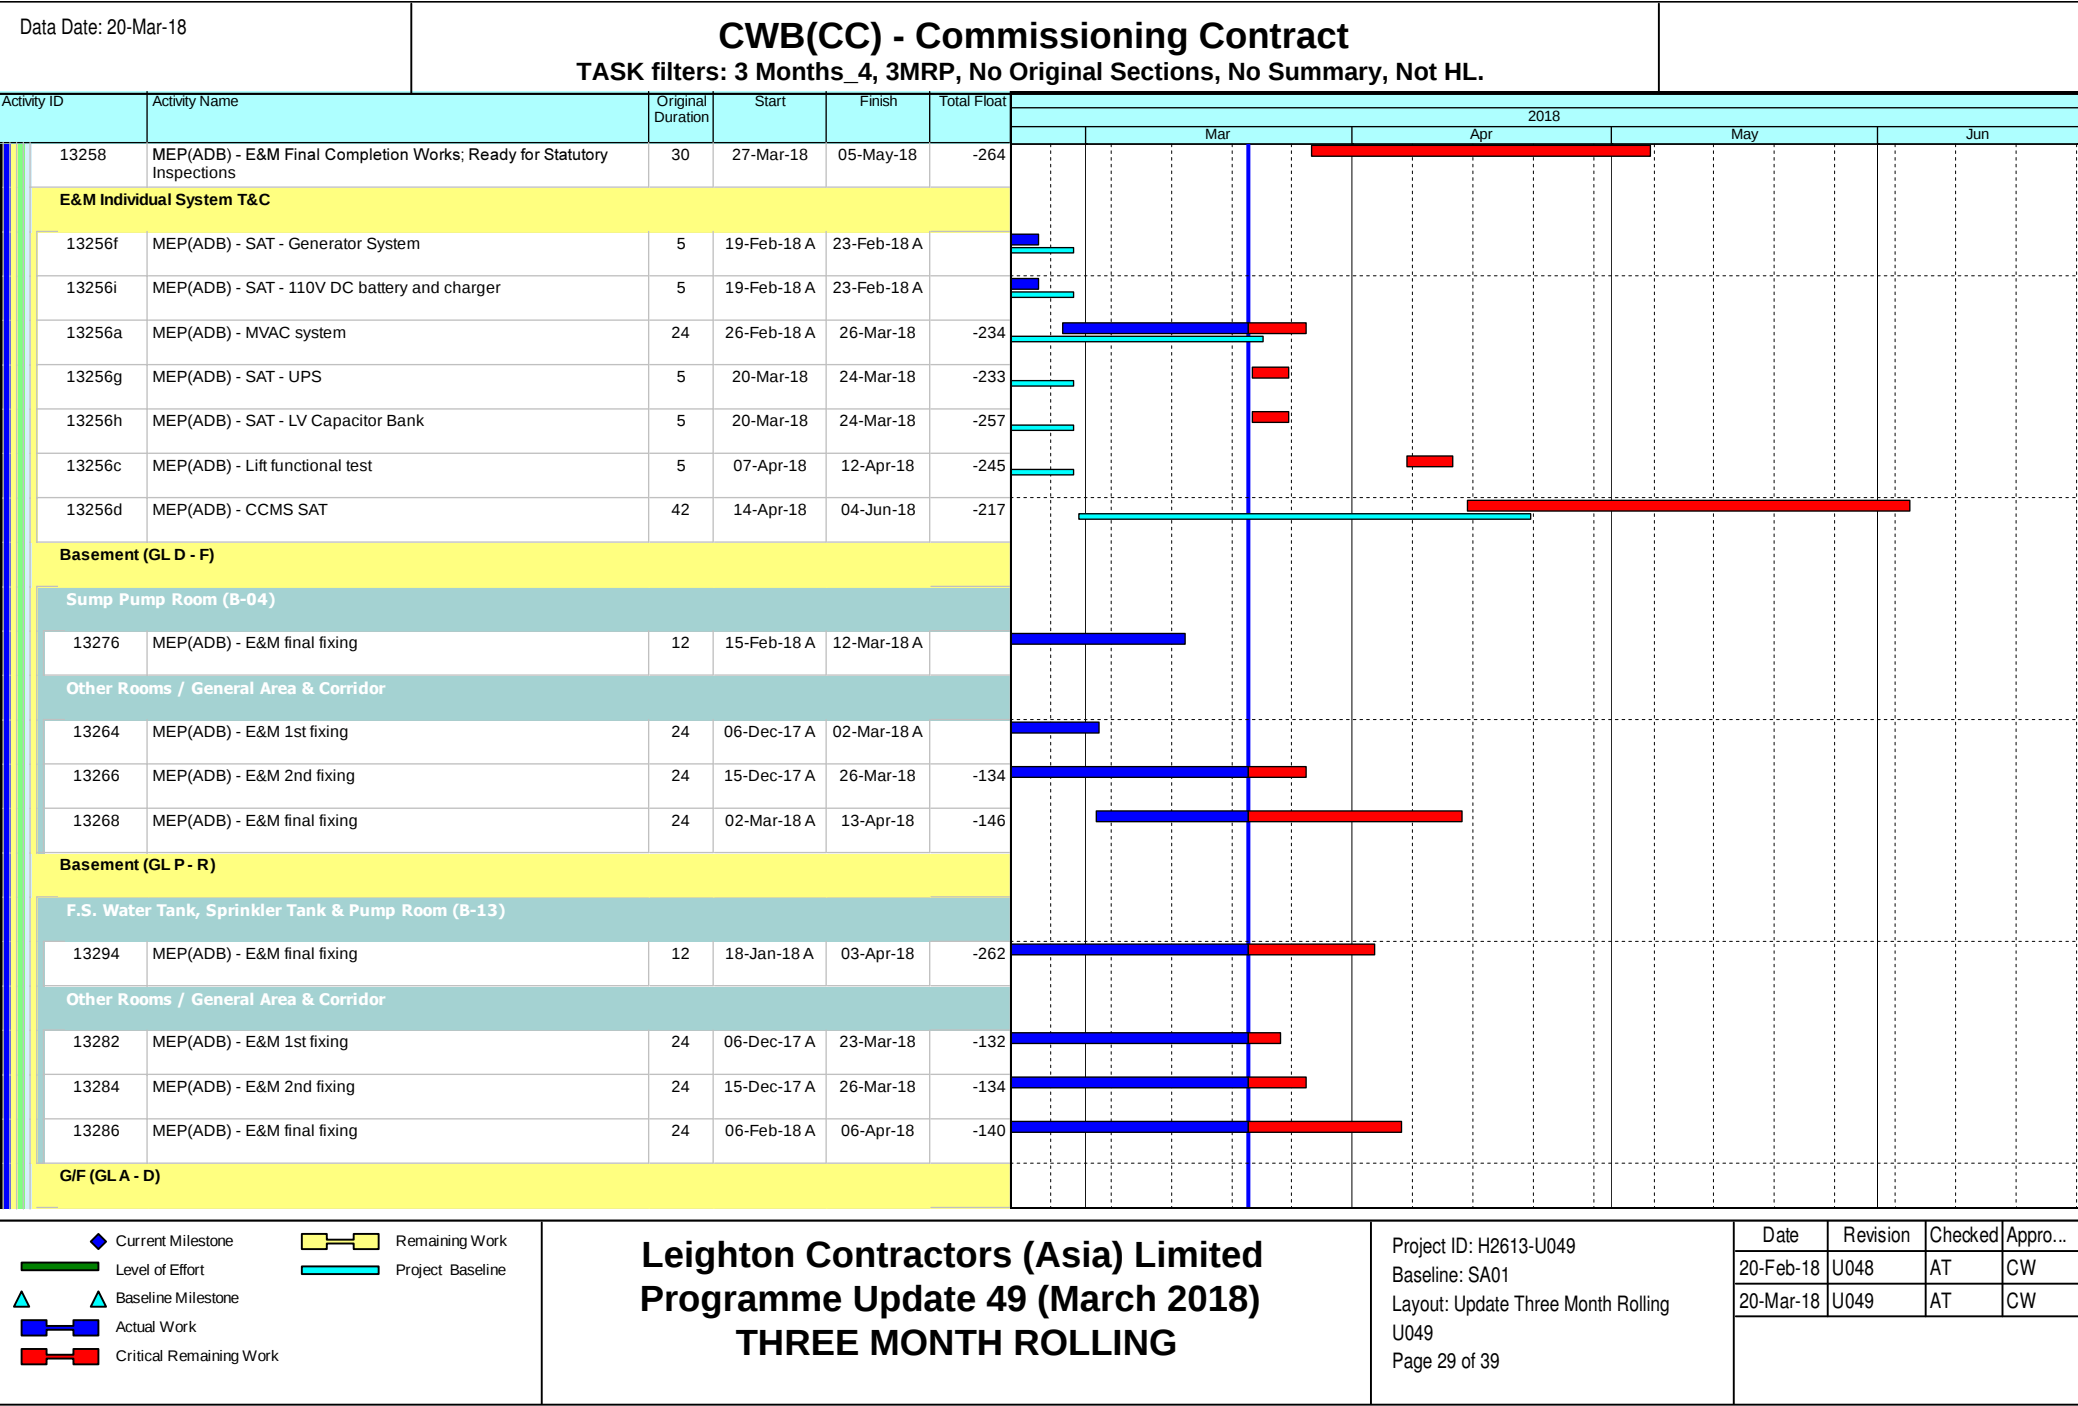


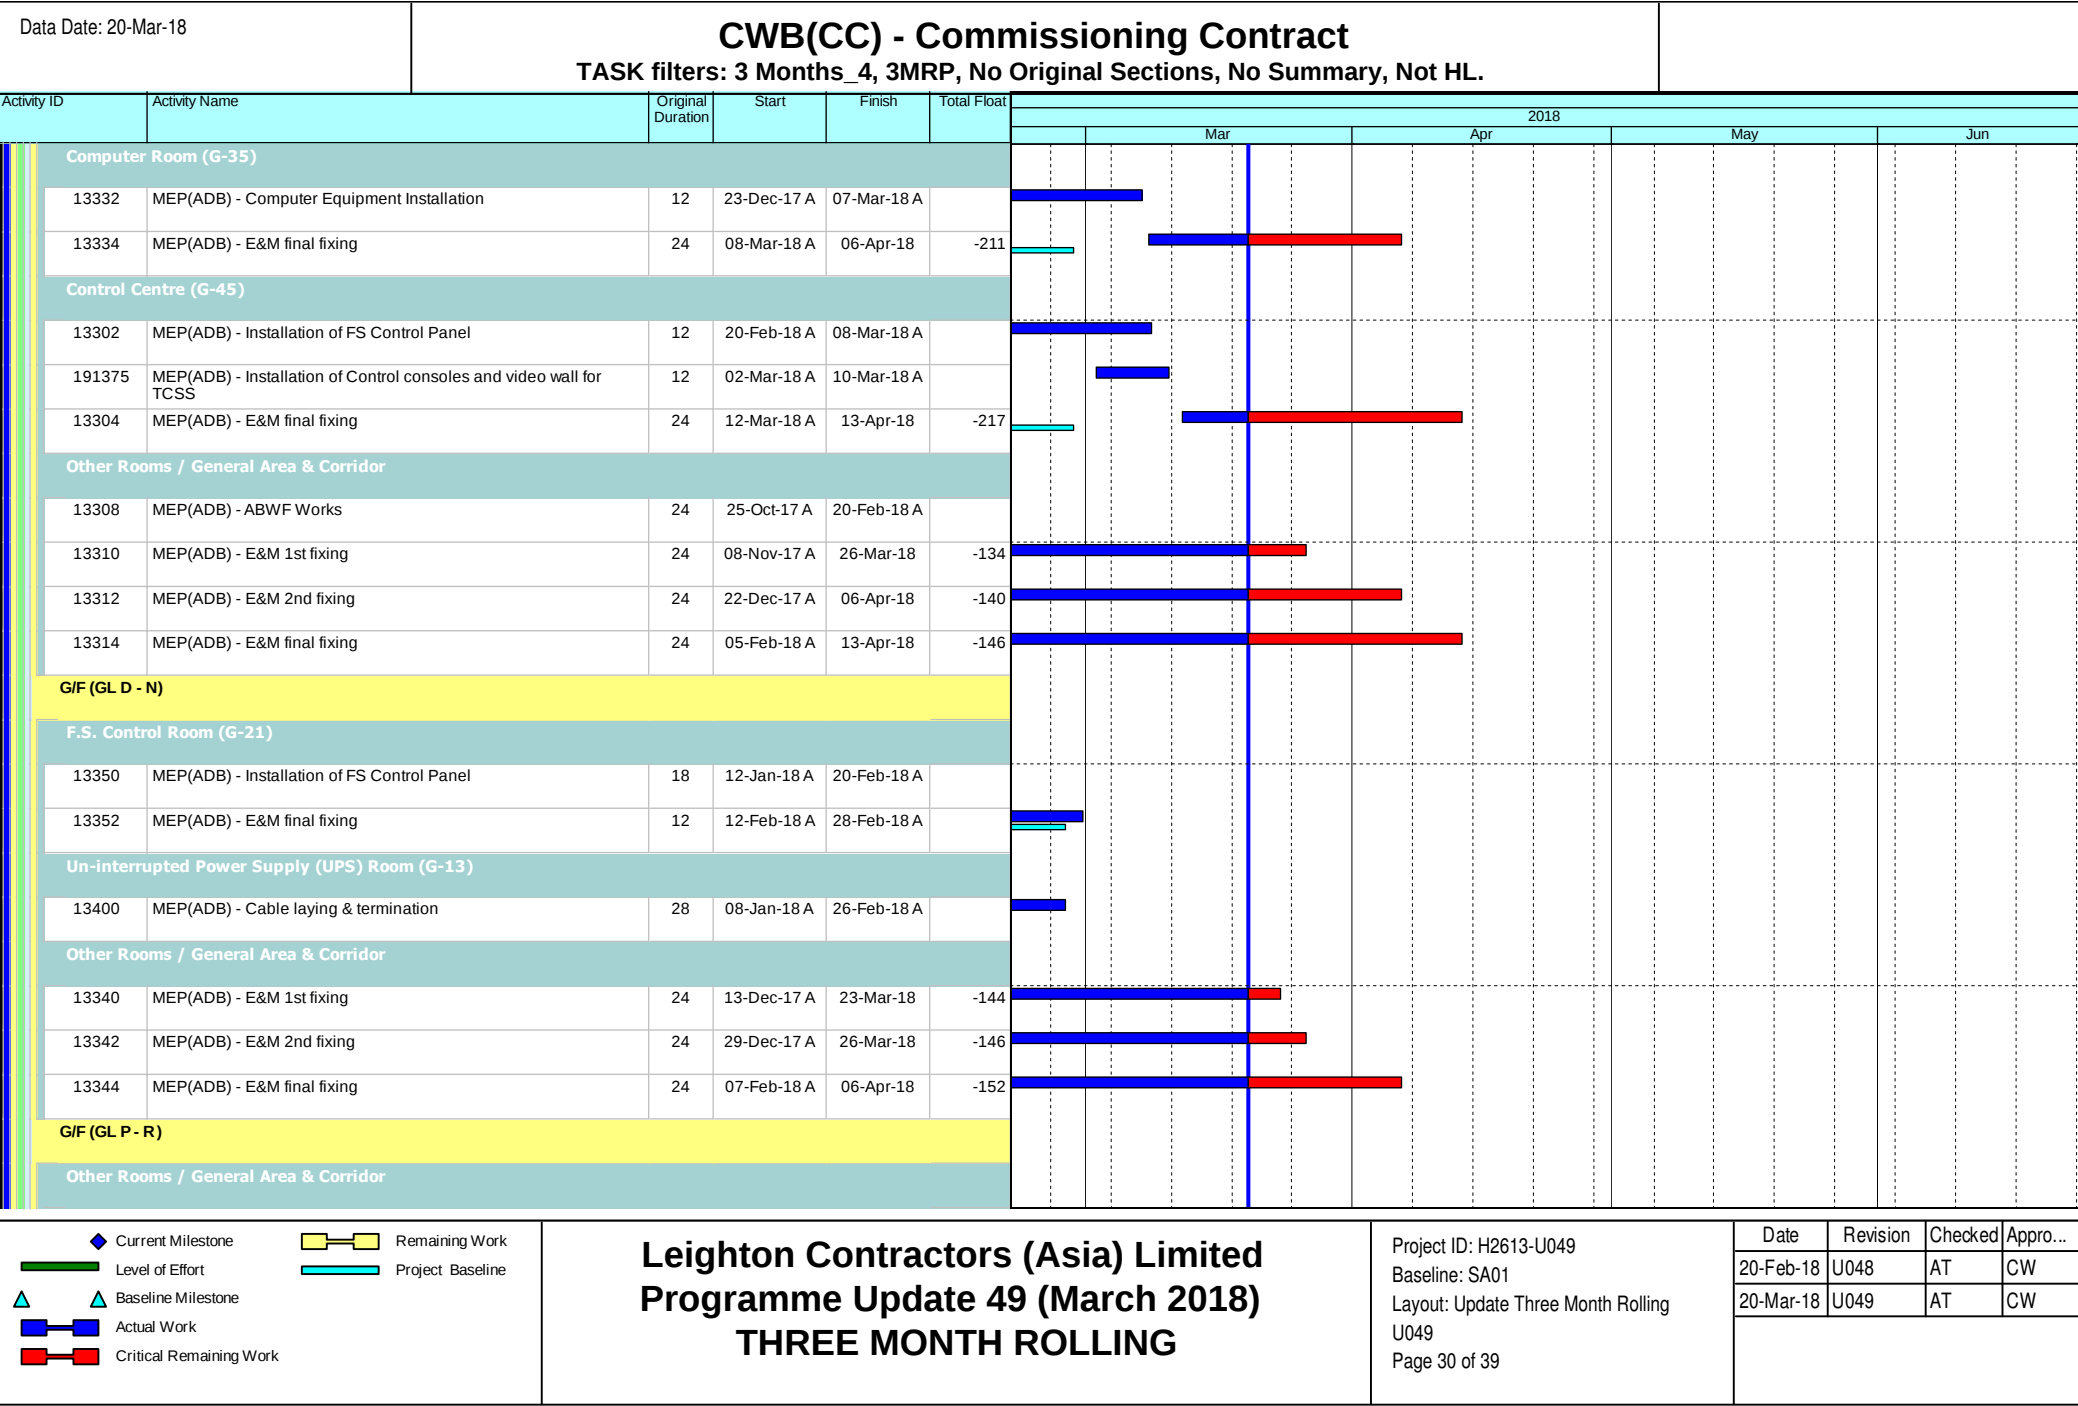

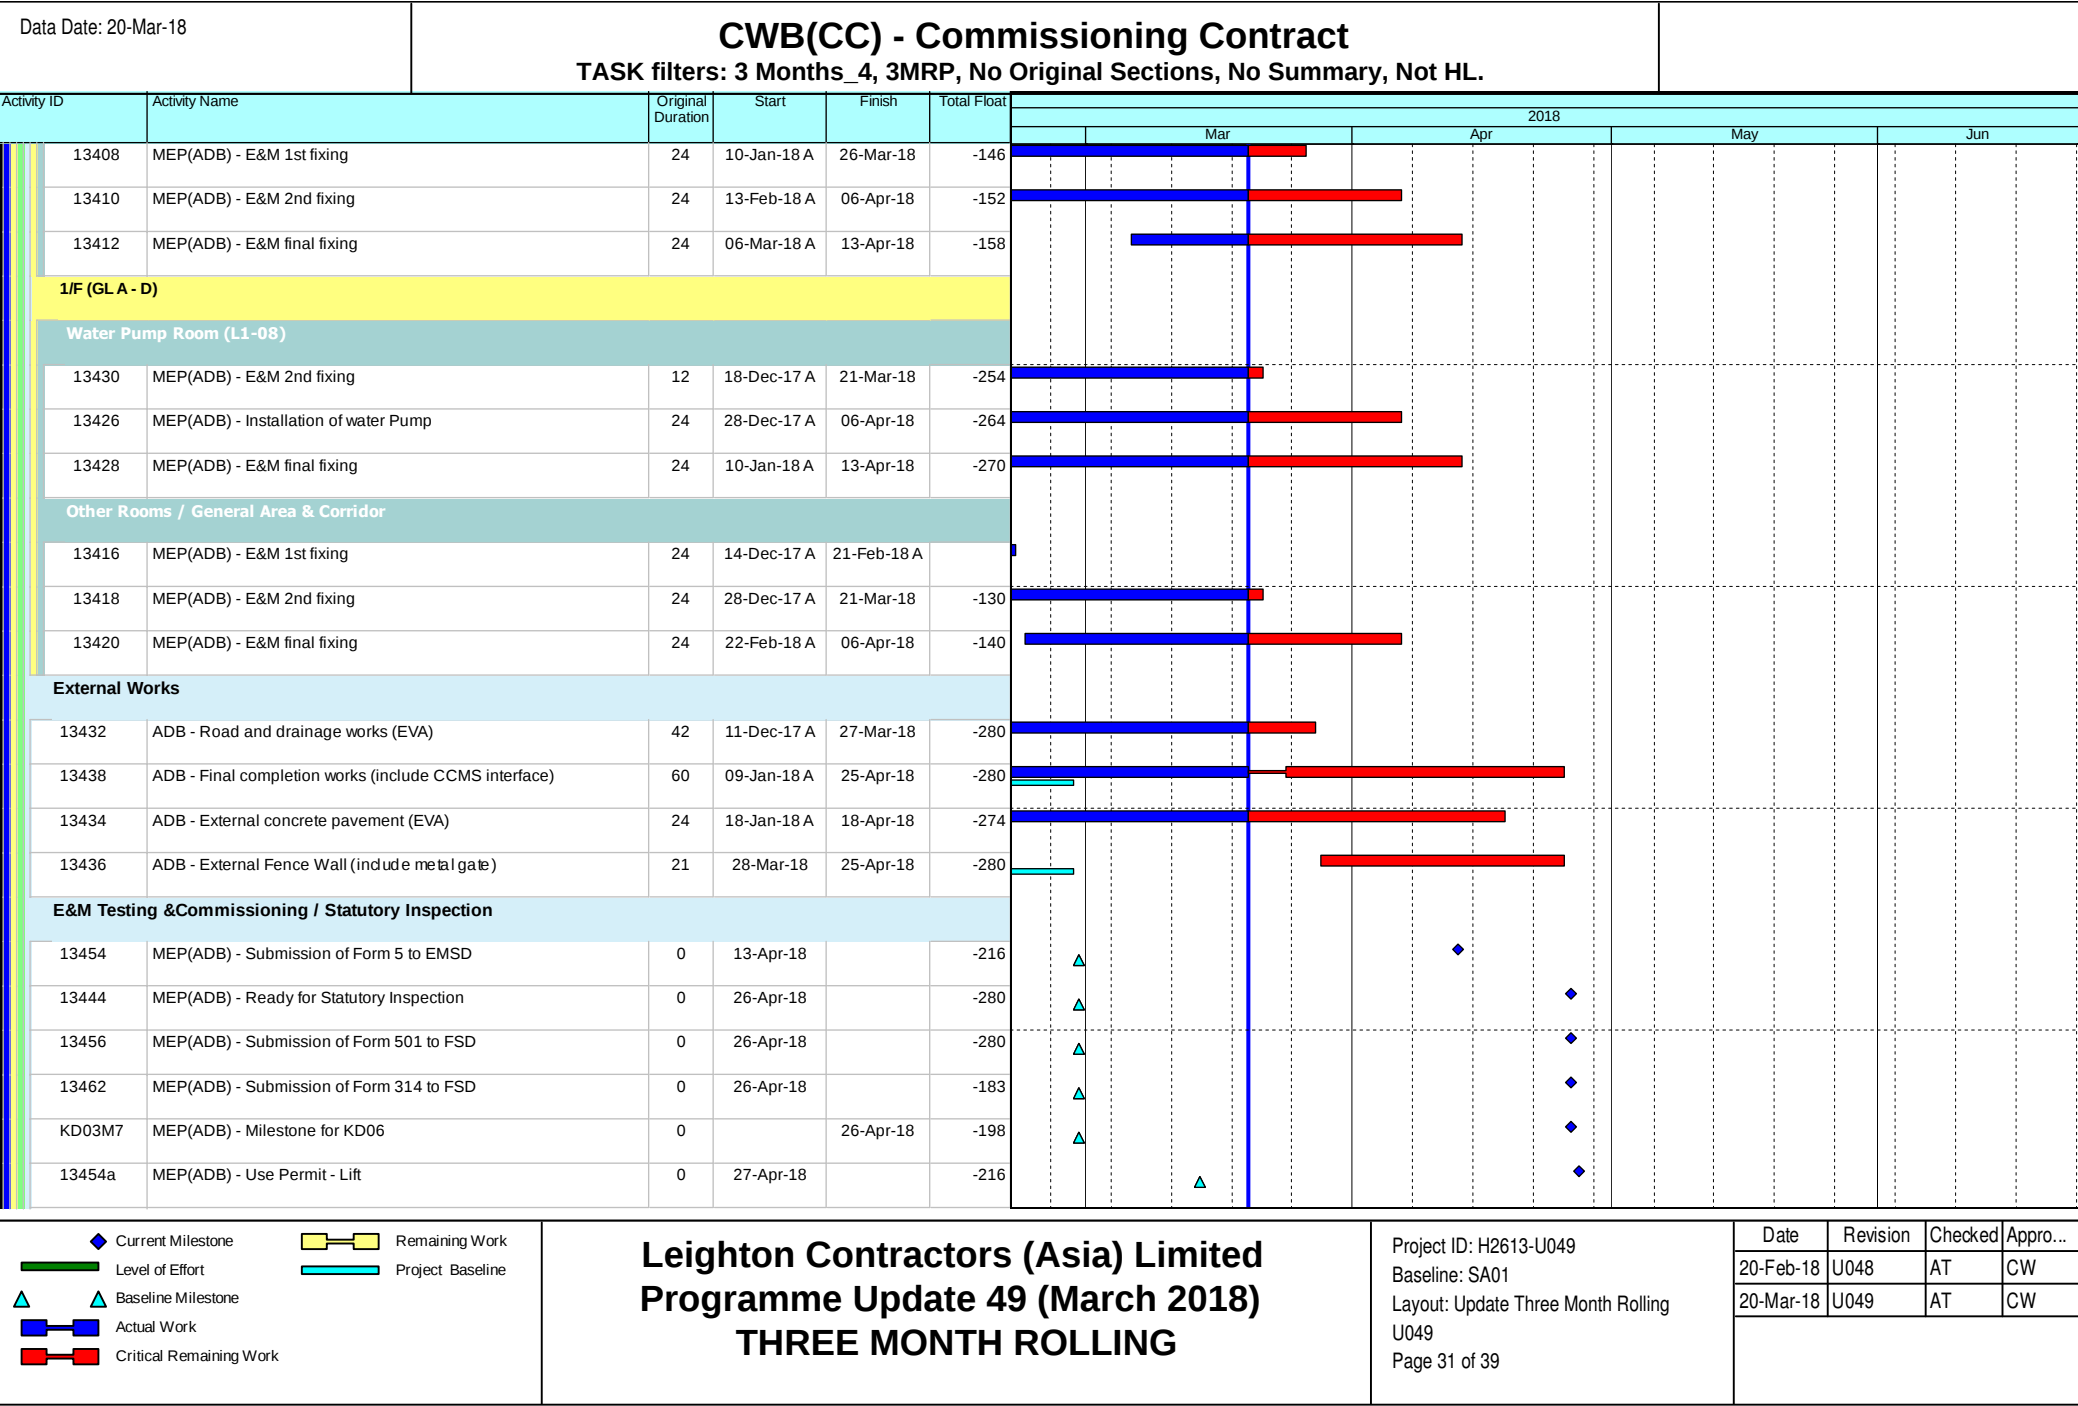

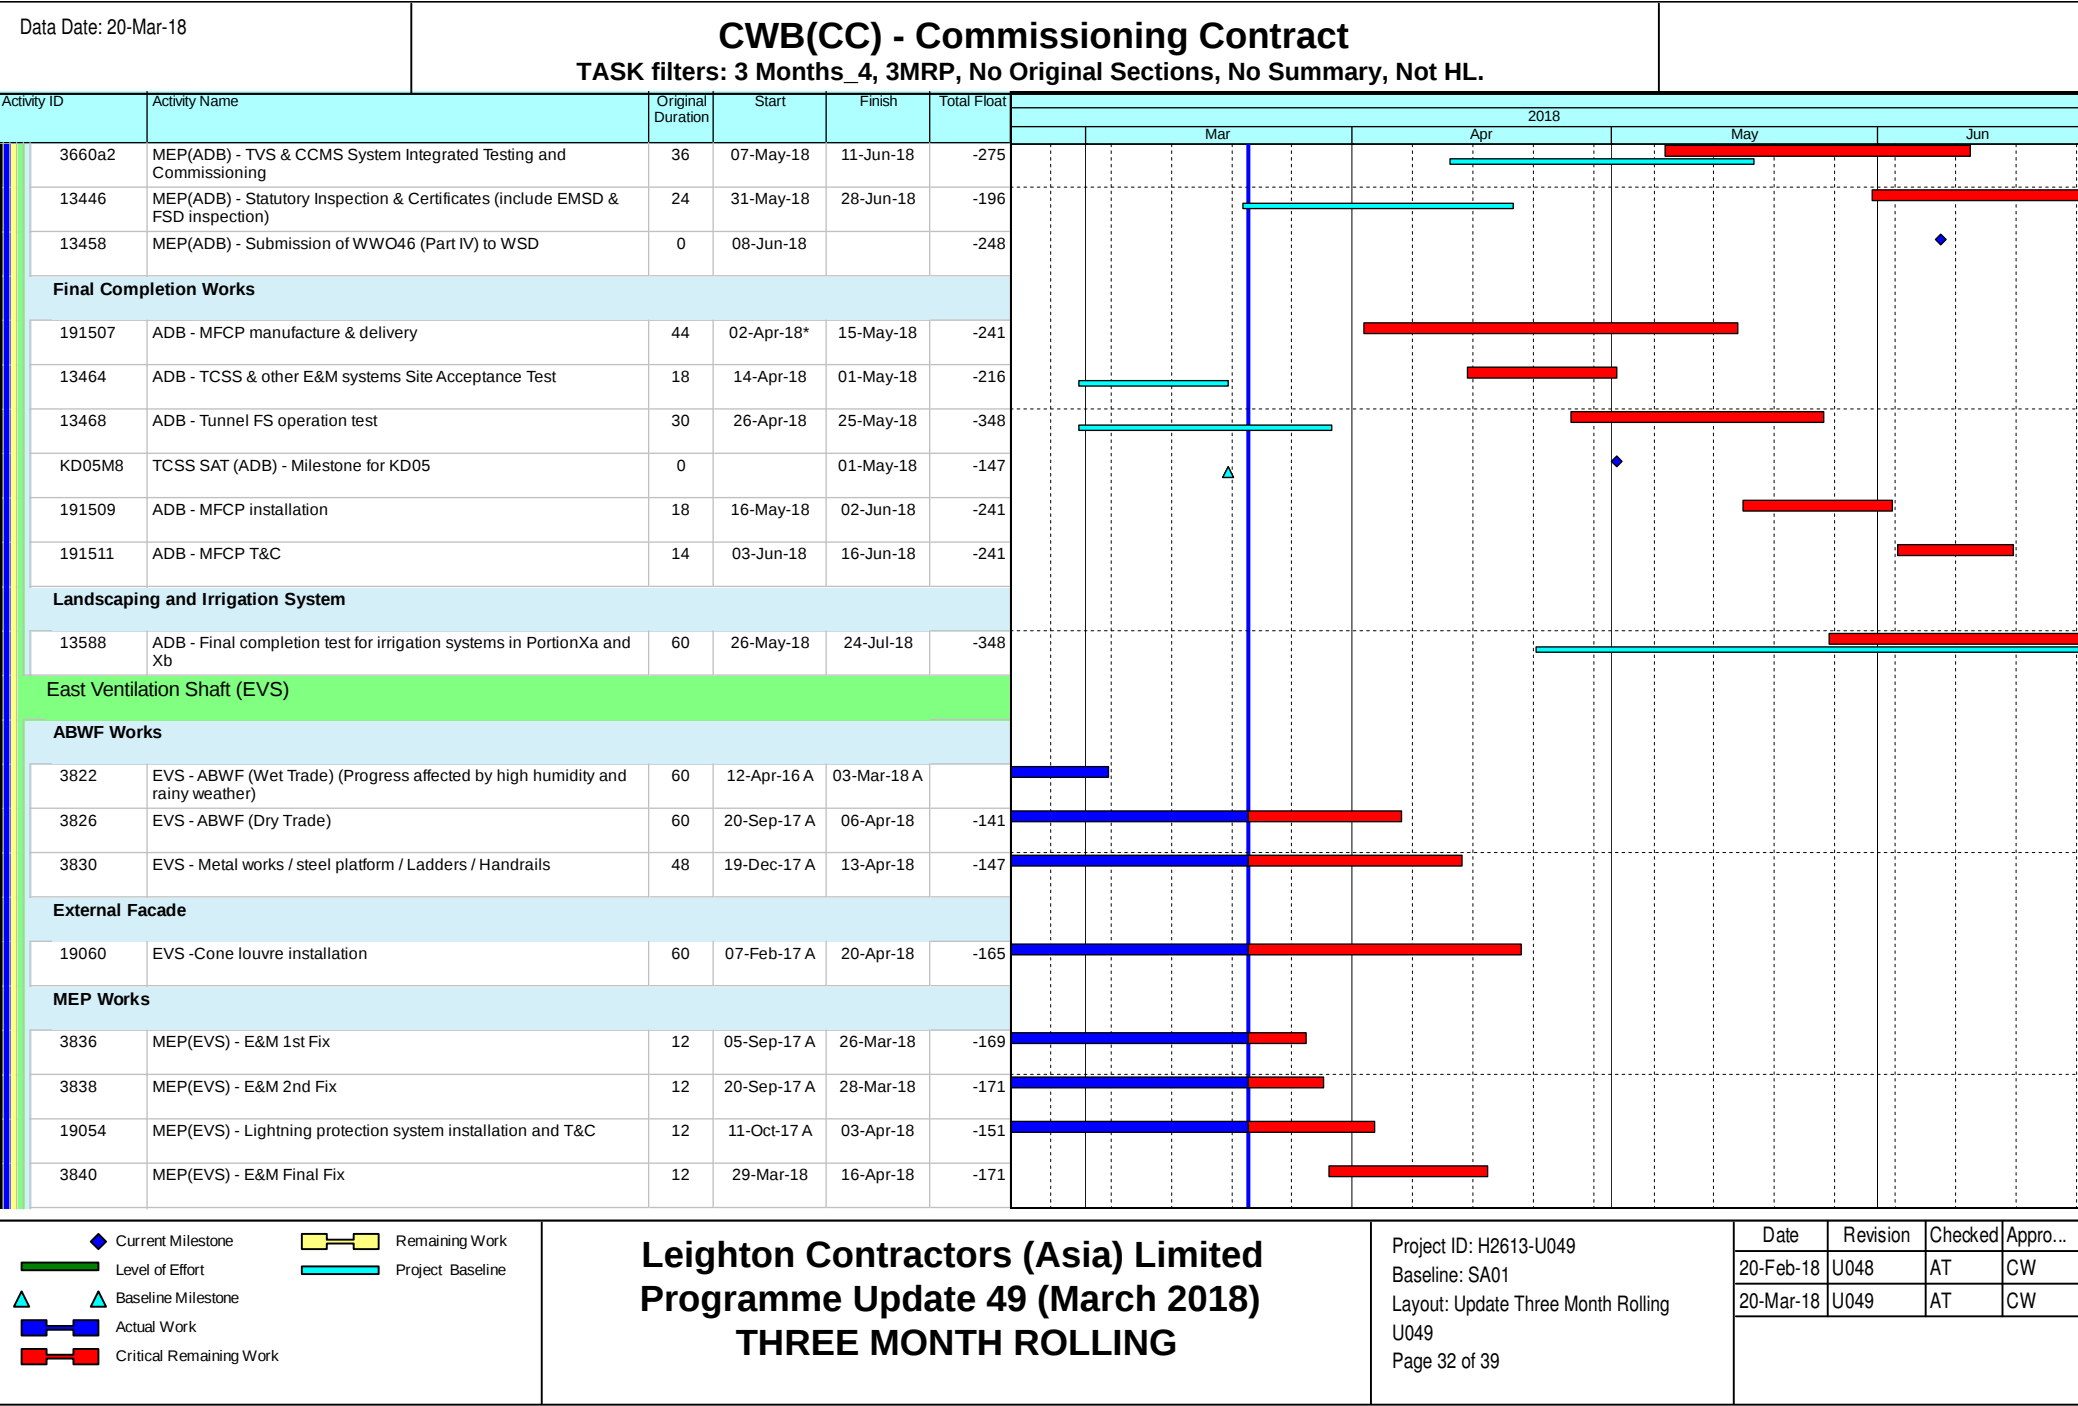


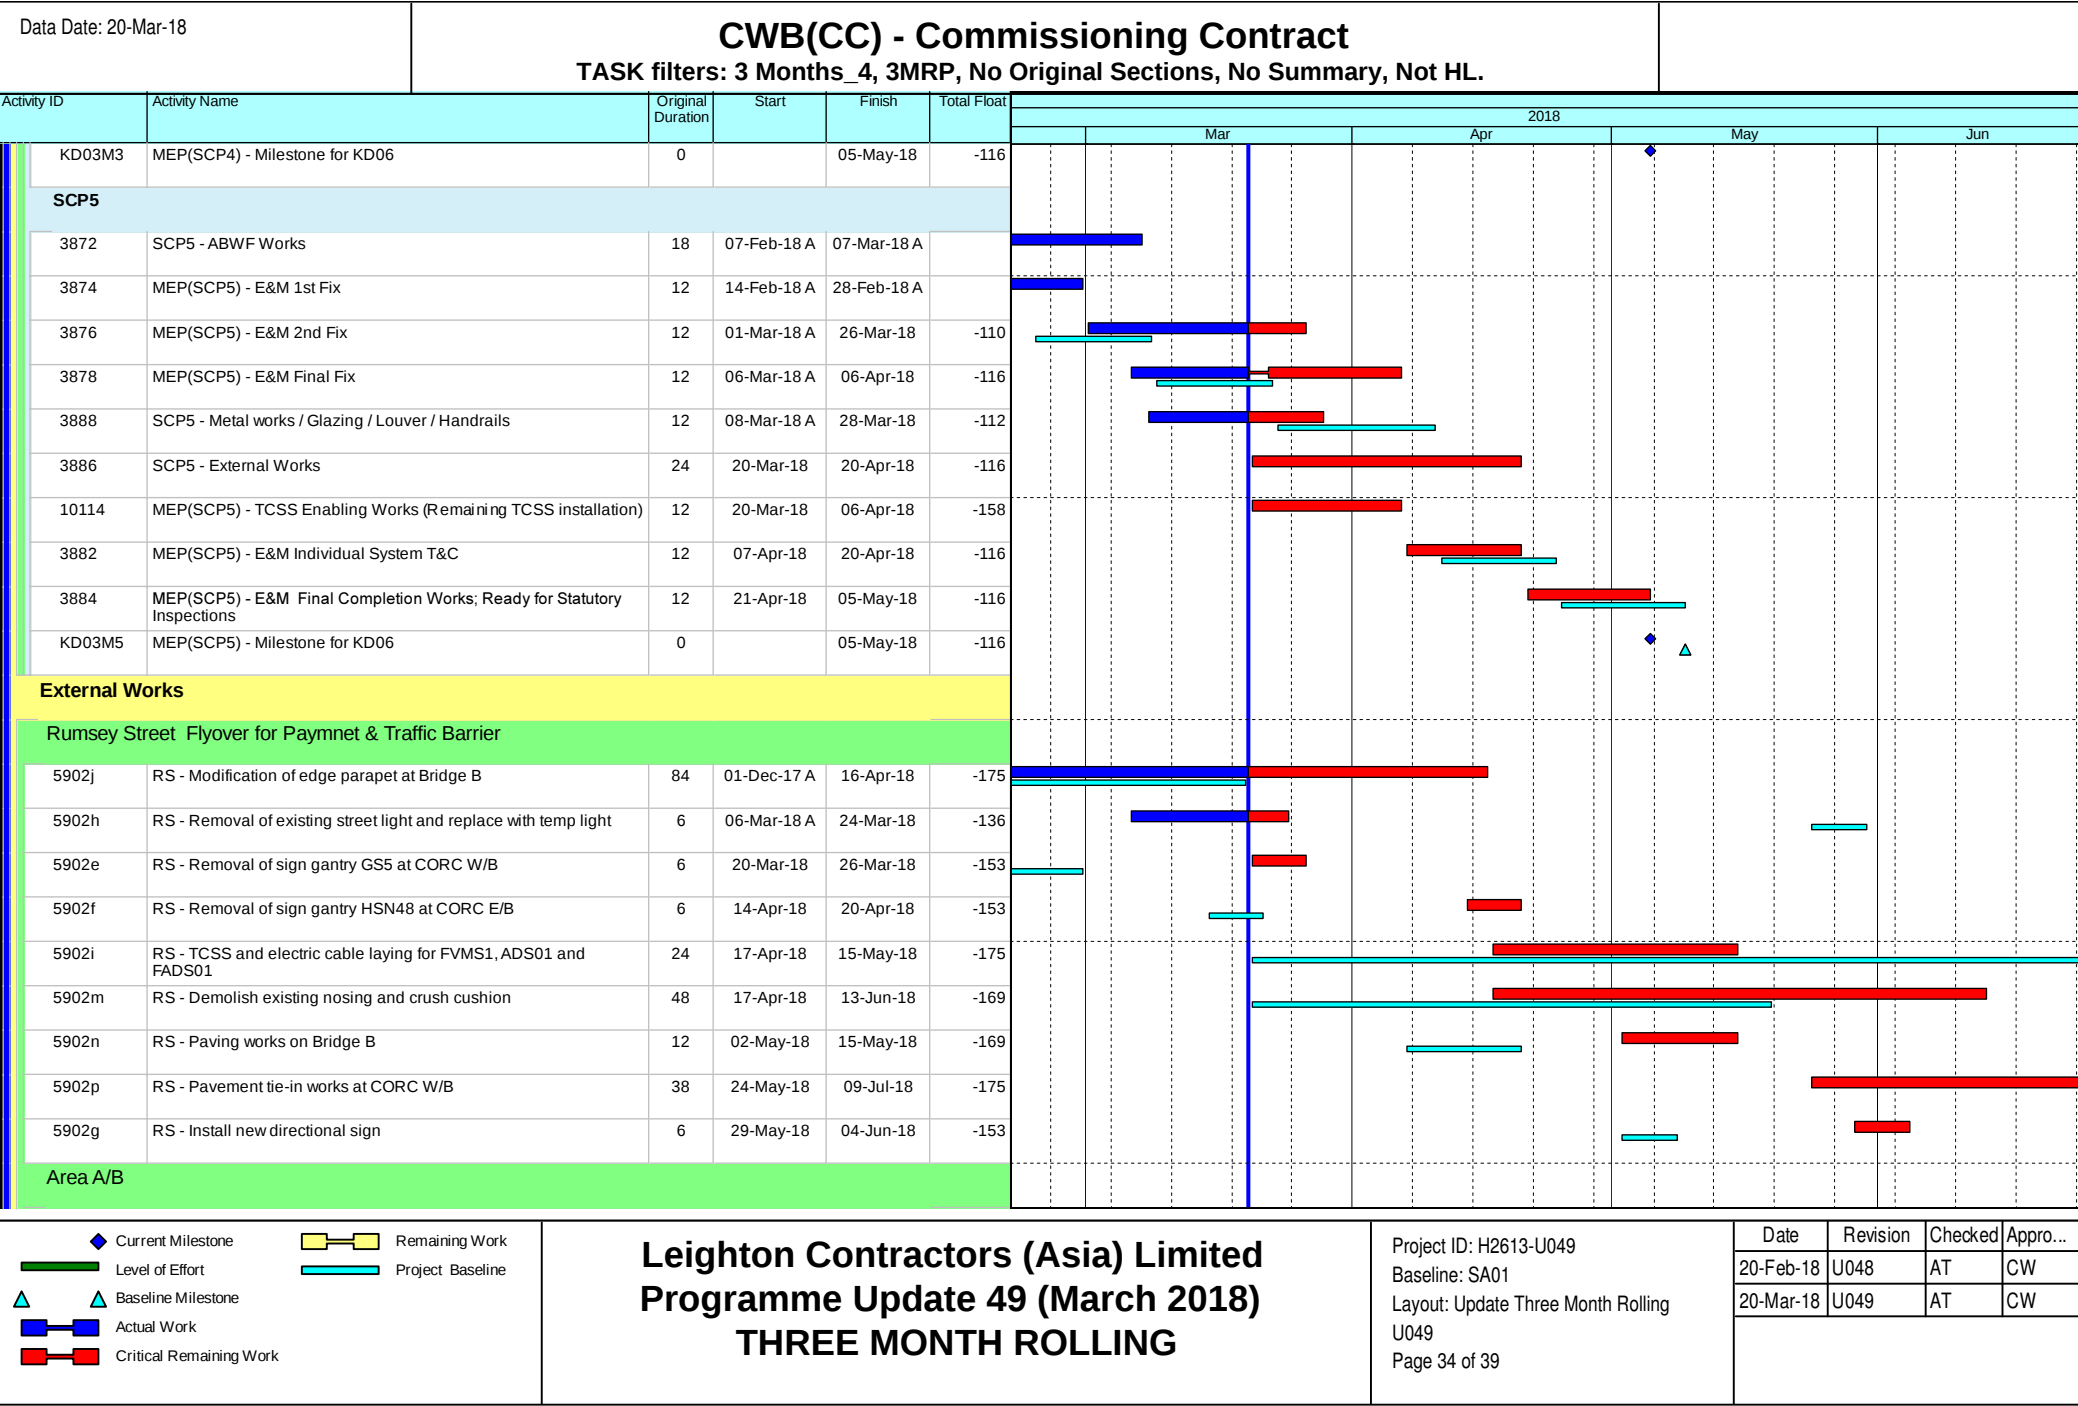


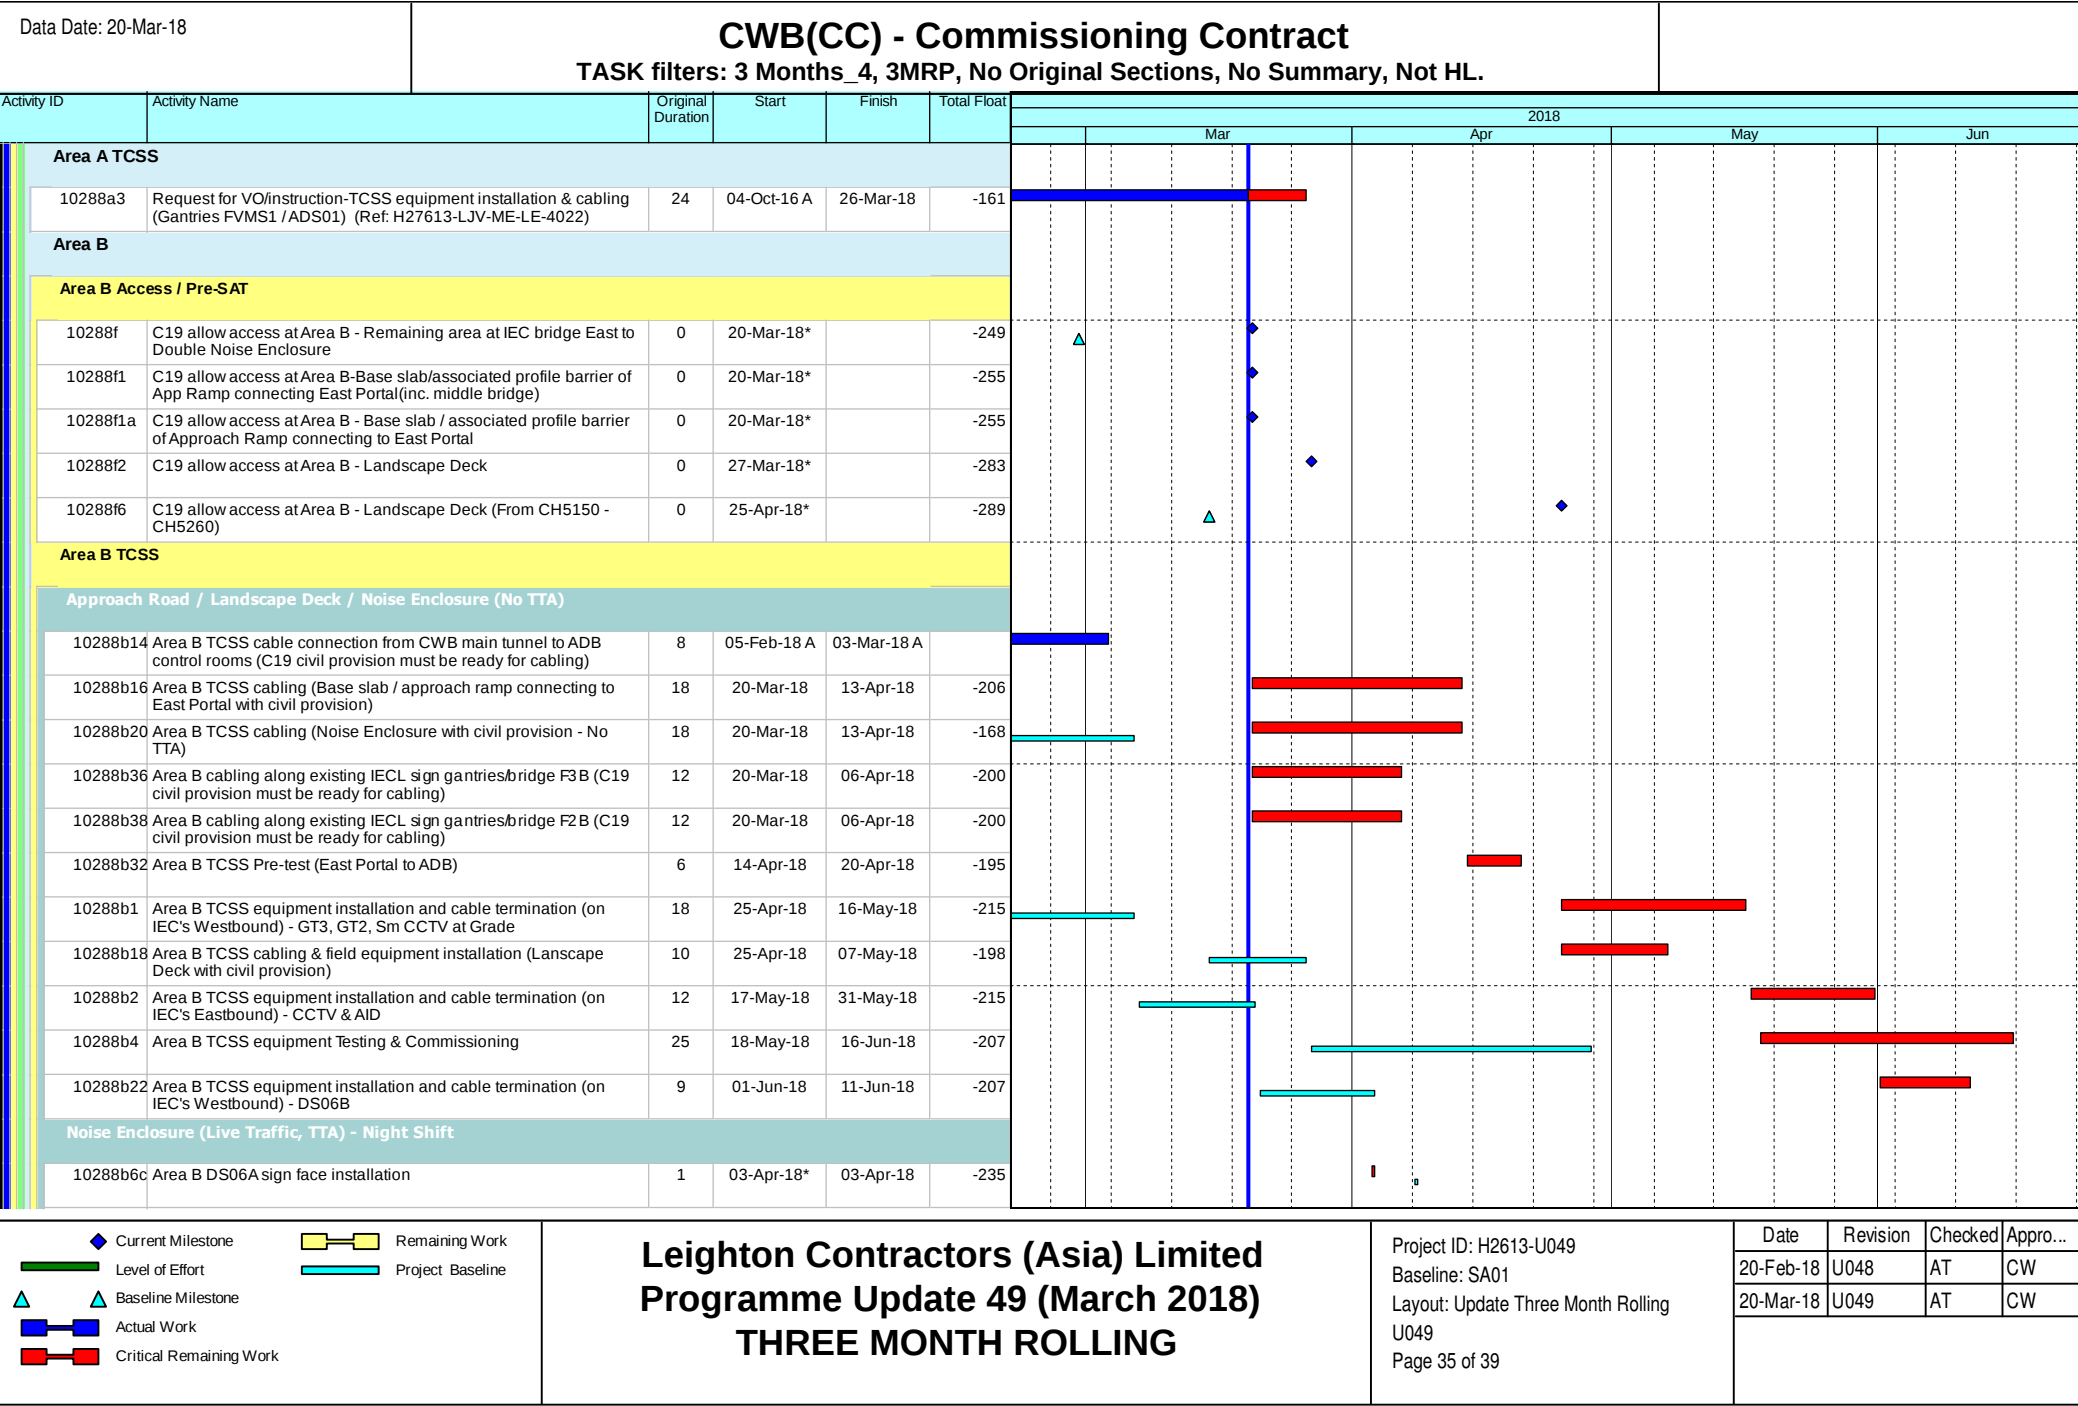

Data Date: 20-Mar-18

CWB(CC) - Commissioning Contract


TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

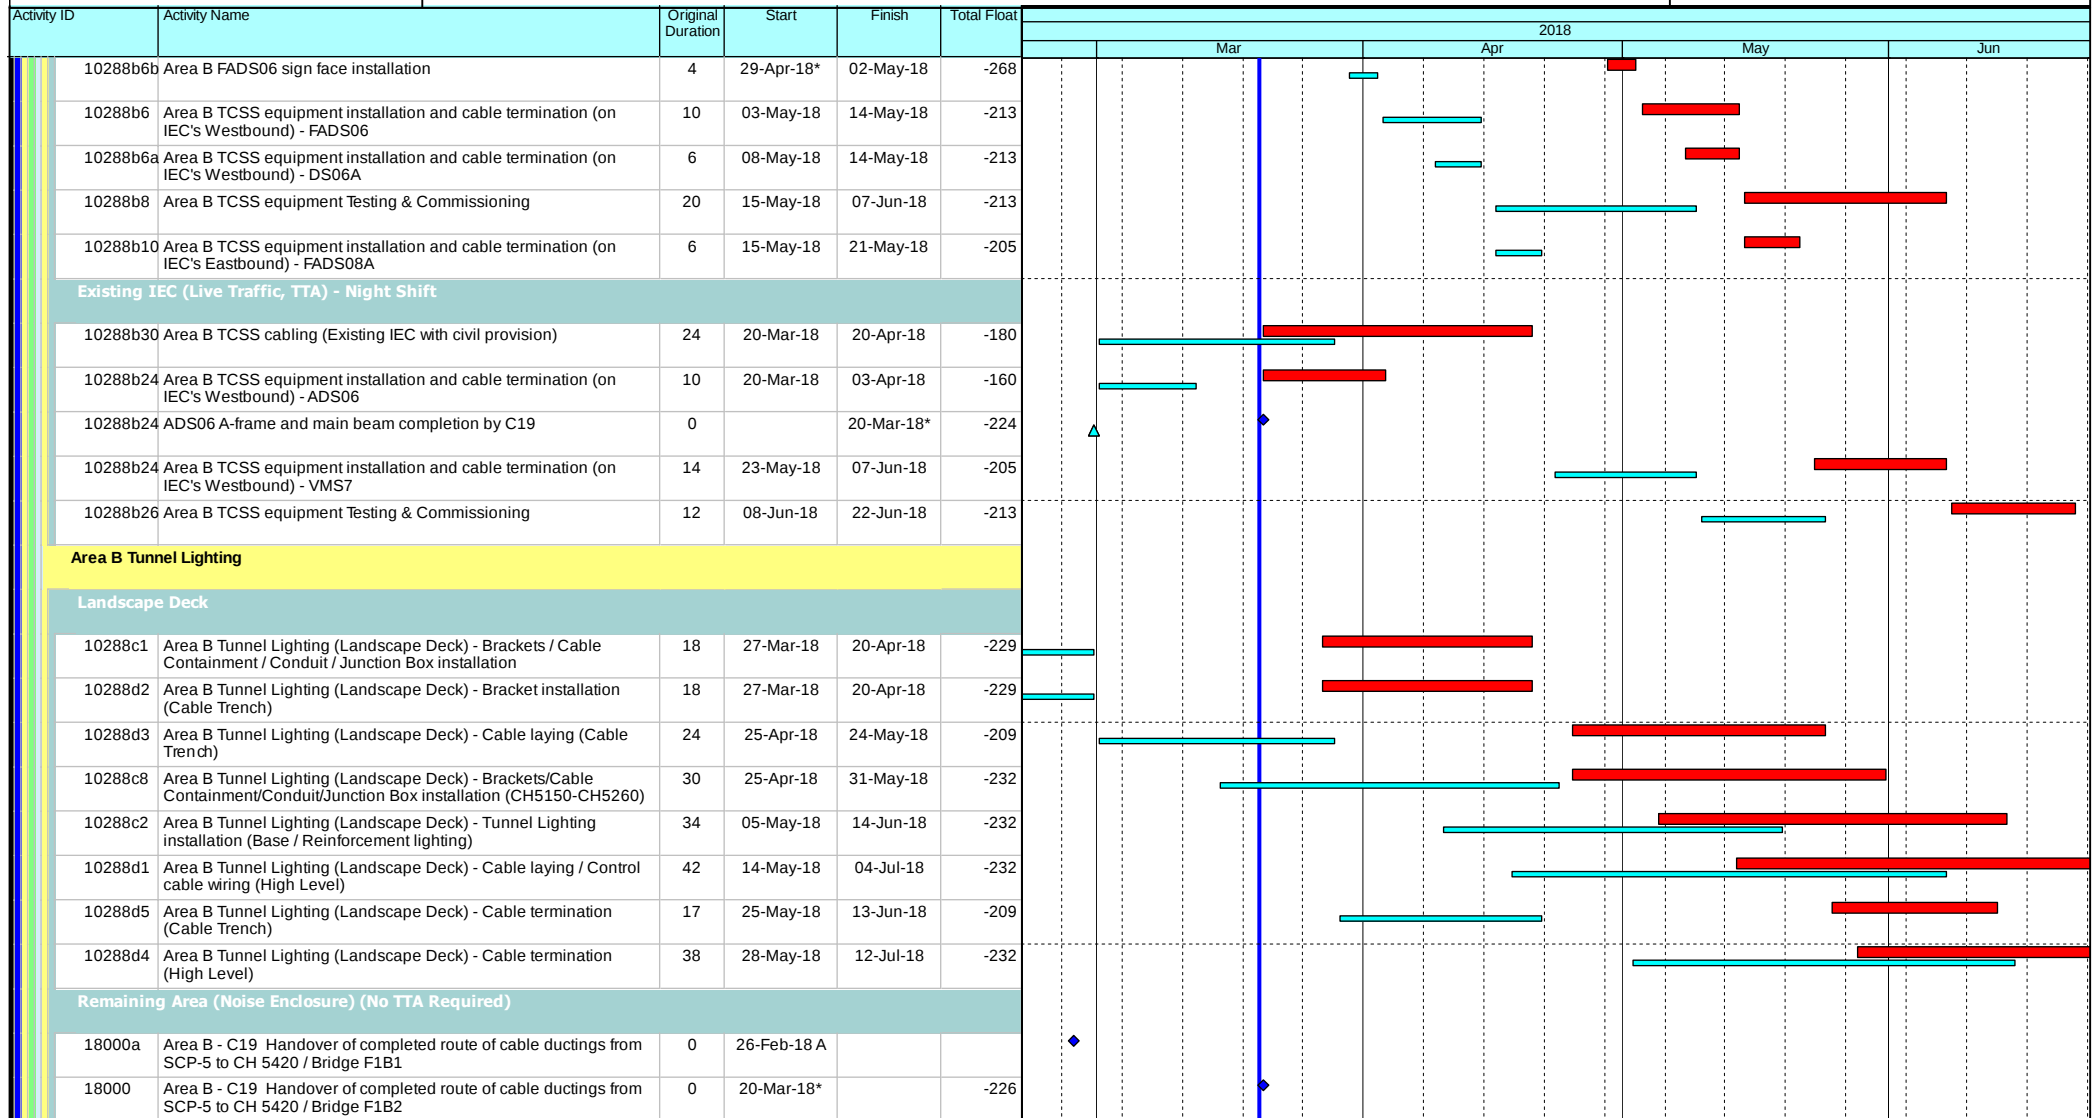

Leighton Contractors (Asia) Limited Programme Update 49 (March 2018) THREE MONTH ROLLING

Project ID: H2613-U049
 Baseline: SA01
 Layout: Update Three Month Rolling
 U049
 Page 36 of 39

Date	Revision	Checked	Appro...
20-Feb-18	U048	AT	CW
20-Mar-18	U049	AT	CW

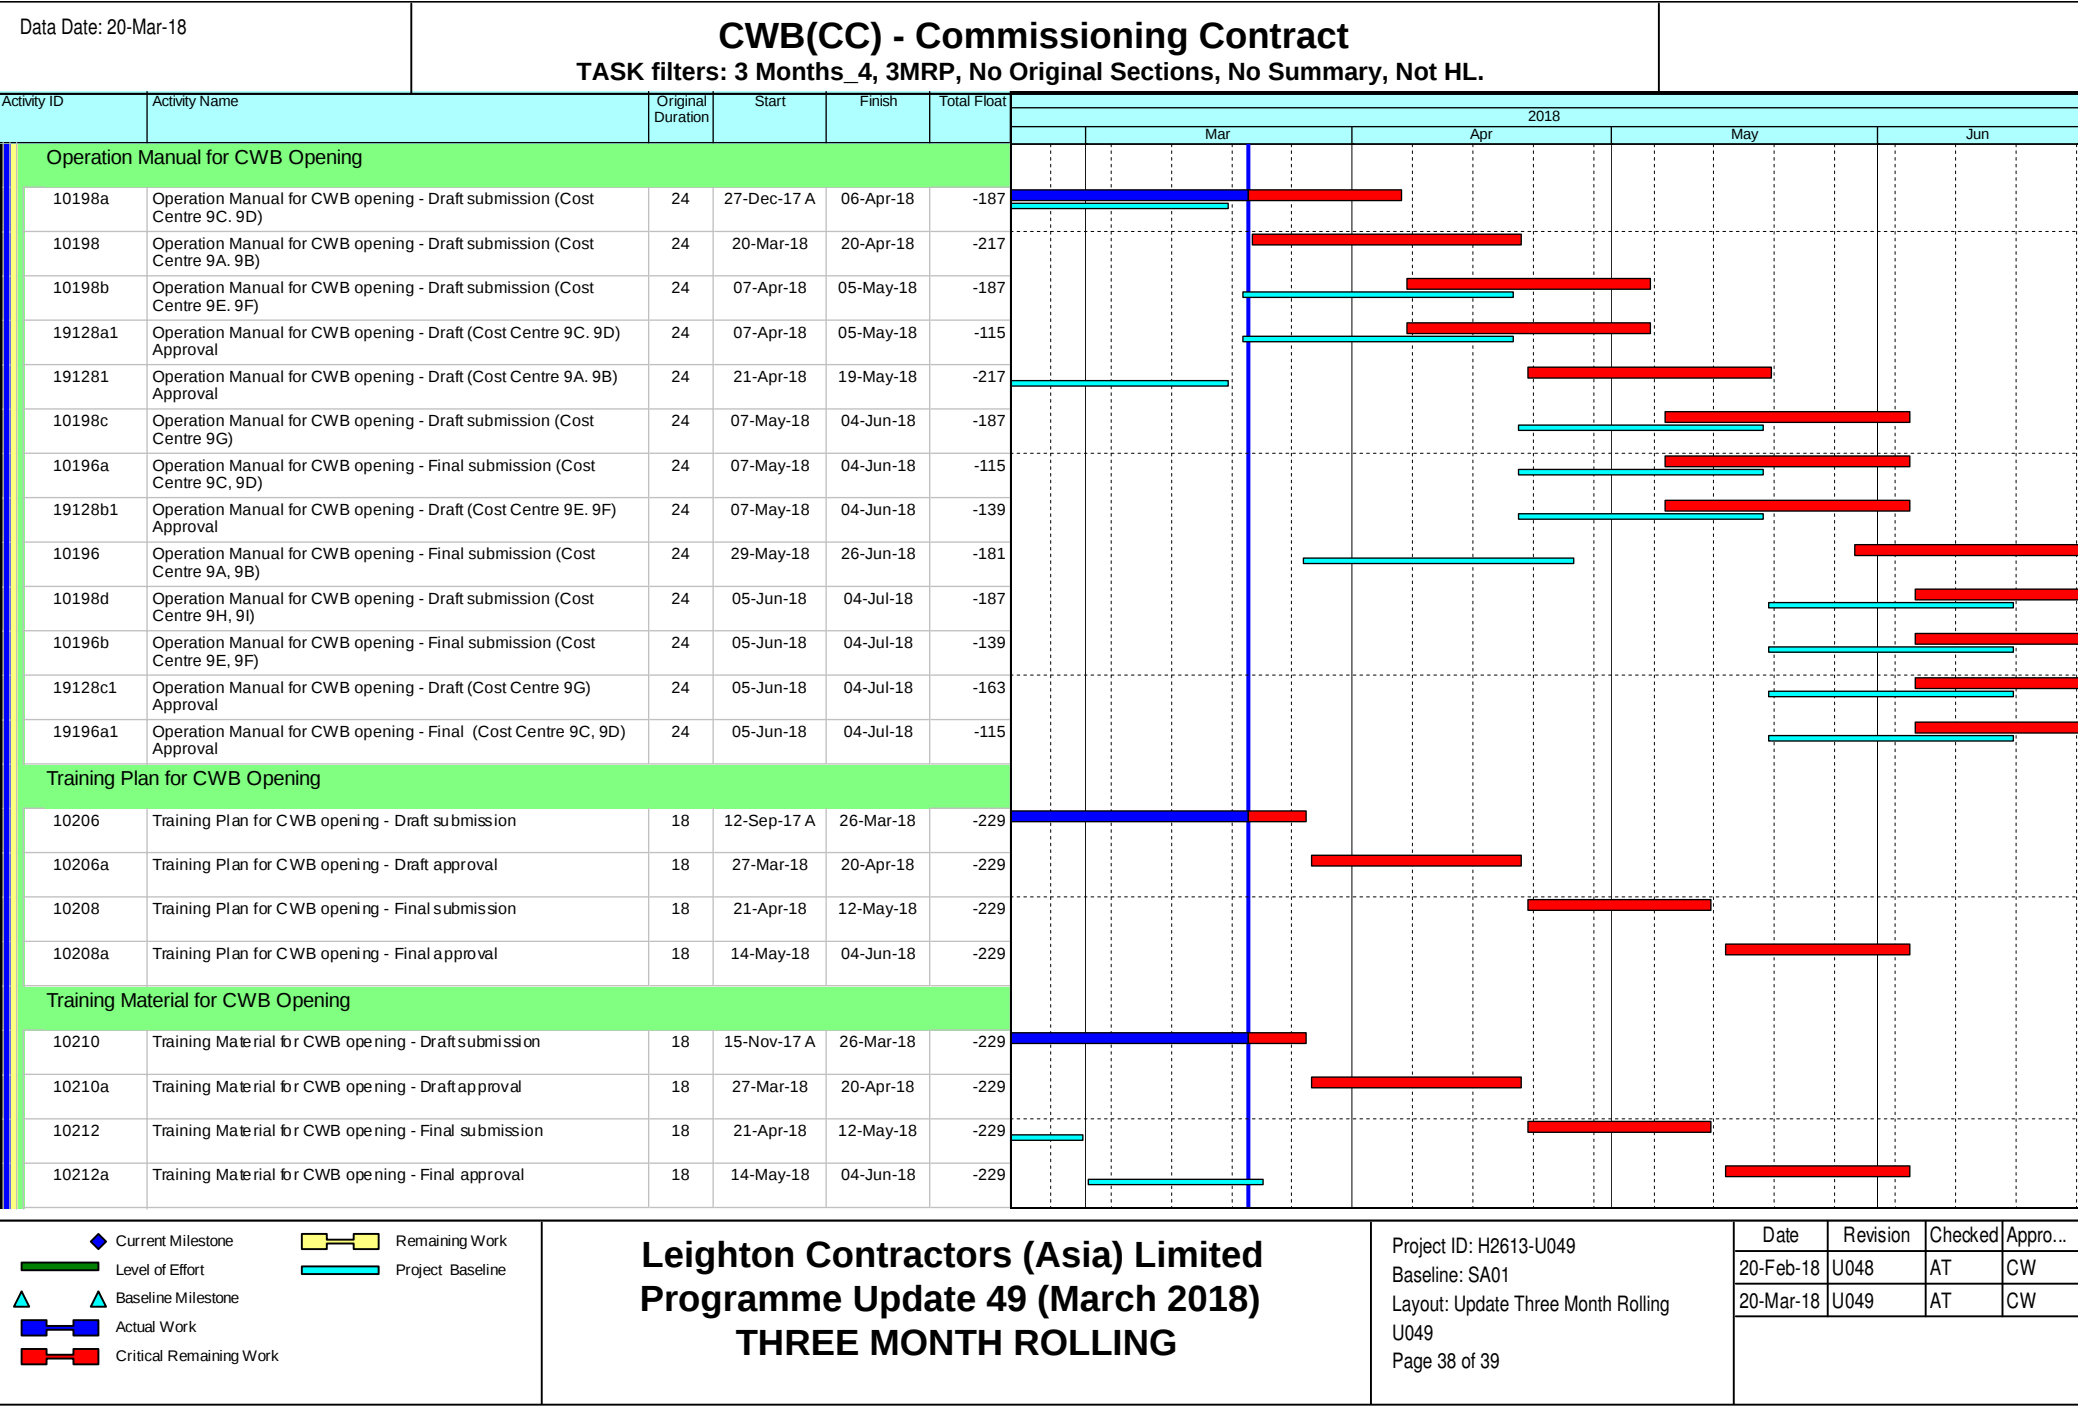

Data Date: 20-Mar-18

CWB(CC) - Commissioning Contract
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

CWB(CC) - Commissioning Contract
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Maintenance Manual / Plan					
10200	Maintenance Plan	18	14-May-18	04-Jun-18	-199
10220	Maintenance Manual / logbook - Draft submission	18	05-Jun-18	26-Jun-18	-199

 Current Milestone  Remaining Work  Level of Effort  Project Baseline  Baseline Milestone  Actual Work  Critical Remaining Work	Leighton Contractors (Asia) Limited Programme Update 49 (March 2018) THREE MONTH ROLLING	Project ID: H2613-U049 Baseline: SA01 Layout: Update Three Month Rolling U049 Page 39 of 39	<table> <tr> <th>Date</th><th>Revision</th><th>Checked</th><th>Appro...</th></tr> <tr> <td>20-Feb-18</td><td>U048</td><td>AT</td><td>CW</td></tr> <tr> <td>20-Mar-18</td><td>U049</td><td>AT</td><td>CW</td></tr> </table>	Date	Revision	Checked	Appro...	20-Feb-18	U048	AT	CW	20-Mar-18	U049	AT	CW
Date	Revision	Checked	Appro...												
20-Feb-18	U048	AT	CW												
20-Mar-18	U049	AT	CW												
