



Lam Geotechnics Limited

Contract No. HK/2011/07
Wan Chai Development Phase II and Central Wanchai Bypass
- Sampling, Field Measurement and Testing Works (Stage 2)
Monthly EM&A Report (July 2013)

CONTRACT NO: HK/2011/07

WANCHAI DEVELOPMENT PHASE II AND CENTRAL
WANCHAI BYPASS
SAMPLING, FIELD MEASUREMENT AND TESTING WORK
(STAGE 2)

ENVIRONMENTAL PERMIT NO. EP-364/2009/B,
FURTHER ENVIRONMENTAL PERMIT NOS. FEP-01/364/2009,
FEP-02/364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A, FEP-
07/364/2009/A, FEP-08/364/2009/A, FEP-09/364/2009/B AND
FEP-10/364/2009/B

MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT

- JULY 2013 -

CLIENTS:

Civil Engineering and Development
Department

and

Highways Department

PREPARED BY:

Lam Geotechnics Limited

11/F Centre Point
181-185 Gloucester Road,
Wanchai, H.K.

Telephone: (852) 2882-3939
Facsimile: (852) 2882-3331
E-mail: info@lamenviro.com
Website: <http://www.lamenviro.com>

CERTIFIED BY:

Raymond Dai
Environmental Team Leader

DATE:

13 August 2013

Ref.: AACWBIECEM00_0_4241L.13

14 August 2013

By Post and Fax (2691 2649)

AECOM Asia Company Limited
11/F, Tower 2
Grand Central Plaza
138 Shatin Rural Committee Road
Shatin, New Territories
Hong Kong

Attention: Mr. Conrad Ng

Dear Sir,

**Re: Wan Chai Development Phase II and Central-Wan Chai Bypass
Monthly Environmental Monitoring and Audit Report (July 2013) for EP-364/2009/B,
FEP-01/364/2009, FEP-02/364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A,
FEP-07/364/2009/A, FEP-08/364/2009/A, FEP-09/364/2009/B & FEP-10/364/2009/B**

Reference is made to the Environmental Team's submission of the captioned Monthly Environmental Monitoring and Audit (EM&A) Report for July 2013 received by email on 13 August 2013.

Please be informed that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 in the captioned Environmental Permits.

Thank you very much for your kind attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,



David Yeung
Independent Environmental Checker

c.c.	HyD	Mr. Jones Lai	by fax: 2714 5289
	CEDD	Mr. Robert Tsoi	by fax: 2577 5040
	AECOM	Mr. Francis Leong / Mr. Stephen Lai	by fax: 2691 2649
	Lam	Mr. Raymond Dai	by fax: 2882 3331

Q:\Projects\AACWBIECEM00\Corr\AACWBIECEM00_0_4241L.13.doc

TABLE OF CONTENTS

EXECUTIVE SUMMARY	4
1. INTRODUCTION	9
1.1 Scope of the Report	10
1.2 Structure of the Report	10
2. PROJECT BACKGROUND	12
2.1 Background	12
2.2 Scope of the Project and Site Description	12
2.3 Division of the Project Responsibility	13
2.4 Project Organization and Contact Personnel	14
3. STATUS OF REGULATORY COMPLIANCE	20
3.1 Status of Environmental Licensing and Permitting under the Project	21
4. MONITORING REQUIREMENTS	34
4.1 Noise Monitoring	36
4.2 Air Monitoring	38
5. MONITORING RESULTS	40
5.1 Noise Monitoring Results	40
5.2 Real Time Noise Monitoring Results	43
5.3 Air Monitoring Results	44
5.4 Waste Monitoring Results	46
6. COMPLIANCE AUDIT	51
6.1 Noise Monitoring	51
6.2 Real Time Noise Monitoring	51
6.3 Air Monitoring	52
6.4 Review of the Reasons for and the Implications of Non-compliance	52
6.5 Summary of action taken in the event of and follow-up on non-compliance	53
7. CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS	53
8. ENVIRONMENTAL SITE AUDIT	55
9. COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION	47
10. CONCLUSION	59

LIST OF TABLES

Table 2.1	<i>Schedule 2 Designated Projects under this Project</i>
Table 2.2	<i>Details of Individual Contracts under the Project</i>
Table 2.3	<i>Contact Details of Key Personnel</i>
Table 3.1	<i>Summary of the current status on licences and/or permits on environmental protection pertinent to the Project</i>
Table 3.4	<i>Cumulative Summary of Valid Licences and Permits under Contract no. HK/2009/01</i>
Table 3.5	<i>Summary of submission status under FEP-02/364/2009</i>
Table 3.6	<i>Cumulative Summary of Valid Licences and Permits under Contract no. HK/2009/02</i>
Table 3.7	<i>Summary of submission status under FEP-01/364/2009</i>
Table 3.8	<i>Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/18</i>
Table 3.9	<i>Summary of submission status under FEP-05/364/2009/A</i>
Table 3.10	<i>Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/15</i>
Table 3.11	<i>Summary of submission status under FEP-06/364/2009/A</i>
Table 3.12	<i>Cumulative Summary of Valid License and Permits under Contract no. HY/2009/19</i>
Table 3.13	<i>Summary of submission status under FEP-07/364/2009/A</i>
Table 3.14	<i>Cumulative Summary of Valid Licences and Permits under Contract no. HK/2010/06</i>
Table 3.15	<i>Summary of submission status under FEP-08/364/2009/B</i>
Table 3.16	<i>Cumulative Summary of Valid License and Permits under Contract no. HK/2012/08</i>
Table 3.17	<i>Summary of submission status under FEP-09/364/2009/B</i>
Table 3.18	<i>Cumulative Summary of Valid License and Permits under Contract no. HY/2010/08</i>
Table 4.1	<i>Noise Monitoring Stations</i>
Table 4.2	<i>Real Time Noise Monitoring Stations</i>
Table 4.3	<i>Air Monitoring Stations</i>
Table 5.2	<i>Noise Monitoring Stations for Contract no. HY/2009/18</i>
Table 5.3	<i>Noise Monitoring Station for Contract no HK/2009/01 and HK/2009/02</i>
Table 5.4	<i>Noise Monitoring Stations for Contract no. HY/2009/15</i>
Table 5.5	<i>Noise Monitoring Stations for Contract no. HY/2009/19</i>
Table 5.7	<i>Real Time Noise Monitoring Stations for Contract no. HY/2009/19</i>
Table 5.9	<i>Air Monitoring Stations for Contract no. HY/2009/18</i>
Table 5.10	<i>Air Monitoring Station for Contract no. HK/2009/01</i>
Table 5.11	<i>Air Monitoring Station for Contract no. HK/2009/02</i>
Table 5.12	<i>Air Monitoring Station for Contract no. HY/2009/15</i>
Table 5.13	<i>Air Monitoring Stations for Contract no. HY/2009/19</i>
Table 5.15	<i>Details of Waste Disposal for Contract no. HK/2009/01</i>
Table 5.16	<i>Details of Waste Disposal for Contract no. HK/2009/02</i>
Table 5.17	<i>Details of Waste Disposal for Contract no. HY/2009/18</i>
Table 5.18	<i>Details of Waste Disposal for Contract no. HY/2009/15</i>
Table 5.19	<i>Details of Waste Disposal for Contract no. HY/2009/19</i>
Table 5.20	<i>Details of Waste Disposal for Contract no. HK/2010/06</i>
Table 5.21	<i>Details of Waste Disposal for Contract no. HK/2012/08</i>
Table 5.22	<i>Details of Waste Disposal for Contract no. HY/2010/08</i>
Table 8.1	<i>Summary of Environmental Inspections for Contract no. HY/2009/15</i>
Table 8.2	<i>Summary of Environmental Inspections for Contract no. HK/2009/18</i>
Table 8.3	<i>Summary of Environmental Inspections for Contract no. HK/2009/01</i>
Table 8.4	<i>Summary of Environmental Inspections for Contract no. HK/2009/02</i>
Table 9.1	<i>Cumulative Statistics on Complaints</i>
Table 9.2	<i>Cumulative Statistics on Successful Prosecutions</i>
Table 10.1	<i>Summary of Key Construction Activities of Individual Contract(s) to be commenced in Coming Reporting Month</i>



LIST OF FIGURES

<u>Figure 2.1</u>	Project Layout
<u>Figure 2.2</u>	Project Organization Chart
<u>Figure 4.1</u>	Locations of Environmental Monitoring Stations

LIST OF APPENDICES

<u>Appendix 3.1</u>	Environmental Mitigation Implementation Schedule
<u>Appendix 4.1</u>	Action and Limit Level
<u>Appendix 4.2</u>	Copies of Calibration Certificates
<u>Appendix 5.1</u>	Monitoring Schedule for Reporting Month and Coming month
<u>Appendix 5.2</u>	Noise Monitoring Results and Graphical Presentations
<u>Appendix 5.3</u>	Air Quality Monitoring Results and Graphical Presentations
<u>Appendix 5.4</u>	Real-time Noise Monitoring Results and Graphical Presentations
<u>Appendix 6.1</u>	Event Action Plans
<u>Appendix 6.2</u>	Notification of Exceedance
<u>Appendix 9.1</u>	Complaint Log
<u>Appendix 10.1</u>	Construction Programme of Individual Contracts

EXECUTIVE SUMMARY

- i. This is the Environmental Monitoring and Audit (EM&A) Monthly Report – **July 2013** specific for Environmental Permit no. EP-364/2009/B, Further Environmental Permit nos. FEP-01/364/2009, FEP-02/364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A FEP-07/364/2009/A, FEP-08/364/2009/A and FEP-09/364/2009/B. The EM&A report is prepared by the Environmental Team (ET) employed under Contract No. HK/2011/07 – Wan Chai Development Phase II and Central Wanchai Bypass – Sampling, Field Measurement and Testing Works (Stage 2). This report presents the environmental monitoring findings and information recorded during the period of **July 2013**. The cut-off date of reporting is at 27th of each reporting month.
- ii. In the reporting month, the principal work activities of individual contracts are included as follows:

Contract no. HY/2009/18 - Central - Wan Chai Bypass (CWB) - Central Interchange under FEP-05/364/2009/A

- Excavation of trial pit
- Transplanting of trees
- Hoarding erection and modification
- Installation of couplers, UU detection, trial trench, pre-drilling
- Excavation
- Drainage works
- Tunnel works
- Trough structure construction and associated drilling and grouting
- Road works
- OHVD installation
- Pre-bored H-piling
- Bridges construction
- Scaffolding / false-work erection

Contract no. HK/2009/01 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Hong Kong Convention and Exhibition Centre - Tunnel Works under FEP-02/364/2009

- Installation of pre-bored H-pile in CWB Stage 1 underneath Atrium Link (from CH80 to CH120)
- Installation of pre-bored H-pile in CWB Stage 2 Atrium Link (from CH120 to CH220) would be continued. 14 nos. pre-bored H-piles had been excavated. 2 nos. pre-bored H-piles were grouted
- Construction of bulkhead wall at CH3129 (18 panels)
- Filling of the existing open water channel at CH260.
- Construction of the Common D-wall
- Demolition of the Promenade Deck
- Installation of dewatering wells, observation wells and piezometers at CWB Stage 1

Contract no. HK/2009/02 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

- ELS removal of strut S5
- Rebar fixing for the center wall Bay 4 and Bay 5
- Formwork delivery
- Installation of waterproofing for side wall at Bay 4 & Bay 5
- Total 123 nos. out of 290 nos. of pre-grouting at WCR2
- Total 66 m guide wall for D-wall construction at WCR2 was casted
- Silo installation and pipe connect from desander to silo was in progress.
- Desander setup for D-Wall construction at Tunnel Portion 2 at WCR2 area

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- ELS works and pipe roofing works at TS4
- Cut and cover tunnel construction at TPCWAE
- Construction of OHVD at TS1
- Excavation and tunnel lining construction for mined tunnel
- Construction of Diaphragm Wall, Post Diaphragm Wall Works and Installation of King Post at TS2

Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- Road works at Watson Road
- Bored piling (Land)
- D-wall and Barrette Construction
- Construction works for Box Culvert T1
- Construction works for Culvert U1
- Construction of Pile cap (Land)
- Construction of dewatering well for Cut & Cover Tunnel
- Removal of marine platform
- Construction of pile cap, column & cross head (Marine)
- ELS for Cut & Cover Tunnel
- Laying of 1500 pipe
- Launching of segments
- Unloading segments from derrick
- Extraction of temporary pile from marine section

Contract no. HK/2010/06 - Wan Chai Development Phase II - Central - Wan Chai Bypass over MTR Tsuen Wan Line under FEP-08/364/2009/A

- Installation Works of Precast Concrete Box Unit
- Installation of 150T anchors

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West under FEP-09/364/2009B

- Site preparation works
- Site survey
- Hoarding erection

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8) under FEP-10/364/2009B

- Tree Pruning works
- Tree removal works,
- Tree transplanting works,
- Instrumentation works,
- Ground investigation works and
- Erection of site hoarding.

Noise Monitoring

- iii. Noise monitoring during daytime was conducted at M1a - Harbour Road Sports Center; M2b - Noon-day gun area; M3a - Tung Lo Wan Fire Station; M4b - Victoria Center; M5b - City Garden, M6 - HK Baptist Church Henrietta Secondary School, M7e and M7w – International Finance Centre Eastern and Western End of Podium, and M8 - City Hall on a weekly basis.
- iv. No action and 2 limit level exceedances at M6 – HK Baptist Church Henrietta Secondary School were recorded on 9 and 16 July 2013 in this reporting month. The exceedances were concluded as non-project related.
- v. 24-hour real time noise monitoring was conducted at RTN1 - FEHD Hong Kong Transport Section Whitfield Depot for construction activities under IECL bridge deck. No project related exceedance was recorded in the reporting month.
- vi. 24-hour real time noise monitoring was conducted at RTN2a – Hong Kong Electric Centre. No project related exceedance was recorded in the reporting month.
- vii. 24-hour real time noise monitoring was conducted at RTN3 – Yu Lee Mo Fan Memorial School. No project related exceedance was recorded in the reporting month.
- viii. 24-hour real time noise monitoring was conducted at RTN4 – Causeway Bay Community Centre. No limit level exceedance was recorded in the reporting month.
- ix. As confirmed by CWB RSS, the IECL parapet removal operations will commence in May 2013. Liaison was conducted with HK Baptist Church Henrietta Secondary School and Po Leung Kuk Yu Lee Mo Fan Memorial School regarding the set up of RTN3 real time noise monitoring station. Po Leung Kuk Yu Lee Mo Fan Memorial School grant permission for set up on 4 Sep 2012 and station set up was performed on 14 Sep 2012.
- x. Real time noise monitoring station at Oil Street Community Liaison Centre (RTN2- Oil Street Community Centre) was relocated from Oil Street Community Liaison Centre to Hong Kong Electric (RTN2a- Electric Centre) on 5 Oct 2012 which is a representative of the noise sensitive receiver City Garden. The baseline noise level of RTN2a will adopt the results derived from the baseline noise monitoring conducted in Electric Centre from 4 December 2009 to 17 December 2009.

- xi. Real-time noise baseline capturing was conducted from 21 Sep 2012 to 04 Oct 2012 at RTN3-Po Leung Kuk Yu Lee Mo Fan Memorial School.
- xii. Real-time Noise Monitoring at RTN3- Po Leung Kuk Yu Lee Mo Fan Memorial School was commenced since 06 Oct 2012.
- xiii. Causeway Bay Community Centre has granted permission for set up of real time noise monitoring station on 21 Dec 2012 and station set up was performed on 27 Dec 2012. The Baseline noise level of RTN4- Causeway Bay Community Centre will adopt the results from the baseline noise monitoring report for EP/364/2009 in 22 April 2010 in which approved by EPD.
- xiv. According to clause 3.1 stated in EP-364/2009B, "the real-time monitoring system shall be in place no later than two weeks before the commencement date of demolition works of the existing Island Eastern Corridor". IEC demolition associated construction works was commenced on 3 Feb 2013 and Real time noise monitoring at RTN4-Causeway Bay Community Centre was commenced on 13 Jan 2013.
- xv. Real-time noise monitoring station RTN1-FEHD Whitfield Depot was finely adjusted from 2/F to roof-top at FEHD Whitfield Depot on 24 June 2013 with respect to the commencement of advance works for IEC parapet demolition.

Air Monitoring

- xvi. Due to extension of site boundary by contractor of HY/2009/19, location of air monitoring station CMA1b – Oil Street Community Liaison Centre has been finely adjusted on 21 April 2012.
- xvii. The location ID of air monitoring station CMA1b was updated as Oil Street Site Office in April 2013.
- xviii. Due to the interruption of electricity supply, the 24hr TSP monitoring at CMA5a was rescheduled from 3 July 2013 to 4 July 2013.
1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted at CMA1b – Oil Street Site Office; CMA2a - Causeway Bay Community Center; CMA3a - CWB PRE Site Office Area; CMA4a – Society for the Prevention of Cruelty to Animals; CMA5a - Children Garden opposite to Pedestrian Plaza; MA1e and MA1w – International Finance Centre eastern and western wing on every six days basis.

Complaints, Notifications of Summons and Successful Prosecutions

- xix. There were no environmental complaints received in this reporting month.

Site Inspections and Audit

- xx. The Environmental Team (ET) conducted weekly site inspections for Contract no. HY/2009/15, HY/2009/18, HY/2009/19, HK/2009/01, HK/2009/02, HK/2012/08 and HK/2010/06 in this reporting period. Construction of bored pile E3B under HY/2009/17 was confirmed completed and the respective work area under FEP was inspected under HY/2009/19 from 19 Dec 2012 onwards. The Contractors rectified major observations and recommendations made during the audit sessions. No non-conformance was identified during the site inspections.

Future Key Issues

- xxi. In the coming reporting month, the principal work activities of individual contracts are anticipated as follows:

Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- Excavation of trial pit
- Transplanting of trees
- Hoarding erection and modification
- Installation of couplers, UU detection, trial trench, pre-drilling
- Excavation
- Drainage works
- Tunnel works
- Trough structure construction and associated drilling and grouting
- Road works
- OHVD installation
- Bridges construction
- Scaffolding / false-work erection
- Profile barrier construction

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre – Tunnel Works under FEP-02/364/2009

- Installation of pre-bored H-pile in CWB Stage 2 Atrium Link.
- Filling of the existing open water channel and Dome
- Construction of the south Common D-wall.
- Demolition of the Promenade Deck.
- Installation of dewatering wells, observation wells and piezometers at CWB stage 1
- ELS for Stage 1 CWB

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

- Continue wall construction at Tunnel Portion 1
- Commence D-Wall construction at Tunnel Portion 2

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- ELS works, pipe roofing works and tunnel construction at TS4
- Cut and cover tunnel construction at TPCWAE
- Construction of OHVD at TS1
- Excavation and tunnel lining construction for mined tunnel
- Post Diaphragm Wall Works, ELS works and Installation of King Post at TS2

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- Road works at Watson Road
- Bored piling (Land)
- D-wall and Barrette Construction
- Construction works for Box Culvert T1
- Construction of Pile cap (Land)
- Demolition of parapet at IEC Link
- Construction of dewatering well for Cut & Cover Tunnel
- Removal of marine platform
- Construction of pile cap, column & cross head (Marine)
- ELS for Cut & Cover Tunnel
- Installation of dewatering well
- Laying of 1500 pipe
- Launching of segments
- Unloading segments from derrick
- Extraction of temporary pile from marine section

Contract no. HK/2010/06 - Wan Chai Development Phase II - Central - Wan Chai Bypass over MTR Tsuen Wan Line under FEP-08/364/2009/A

- Stitching Works
- Foam Concreting Works
- Other Miscellaneous Works in precast unit

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West under FEP-09/364/2009/B

- Hoarding erection

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8) under FEP-10/364/2009B

- Tree Pruning works
- Tree removal works,
- Tree transplanting works,
- Instrumentation works,
- Ground investigation works,
- Erection of site hoarding and
- Concrete works.

1 INTRODUCTION

1.1 Scope of the Report

- 1.1.1. Lam Geotechnics Limited (LGL) has been appointed to work as the Environmental Team (ET) under Environmental Permit no. EP-364/2009/B and Further Environmental permit nos. FEP-01/364/2009, FEP-02/364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A, FEP-07/364/2009/A, FEP-08/364/2009/A and FEP-09/364/2009/B to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) and in the EM&A Manual of the approved EIA Report for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-014/2001).
- 1.1.2. This report presents the environmental monitoring and auditing work carried out in accordance to the Section 10.3 of EM&A Manual and “*Environmental Monitoring and Audit Requirements*” under Particular Specification Section 27.
- 1.1.3. This report documents the finding of EM&A works for Environmental Permit (EP) no. EP-364/2009/B, Further Environmental Permit (FEP) nos. FEP-01-364/2009, FEP-02/364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A, FEP-07/364/2009/A, FEP-08/364/2009/A and FEP-09/364/2009B during the period [June to July 2013](#). The cut-off date of reporting is at 27th of each reporting month

1.2 Structure of the Report

- Section 1** ***Introduction*** – details the scope and structure of the report.
- Section 2** ***Project Background*** – summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.
- Section 3** ***Status of Regulatory Compliance*** – summarizes the status of valid Environmental Permits / Licenses during the reporting period.
- Section 4** ***Monitoring Requirements*** – summarizes all monitoring parameters, monitoring methodology and equipment, monitoring locations, monitoring frequency, criteria and respective event and action plan and monitoring programmes.
- Section 5** ***Monitoring Results*** – summarizes the monitoring results obtained in the reporting period.
- Section 6** ***Compliance Audit*** – summarizes the auditing of monitoring results, all exceedances environmental parameters.

- Section 7** ***Cumulative Construction Impact due to the Concurrent Projects*** – summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.
- Section 8** ***Site Inspection*** – summarizes the findings of weekly site inspections undertaken within the reporting period, with a review of any relevant follow-up actions within the reporting period.
- Section 9** ***Complaints, Notification of summons and Prosecution*** – summarizes the cumulative statistics on complaints, notification of summons and prosecution
- Section 10** ***Conclusion***

22 PROJECT BACKGROUND

2.1 Background

- 2.1.1. “Wan Chai Development phase II and Central-Wan Chai Bypass” and “Central-Wan Chai Bypass and Island Eastern Corridor Link” (hereafter called “the Project”) are Designated Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Reports for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001) and Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) have been approved on 31 August 2001 and 11 December 2008 respectively.
- 2.1.2. The key purpose of Wan Chai Development Phase II (WDII) is to provide land at Wan Chai North and North Point for construction of the Central-Wan Chai Bypass and Island Eastern Corridor Link (CWB). Land formed under the project will be developed as a world-class waterfront promenade joining that at the new Central waterfront for public enjoyment.
- 2.1.3. There is a compelling and present need for the CWB to provide relief to the very congested east-west Connaught Road Central/Harcourt Road / Gloucester Road Corridor (the Corridor) which is currently operating beyond its capacity. The CWB will provide relief to the existing congestion along the Corridor and cater for the anticipated growth of traffic on Hong Kong Island. Without the CWB and its access roads, there will not be sufficient capacity to serve the heavy traffic demands at both strategic and local levels.

2.2 Scope of the Project and Site Description

- 2.2.1. Design and Construction of Central – Wan Chai Bypass and Island Eastern Corridor Link under the Project involves the construction and operation of a trunk road and its road tunnel more than 800m in length between portals that is shown at Figure 2.1.
- 2.2.2. The study area encompasses existing developments from Central to North Point. The scope of the Central-Wanchai Bypass (CWB) and Island Eastern Corridor Link (IECL) includes:
- A dual three-lane trunk road, approximately 4.5 km in length, and tunnel approximately 3.7 km in length defined from the connection with the existing Rumsey Street Flyover in Central, through to a connection with the existing Island Eastern Corridor to the east of the Causeway Bay Typhoon Shelter (CBTS);
 - The Central Interchange near the Rumsey Street Flyover to provide road connections to the Central area;
 - Tunnel control buildings and ventilation buildings;
 - Slip roads to connect the CWB to the local road system in the Wan Chai North and Causeway Bay area;
 - Associated road lighting, road signing, traffic control and surveillance system; and
 - Other associated works.

2.2.3. The project also contains various Schedule 2 DPs that, under the EIAO, require Environmental Permits (EPs) to be granted by the DEP before they may be either constructed or operated. **Table 2.1** summarises the five individual DPs under this Project. **Figure 2.1** shows the locations of these Schedule 2 DPs.

Table 2.1 Schedule 2 Designated Projects under this Project

Item	Designated Project	EIAO Reference	Reason for inclusion
DP1	Central-Wanchai Bypass (CWB) including its road tunnel and slip roads	Schedule 2, Part I, A.1 and A.7	Trunk road and road tunnel more than 800 m in length
DP2	Road P2 and other roads which are classified as primary/district distributor roads	Schedule 2, Part I, A.1	Primary / district distributor roads
DP3	Reclamation works including associated dredging works	Schedule 2, Part I, C.1 and C.12	Reclamation more than 5 ha in size and a dredging operation less than 100 m from a seawater intake point
DP5	Wan Chai East Sewage Outfall	Schedule 2, Part I, F.5 and F.6	Submarine sewage pipelines with a total diameter more than 1,200 mm and include a submarine sewage outfall
DP6	Dredging for the Cross-harbour Water Mains from Wan Chai to Tsim Sha Tsui	Schedule 2, Part I, C.12	A dredging operation less than 100 m from a seawater intake point

2.3 Division of the Project Responsibility

2.3.1. Due to the multi-contract nature of the Project, there are a number of contracts sub-dividing the whole works area into different work areas to be commenced. Contractors of individual contracts will be required by the EP holder to apply Further Environmental Permits such that the impact monitoring stations are sub-divided accordingly to facilitate the implementation of EM&A programme and to streamline the EM&A reporting for individual FEP holders correspondingly.

2.3.2. The details of individual contracts are summarized in **Table 2.2**.

Table 2.2 Details of Individual Contracts under the Project

Contract No.	Contract Title	Associated DP(s)	Construction Commencement Date
HY/2009/17	Central – Wan Chai Bypass (CWB) at FEHD Whitfield Depot – Advanced piling works.	DP1	5 October 2010
HY/2009/18	Central – Wan Chai Bypass (CWB) – Central Interchange	DP1	21 April 2011
04/HY/2006	Reconstruction of Bus Terminus near Man Yiu Street and Man Kwong Street	DP1	September 2010 (Completed)
HK/2009/01	Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre – Tunnel Works	DP1, DP2	25 August 2011

Contract No.	Contract Title	Associated DP(s)	Construction Commencement Date
HK/2009/02	Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East(CWB Tunnel)	DP1	26 April 2011
HY/2009/15	Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)	DP1	13 July 2011
HY/2009/19	Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link	DP1	24 March 2011
HK/2010/06	Wan Chai Development Phase II- Central-Wan Chai Bypass over MTR Tsuen Wan Line	DP3	22 March 2011
HK/2012/08	Wan Chai Development Phase II- Central-Wan Chai Bypass at Wan Chai West	DP1,DP2, DP3	DP works under EP-364 to be commenced tentatively in late 2013.
HY/2010/08	Central- Wanchai Bypass Tunnel – Tunnel (Slip Road 8)	DP1, DP2, DP3	21 March 2013

2.4 Project Organization and Contact Personnel

- 2.4.1. Civil Engineering and Development Department and Highways Department are the overall project controllers for the Wan Chai Development Phase II and Central-Wan Chai Bypass respectively. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.4.2. The proposed project organization and lines of communication with respect to environmental protection works are shown in **Figure 2.2**. Key personnel and contact particulars are summarized in **Table 2.3**:

Table 2.3 Contact Details of Key Personnel

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Principal Resident Engineer	Mr. Frankie Fan	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3922 3388	3912 3010
Lam Woo & CO., LTD.	Contractor under Contract no. HY/2009/17	General Manager	Mr. Thomas Tang	6111 5351	2566 7522
		Contractor's Representative	Mr. Chung Man Shek	2566 4866	
		Site Agent	Mr. Tong Au	9725 5874	
		Environmental Officer	Dr. Priscilla Choy	9161 7287	
		Environmental Supervisor	Mr. Tam Chun Pong	6461 3062	

Party	Role	Post	Name	Contact No.	Contact Fax
Chun Wo – Leader Joint Venture	Contractor under Contract no. HK/2009/01	Joint Venture Board Representative	Mr. PL Yue	2162 9909	2634 1626
		Construction Manager	Mr. Terry Wong	9757 9846	
		Deputy Site Agent	Mr. Andy Yu	9648 4896	
		Construction Manager	Mr. Wyman Wong	9627 2467	
		Construction Manager	Mr. Jack Chu	9775 2467	
		Environmental Officer (Compliance Manager)	Mr. Andy Mak	9103 2370	
		Environmental Supervisor	Mr. Kwong Weng Kit	6253 3356	
Chun Wo – CRGL Joint Venture	Contractor under Contract no. HK/2009/02	Site Agent	Mr. Chan Sing Cho	3658-3002	2827 9996
		Quality & Environmental Manager (Environmental Officer)	Mr. C.P. Ho	3658-3000	
Chun Wo - CRGL - MBEC_Joint Venture	Contractor under Contract no. HY/2009/19	Project Manager	Mr. Rayland Lee	3758 8879	2570 8013
		Site Agent	Mr. Paul Yu	9456 9819	
		Environmental Manager / Environmental Officer	Mr. M.H. Isa	9884 0810	
		Environmental Engineer	Mr. Calvin Leung	9286 9208	
		Construction Manager (Marine)	Mr. William Luk	9610 1101	
		Construction Manager (Land)	Mr. Patrick Cheung	9643 3012	
		Construction Manager (Land)	Mr. Eric Fong	6191 9337	
		Operation Manager (Land)	Mr. Yung Kwok Wah	9834 1010	
Leighton Contractors (Asia) Limited	Contractor under Contract no. HY/2009/18	Site Agent	Mr. Jimmy Chu	2214 7700	2140 6799
		Deputy Site Agent	Mr. Roger Wong	2214 7703	
		Environmental Officer	Ms. Lighting Chan	2823 1161	

Party	Role	Post	Name	Contact No.	Contact Fax
		Environmental Engineer	Mr. Donald Yip	2214 7721	
		Environmental Engineer Graduate	Mr. Phil Mak	2214 7738	
		Environmental Supervisor	Mr. K. P. Lai	6461 4660	
		Environmental Supervisor	Mr. Ray Cheng	2214 7742	
		Environmental Supervisor	Mr. K. W. Lee	6461 4623	
		Environmental Supervisor	Mr. Ryan Tsui	2214 7705	
		Environmental Supervisor	Mr. C. Y. Au Yeung	6461 8631	
China State Construction Engineering (HK) Ltd.	Contractor under Contract no. HY/2009/15	Project Director	Mr. K C Cheung	2823 7813	2865 5229
		Site Manager	Mr. J.H. Chen	3557 6368	2566 2192
		Contractor's Representative	Mr. Andrew Wong	3557 6407	
		Head of construction	Mr. Roger Cheung	3557 6371	
		Environmental Officer	Mr. Daniel Sin	3557 6215	
		Environmental Supervisor	Ms. Esther Choi	35576348	
Gammon - Leader JV	Contractor under Contract no. HK/2010/06	Project Manager	Mr. Paul Lui	9095 7922	2529 2880
		Site Agent	Mr. Keith Tse	2529 2068	
		Environmental Officer	Mr. Clement Pang	9481 6024	
		Environmental Supervisor	Mr. Jacky Cheung	9735 9200	
China State-Leader JV	Contractor under Contract no. HK/2012/08	Project Director	Mr. Andrew TSE	9137 1811	2877 1522
		Project Manager	Mr. Victor WU	9193 8871	
		Deputy Project Manager	Mr. George CHEUNG	9268 1918	
		Site Agent	Mr. Paul LUI	9095 7922	
		Environmental Officer	Mr. James MA	9130 9549	
		Environmental Supervisor	Mr. Ching Man, CHAN	6050 4919	
China State	Contractor under Contract no. HY/2010/08	Project Director	Cheung Kit Cheung	3557 6399	
		Project Manager	Chan Ying Lun	9812 0592	
		Deputy Project Manager	Chris Leung	3467 4299	

Party	Role	Post	Name	Contact No.	Contact Fax
		Site Agent	Dave Chan	3467 4277	
		Environmental Officer	C.M. Wong	3557 6464	
		Environmental Supervisor	Louis Lam Tsz Kwan	3557 6470	
ENVIRON Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	3465 2888	3465 2899
Lam Geotechnics Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331

2.4.3. In this reporting month, the principal work activities of individual contracts are included as follows:

Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- Excavation of trial pit
- Transplanting of trees
- Hoarding erection and modification
- Installation of couplers, UU detection, trial trench, pre-drilling
- Excavation
- Drainage works
- Tunnel works
- Trough structure construction and associated drilling and grouting
- Road works
- OHVD installation
- Pre-bored H-piling
- Bridges construction
- Scaffolding / false-work erection

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre – Tunnel Works under FEP-02/364/2009

- Installation of pre-bored H-pile in CWB Stage 1 underneath Atrium Link (from CH80 to CH120)
- Installation of pre-bored H-pile in CWB Stage 2 Atrium Link (from CH120 to CH220) would be continued. 14 nos. pre-bored H-piles had been excavated. 2 nos. pre-bored H-piles were grouted
- Construction of bulkhead wall at CH3129 (18 panels)
- Filling of the existing open water channel at CH260.
- Construction of the Common D-wall
- Demolition of the Promenade Deck
- Installation of dewatering wells, observation wells and piezometers at CWB Stage 1

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

- ELS removal of strut S5
- Rebar fixing for the center wall Bay 4 and Bay 5
- Formwork delivery
- Installation of waterproofing for side wall at Bay 4 & Bay 5
- Total 123 nos. out of 290 nos. of pre-grouting at WCR2
- Total 66 m guide wall for D-wall construction at WCR2 was casted
- Silo installation and pipe connect from desander to silo was in progress.
- Desander setup for D-Wall construction at Tunnel Portion 2 at WCR2 area

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- ELS works and pipe roofing works at TS4
- Cut and cover tunnel construction at TPCWAE
- Construction of OHVD at TS1
- Excavation and tunnel lining construction for mined tunnel
- Construction of Diaphragm Wall, Post Diaphragm Wall Works and Installation of King Post at TS2
-

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- Road works at Watson Road
- Bored piling (Land)
- D-wall and Barrette Construction
- Construction works for Box Culvert T1
- Construction works for Culvert U1
- Construction of Pile cap (Land)
- Construction of dewatering well for Cut & Cover Tunnel
- Removal of marine platform
- Construction of pile cap, column & cross head (Marine)
- ELS for Cut & Cover Tunnel
- Laying of 1500 pipe
- Launching of segments
- Unloading segments from derrick
- Extraction of temporary pile from marine section

Contract no. HK/2010/06 - Wan Chai Development Phase II - Central - Wan Chai Bypass over MTR Tsuen Wan Line under FEP-08/364/2009/A

- Installation Works of Precast Concrete Box Unit
- Installation of 150T anchors

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West under FEP-09/364/2009/B

- Site preparation works

- Site survey
- Hoarding erection

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8) under FEP-10/364/2009B

- Tree Pruning works
- Tree removal works,
- Tree transplanting works,
- Instrumentation works,
- Ground investigation works and
- Erection of site hoarding.

2.4.4. In coming reporting month, the principal work activities of individual contracts are anticipated as follows:

Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- Excavation of trial pit
- Transplanting of trees
- Hoarding erection and modification
- Installation of couplers, UU detection, trial trench, pre-drilling
- Excavation
- Drainage works
- Tunnel works
- Trough structure construction and associated drilling and grouting
- Road works
- OHVD installation
- Bridges construction
- Scaffolding / false-work erection
- Profile barrier construction

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre – Tunnel Works under FEP-02/364/2009

- Installation of pre-bored H-pile in CWB Stage 2 Atrium Link.
- Filling of the existing open water channel and Dome
- Construction of the south Common D-wall.
- Demolition of the Promenade Deck.
- Installation of dewatering wells, observation wells and piezometers at CWB stage 1
- ELS for Stage 1 CWB

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

- Continue wall construction at Tunnel Portion 1.
- Commence D-Wall construction at Tunnel Portion 2

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- ELS works, pipe roofing works and tunnel construction at TS4
- Cut and cover tunnel construction at TPCWAE
- Construction of OHVD at TS1
- Excavation and tunnel lining construction for mined tunnel
- Post Diaphragm Wall Works, ELS works and Installation of King Post at TS2

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- Road works at Watson Road
- Bored piling (Land)
- D-wall and Barrette Construction
- Construction works for Box Culvert T1
- Construction of Pile cap (Land)
- Demolition of parapet at IEC Link
- Construction of dewatering well for Cut & Cover Tunnel
- Removal of marine platform
- Construction of pile cap, column & cross head (Marine)
- ELS for Cut & Cover Tunnel
- Installation of dewatering well
- Laying of 1500 pipe
- Launching of segments
- Unloading segments from derrick
- Extraction of temporary pile from marine section

Contract no. HK/2010/06 - Wan Chai Development Phase II - Central - Wan Chai Bypass over MTR Tsuen Wan Line under FEP-08/364/2009/A

- Stitching Works
- Foam Concreting Works
- Other Miscellaneous Works in precast unit

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West under FEP-09/364/2009/B

- Hoarding erection

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8) under FEP-10/364/2009B

- Tree Pruning works
- Tree removal works,
- Tree transplanting works,
- Instrumentation works,
- Ground investigation works,
- Erection of site hoarding and
- Concrete works

3 STATUS OF REGULATORY COMPLIANCE

3.1 Status of Environmental Licensing and Permitting under the Project

3.1.1. A summary of the current status on licences and/or permits on environmental protection pertinent to the Project is shown in **Table 3.1**.

Table 3.1 Summary of the current status on licences and/or permits on environmental protection pertinent to the Project

Permits and/or Licences	Reference No.	Issued Date	Status
Environmental Permit	EP-356/2009	30 Jul 2009	Valid
Environmental Permit	EP-364/2009	17 Aug 2009	Superseded
Environmental Permit	EP-364/2009/A	4 Aug 2010	Superseded
Environmental Permit	EP-364/2009/B	20 Sep 2012	Valid
Environmental Permit	EP-376/2009	13 Nov 2010	Valid
Further Environmental Permit	FEP-01/356/2009	18 Feb 2010	Surrendered
Further Environmental Permit	FEP-02/356/2009	24 Mar 2010	Valid
Further Environmental Permit	FEP-03/356/2009	24 Mar 2010	Valid
Further Environmental Permit	FEP-04/356/2009	15 Nov 2010	Valid
Further Environmental Permit	FEP-05/356/2009	24 Mar 2011	Valid
Further Environmental Permit	FEP-06/356/2009	5 March 2013	Valid
Further Environmental Permit	FEP-07/356/2009	26 July 2013	Valid
Further Environmental Permit	FEP-01/364/2009	24 Mar 2010	Valid
Further Environmental Permit	FEP-02/364/2009	21 Apr 2010	Valid
Further Environmental Permit	FEP-03/364/2009	12 July 2010	Surrendered
Further Environmental Permit	FEP-04/364/2009/A	14 Oct 2010	Surrendered
Further Environmental Permit	FEP-05/364/2009/A	15 Nov 2010	Valid
Further Environmental Permit	FEP-06/364/2009/A	22 Nov 2010	Valid
Further Environmental Permit	FEP-07/364/2009/A	25 Feb 2011	Valid
Further Environmental Permit	FEP-08/364/2009/A	15 June 2012	Valid
Further Environmental Permit	FEP-09/364/2009/B	5 March 2013	Valid
Further Environmental Permit	FEP-10/364/2009/B	26 July 2013	Valid



- 3.1.2. Due to the multi-contract nature of the Project, the status of permits and/or licences under the individual contract(s) are presented as below:

Contract no. HY/2009/17 – Central – Wan Chai Bypass (CWB) at FEHD Whitfield Depot –
Advanced piling works under FEP-03/364/2009

- 3.1.3. The construction works was completed and the FEP was surrendered by the Contractor on 25 April 2013.

Contract no. 04/HY/2006 – Reconstruction of Bus Terminus near Man Yiu Street and Man Kwong Street under FEP-04/364/2009/A

- 3.1.4. The construction works was completed, and the FEP was surrendered by the Contractor on 11 February 2011.

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre – Tunnel Works under FEP-02/364/2009

- 3.1.5. Summary of the current status on licences and/or permits on environmental protection pertinent and submission under FEP-02/364/2009 for contract no. HK/2009/01 are shown in **Table 3.4** and **Table 3.5**

Table 3.4 Cumulative Summary of Valid Licences and Permits under Contract no. HK/2009/01

Permits and/or Licences	Reference No.	Issued Date	Valid Period/Expiry Date	Status
Further Environmental Permit	FEP-02/356/2009	24 Mar 2010	N/A	Valid
	FEP-02/364/2009	21 Apr 2010	N/A	Valid
Notification of Works Under APCO	313088	06 Jan 2010	N/A	Valid
Construction Noise Permit (CNP) for non-piling equipment	GW-RS0166-13	14 Feb 2013	16 Feb 2013 to 13 Aug 2013	Valid
	GW-RS0310-13	25 Mar 2013	27 Mar 2013 to 25 Sept 2013	Valid
	GW-RE0274-13	26 Mar 2013	30 Mar 2013 to 29 Sept 2013	Valid
	GW-RS0274-13	19 Mar 2013	25 Mar 2013 to 24 Sep 2013	Valid
	GW-RS-0052-13	18 Jan 2013	20 Jan 2013 to 19 July 2013	Expired
	GW-RE-0371-13	9 Apr 2013	13 Apr 2013 to 12 Oct 2013	Valid
	GW-RE-0372-13	12 Apr 2013	15 Apr 2013 to 7 Oct 2013	Valid
	GW-RS0368-13	12 Apr 2013	15 Apr 2013 to 7 Oct 2013	Valid
	GW-RS1177-12	15 Nov 2012	17 Nov 2012 to 10 May 2013	Expired
	GW-RS0797-13	16 Jul 2013	18 Jul 2013 to 15 Jan 2014	Valid
	GW-RS0773-13	16 Jul 2013	20 July 2013 to 19 Jan 2014	Valid
	GW-RS0807-13	24 Jul 2013	25 Jul 2013 to 21 Jan 2014	Valid
	GW-RE0757-13	23 Jul 2013	25 Jul 2013 to 31 Aug 2013	Valid
	GW-RS0470-13	29 Apr 2013	9 May 2013 to 24 Oct 2013	Valid
	GW-RS0501-13	9 May 2013	11 May 2013 to 8 Nov 2013	Valid
	GW-RS0510-13	14 May 2013	15 May 2013 to 13 Nov 2013	Valid

Permits and/or Licences	Reference No.	Issued Date	Valid Period/Expiry Date	Status
	GW-RS0579-13	29 May 2013	29 May 2013 to 26 Nov 2013	Cancelled
	GW-RS0626-13	13 Jun 2013	15 Jun 2013 to 12 Dec 2013	Valid
	GW-RS0631-13	14 Jun 2013	14 Jun 2013 to 13 Dec 2013	Valid
	GW-RS0651-13	21 Jun 2013	22 Jun 2013 to 20 Dec 2013	Valid
Discharge Licence	WT00009641-2011	24 Jul 2011	31 Jul 2016	Valid
	WT00006220-2010	18 Mar 2010	31 Mar 2015	Valid
Billing account under Waste Disposal Ordinance	7010069	21 Jan 2010	N/A	Valid
Registration as a Chemical Waste Producer	WPN5213-134-C3585-01	21 Jan 2010	N/A	Valid

Table 3.5 Summary of submission status under FEP-02/364/2009

EP Condition	Submission	Date of Submission
Special Conditions, Clause 2.7 & 2.8	Works Schedule and Location Plan	18 May 2011
Special Conditions, Clause 2.6	Environmental Management Organization Chart	18 May 2011
Special Conditions, Clause 2.6	Commencement Date of Works	20 Jun 2011
Special Conditions, Clause 2.9	Noise Management Plan	10 Jun 2011

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

3.1.6. Summary of the current status on licences and/or permits on environmental protection pertinent and submission under FEP-01/364/2009 for contract no. HK/2009/02 are shown in **Table 3.6** and **Table 3.7**.

Table 3.6 Cumulative Summary of Valid Licences and Permits under Contract no. HK/2009/02

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-03/356/2009	24 Mar 2010	N/A	Valid
	FEP-01/364/2009	24 Mar 2010	N/A	Valid
Notification of Works Under APCO	313962	2 Feb 2010	N/A	Valid
Construction Noise Permit (CNP) for non-pilling equipment	GW-RS1363-12	24 Dec 2012	9 Jan 2013 to 7 July 2013	Cancelled
	GW-RS1381-12	31 Dec 2012	9 Jan 2013 to 7 July 2013	Expired
	GW-RS1384-12	31 Dec 2012	17 Jan 2013 to 16 July 2013	Valid
	GW-RS0206-13	22 Feb 2013	24 Feb 2013 to 19 Aug 2013	Valid
	GW-RS0061-13	17 Jan 2013	1 Feb 2013 to 31 July 2013	Cancelled
	GW-RS0062-13	17 Jan 2013	21 Jan 2013 to 15 July 2013	Valid
	GW-RS0241-13	11 Mar 2013	13 Mar 2013 to 10 Sept 2013	Valid
	GW-RS0251-13	11 Mar 2013	26 Mar 2013 to 24 Sept 2013	Valid
	GW-RS0340-13	28 Mar 2013	10 Apr 2013 to 8 Oct 2013	Valid
	GW-RS0373-13	9 Apr 2013	19 Apr 2013 to 17 Oct 2013	Valid
	GW-RS0437-13	26 Apr 2013	1 May 2013 to 29 Oct 2013	Valid
	GW-RS0155-13	15 Feb 2013	16 Feb 2013 to 14 Aug 2013	Valid
	GW-RS0269-13	23 Mar 2013	23 Mar 2013 to 19 Sept 2013	Valid
	GW-RS0467-13	6/5/2013	17/5/2013 to 16/11/2013	Valid
	GW-RS0517-13	20/5/2013	27/5/2013 to 26/11/2013	Valid
	GW-RS0521-13	20/5/2013	22/5/2013 to 21/11/2013	Valid

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
	GW-RS0530-13	20/5/2013	28/5/2013 to 27/11/2013	Valid
	GW-RE0508-13	21/5/2013	30/5/2013 to 29/11/2013	Valid
	GW-RS0525-13	21/5/2013	30/5/2013 to 29/11/2013	Valid
	GW-RS0538-13	21/5/2013	30/5/2013 to 29/11/2013	Valid
	GW-RS0539-13	23/5/2013	6/6/2013 to 5/12/2013	Valid
	GW-RS0554-13	23/5/2013	6/6/2013 to 5/12/2013	Valid
	GW-RS0586-13	27/5/2013	28/5/2013 to 22/11/2013	Valid
	GW-RS0633-13	14/6/2013	16/6/2013 to 13/12/2013	Valid
	GW-RS0739-13	09/07/2013	17/07/2013 to 16/01/2014	Valid
	GW-RS0708-13	03/07/2013	03/07/2013 to 01/01/2014	Valid
Discharge Licenses	WT00006249-2010	22 Mar 2010	31 Mar 2015	Valid
	WT00006436-2010	15 Apr 2010	30 Apr 2015	Valid
	WT00006673-2010	14 May 2010	31 Mar 2015	Cancelled
	WT00006757-2010	28 May 2010	31 May 2015	Valid
	WT00007129-2010	28 July 2010	31 Jul 2015	Valid
	WT00008982-2011	26 April 2011	30 April 2016	Valid
	WT00009691-2011	1 Aug 2011	31 July 2016	Valid
Billing Account under Waste Disposal Ordinance (Land)	7010255	10 Feb 2010	N/A	Valid
Registration as Chemical Waste Producer (Wan Chai)	WPN5213-135-C3593-01	10 Mar 2010	N/A	Valid
Registration as Chemical Waste Producer (TKO 137)	WPN5213-839-C3593-02	22 Sep 2010	N/A	Valid

Table 3.7 Summary of submission status under FEP-01/364/2009

EP Condition	Submission	Date of Submission
Condition 2.7 and 2.8	Works Schedule and Location Plan	14 Jun 2011
Condition 2.6	Environmental Management Organization Chart	14 Jun 2011
Condition 2.6	Commencement Date of Works	21 Jun 2011
Condition 2.11	Landscape Plan (Revision B)	20 Nov 2012
Condition 2.9	Noise Management Plan (Revision A)	13 Jan 2012

Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

3.1.7. Summary of the current status on licences and/or permits on environmental protection pertinent and submission under FEP-05/364/2009A for contract no. HY/2009/18 are shown in Table 3.8 and Table 3.9.

Table 3.8 Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/18

Permit / Licence / Notification / Approval	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-05/364/2009/A	15 Nov 2010	Permit issued	Valid
Notification of Works Under APCO	322293	07 Oct 2010	Notified	Valid
Construction Noise Permit (CNP) for non-piling equipment	GW-RS0396-13	16 Apr 2013	22 Apr 2013- 21 Oct 2013	Valid
	GW-RS-0459-13	30 Apr 2013	03 May 2013- 02 Nov 2013	Valid
	GW-RS1382-12	02 Jan 2013	04 Jan 2013 to 30 Jun 2013	Valid
	GW-RS0068-13	18 Jan 2013	05 Feb 2013 to 03 Aug 2013	Valid
	GW-RS0036-13	11 Jan 2013	23 Jan 2013 to 22 Jul 2013	Cancelled
	GW-RS0833-12	26 July 2013	4 Aug 2013 to 5 Feb 2013	Valid
	GW-RS0644-13	13 June 2013	01 Jul 2013 – 31 Dec 2013	Valid
	GW-RS0777-13	15 July 2013	22 Jul 2013 – 31 Aug 2013	Valid
Discharge Licence	WT00012998-2012	25 May 2012	31 Jan 2016	Valid
	WT00013967-2012	17 Sep 2012	30 Sep 2017	Valid

Permit / Licence / Notification / Approval	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
	WT00014966-2013	08 Jan 2013	31 Jan 2018	Valid
Registration as a Waste Producer	WPN: 8335-121-L1048-04	17 Dec 2010	N/A	Registration completed
Billing Account under Waste Disposal Ordinance (Land)	Account No.: 7011587	11 Oct 2010	Account approved	Valid

Table 3.9 Summary of submission status under FEP-05/364/2009/A

EP Condition	Submission	Date of Submission
Condition 2.9	Noise Management Plan	01 March 2011
Condition 2.10	Landscape Plan (Rev. 5)	12 March 2012

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

3.1.8. Summary of the current status on licences and/or permits on environmental protection pertinent and submission under FEP-06/364/2009/A for contract no. HY/2009/15 are shown in **Table 3.10** and **Table 3.11**

Table 3.10 Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/15

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-04/356/2009	22 Nov 2010	N/A	Valid
	FEP-06/364/2009/A	22 Nov 2010	N/A	Valid
Notification of Works Under APCO	321822	24 Sep 2010	N/A	Valid
Construction Noise Permit (CNP) for non-piling equipment	GW-RS0434-13	23 Apr 2013	23 Apr 2013 to 16 Oct 2013	Cancelled
	GW-RS0588-13	31 May 2013	2 Jun 2013 to 26 Nov 2013	Valid
	GW-RS0601-13	31 May 2013	2 Jun 2013 to 29 Nov 2013	Valid
	GW-RS0087-13	24 Jan 2013	26 Jan 2013 to 20 July 2013	Cancelled

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
	GW-RS0399-13	18 Apr 2013	18 Apr 2013 to 10 Oct 2013	Valid
	GW-RS1342-12	21 Dec 2012	26 Dec 2012 to 25 Jun 2013	Expired
	GW-RS0175-13	25 Feb 2013	27 Feb 2013 to 13 Aug 2013	Cancelled
	GW-RS0306-13	26 Mar 2013	27 Mar 2013 to 22 Sep 2013	Cancelled
	GW-RS0276-13	19 Mar 2013	19 Mar 2013 to 7 Sep 2013	Cancelled
	GW-RS0231-13	6 Mar 2013	6 Mar 2013 to 21 Aug 2013	Cancelled
	GW-RS0217-13	28 Feb 2013	28 Feb 2013 to 30 Jun 2013	Expired
	GW-RS0463-13	6 May 2013	7 May 2013 to 6 Nov 2013	Cancelled
Registration as a Chemical Waste Producer	WPN: 5213-147-C1169-35	15 Nov 2010	N/A	Valid
Billing Account under Waste Disposal Ordinance	7011553	30 Sep 2010	27 Sep 2010 to 27 Jan 2016	Valid
Billing Account under Waste Disposal Ordinance (Dumping by Vessel)	7011761	10 Oct12	17 Jan 2013 to 16 Apr 2013	Valid
Water Discharge License (TS1)	WT00008780-2011	24 Nov 2011	24 Nov 2011 to 31 Mar 2016	Valid
Water Discharge License (Discharge at CHT area)	WT00012941-2012	10 May 2012	10 May 2012 to 31 May 2014	Valid
Water Discharge License (Discharge at TPCWAE)	WT00011322-2011	15 Dec 2011	15 Dec 2011 to 31 Dec 2013	Valid
Water Discharge License (Discharge at TS4)	WT00011718-2012	16 Jan 2012	16 Jan 2012 to 31 Jan 2014	Valid
Water Discharge License (Discharge at TS2)	WT00014974-2013	10 Jan 2013	10 Jan 2013 to 31 Jan 2015	Valid

Table 3.11 Summary of submission status under FEP-06/364/2009/A

EP Condition	Submission	Date of Submission
Condition 2.6	Management Organization of Main Construction Companies	11 Mar 2011
	Amendment for Management Organization of Main Construction Companies	16 May 2011
Condition 2.7	Works Schedule	15 Mar 2011
Condition 2.8	Location Plan	15 Mar 2011
Condition 2.23	Noise Management Plan	6 May 2011

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- 3.1.9. The current status on licences and/or permits on environmental protection pertinent and submission under FEP-07/364/2009/A for contract no. HY/2009/19 are shown in **Table 3.12** and **Table 3.13**

Table 3.12 Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/19

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-07/364/2009/A	25 Feb 2011	N/A	Valid
Notification of Works Under APCO	326160	24 Jan 2011	N/A	Valid
Registration as a Waste Producer	7012306	10 Feb 2011	N/A	Valid
Registration as Chemical Waste Producer	5213-151-C3654-01	24 Mar 2011	N/A	Valid
Application for Vessel Disposal	7012306	21 July 2011	N/A	Valid
Construction Noise Permit (CNP)	GW-RS0013-13	08 Jan 2013	07 Jul 2013	Expired
	GW-RS0503-13	20 May 2013	21 May 13- 20 Nov 13	Valid
	GW-RS0528-13	16 May 2013	26 May 13- 25 Nov 13	Valid
	GW-RS0286-13	15 Mar 2013	15-Mar-12 to 14 -Sep-13	Cancelled
	GW-RS0046-13	18 Jan 2013	10 Jul 2013	Expired
	GW-RS0365-13	21 Apr 2013	21-Apr-13 to 20-Oct-13	Valid
	GW-RS0337-13	05 May 2013	05-May-13 to 01- Oct-13	Valid
	GW-RS0767-13	11 Jul 2013	11 Jul 13 to 10 Jan 14	Valid
	GW-RS0010-13	08 Jan 2013	08 Jan 12 to 07 Jul 13	Cancelled
	GW-RS0706-13	11 Jul 201	11 Jul 13 to 10 Jan 14	Valid
	GW-RS0724-13	08 Jul 2013	08 Jul 13 to 07 Jan 14	Valid
Water Discharge Licence	WT00010093-2011	31-Aug-11	30-Sep-16	Cancelled
	WT00010093-2011	17-Aug-12	30-Sep-16	Valid
	WT00010865-2011	3-Nov-11	30-Nov-16	Valid

Table 3.13 Summary of submission status under FEP-07/364/2009/A

EP Condition	Submission	Date of Submission
Condition 2.13	Landscape Plan (Rev.2)	29 July 2012
Condition 2.9	Noise Management Plan (Rev.3)	15 March 2013

Contract no. HK/2010/06 - Wan Chai Development Phase II – Central –Wanchai Bypass over MTR Tsuen Wan Line

3.1.10. The current status on licences and/or permits on environmental protection pertinent and submission under FEP-08/364/2009/A for contract no. HK/2010/06 showed in **Table 3.14** and **Table 3.15**.

Table 3.14 Cumulative Summary of Valid Licences and Permits under Contract no. HK/2010/06

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-08/364/2009/A	15 June 2012	N/A	Valid
Notification of Works Under APCO	326344	18 Jan 2011	N/A	Valid
Construction Noise Permit (CNP)	GW-RS0056-13	14 Jan 2013	16 Jan 2013 – 12 Jul 2013	Expired
	GW-RS0681-13	26 Jun 2013	13 Jul 2013 – 12 Jan 2014	Valid

Table 3.15 Summary of submission status under FEP-08/364/2009

EP Condition	Submission	Date of Submission
	Acknowledgement letter of FEP-08/364/2009A	14 Aug 2012
Condition 2.9	Noise Management Plan	26 Nov 2012

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

3.1.11 The current status on licences and/or permits on environmental protection pertinent and submission under FEP-09/264/2009/B for contract no. HK/2012/08 showed in **Table 3.16 and Table 3.17**

Table 3.16 Cumulative Summary of Valid Licences and Permits under Contract no. HK/2012/08

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-09/364/2009/B	5 March 2013	N/A	Valid
Notification of Works Under APCO	355439	4 Feb 2013	N/A	Valid
Registration as a Chemical Waste Producer	5213-134-C3790-01	8 Mar 2013	N/A	Valid
Billing Account under Waste Disposal Ordinance	7016883	18 Feb 2013	18 Jul 2017	Valid

Table 3.17 Summary of submission status under FEP-09/364/2009

EP Condition	Submission	Date of Submission
Condition 2.9	Noise Management Plan (Rev.2)	9 July 2013
Condition 2.14	Landscape Plan (Rev.1)	31 May 2013

Contract no. HY/2010/08 –Central – Wanchai Bypass Tunnel – Tunnel (Slip Road 8)

3.1.12 The current status on licences and/or permits on environmental protection pertinent and submission under FEP-09/264/2009/B for contract no. HK/2012/08 showed in **Table 3.18**

Table 3.18 Cumulative Summary of Valid Licences and Permits under Contract no. HY/2010/08

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-10/364/2009/B	2013-07-26	NA	Valid
Notification of Works Under APCO	357176	2013-04-02	NIL	Valid
Registration as a Chemical Waste Producer	WPN5213-147-C1169-44	2013-03-27	NIL	Valid
Billing Account under Waste Disposal Ordinance	7017170	2013-03-27	NIL	Valid
Water Discharge License	WT0001651-2013	2013-04-26	NIL	Valid
Construction Noise Permit (CNP)	GW-RS0672-13	2013-06-21	2013-06-25 to 2013-08-24	Valid
	GW-RS0668-13	2013-06-21	2013-06-24 to 2013-08-23	Valid
	GW-RS0691-13	2013-06-24	2013-06-26 to 2013-08-25	Valid
	GW-RS0816-13	2013-07-30	2013-07-30 to 2013-10-29	Valid

4 Monitoring Requirements

4.1 Noise Monitoring

NOISE MONITORING STATIONS

- 4.1.1. The noise monitoring stations for the Project are listed and shown in **Table 4.1** and **Figure 4.1**. **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

Table 4.1 Noise Monitoring Stations

Station	Description
M1a	Harbour Road Sports Centre
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School
*M7e	International Finance Centre (Eastern End of Podium)
M7w	International Finance Centre (Western End of Podium)
*M8	City Hall

* Remark 1: Location ID has been updated from M7 to M8 for City Hall

* Remark 2: M7e has become a reference station starting from 7 Aug 2012

REAL TIME NOISE MONITORING STATIONS

- 4.1.2. Review of feasibility on the real time noise monitoring stations was conducted in July with IEC. Station, RTN1a, Tung Lo Wan fireboat Station was found not appropriate to be a monitoring station for monitoring the IECL Piling works and Demolition after visited.
- 4.1.3. The noise monitoring stations for the Project are listed and shown in **Table 4.2** and **Figure 4.1**. **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

Table 4.2 Real Time Noise Monitoring Stations

District	Station	Description
Tin Hau	RTN1	FEHD Hong Kong Transport Section Whitfield Depot
North Point	RTN2a	Electric Centre
North Point	RTN3	Po Leung Kuk Yu Lee Mo Fan Memorial School
Tin Hau	RTN4	Causeway Bay Community Centre

NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.1.4. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). L_{eq} (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods, L_{eq} (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. Supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.
- 4.1.5. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
- One set of measurements between 0700 and 1900 hours on normal weekdays.
- 4.1.6. Real time noise shall be carried out at the designated monitoring stations. The following is an initial guide on the regular monitoring frequency for each station on a 24 hours daily basis when noise generating activities are underway:
- One set of measurements between 0700 and 1900 hours on normal weekdays.
 - One set of measurements between 1900 and 2300 hours on normal weekdays and 0700 and 2300 hours on public holidays.
 - One set of measurements between 2300 and 0700 hours on next day on everyday.
- 4.1.7. If construction works are extended to include works during the hours of 1900 – 0700 as well as public holidays and Sundays, additional weekly impact monitoring shall be carried out during respective restricted hours periods. Applicable permits under NCO shall be obtained by the Contractor.

MONITORING EQUIPMENT

- 4.1.8. As referred to in the Technical Memorandum TM issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.
- 4.1.9. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.
- 4.1.10. The sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency before deployment to the site and during each site visit. Measurements will be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.

Air Monitoring

AIR QUALITY MONITORING STATIONS

- 4.2.1. The air monitoring stations for the Project are listed and shown in **Table 4.3** and **Figure 4.1**. **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

Table 4.3 Air Monitoring Stations

Station ID	Monitoring Location	Description
CMA1b	Oil Street Site Office**	North Point (Re-commenced on 14 November 2011)
CMA2a	Causeway Bay Community Centre	Causeway Bay
CMA3a	CWB PRE Site Office *	Causeway Bay
CMA4a	Society for the Prevention of Cruelty to Animals	Wan Chai
CMA5a	Children Garden opposite to Pedestrian Plaza	Wan Chai
MA1e	International Finance Centre (Eastern End of Podium)	Central
MA1w	International Finance Centre (western End of Podium)	Central

Remarks*: As per the ENPC meeting in March 2011, the monitoring stations CMA3a – Future CWB site office at Wanchai Waterfront Promenade was renamed as remark.

Remarks**: The location ID of monitoring station CMA1b was updated as “Oil Street Site Office” in April 2013.

AIR MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 4.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.
- 4.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.

SAMPLING PROCEDURE AND MONITORING EQUIPMENT

4.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:

- 0.6 – 1.7 m³ per minute adjustable flow range;
- Equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
- Installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
- Capable of providing a minimum exposed area of 406 cm²;
- Flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
- Equipped with a shelter to protect the filter and sampler;
- Incorporated with an electronic mass flow rate controller or other equivalent devices;
- Equipped with a flow recorder for continuous monitoring;
- Provided with a peaked roof inlet;
- Incorporated with a manometer;
- Able to hold and seal the filter paper to the sampler housing at horizontal position;
- Easily changeable filter; and
- Capable of operating continuously for a 24-hour period.

4.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

LABORATORY MEASUREMENT / ANALYSIS

4.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.

4.2.8. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.

4.2.9. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.

4.2.10. All the collected samples shall be kept in a good condition for 6 months before disposal.

4.2.11. Current calibration certificates of equipments are presented in **Appendix 4.2.**

5.0 MONITORING RESULTS

5.0.1. The environmental monitoring will be implemented based on the division of works areas of each designated project managed under different contracts with separate FEP applied by individual contractors. Overall layout showing work areas of various contracts, latest status of work commencement and monitoring stations is shown in **Figure 2.1** and **Figure 4.1**. The monitoring results are presented in according to the Individual Contract(s).

5.0.2. In the reporting month, the concurrent contracts are as follows:

- Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A
- Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A
- Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009
- Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre
- Contract no. HK/2009/02 - Wan Chai Development Phase II – Central - Wan Chai Bypass at Wan Chai East
- Contract no. HK/2010/06 - Wan Chai Development Phase II – Central - Wan Chai Bypass over MTR Tsuen Wan Line
- Contract no. HK/2012/08 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai West

5.0.3. The environment monitoring schedules for reporting month and coming month are presented in **Appendix 5.1**.

5.1 Noise Monitoring Results

5.1.1 Monitoring for report of review baseline noise level was performed from 11 April 2011 to 8 June 2011. Then the report was submitted on the 20 June 2011, verified by IEC on 18 July 2011 and was approved by ER by January 2012. The new baseline is used for the noise calculation starting from January 2012.

Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- 5.1.2 Noise monitoring for the Central Interchange works under contract no. HY/2009/18 was commenced on 22 April 2011. The proposed division of noise monitoring stations for Contract no. HY/2009/18 are summarized in **Table 5.2** below:

Table 5.2 Noise Monitoring Stations for Contract no. HY/2009/18

Station	Description
*M7e	International Finance Centre (Eastern End of Podium)
M7w	International Finance Centre (Western End of Podium)
M8	City Hall

* Remark: M7e has become a reference station starting from 7 Aug 2012

- 5.1.3 No action and limit level exceedance was recorded in this reporting month.
- 5.1.4 Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in **Appendix 5.2**.

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre – Tunnel Works under FEP-02/364/2009 and Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

- 5.1.5 The commencement of construction works for Contract no. HK/2009/01 under FEP-02/364/2009 is on 25 August 2011 and HK/2009/02 under FEP-01/364/2009 is on 26 April 2011. The proposed division of noise monitoring stations are summarized in **Table 5.3** below.

Table 5.3 Noise Monitoring Station for Contract no HK/2009/01 and HK/2009/02

Station	Description
M1a	Harbour Road Sports Centre

- 5.1.6 No action or limit level exceedance was recorded in this reporting month.
- 5.1.7 Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in **Appendix 5.2**.

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- 5.1.8 The commencement of construction works for Contract no. HY/2009/15 under FEP-06/364/2009/A was on 13 July 2011. Noise monitoring was commenced on 13 July 2011. The proposed divisions of noise monitoring stations are summarized in **Table 5.4** below.

Table 5.4 Noise Monitoring Stations for Contract no. HY/2009/15

Station	Description
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station

- 5.1.9 No action or limit level exceedance was recorded in this reporting month.
- 5.1.10 Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in **Appendix 5.2**.

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- 5.1.11 Noise monitoring for the tunnel works under contract no. HY/2009/19 was commenced on 24 April 2011. The proposed division of noise monitoring stations are summarized in **Table 5.5** below.

Table 5.5 Noise Monitoring Stations for Contract no. HY/2009/19

Station	Description
M3a	Tung Lo Wan Fire Station
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School

- 5.1.12 Two limit level exceedances were recorded on 9 and 16 July 2013 at M6 – HK Baptist Church Henrietta Secondary School in the reporting month.
- 5.1.13 Major traffic noise observed during monitoring on 9 and 16 July 2013 and it was considered as the major noise contribution. As such, the limit level exceedances were concluded as non-project related.
- 5.1.14 Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in **Appendix 5.2**. Details of the Notification of Exceedance can be referred in **Appendix 6.2**.

5.2 Real Time Noise Monitoring Results

- 5.2.1. As confirmed by CWB RSS, the IECL parapet removal operations and associated construction work will commence in June 2013. Liaison was conducted with HK Baptist Church Henrietta Secondary School, Po Leung Kuk Yu Lee Mo Fan Memorial School and Causeway Bay Community Centre regarding the set up of RTN3 real time noise monitoring station.
- 5.2.2. Causeway Bay Community Centre has granted permission for set up on 21 Dec 2012 and station set up was performed on 27 Dec 2012. The Baseline noise level of RTN4- Causeway Bay Community Centre will adopt the results from the baseline noise monitoring report for EP/364/2009 in 22 April 2010 in which approved by EPD.
- 5.2.3. Real time noise monitoring at RTN4-Causeway Bay Community Centre was commenced on 13 Jan 2013.
- 5.2.4. Po Leung Kuk Yu Lee Mo Fan Memorial School grant permission for set up on 4 Sep 2012 and station set up was performed on 14 Sep 2012. Real time noise baseline capturing was conducted during time period without construction work from 21 Sep 2012 to 04 Oct 2012.
- 5.2.5. Real time noise monitoring at RTN3 – Po Leung Kuk Yu Lee Mo Fan Memorial School was commenced since 06 Oct 2012.
- 5.2.6. Oil Street Community Liaison Centre was confirmed to be demolished in mid-October by CWB RSS. This presented a need for relocation of RTN2 – Oil Street Community Liaison Centre. After liaison with Hong Kong Electric, permission was granted on 21 Sep 2012 for real time noise monitoring set up at City Garden Electric Centre (RTN2a – Electric Centre), which is a representative of the noise sensitive receiver City Garden.
- 5.2.7. RTN2 previously located at oil Street Community Liaison Centre was relocated to Hong Kong Electric Centre on 5 Oct 2012, which is a representative of the noise sensitive receiver City Garden. The baseline noise level of RTN2a will adopt the results derived from the baseline noise monitoring conducted at Electric Centre from 4 December 2009 to 17 December 2009.
- 5.2.8. Real-time noise monitoring station RTN1-FEHD Whitfield Depot was finely adjusted from 2/F to roof-top at FEHD Whitfield Depot on 24 June 2013 with respect to the commencement of advance works for IEC parapet demolition.

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- 5.2.9. The proposed division of noise monitoring stations are summarized in **Table 5.7** below. Real time noise monitoring for major construction works under contract no. HY/2009/19 was commenced on 24 April 2011.

Table 5.7 Real Time Noise Monitoring Stations for Contract no. HY/2009/19

Location ID	District	Description
RTN1	Tin Hau	FEHD Hong Kong Transport Section Whitfield Depot
RTN2a	North Point	Electric Centre
RTN3	North Point	Po Leung Kuk Yu Lee Mo Fan Memorial School
RTN4	Tin Hau	Causeway Bay Community Centre

** Real time noise monitoring results and graphical presentation during night time period are for information only.*

**Real-time noise monitoring results and graphical presentation for RTN3 during restricted hours are for information only as no night classes were conducted at the educational institute.*

- 5.2.10. Limit level exceedances were recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot during restricted hours on 14 July 2013. After checking with contractor, no construction works was conducted at the concerned location during the recorded period. As such, the exceedances were considered not contributed by the project works but due to the nearby IEC traffic.
- 5.2.11. Limit level exceedance was recorded at RTN2a-Electric Centre during restricted hours on 14 July 2013. After checking with contractor, no construction work was conducted at the concerned location during the recorded period. As such, the exceedances were considered to be contributed by near by IEC traffic.
- 5.2.12. Limit level exceedance was recorded at RTN3-Yue Lee Mo Fan Memorial School during restricted hours on 14 July 2013. After checking with contractor, no construction work was conducted at the concerned location during the recorded period. As such, the exceedances were considered to be contributed by near by IEC traffic.
- 5.2.13. No limit level exceedance was recorded at RTN4-Causeway Bay Community Centre in the reporting month.
- 5.2.14. Real time noise monitoring results measured in this reporting period are reviewed and summarized. Details of real time noise monitoring results and graphical presentation can be referred to **Appendix 5.4.**

5.3 Air Monitoring Results

- 5.3.1 Due to interruption of electricity supply, the 24hr TSP monitoring at CMA5a was rescheduled from 3 July 2013 to 4 July 2013.

Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- 5.3.2 Air monitoring for the Central Interchange works under contract no. HY/2009/18 was commenced on 21 April 2011. The proposed division of air monitoring stations are summarized in **Table 5.9** below.

Table 5.9 Air Monitoring Stations for Contract no. HY/2009/18

Station	Description
MA1e	International Finance Centre (Eastern End of Podium)
MA1w	International Finance Centre (Western End of Podium)

- 5.3.3 No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in [Appendix 5.3](#).

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre – Tunnel Works under FEP-02/364/2009

- 5.3.4 The commencement of construction works for Contract no. HK/2009/01 under FEP-02/364/2009 is on 25 August 2011. Air quality monitoring was commenced on 25 August 2011. The proposed division of air monitoring stations are summarized in **Table 5.10** below.

Table 5.10 Air Monitoring Station for Contract no. HK/2009/01

Station	Description
CMA5a	Children Playgrounds opposite to Pedestrian Plaza

- 5.3.5 No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in [Appendix 5.3](#).

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

- 5.3.6 The commencement of construction works for HK/2009/02 under FEP-01/364/2009 is on 26 April 2011. The proposed division of air monitoring stations are summarized in **Table 5.11** below.

Table 5.11 Air Monitoring Station for Contract no. HK/2009/02

Station	Description
CMA4a	Society for the Prevention of Cruelty to Animals

- 5.3.7 No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in [Appendix 5.3](#).

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- 5.3.8 The commencement of construction works for Contract no. HY/2009/15 under FEP-06/364/2009/A was on 13 July 2011. Air quality monitoring was commenced on 14 July 2011. The proposed division of air monitoring stations are summarized in **Table 5.12** below.

Table 5.12 Air Monitoring Station for Contract no. HY/2009/15

Station	Description
CMA3a	CWB PRE Site Office

- 5.3.9 No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in **Appendix 5.3**.

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- 5.3.10 The proposed division of air monitoring stations are summarized in **Table 5.13** below. Air monitoring for the tunnel works under contract no. HY/2009/19 was commenced on 26 April 2011.

Table 5.13 Air Monitoring Stations for Contract no. HY/2009/19

Station	Description
CMA1b	Oil Street Site Office
CMA2a	Causeway Bay Community Centre

- 5.3.11 No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in **Appendix 5.3**.

5.4 Waste Monitoring Results

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre – Tunnel Works under FEP-02/364/2009

- 5.4.1. Inert C&D wastes and non-inert C&D wastes were disposed in this reporting month. Details of the waste flow table are summarized in **Table 5.15**.

Table 5.15 Details of Waste Disposal for Contract no. HK/2009/01

Waste Type	Quantity this month, m ³	Cumulative-to-Date, m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	306.77	29665.015	TKO137, TM38
Inert C&D materials recycled	Nil	5104.5	N/A
Non-inert C&D materials disposed	29.00	1332.16	SENT Landfill

Waste Type	Quantity this month, m ³	Cumulative-to-Date, m ³	Disposal / Dumping Grounds
Non-inert C&D materials recycled	Nil	205943	N/A
Chemical waste disposed	200	9950	N/A

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

5.4.2. Inert C&D & non-inert C&D wastes were disposed of in this reporting month. Details of the waste flow table are summarized in **Table 5.16**.

Table 5.16 Details of Waste Disposal for Contract no. HK/2009/02

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds	Remarks
Inert C&D materials disposed, m ³	557.075	237620.045	TKO137 / TM 38	N/A
Inert C&D materials recycled, m ³	Nil	18161	n/a	N/A
Non-inert C&D materials disposed, m ³	52.76	1020.44	SENT Landfill	N/A
Non-inert C&D materials recycled, m ³	N/A	N/A	N/A	N/A
Chemical waste disposed, kg	Nil	7971	SENT Landfill	N/A

Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

5.4.3. Inert C&D and non-inert C&D waste was disposed of in this reporting month. Details of the waste flow table are summarized in **Table 5.17**.

Table 5.17 Details of Waste Disposal for Contract no. HY/2009/18

Waste Type*	Quantity this month, (m3)	Cumulative-to-Date, (m3)	Disposal / Dumping Grounds
Inert C&D materials disposed	2400	97071	T.K.O. 137, TM 38
Inert C&D materials recycled	0	56223	N/A
Non-inert C&D materials disposed	99	1272	SENT Landfill
Non-inert C&D materials recycled (tonnes)	0	77.87	N/A
Chemical waste disposed (kg)	650	4215	N/A

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- 5.4.4. Inert & Non-inert C&D wastes were disposed of in this reporting month. Details of the waste flow table are summarized in **Table 5.18**.

Table 5.18 Details of Waste Disposal for Contract no. HY/2009/15

Waste Type	Quantity this month(m ³)	Cumulative Quantity-to-Date(m ³)	Disposal / Dumping Grounds
Inert C&D materials disposed, m ³	16834.1 4918.2	369504.2 212196.5	Tuen Mun Area 38 TKO137 FB
Inert C&D materials recycled, m ³	Nil	217596.2	HY/2009/11 ex-PCWA TS4 TS2 WDII Lun Ku Tan
Non-inert C&D materials disposed, m ³	41.3	904	SENT Landfill
Non-inert C&D materials recycled, m ³	308.4	543354.2	Xun Xiang Metalware Skylight Recycle (paper)
Chemical waste disposed, kg	72	17555	Dunwell Group

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- 5.4.5. Inert and Non-inert C&D wastes were disposed of in this reporting month. Details of the waste flow table are summarized in **Table 5.19**.

Table 5.19 Details of Waste Disposal for Contract no. HY/2009/19

Waste Type*	Quantity this month, m ³	Cumulative-to-Date, m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	23190.35	322649.31	N/A
Inert C&D materials recycled	0	54001.81	N/A
Non-inert C&D materials disposed	20.86	872.78	SENT Landfill
Non-inert C&D materials recycled	0	297.52	N/A
Chemical waste disposed	0	4.59	N/A

Contract no. HK/2010/06 Wan Chai Development Phase II - Central-Wan Chai Bypass over MTR Tsuen Wan Line under FEP-08/364/2009/A

- 5.4.6. No inert and Non-inert C&D wastes were disposed of in this reporting month. Details of the waste flow table are summarized in **Table 5.20**.

Table 5.20 Details of Waste Disposal for Contract no. HK/2010/06

Waste Type*	Quantity this month, m ³	Cumulative-to-Date, m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	NIL	NIL	TM38
Inert C&D materials recycled	NIL	NIL	N/A
Non-inert C&D materials disposed	NIL	NIL	N/A
Non-inert C&D materials recycled	NIL	NIL	Recyclers
Chemical waste disposed	NIL	NIL	N/A

Contract no. HK/2012/08 Wan Chai Development Phase II - Central-Wan Chai Bypass at Wan Chai West under FEP-09/364/2009/B

- 5.4.7. No inert and Non-inert C&D wastes were disposed of in this reporting month. Details of the waste flow table are summarized in **Table 5.21**.

Table 5.21 Details of Waste Disposal for Contract no. HK/2012/08

Waste Type*	Quantity this month, m ³	Cumulative-to-Date, m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	Nil	Nil	N/A
Inert C&D materials recycled	Nil	Nil	N/A
Non-inert C&D materials disposed	Nil	Nil	N/A
Non-inert C&D materials recycled	Nil	Nil	N/A
Chemical waste disposed	Nil	Nil	N/A

Contract no. HY/2010/08 Central – Wan Chai Bypass (CWB) – Tunnel (Slip Road 8) under FEP-10/364/2009/B

- 5.4.8. No inert and Non-inert C&D wastes were disposed of in this reporting month. Details of the waste flow table are summarized in **Table 5.22**.

Table 5.22 Details of Waste Disposal for Contract no. HY/2010/08

Waste Type*	Quantity this month, m ³	Cumulative-to-Date, m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	217	668	TM 38
Inert C&D materials recycled	Nil	Nil	Nil
Non-inert C&D materials disposed	11	22	SENT
Non-inert C&D materials recycled	Nil	Nil	Nil
Chemical waste disposed	Nil	Nil	Nil

6 Compliance Audit

- 6.0.1. The Event Action Plan for construction noise, air qualities are presented in **Appendix 6.1**.

6.1 Noise Monitoring

Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- 6.1.1. No exceedance was recorded in the reporting month.

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention Exhibition Centre – Tunnel Works under FEP-02/364/2009

- 6.1.2. No exceedance was recorded in the reporting month.

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

- 6.1.3. No exceedance was recorded in the reporting month.

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- 6.1.4. No exceedance was recorded in the reporting month.

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- 6.1.5. Two limit level exceedances were recorded on 9 and 16 July 2013 at M6 – HK Baptist Church Henrietta Secondary School in the reporting month. Investigations found that on 9 and 16 July 2013, major traffic noise was contributed in the noise monitoring and exceedances were not related to the Project.

Real Time Noise Monitoring

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- 6.1.6. Non project related limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot on 14 July 2013. Investigation found that exceedances were contributed by IEC traffic.
- 6.1.7. Non project related limit level exceedance was recorded at RTN2a- Electric Centre on 14 July 2013. Investigation found that exceedances were contributed by IEC traffic.
- 6.1.8. Non project related limit level exceedance was recorded at RTN3- Yue Lee Mo Fan Memorial School on 14 July 2013. Investigation found that exceedances were contributed by IEC traffic.
- 6.1.9. No limit level exceedances were recorded at RTN4- Causeway Bay Community Centre in this reporting month.

6.2 Air Monitoring

Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- 6.2.1. No exceedance was recorded in the reporting month.

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre – Tunnel Works under FEP-02/364/2009

- 6.2.2. No exceedance was recorded in the reporting month.

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

- 6.2.3. No exceedance was recorded in the reporting month.

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) FEP-06/364/2009/A

- 6.2.4. No exceedance was recorded in the reporting month.

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- 6.2.1. No exceedance was recorded in the reporting month.

6.3 Review of the Reasons for and the Implications of Non-compliance

- 6.3.1. There was no non-compliance from the site audits in the reporting period. The observations and recommendations made in each individual site audit session were presented in Section 8.
- 6.3.2. No project-related non-compliance from monitoring was recorded in the reporting month.

6.4 Summary of action taken in the event of and follow-up on non-compliance

- 6.4.1 There was no particular action taken since no non-compliance was recorded from the site audits in the reporting period.

7 Cumulative Construction Impact due to the Concurrent Projects

- 7.0.1. According to Condition 3.4 of the EP-364/2009/B, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) and Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel).
- 7.0.2. [According to the Monthly EM&A report \(June 2013\) of Central Reclamation Phase III \(CRIII\), Underground drainage and footpath construction, modification to the junction of Road D8 and Road P2 and modification of timber decks at advance promenade were performed in the July 2013 reporting month.](#) The water quality monitoring was completed in October 2011 and no Project-related exceedance was recorded for air and noise monitoring. It can be concluded that cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was insignificant.
- 7.0.3. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activity under Wan Chai Development Phase II were marine works at HKCEC areas, cross-harbour Watermains, Fresh Watermains and Cooling Watermains Installations, tunnel works at Wan Chai East, [ELS work and pipe roofing works at TS4 and cut and cover tunnel construction at TPCWAE](#). Excavation and tunnel works at Central Interchange, ELS and box culvert construction at North Point area. The major environmental impact was water quality impact at Causeway Bay and Wan Chai. Land-based construction activities were diaphragm wall construction at TS2, [ELS work and pipe roofing works at TS4, cut and cover tunnel construction at TPCWAE](#), tunnel works at Central and ELS work at North Point and tunnel works at Wan Chai East in the reporting month.
- 7.0.4. The major environmental impacts generated from tunnel works at Central and tunnel works at Wan Chai East, IECL and Causeway Bay Typhoon Shelter were undertaken in the reporting month. No significant air impact from construction activities was anticipated in the reporting month. Besides, no project-related exceedances were recorded during the air and noise environmental monitoring events in the reporting month. Thus, it is evaluated that the cumulative construction impact from the concurrent projects including Wan Chai Development Phase II was insignificant.

8 Environmental Site Audit

8.0.1. During this reporting month, weekly environmental site audits were conducted for Contracts no. HY/2009/15, HY/2009/18, HY/2009/19, HK/2012/08, HK/2009/01, HK/2009/02, HY/2010/08 and HK/2010/06. No non-conformance was identified during the site audits. The Contractors rectified major observations and recommendations made during the audit sessions. No non-conformance was identified during the site inspections.

8.0.2. Four site inspections for Contract no. HY/2009/15 was carried out during this reporting period. The results of these inspections and outcomes are summarized in **Table 8.1**.

Table 8.1 Summary of Environmental Inspections for Contract no. HY/2009/15

Date	Item	Observations	Action taken by Contractor	Outcome
130702_01	2-Jul-13	The contractor should critically review the wastewater treatment procedure to avoid muddy discharge (TS2 Eastern Side)	No further muddy discharge was observed	Completion as observed 9 July 2013
130702_01	2-Jul-13	Provide three side and top side enclosure for mixing station (Ex-PWCA)	Three sides and top side enclosure was provided	Completion as observed 9 July 2013
130709_01	9-Jul-13	Oil Stain should be cleared as chemical waste (TS1)	Oil stain was cleared	Completion as observed on 16 July 2013
130709_02	9-Jul-13	Provide drip tray to oil drums	Drip trays were provided	Completion as observed on 16 July 2013
130716_01	16-Jul-13	Drip tray should be provided to oil drums and used chemical container should be properly stored as chemical waste (TS4)	Drip tray was provided	Completion as observed on 23 July 2013
130716_02	16-Jul-13	Review the wastewater treatment process to avoid milky discharge (TS2)	No further milky discharge was observed	Completion as observed on 23 July 2013
130723_01	23-Jul-13	Clear leaked oil as chemical waste	Leaked oil was cleared as chemical waste.	Completion as observed on 30 July 2013

8.0.3. Four site inspections for Contract no. HY/2009/18 was carried out during this reporting period. The results of these inspections and outcomes are summarized in **Table 8.2**.

Table 8.2 Summary of Environmental Inspections for Contract no. HY/2009/18

Date	Item	Observations	Action taken by Contractor	Outcome
130713_01	19-Jul-13	Clear the leaked oil as chemical waste	Leaked oil are treated as chemical waste	Completed as observed on 25 July 2013

8.0.4. Four site inspections for Contract no. HY/2009/19 was carried out during this reporting period. No observation was found in the reporting month.

8.0.5. Four site inspections for Contract no. HK/2009/01 was carried out during this reporting period. The results of these inspections and outcomes are summarized in **Table 8.3**

Table 8.3 Summary of Environmental Inspections for Contract no. HK/2009/01

Item	Date	Observations	Action taken by Contractor	Outcome
130703_01	3-Jul-13	Oil stain found on the ground. Oil should be prevented from leakage on the ground (East Bridge)	Oil stain was removed.	Completion as observed on 10 July 2013
130718_01	18-Jul-13	Oil stain was found under backhoe, boring machine. Oil stain should be cleared as chemical waste (Convention avenue, Water channel, Expo drive West)	Oil stain was removed.	Completion as observed on 24 July 2013
130724_01	24-Jul-13	Material should be prevented from spillage into the public road (Expo Drive East)	No further spillage was observed.	Completion as observed on 31 July 2013

8.0.6. Four site inspections for Contract no. HK/2009/02 was carried out during this reporting period. The results of these inspections and outcomes are summarized in **Table 8.4**

Table 8.4 Summary of Environmental Inspections for Contract no. HK/2009/02

Item	Date	Observations	Action taken by Contractor	Outcome
130704_01	4-Jul-13	Stockpile should be properly covered (Hung Hing Road)	covering was provided to the stockpile	Completion as observed on 11 July 2013
130725_01	25-Jul-13	Chemical container should be properly stored or cleared as chemical waste	The chemical container was removed	Completion as observed on 1 Aug 2013

8.0.7. Four site inspections for Contract no. HK/2010/06 was carried out during this reporting period. No observation was found in the reporting month.

8.0.8. Four site inspection for Contract no. HK/2012/08 was carried out during this reporting period. The results of these inspections and outcomes are summarized in **Table 8.5**

Table 8.5 Summary of Environmental Inspections for Contract no. HK/2012/08

Item	Date	Observations	Action taken by Contractor	Outcome
130723_01	23-Jul-13	Refuse floating on the sea should be cleared more frequently	Floating refuses were cleared	Completion as observed on 30 July 2013

8.0.9. Four site inspection for Contract no. HY/2010/08 was carried out during this reporting period. No observation was found in the reporting month.

9 COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION

- 9.0.1. No environmental complaints were received in the reporting period.
- 9.0.2. The details of cumulative complaint log and updated summary of complaints are presented in **Appendix 9.1**
- 9.0.3. Cumulative statistic on complaints and successful prosecutions are summarized in **Table 9.1** and **Table 9.2** respectively.

Table 9.1 Cumulative Statistics on Complaints

Reporting Period	No. of Complaints
July 2013	0
Sep 2010 – June 2013	22
Total	22

Table 9.2 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative No. Project-to-Date
Air	-	0	0
Noise	-	0	0
Water	-	0	0
Waste	-	0	0
Total	-	0	0

10 CONCLUSION

10.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.

10.0.2. The scheduled construction activities and the recommended mitigation measures for the coming month are listed in **Table 10.1**. The construction programmes of individual contracts are provided in **Appendix 10.1**.

Table 10.1 Summary of Key Construction Activities of Individual Contract(s) to be commenced in Coming Reporting Month

Contract No.	Key Construction Works	Recommended Mitigation Measures
HY/2009/15	• ELS works, pipe roofing works and tunnel construction at TS4 • Cut and cover tunnel construction at TPCWAE • Construction of OHVD at TS1 • Excavation and tunnel lining construction for mined tunnel • Post Diaphragm Wall Works, ELS works and Installation of King Post at TS2	• Watering any dust generating activities • Well maintained enclosures for grouting mixing plants. • Noise control measures shall be provided during restricted hours • Provide protection works and adequate drainage system to ensure no direct discharge into public drainage system or the sea
HY/2009/18	• Excavation of trial pit • Transplanting of trees • Hoarding erection and modification • Installation of couplers, UU detection, trial trench, pre-drilling • Excavation • Drainage works • Tunnel works • Trough structure construction and associated drilling and grouting • Road works • OHVD installation • Bridges construction • Scaffolding / false-work erection • Profile barrier construction	• Noise barrier shall be implemented; and • Noise level shall be controlled by reducing piling rate and no. of plants working in parallel. • Dust control during dust generating activities • Provide protection works to ensure no runoff out of site area or direct discharge into public drainage system. • Appropriate plants and measures should be taken to ensure adequate protections are provided for trees being transplanted.

HY2009/19	• Road works at Watson Road • Bored piling (Land) • D-wall and Barrette Construction • Construction works for Box Culvert T1 • Construction of Pile cap (Land) • Demolition of parapet at IEC Link • Construction of dewatering well for Cut & Cover Tunnel • Removal of marine platform • Construction of pile cap, column & cross head (Marine) • ELS for Cut & Cover Tunnel • Installation of dewatering well • Laying of 1500 pipe • Launching of segments • Unloading segments from derrick • Extraction of temporary pile from marine section	• Noise level shall be controlled by reducing the breaking operation rate. • Noise barrier shall be implemented. • Dust control during dust generating works • Provide protection works and adequate drainage system to ensure no direct discharge into public drainage system or the sea.
HK2009/01	• Installation of pre-bored H-pile in CWB Stage 2 Atrium Link. • Filling of the existing open water channel and Dome • Construction of the south Common D-wall. • Demolition of the Promenade Deck. • Installation of dewatering wells, observation wells and piezometers at CWB stage 1 • ELS for Stage 1 CWB	• Noise level shall be controlled by reducing no. of plants working in parallel. • Well maintained enclosures for grouting mixing plants. • Provide protection works and adequate drainage system to ensure no direct discharge into public drainage system or the sea. • Dust control during dust generating works
HK/2009/02	• Continue wall construction at Tunnel Portion 1. • Commence D-Wall construction at Tunnel Portion 2	• Dust control during dust generating works • Provision of protection to ensure no runoff out of site area or direct discharge into public drainage system.

HK/2010/06	• Stitching Works • Foam Concreting Works • Other Miscellaneous Works in precast unit	• Dust control during dust generating works.
HK/2012/08	• Hoarding erection	• Dust control during dust generating works • Provide protection works and adequate drainage system to ensure no direct discharge into public drainage system.
HY/2010/08	• Tree Pruning works • Tree removal works, • Tree transplanting works, • Instrumentation works, • Ground investigation works, • Erection of site hoarding and • Concrete works.	• Provide protection works and adequate drainage system to ensure no direct discharge into public drainage system. • Provide necessary protection to trees retained on site. • Dust control during dust generating works


10.0.3. The construction works of Contract no. 04/HY/2006 – Reconstruction of Bus Terminus near Man Yiu Street and Man Kwong Street under FEP-04/364/2009/A was completed, and the FEP was surrendered by the Contractor on 11 February 2011.

10.0.4. The construction works of Contract no. HY/2009/17 - Advance piling works at Whitfield Depot under FEP-03/264/2009 was completed, and the FEP was surrendered by the Contractor and found in order by EPD on 25 April 2013.



Figure 2.1

Project Layout

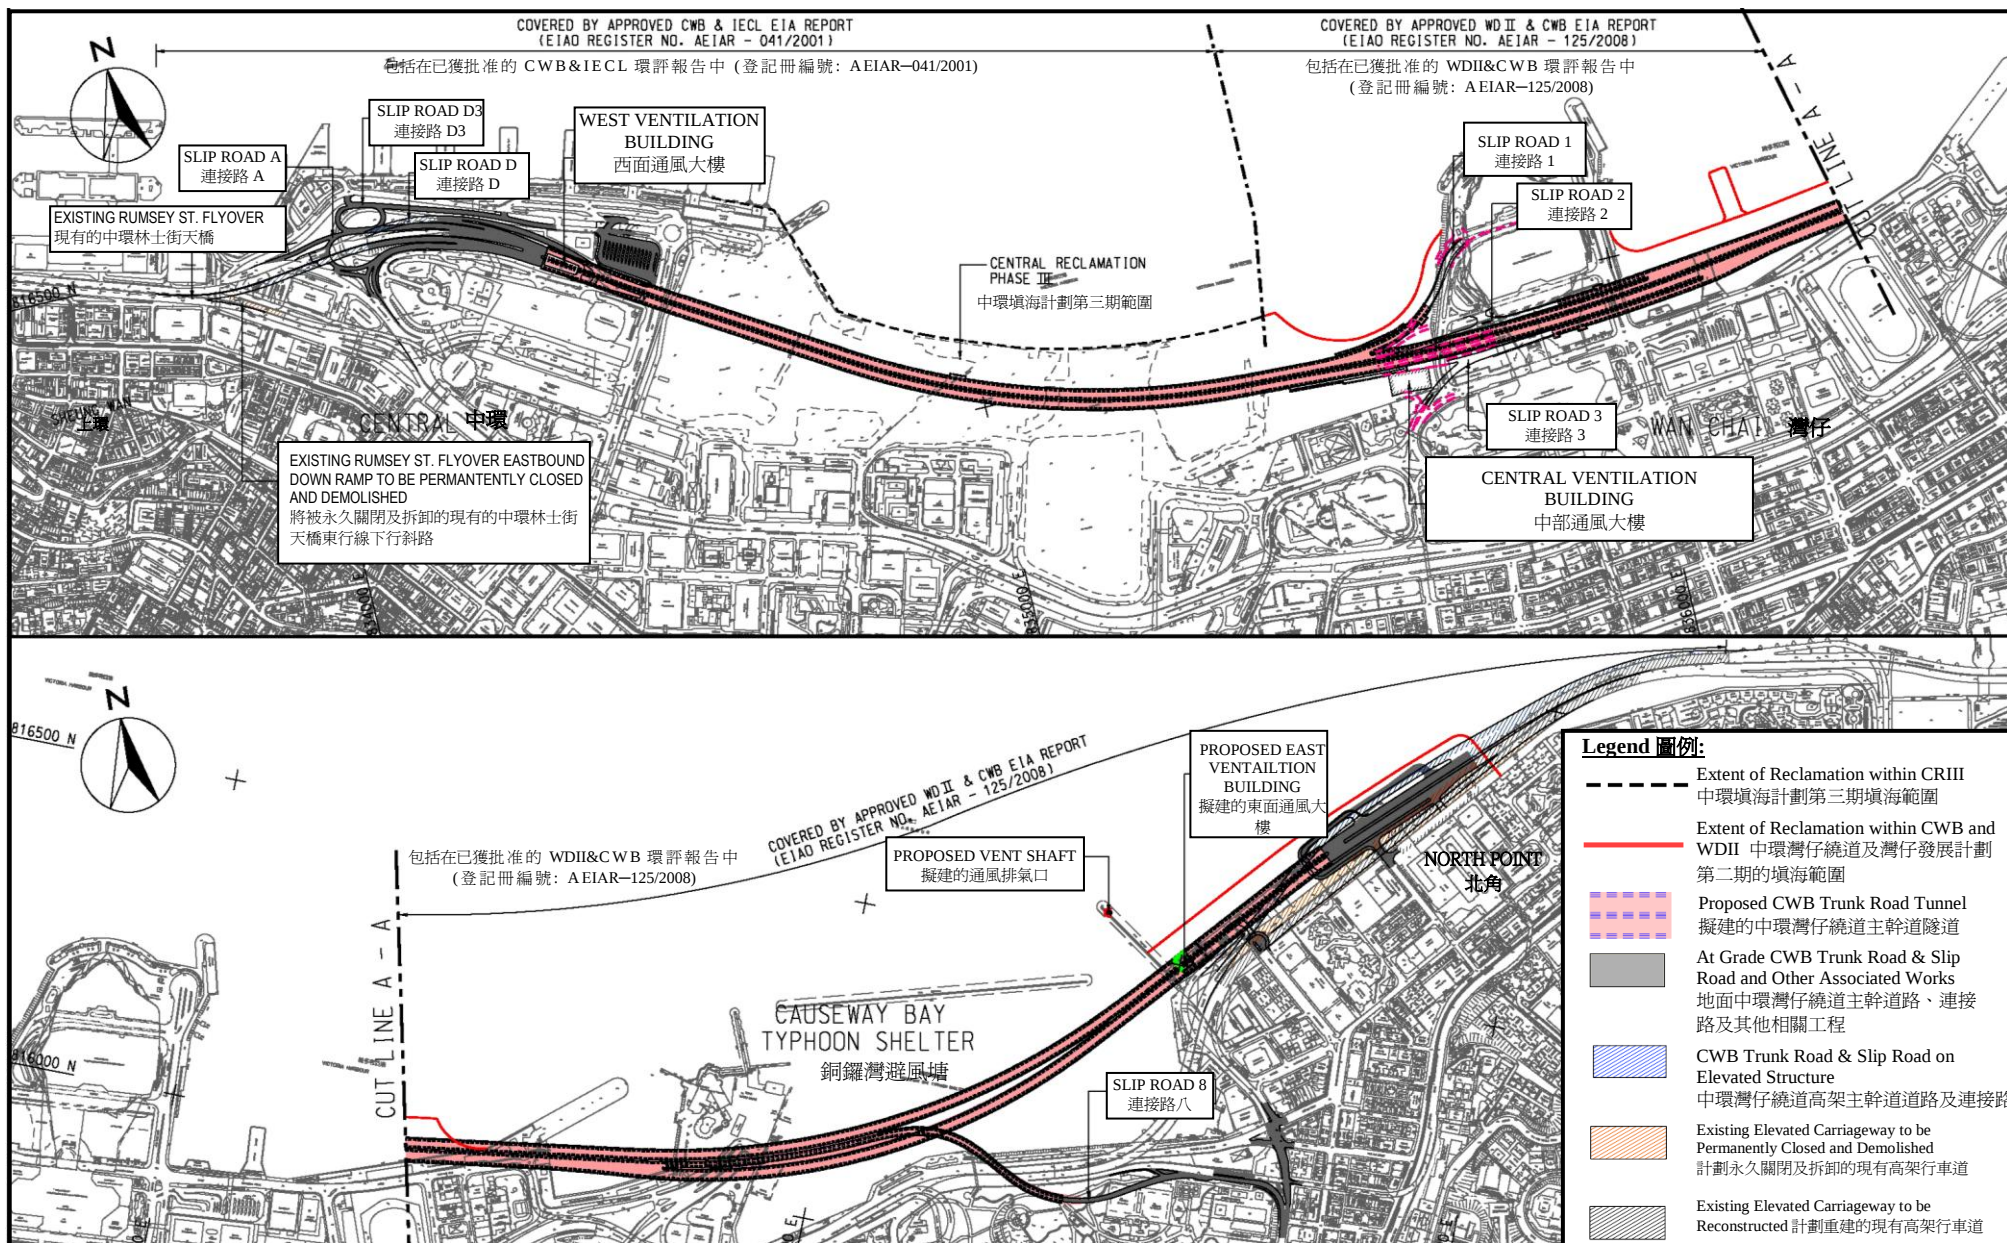


Project Title: Central-Wanchai Bypass (CWB) Including Its Road Tunnel and Slip Roads
工程項目名稱: 中環灣仔繞道包括其行車隧道及連接路

Environmental Permit No.: EP-364/2009/B
環境許可證編號: EP-364/2009/B

Figure 1: Location of the Project
圖 1: 工程項目位置

(This figure was prepared based on Figure 1.1 of the Application for Environmental Permit (Application No.: AEP-364/2009))
(本圖是根據環境許可證的申請(申請書編號 AEP-364/2009 圖 1.1 編製))

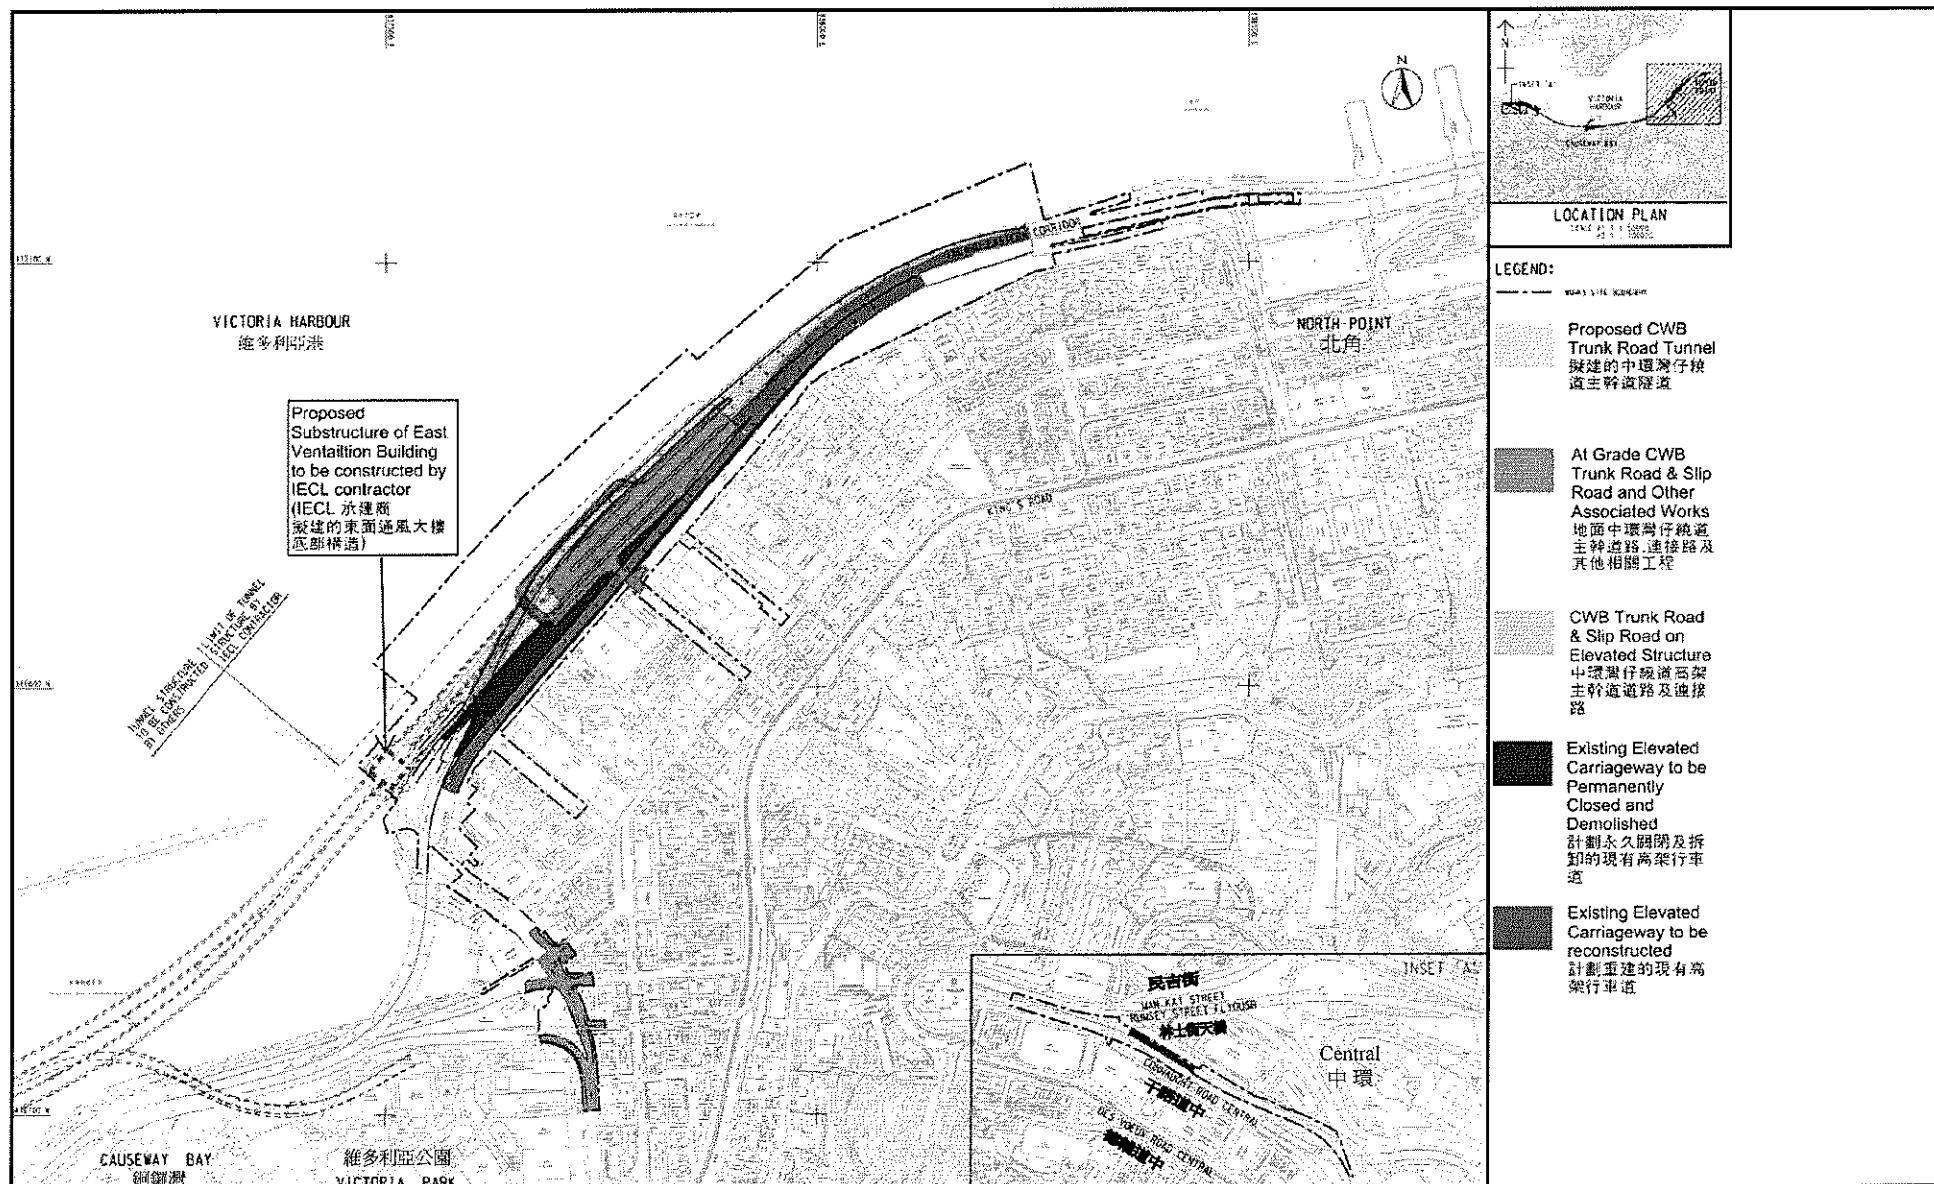

Project Title: Central-Wanchai Bypass (CWB) – Tunnel (North Point Section) and Island Eastern Corridor Link
 工程項目名稱：中環灣仔繞道—北角段隧道及東區走廊連接路
 Environmental Permit No. : FEP-07-364/2009/A
 環境許可證編號 : FEP-07-364/2009/A

Figure 1b: General Layout Plan
 圖 1b: 工程項目佈局圖

(This figure was prepared based on Sketch No. 60095653/IEC/DF0006 of Application for Further Environmental Permit (Application No.: FEP-120/2011))
 (本圖是根據申請新的環境許可證 (申請書編號 FEP-120/2011) 圖 60095653/IEC/DF0006 編製)



Figure 2.2

Project Organization Chart



Project Organization Chart


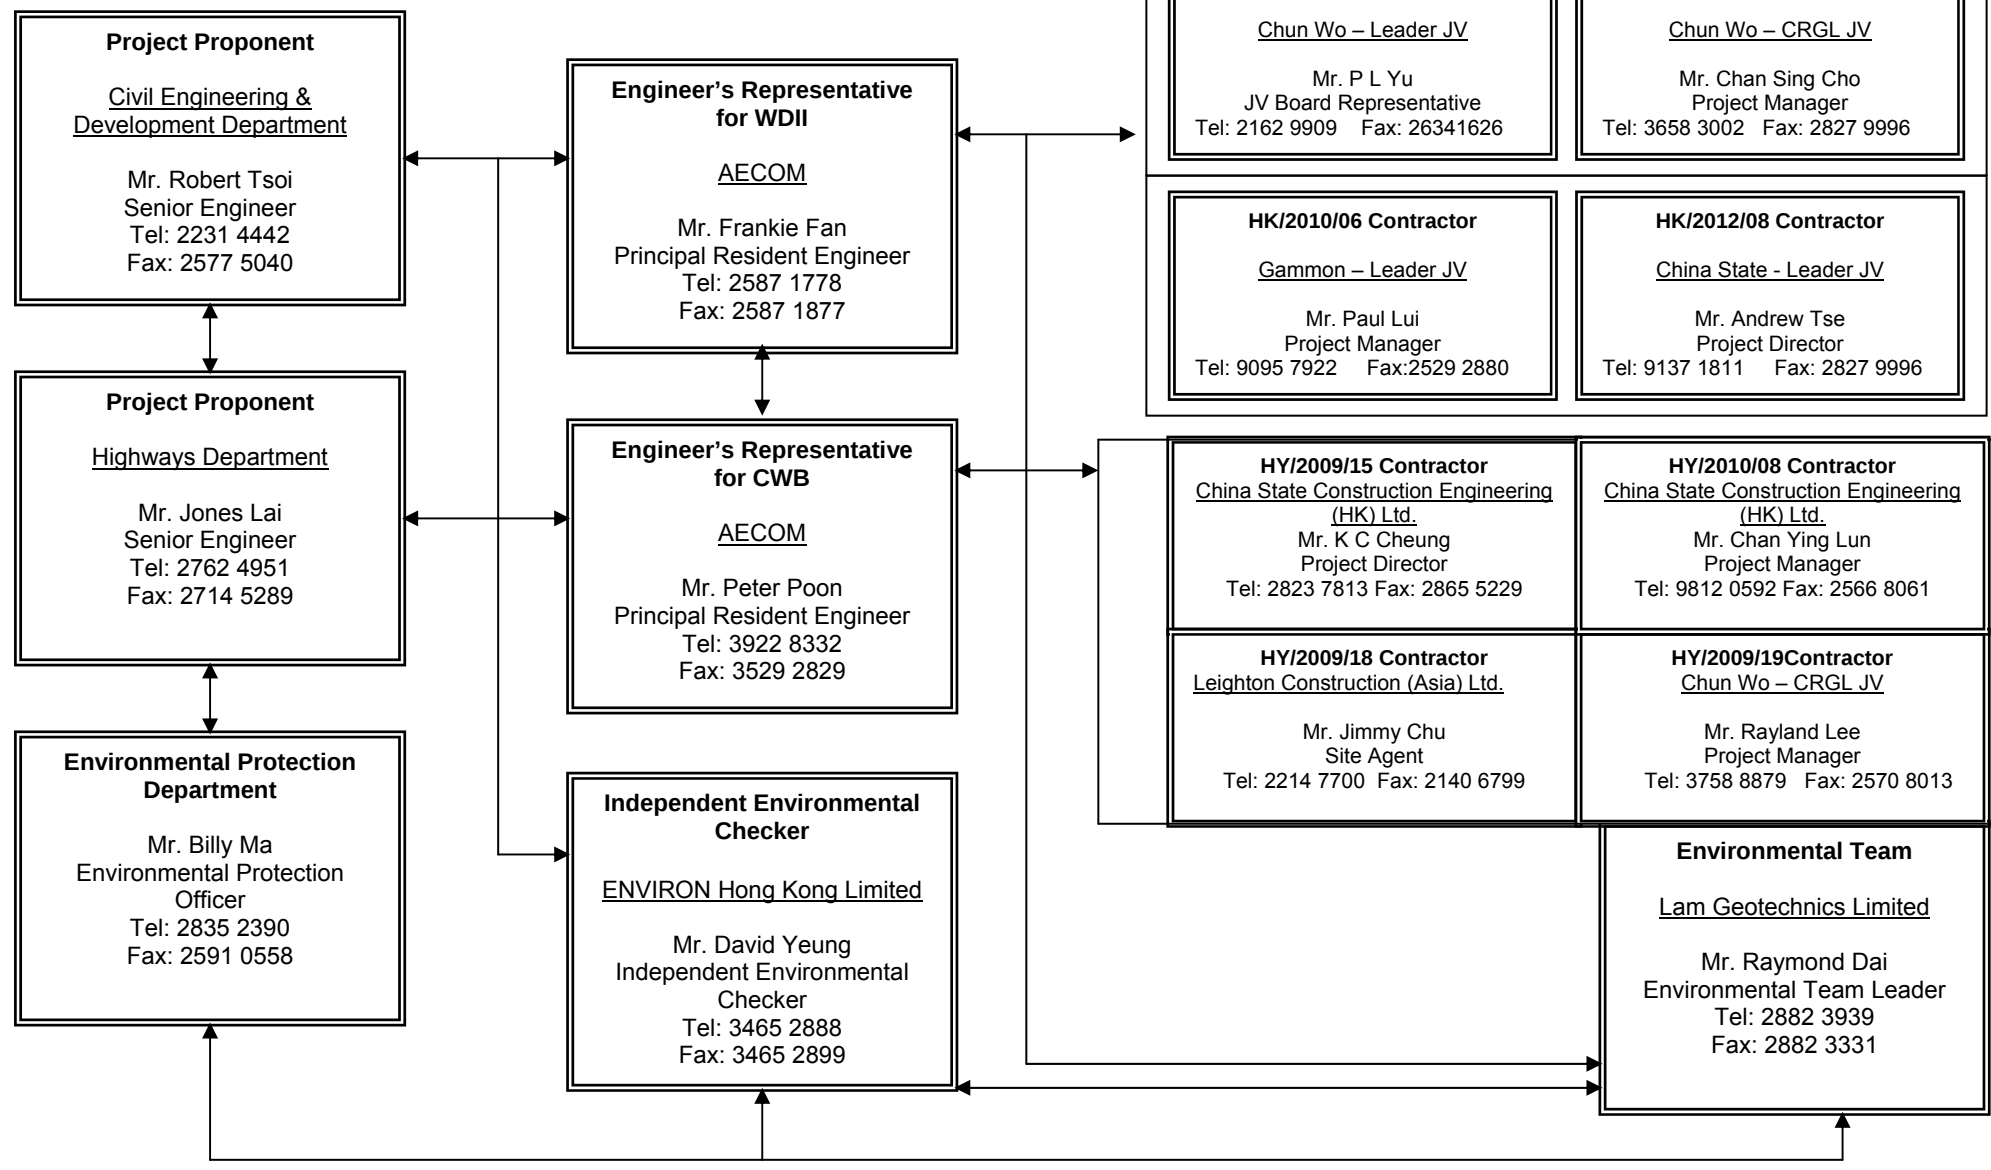




Figure 4.1

Locations of Monitoring Stations



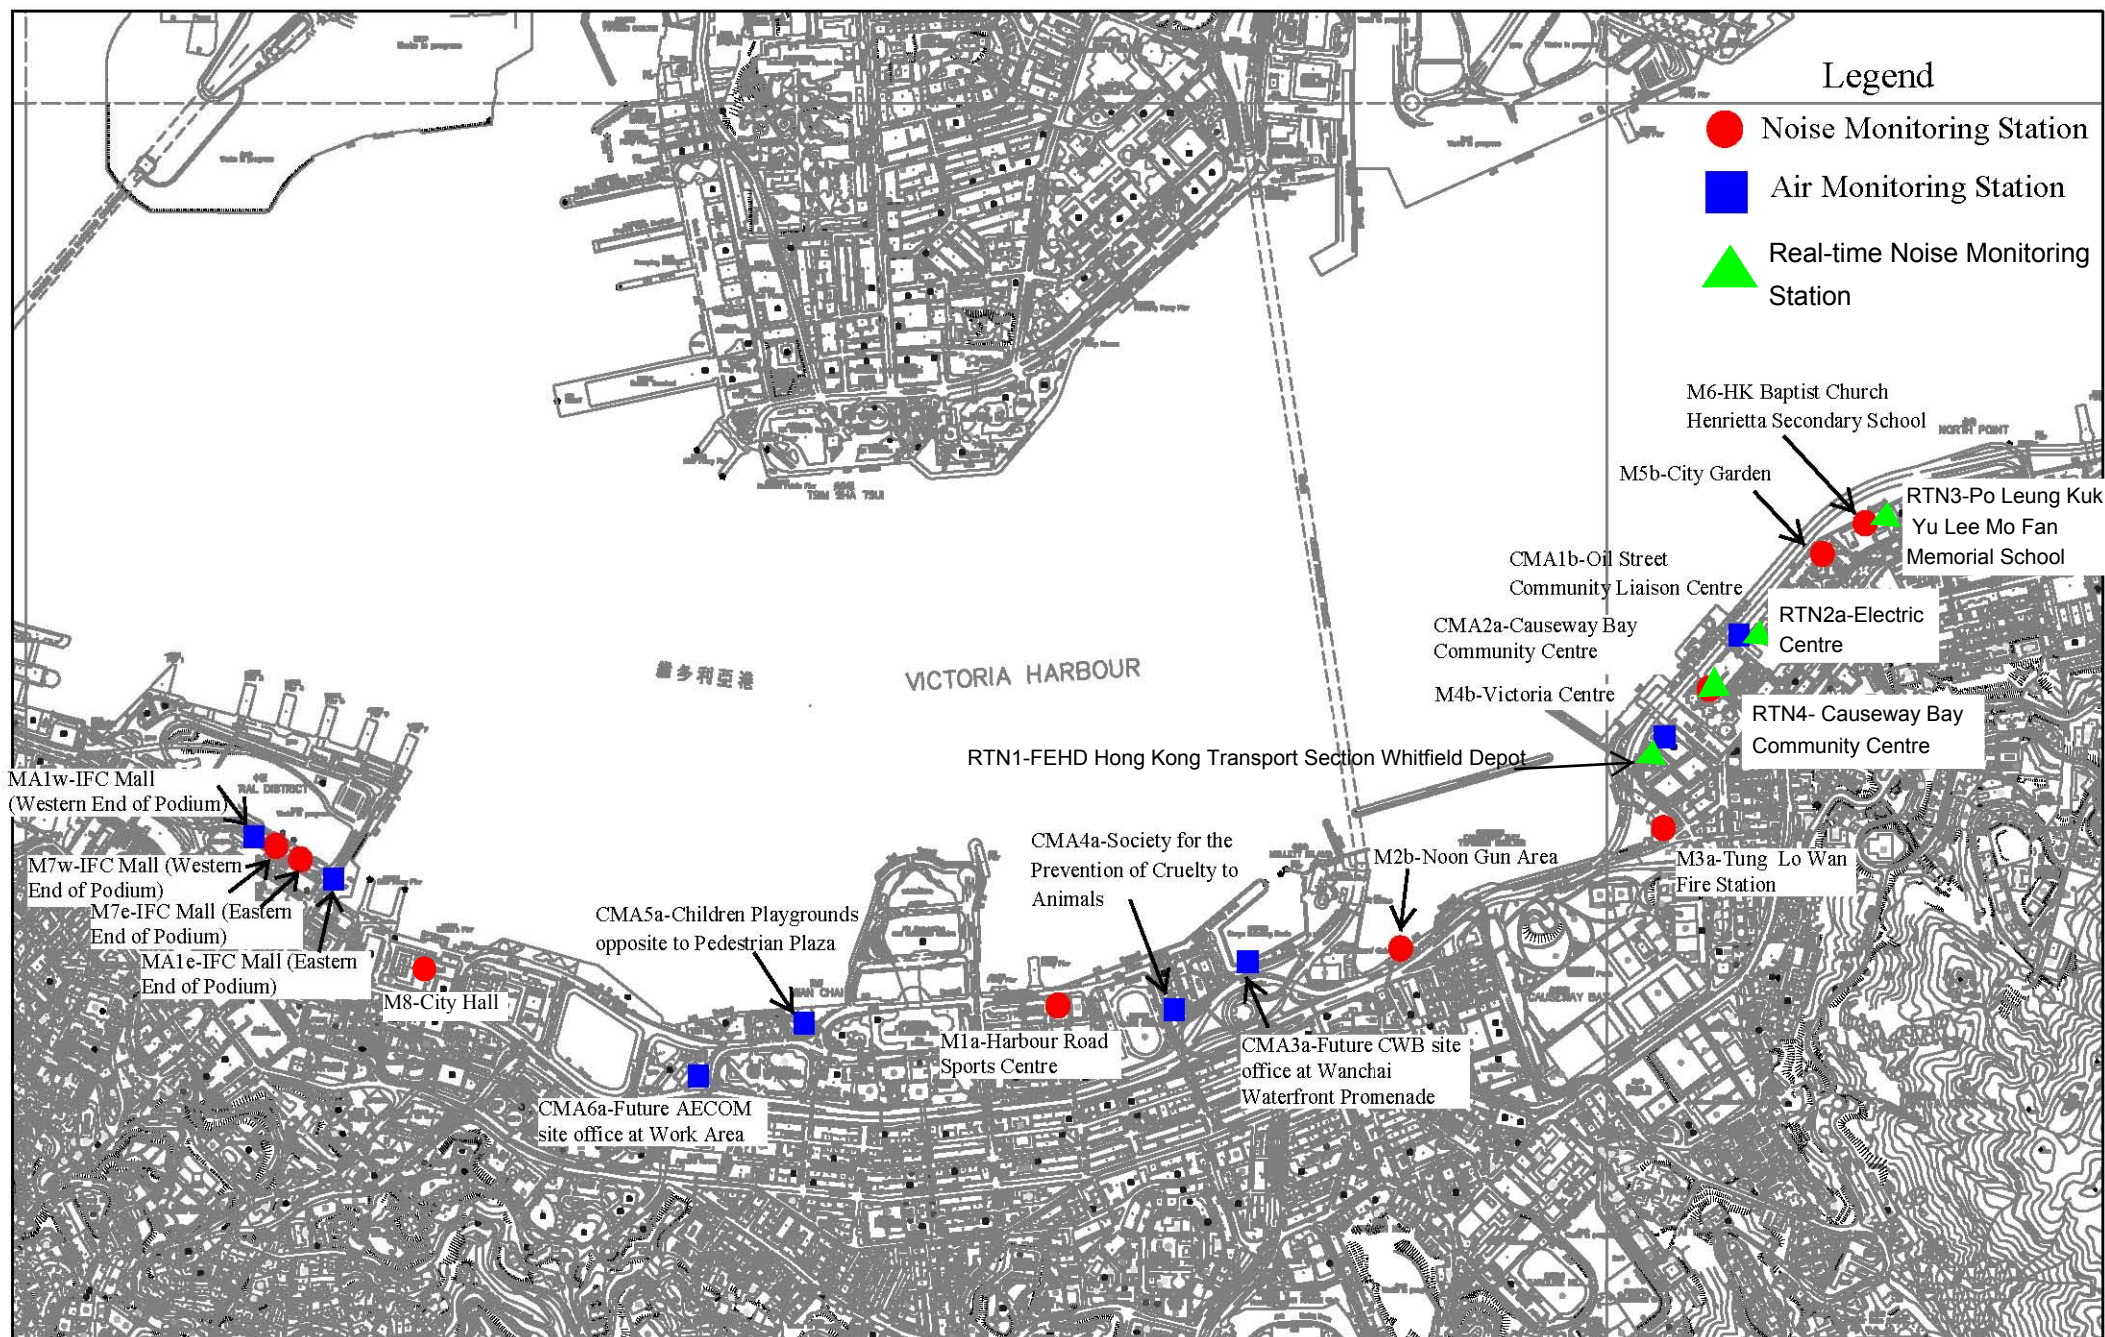

Appendix 3.1

Environmental Mitigation Implementation Schedule

IMPLEMENTATION SCHEDULE OF THE PROPOSED MITIGATION MEASURES**Table A.1 Implementation Schedule for Air Quality Control**

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
S3.6.5	Four times a day watering of the work site with active operations.	Work site / during construction	Contractor		√			EIAO-TM
S3.8.1	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimise cumulative dust impacts. - Strictly limit the truck speed on site to below 10 km per hour and water spraying to keep the haul roads in wet condition; - Watering during excavation and material handling; - Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary; and - Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.	Work site / during construction	Contractor		√			
Operational Phase								
S3.6.53 – S3.6.54	The design parameters of the East and Central Ventilation Buildings as set in Tables 3.10 and 3.11 of Volume 1 of the WDII & CWB EIA Report.	East and Central Ventilation Buildings / During operation of the Trunk Road	HyD			√		
S3.10.2	Air quality monitoring for the operation performance of the East Ventilation Building and associated East Vent Shaft will be conducted.	East Vent Shaft / During operation of the East Ventilation Building and associated East Vent Shaft	HyD			√		EIAO-TM

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table A.2 Implementation Schedule for Noise Control

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
S4.9.3	Good Site Practice: - Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program. - Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program. - Mobile plant, if any, shall be sited as far away from NSRs as possible. - Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum. - Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. - Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from on-site construction activities.	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO
S4.8.1 – S4.8.11	Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following tasks: - Slip road 8 tunnel - Construction of diaphragm wall and substructures of the tunnel approach ramp - Excavation - Construction of slabs - Backfill	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	- Demolition and construction of substructures for the IEC - Demolition works of existing piers and crossheads of the marine section of the existing IEC Use of PME grouping for the following tasks: - At-grade road construction - Substructure for IECL connection							
Operation Phase								
S4.8.12 – S4.8.23	For Existing NSRs - about 235m length of noise semi-enclosure with transparent panel covering the westbound slip road from the IEC - about 230m length of noise semi-enclosure with transparent panel covering the main carriageways (eastbound and westbound) of the CWB and IEC - about 135m length of 5.5m high cantilevered noise barrier with 4.5m cantilever inclined at 45° with transparent panel on the eastbound slip road to the IEC (amended under EP-364/2009/A) - about 95m length of 5.5m high cantilevered noise barrier with 1m cantilever inclined at 45° with transparent panel on the eastbound slip road to the IEC - about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC - low noise road surfacing for the trunk road (except tunnel section and beneath the landscaped deck at the eastern portal area)) with speed limit of 70 km/hour	Near North Point / Before commencement of operation of road project	HyD	√	√	√		EIAO-TM

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	For Future/Planned NSRs - about 265m length of noise semi-enclosure with transparent panel covering the westbound slip road from the IEC - The openable windows of the temple, if any, should be orientated so as to avoid direct line of sight to the existing Victoria Park Road as far as practicable.	In between the Electric Centre (next to City Garden) and CDA(1) site / Before occupation of Planned NSRs in CDA and CDA(1) sites. Near Causeway Bay Fire Station / During detailed design of the re-provisioned Tin Hau Temple	HyD Project Proponent for the re-provisioned Tin Hau Temple	√ √	√ #			

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Only the steel frame for this section of noise semi-enclosure would be erected in advance during the construction of the westbound slip road.

Table A.4 Implementation Schedule for Waste Management

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
S6.5.14	<i>Floating Refuse</i> During the construction phase, the project proponent’s contractor will be responsible for the collection of any refuse within their works area. Floating booms will be provided on the water surface to confine the refuse from the working barges as well as to avoid the accumulation of pollutants within temporary embayment as mentioned in Table D9.3.	Work site / During the construction period	Contractor		√			
S6.6.1	<i>Good Site Practices</i> Recommendations for good site practices during the construction activities include: • nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; • training of site personnel in proper waste management and chemical waste handling procedures; • provision of sufficient waste disposal points and regular collection for disposal; • appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; • regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and • a recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).	Work site / During the construction period	Contractor		√			Waste Disposal Ordinance (Cap.354)

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.6.2	<i>Waste Reduction Measures</i> Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include: • segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; • to encourage collection of aluminium cans, PET bottles and paper, separate labelled bins shall be provided to segregate these wastes from other general refuse generated by the work force; • any unused chemicals or those with remaining functional capacity shall be recycled; • use of reusable non-timber formwork, such as in casting the tunnel box sections, to reduce the amount of C&D material. • prior to disposal of C&D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill; • proper storage and site practices to minimise the potential for damage or contamination of construction materials; and • plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.	Work site / During planning and design stage, and construction stage	Contractor	√	√			

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.6.4	<i>General Refuse</i> General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D material. A collection area shall be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind blow' light material.	Work site / During the construction period	Contractor		√			Public Health and Municipal Services Ordinance (Cap. 132)
S6.6.5	<i>Chemical Wastes</i> After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals shall be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work site / During the construction period	Contractor		√			Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
S6.6.6	<i>Construction and Demolition Material</i> C&D material shall be sorted on-site into inert C&D material (that is, public fill) and C&D waste. All the suitable inert C&D material shall be broken down to 250 mm in size for reuse as public fill in the WDII reclamation. C&D waste, such as wood, glass, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials.	Work site / During the construction period	Contractor		√			ETWB TCW No. 33/2002, 31/2004, 19/2005

WDH & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.6.7	In order to monitor the disposal of public fill and C&D waste at public fill reception facilities and landfills, respectively, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team undertaking the environmental monitoring and audit work. An Independent Environment Checker shall be responsible for auditing the results of the system.	Work site / During the construction period	Contractor and Independent Environmental Checker		√			ETWB TCW No. 31/2004
S6.6.8	<i>Bentonite Slurry</i> The disposal of residual used bentonite slurry shall follow the good practice guidelines stated in ProPECC PN 1/94 "Construction Site Drainage" and listed as follows: • If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis. • If the used bentonite slurry is intended to be disposed of through the public drainage system, it shall be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the Technical Memorandum of Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters. • If the used bentonite slurry is intended to be disposed to public fill reception facilities, it will be mixed with dry soil on site before disposal.	Work site / During the construction period	Contractor		√			ProPECC PN 1/94

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table A.5 Implementation Schedule for Land Contamination

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction and Operation Phase								
S.7.1.1	As no potential contaminative land uses were identified within the Study Area, adverse land contamination impacts associated with the construction and operation of the Project is not expected. As such, environmental protection and mitigation measures are considered not necessary and will not be covered in this EM&A Manual.	-	-					-

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table A.7 Implementation Schedule for Landscape and Visual

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures		Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
					Des	C	O	Dec	
Construction Phase									
Table 10.5	CM1	Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM2	Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM3	Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM4	Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM5	Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM6	Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Operation Phase									
Table 10.6, Figure 10.5.1-10.5.5	OM1	Aesthetic design of buildings and road-related structures, including viaducts, vent buildings, subways, footbridges and noise barriers and enclosure.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM3	Buffer Tree and Shrub Planting to screen proposed roads and associated structures.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM5	Aesthetic streetscape design.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM6	Aesthetic design of roadside amenity areas.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004

*Des - Design, C - Construction, O – Operation, and Dec - Decommissioning



Appendix 4.1

Action and Limit Level

**Action and Limit Level***Action and Limit Level for Noise Monitoring*

Time Period	Action Level	Limit Level
07:00 – 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A)/ 70 dB(A)/ 65 dB(A) ^{Note 1}

Note 1:

- 70dB(A) and 65 dB(A) for schools during normal teaching periods and school examination periods, respectively.
- If works are to be carried out during the restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

Action and Limit Level for Air Monitoring

Monitoring Location	1-hour TSP Level in $\mu\text{g}/\text{m}^3$		24-hour TSP Level in $\mu\text{g}/\text{m}^3$	
	Action Level	Limit Level	Action Level	Limit Level
CMA1b	320.1	500	176.7	260
CMA2a	323.4	500	169.5	260
CMA3a	311.3	500	171.0	260
CMA4a	312.5	500	171.2	260
CMA5a	332.0	500	181.0	260
MA1e	325.1	500	173.4	260
MA1w	325.1	500	173.4	260



Appendix 4.2

Copies of Calibration Certificates



Calibration Certificate

Certificate No. 33624

Page 1 of 4 Pages

Customer : Lam Geotechnics Limited

Address : 11/F, Centre Point, 181-185 Gloucester Road, Wanchai, Hong Kong.

Order No. : Q31494

Date of receipt : 30-May-13

Item Tested

Description : Digital Sound Level Meter

Manufacturer : B&K

Model : Type 2236

Serial No. : 2100736

Test Conditions

Date of Test : 3-Jun-13

Supply Voltage : --

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure : Z01.

Test Results

All results were within the IEC 651 Type 1, IEC 804 Type 1 & IEC 1260 Class 1 specification.

The results are shown in the attached page(s).

Main Test equipment used:


Equipment No.	Description	Cert. No.	Traceable to
S017	Multi-Function Generator	C127181	SCL-HKSAR
S024	Sound Level Calibrator	30620	NIM-PRC & SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI).

The test results apply to the above Unit-Under-Test only

Calibrated by : 
Liam Wong

Approved by : 
Dorothy Cheuk

Date: 3-Jun-13

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646



Calibration Certificate

Certificate No. 33624

Page 2 of 4 Pages

Results :

1. SPL Accuracy

UUT Setting				Applied Value (dB)	UUT Reading (dB)
Range	Parameter	Frequency Wt.	Freq. Response		
20 - 100	SPL	dBA	F	94.0	93.8
			S		93.8
		dB	F		93.8
		dB	F		93.9
		1 kHz	F		93.8
40 - 120	SPL	dBA	F	94.0	93.9
		1 kHz	F		93.9
	SPL	dBA	F	114.0	113.8
			S		113.8
		dB	F		113.9
		dB	F		113.9
		1 kHz	F		113.8

IEC 651 Type 1 Spec. : ± 0.7 dB

Uncertainty : ± 0.1 dB

2. Level Stability : 0.0 dB

IEC 651 Type 1 Spec. : ± 0.3 dB

Uncertainty : ± 0.1 dB

3. Linearity

3.1 Level Linearity

UUT Range (dB)	Applied Value (dB)	UUT Reading (dB)	Variation (dB)	IEC 651 Type 1 Spec. (Primary Indicator Range)
140	114.0	113.9	0.0	± 0.7 dB
130	104.0	103.9	0.0	
120	94.0	93.9 (Ref.)	--	
110	84.0	83.9	0.0	
100	74.0	73.9	0.0	
100	64.0	63.9	0.0	
100	54.0	53.9	0.0	

Uncertainty : ± 0.1 dB



Calibration Certificate

Certificate No. 33624

Page 3 of 4 Pages

3.2 Differential level linearity

UUT Range (dB)	Applied Value (dB)	UUT Reading (dB)	Variation (dB)	IEC 651 Type 1 Spec.
120	84.0	83.9	0.0	± 0.4 dB
	94.0	93.9 (Ref.)	- -	
	95.0	94.9	0.0	± 0.2 dB

Uncertainty : ± 0.1 dB

4. Frequency Weighting

A weighting

Frequency	Attenuation (dB)	IEC 651 Type 1 Spec.
31.5 Hz	-39.6	- 39.4 dB, ± 1.5 dB
63 Hz	-26.4	- 26.2 dB, ± 1.5 dB
125 Hz	-16.3	- 16.1 dB, ± 1 dB
250 Hz	-8.8	- 8.6 dB, ± 1 dB
500 Hz	-3.3	- 3.2 dB, ± 1 dB
1 kHz	0.0 (Ref)	0 dB, ± 1 dB
2 kHz	+1.2	+ 1.2 dB, ± 1 dB
4 kHz	+0.9	+ 1.0 dB, ± 1 dB
8 kHz	-1.2	- 1.1 dB, + 1.5 dB ~ -3 dB
16 kHz	-6.8	- 6.6 dB, + 3 dB $\sim -\infty$

Uncertainty : ± 0.1 dB

5. Time Averaging

Applied Burst duty Factor	Applied Leq Value (dB)	UUT Reading (dB)	IEC 804 Type 1 Spec.
continuous	40.0	40.0	--
1/10	40.0	39.9	± 0.5 dB
1/10 ²	40.0	39.8	
1/10 ³	40.0	39.7	± 1.0 dB
1/10 ⁴	40.0	39.5	

Uncertainty : ± 0.1 dB



Calibration Certificate

Certificate No. 33624

Page 4 of 4 Pages

6. Filter Response

Filter Setting		Attenuation (dB)	IEC 1260 Class 1 Spec.
125	Hz	-63.6	< - 61
250	Hz	-44.8	< - 42
500	Hz	-21.0	< - 17.5
707	Hz	-3.7	- 2 ~ - 5
1	kHz (Ref.)	0.0 (Ref.)	--
1.414	kHz	-4.1	- 2 ~ - 5
2	kHz	-21.4	< - 17.5
4	kHz	-45.0	< - 42
8	kHz	-63.9	< - 61

Uncertainty : ± 0.2 dB


Remark : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 996 hPa

4. The UUT was adjusted with the laboratory's sound calibrator at the reference sound pressure level before the calibration.

----- END -----



Calibration Certificate

Certificate No. **25144**

Page **1** of **2** Pages

Customer : Lam Geotechnics Limited

Address : 11/F, Centre Point, 181-185 Gloucester Road, Wanchai, Hong Kong.

Order No. : Q22033

Date of receipt : 2-Aug-12

Item Tested

Description : Sound Level Calibrator

Manufacturer : B & K

Model : Type 4230

Serial No. : 1411076

Test Conditions

Date of Test : 10-Aug-12

Supply Voltage : --

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure: F21, Z02.

Test Results

All results were within the IEC 942 Class 1 specification.

The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S014	Spectrum Analyzer	13535	NIM-PRC & SCL-HKSAR
S024	Sound Level Calibrator	15136	NIM-PRC & SCL-HKSAR
S041	Universal Counter	15610	SCL-HKSAR
S191	6½ dgt. Multimeter	20033	NIM-PRC

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.


The test equipment used for calibration are traceable to International System of Units (SI).

The test results apply to the above Unit-Under-Test only

Calibrated by :


Stephen Chu

Approved by :


Dorothy Cheuk


Date: 10-Aug-12

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646



Calibration Certificate

Certificate No. **25144**

Page 2 of 2 Pages

Results :

1. Level Accuracy

UUT Nominal Value (dB)	Measured Value (dB)	IEC 942 Class 1 Spec.
94	93.96	± 0.3 dB

Uncertainty : ± 0.2 dB

2. Frequency

UUT Nominal Value	Measured Value	IEC 942 Class 1 Spec.
1 kHz	1.000 kHz	± 2 %

Uncertainty : $\pm 3.6 \times 10^{-6}$

3. Level Stability : 0.0 dB

IEC 942 Class 1 Spec. : ± 0.1 dB

Uncertainty : ± 0.01 dB

4. Total Harmonic Distortion : < 1.5 %

IEC 942 Class 1 Spec. : < 3 %

Uncertainty : ± 2.3 % of reading

Remark : 1. UUT : Unit-Under-Test

2. The above measured values are the mean of 3 measurement.

3. The uncertainty claimed is for a confidence probability of not less than 95%.

4. Atmospheric Pressure : 995 hPa.

----- END -----



TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE.
 VILLAGE OF CLEVELAND, OH 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX
 WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Jul 19, 2012 Rootsmeter S/N 0438320 Ta (K) - 298
 Operator Tisch Orifice I.D. - 0005 Pa (mm) - 751.84

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER	ORFICE
					DIFF Hg (mm)	DIFF H2O (in.)
1	NA	NA	1.00	1.3840	3.2	2.00
2	NA	NA	1.00	0.9760	6.4	4.00
3	NA	NA	1.00	0.8730	7.9	5.00
4	NA	NA	1.00	0.8340	8.8	5.50
5	NA	NA	1.00	0.6890	12.7	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9850	0.7117	1.4066	0.9957	0.7194	0.8903
0.9809	1.0050	1.9892	0.9915	1.0159	1.2591
0.9788	1.1212	2.2240	0.9894	1.1333	1.4078
0.9777	1.1723	2.3326	0.9883	1.1850	1.4765
0.9725	1.4115	2.8132	0.9831	1.4268	1.7807
Qstd slope (m) = 2.01145			Qa slope (m) = 1.25953		
intercept (b) = -0.02803			intercept (b) = -0.01774		
coefficient (r) = 0.99995			coefficient (r) = 0.99995		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

$$Vstd = \text{Diff. Vol}[(Pa - \text{Diff. Hg})/760] (298/Ta)$$

$$Qstd = Vstd/Time$$

$$Va = \text{Diff Vol} [(Pa - \text{Diff Hg})/Pa]$$

$$Qa = Va/Time$$

For subsequent flow rate calculations:

$$Qstd = 1/m\{[\text{SQRT}(H2O(Pa/760) (298/Ta))] - b\}$$

$$Qa = 1/m\{[\text{SQRT } H2O(Ta/Pa)] - b\}$$



Lam Geotechnics Limited

Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA1b
 Equipment no. : EL452

Calibration Date : 1-Jun-13
 Calibration Due Date : 1-Aug-13

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition			
Temperature, T _a	304	Kelvin	Pressure, P _a
			1008 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m _c	2.01145	Intercept, b _c	-0.02803
Last Calibration Date	19-Jul-12	$\left(H \times P_a / 1013.3 \times 298 / T_a \right)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	19-Jul-13				

Calibration of RSP						
Calibration Point	Manometer Reading			Q _{std}	Continuous Flow	IC
	H (inches of water)			(m ³ / min.)	Recorder, W	(W(P _a /1013.3x298/T _a) ^{1/2} /35.31)
	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis
1	6.2	6.2	12.4	1.7427	60	59.2494
2	5.1	5.1	10.2	1.5819	53	52.3370
3	4.1	4.1	8.2	1.4198	45	44.4370
4	2.5	2.5	5.0	1.1117	32	31.5997
5	1.5	1.5	3.0	0.8643	22	21.7248

By Linear Regression of Y on X

Slope, m = 42.8651 Intercept, b = -15.7434
 Correlation Coefficient* = 0.9995
 Calibration Accepted = Yes/No**

* if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : _____

Calibrated by : Sam
 Date : 1-Jun-13

Checked by : Derek Lo
 Date : 1-Jun-13



Lam Geotechnics Limited

Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA2a

Equipment no. : EL449

Calibration Date : 1-Jun-13

Calibration Due Date : 1-Aug-13

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition			
Temperature, T _a	304	Kelvin	Pressure, P _a
			1008 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m _c	2.01145	Intercept, b _c	-0.02803
Last Calibration Date	19-Jul-12	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	19-Jul-13				

Calibration of RSP						
Calibration Point	Manometer Reading			Q _{std}	Continuous Flow	IC
	H (inches of water)			(m ³ / min.)	Recorder, W	(W(P _a /1013.3x298/T _a) ^{1/2} /35.31)
	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis
1	6.0	6.0	12.0	1.7146	59	58.2619
2	5.0	5.0	10.0	1.5664	50	49.3745
3	4.1	4.1	8.2	1.4198	42	41.4746
4	2.5	2.5	5.0	1.1117	26	25.6747
5	1.5	1.5	3.0	0.8643	14	13.8249

By Linear Regression of Y on X

Slope, m = 51.9671 Intercept, b = -31.6716

Correlation Coefficient* = 0.9993

Calibration Accepted = Yes/No**

* if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : _____

Calibrated by : Sam

Date : 1-Jun-13

Checked by : Derek Lo

Date : 1-Jun-13



Lam Geotechnics Limited

Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA3a

Equipment no. : EL333

Calibration Date : 25-Jun-13

Calibration Due Date : 25-Aug-13

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition			
Temperature, T_a	304	Kelvin	Pressure, P_a
			1012 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m_c	2.01145	Intercept, b_c	-0.02803
Last Calibration Date	19-Jul-12	$\left(H \times P_a / 1013.3 \times 298 / T_a \right)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	19-Jul-13				

Calibration of RSP						
Calibration Point	Manometer Reading			Q _{std} (m ³ / min.)	Continuous Flow Recorder, W	IC (W(P _a /1013.3x298/T _a) ^{1/2} /35.31)
	H (inches of water)					
	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis
1	5.8	5.8	11.6	1.6893	58	57.3879
2	4.8	4.8	9.6	1.5381	49	48.4829
3	4.0	4.0	8.0	1.4053	41	40.5673
4	2.4	2.4	4.8	1.0917	25	24.7362
5	1.5	1.5	3.0	0.8659	14	13.8523

By Linear Regression of Y on X

Slope, m = 52.6106 Intercept, b = -32.3377

Correlation Coefficient* = 0.9991

Calibration Accepted = Yes/No**

* if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : _____

Calibrated by : Henry

Date : 25-Jun-13

Checked by : Derek Lo

Date : 25-Jun-13



Lam Geotechnics Limited

Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA4a

Equipment no. : EL390

Calibration Date : 1-Jun-13

Calibration Due Date : 1-Aug-13

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition			
Temperature, T _a	304	Kelvin	Pressure, P _a
			1008 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m _c	2.01145	Intercept, b _c	-0.02803
Last Calibration Date	19-Jul-12	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	19-Jul-13				

Calibration of RSP						
Calibration Point	Manometer Reading			Q _{std}	Continuous Flow	IC
	H (inches of water)			(m ³ / min.)	Recorder, W	(W(P _a /1013.3x298/T _a) ^{1/2} /35.31)
	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis
1	6.1	6.1	12.2	1.7287	61	60.2369
2	5.0	5.0	10.0	1.5664	54	53.3244
3	4.1	4.1	8.2	1.4198	46	45.4245
4	2.5	2.5	5.0	1.1117	31	30.6122
5	1.5	1.5	3.0	0.8643	20	19.7498

By Linear Regression of Y on X

Slope, m = 47.4395 Intercept, b = -21.6122

Correlation Coefficient* = 0.9996

Calibration Accepted = Yes/No**

* if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : _____

Calibrated by : Sam

Date : 1-Jun-13

Checked by : Derek Lo

Date : 1-Jun-13



Lam Geotechnics Limited

Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA5a

Equipment no. : EL380

Calibration Date : 1-Jun-13

Calibration Due Date : 1-Aug-13

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition			
Temperature, T _a	304	Kelvin	Pressure, P _a
			1008 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m _c	2.01145	Intercept, b _c	-0.02803
Last Calibration Date	19-Jul-12	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	19-Jul-13				

Calibration of RSP						
Calibration Point	Manometer Reading			Q _{std}	Continuous Flow	IC
	H (inches of water)			(m ³ / min.)	Recorder, W	(W(P _a /1013.3x298/T _a) ^{1/2} /35.31)
	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis
1	6.1	6.1	12.2	1.7287	62	61.2244
2	5.0	5.0	10.0	1.5664	53	52.3370
3	4.0	4.0	8.0	1.4025	46	45.4245
4	2.4	2.4	4.8	1.0895	31	30.6122
5	1.5	1.5	3.0	0.8643	21	20.7373

By Linear Regression of Y on X

Slope, m = 46.4749 Intercept, b = -19.7575

Correlation Coefficient* = 0.9995

Calibration Accepted = Yes/No**

* if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : _____

Calibrated by : Sam

Date : 1-Jun-13

Checked by : Derek Lo

Date : 1-Jun-13



Lam Geotechnics Limited

Calibration Data for High Volume Sampler (TSP Sampler)

Location	:	MA1w	Calibration Date	:	1-Jun-13
Equipment no.	:	EL080	Calibration Due Date	:	1-Aug-13

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition						
Temperature, T _a	304		Kelvin	Pressure, P _a	1008 mmHg	

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m _c	2.01145	Intercept, b _c	-0.02803
Last Calibration Date	19-Jul-12	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	19-Jul-13				

Calibration of RSP						
Calibration Point	Manometer Reading			Q _{std} (m ³ / min.)	Continuous Flow Recorder, W (CFM)	IC (W(P _a /1013.3x298/T _a) ^{1/2} /35.31)
	H (inches of water)					
	(up)	(down)	(difference)	X-axis	Y-axis	
1	6.2	6.2	12.4	1.7427	59	58.2619
2	5.1	5.1	10.2	1.5819	50	49.3745
3	4.2	4.2	8.4	1.4368	42	41.4746
4	2.5	2.5	5.0	1.1117	26	25.6747
5	1.5	1.5	3.0	0.8643	14	13.8249

By Linear Regression of Y on X						
Slope, m	=	50.3189	Intercept, b	=	-30.0806	
Correlation Coefficient*	=	0.9995				
Calibration Accepted	=	Yes/No**				

* if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : _____

Calibrated by	:	Sam	Checked by	:	Derek Lo
Date	:	1-Jun-13	Date	:	1-Jun-13

Calibration Data for High Volume Sampler (TSP Sampler)

Location	:	MA1e	Calibration Date	:	1-Jun-13
Equipment no.	:	EL455	Calibration Due Date	:	1-Aug-13

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition					
Temperature, T _a	304	Kelvin	Pressure, P _a	1008	mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m _c	2.01145	Intercept, b _c	-0.02803
Last Calibration Date	19-Jul-12	$\left(H \times P_a / 1013.3 \times 298 / T_a \right)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	19-Jul-13				

Calibration of RSP						
Calibration Point	Manometer Reading			Q _{std}	Continuous Flow	IC
	H (inches of water)			(m ³ / min.)	Recorder, W	(W(P _a /1013.3x298/T _a) ^{1/2} /35.31)
	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis
1	6.1	6.1	12.2	1.7287	63	62.2119
2	5.1	5.1	10.2	1.5819	55	54.3119
3	4.1	4.1	8.2	1.4198	45	44.4370
4	2.8	2.8	5.6	1.1757	32	31.5997
5	1.8	1.8	3.6	0.9454	20	19.7498

By Linear Regression of Y on X

Slope, m	=	54.4272	Intercept, b	=	-32.1187
Correlation Coefficient*	=	0.9996			
Calibration Accepted	=	Yes/No**			

* if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : _____

Calibrated by	:	Sam	Checked by	:	Derek Lo
Date	:	1-Jun-13	Date	:	1-Jun-13



Appendix 5.1

Monitoring Schedules for Reporting Month and Coming Reporting Month

**Wan Chai Development Phase II and Central-Wan Chai Bypass
Sampling, Field Measurement and Testing Works (Stage 2)**

**Environmental Monitoring Schedule
July 2013**

						29-Jun
30-Jun	1-Jul	2-Jul	3-Jul	4-Jul	5-Jul	6-Jul
		Noise (Daytime) (M7e,M7w,M8)	24hr TSP Noise (Daytime) (M1a,M2b,M3a,M4b, M5b,M6)	24hr TSP(CMA5a) 1hr TSP		
7-Jul	8-Jul	9-Jul	10-Jul	11-Jul	12-Jul	13-Jul
	Noise (Daytime) (M7e,M7w,M8)	24hr TSP Noise (Daytime) (M1a,M2b,M3a,M4b , M5b,M6)	1hr TSP			
14-Jul	15-Jul	16-Jul	17-Jul	18-Jul	19-Jul	20-Jul
	24hr TSP	1hr TSP Noise (Daytime) (M6,M7e,M7w,M8)	Noise (Daytime) M1a,M2b,M3a,M4b,M5b			24hr TSP
21-Jul	22-Jul	23-Jul	24-Jul	25-Jul	26-Jul	27-Jul
	1hr TSP	Noise (Daytime)			24hr TSP	1hr TSP

**Wan Chai Development Phase II and Central-Wan Chai Bypass
Sampling, Field Measurement and Testing Works (Stage 2)**

**Tentative Environmental Monitoring Schedule
August 2013**

28-Jul	29-Jul	30-Jul	31-Jul	1-Aug	2-Aug	3-Aug
	Noise (Daytime)	Noise (Daytime)		24hr TSP	1hr TSP	
4-Aug	5-Aug	6-Aug	7-Aug	8-Aug	9-Aug	10-Aug
	Noise (Daytime)	Noise (Daytime)	24hr TSP	1hr TSP		
11-Aug	12-Aug	13-Aug	14-Aug	15-Aug	16-Aug	17-Aug
		24hr TSP Noise (Daytime)	1hr TSP Noise (Daytime)			
18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug
	24hr TSP	1hr TSP Noise (Daytime)	Noise (Daytime)			24hr TSP
25-Aug	26-Aug	27-Aug				
	1hr TSP	Noise (Daytime)				



Appendix 5.2

Noise Monitoring Results and Graphical Presentations



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M1a - Harbour Road Sports Centre

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
03/07/13	9:10	Fine	74.0	76.5	69.0	72	69	75
09/07/13	9:00	Fine	73.9	76.5	68.5	72	69	75
17/07/13	10:10	Fine	72.7	75.5	67.0	72	63	75
23/07/13	11:10	Fine	72.4	75.4	67.0	72	59	75

Location: M2b - Noon-day gun area

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
03/07/13	10:00	Fine	71.4	72.5	69.5	68	69	75
09/07/13	9:50	Fine	70.2	71.0	68.5	68	67	75
17/07/13	11:00	Fine	71.6	72.5	68.5	68	69	75
23/07/13	13:00	Cloudy	75.1	76.5	72.5	68	74	75

Location: M3a - Tung Lo Wan Fire Station

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
03/07/13	10:45	Fine	69.7	76.0	66.0	69	62	75
09/07/13	10:30	Fine	66.3	68.0	64.0	69	66	75
17/07/13	13:00	Fine	66.9	67.5	63.5	69	67	75
23/07/13	13:50	Cloudy	66.2	68.0	63.5	69	66	75

Location: M4b - Victoria Centre

Date	Time	Weather	Measurement Noise Level			Baseline Noise Level	Construction Noise Level		Limit Level
			Leq	L10	L90	Leq	Leq	Leq	
			Unit: dB(A), (30min)						
03/07/13	11:25	Fine	70.0	71.5	68.5	67	67	75	
09/07/13	11:15	Fine	70.9	72.0	68.5	67	68	75	
17/07/13	13:45	Fine	70.8	71.5	69.0	67	68	75	
23/07/13	14:45	Fine	70.7	72.0	69.0	67	68	75	

Location: M5b - City Garden

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30min)								
03/07/13	13:10	Fine	70.7	71.5	69.0	68	67	75
09/07/13	13:00	Fine	69.9	71.0	68.0	68	65	75
17/07/13	14:30	Cloudy	72.3	72.0	68.5	68	70	75
23/07/13	15:35	Cloudy	71.9	72.5	70.5	68	70	75

Location: M6 - HK Baptist Church Henrietta Secondary School

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30-min)								
03/07/13	13:55	Fine	73.0	74.0	71.0	71	69	70
09/07/13	13:45	Fine	74.9	76.0	72.5	71	73	70
16/07/13	15:50	Cloudy	74.4	75.0	72.5	71	72	70
23/07/13	14:20	Cloudy	73.5	75.0	72.0	71	70	70



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M7e - International Finance Centre (Eastern End of Podium) (Reference Station)

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
02/07/13	14:34	Fine	73.1	74.5	70.5	67	72	N/A
08/07/13	13:58	Fine	75.0	77.0	69.0	67	74	N/A
16/07/13	9:15	Fine	74.0	74.5	72.5	67	73	N/A
23/07/13	8:45	Fine	71.6	73.0	69.5	67	70	N/A


Location: M7w - International Finance Centre (Western End of Podium)

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
02/07/13	13:58	Fine	66.5	67.5	64.0	69	67	75
08/07/13	14:38	Fine	65.6	67.0	63.0	69	66	75
16/07/13	9:47	Cloudy	66.8	68.0	65.5	69	67	75
23/07/13	9:30	Fine	67.2	68.5	65.5	69	67	75


Location: M8 - City Hall

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30-min)								
02/07/13	15:29	Fine	59.4	62.0	56.0	64	59	70
08/07/13	15:28	Fine	60.4	62.0	57.0	64	60	70
16/07/13	11:00	Cloudy	62.8	65.0	57.5	64	63	70
23/07/13	10:15	Fine	60.3	63.0	57.0	64	60	70




Graphic Presentation of Noise Monitoring Result
Day Time (0700 - 1900hrs on normal weekdays)

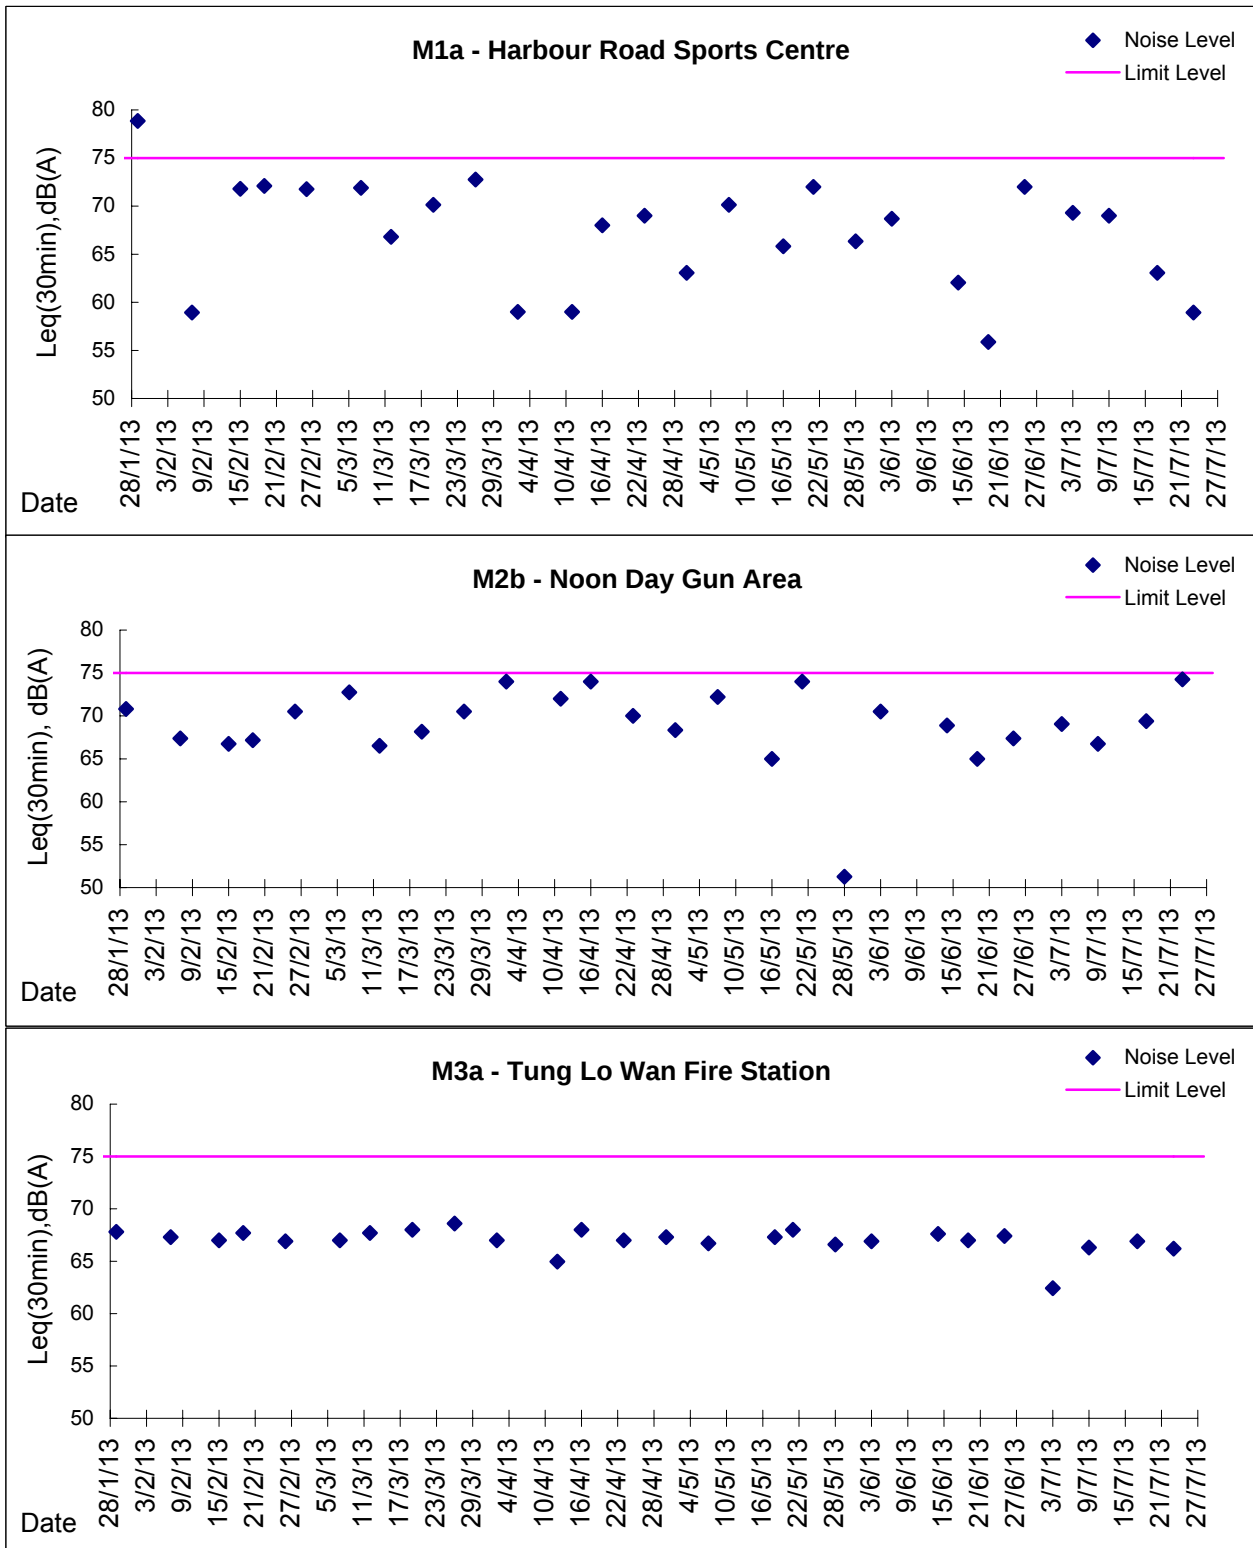

Graphic Presentation of Noise Monitoring Result
Day Time (0700 - 1900hrs on normal weekdays)

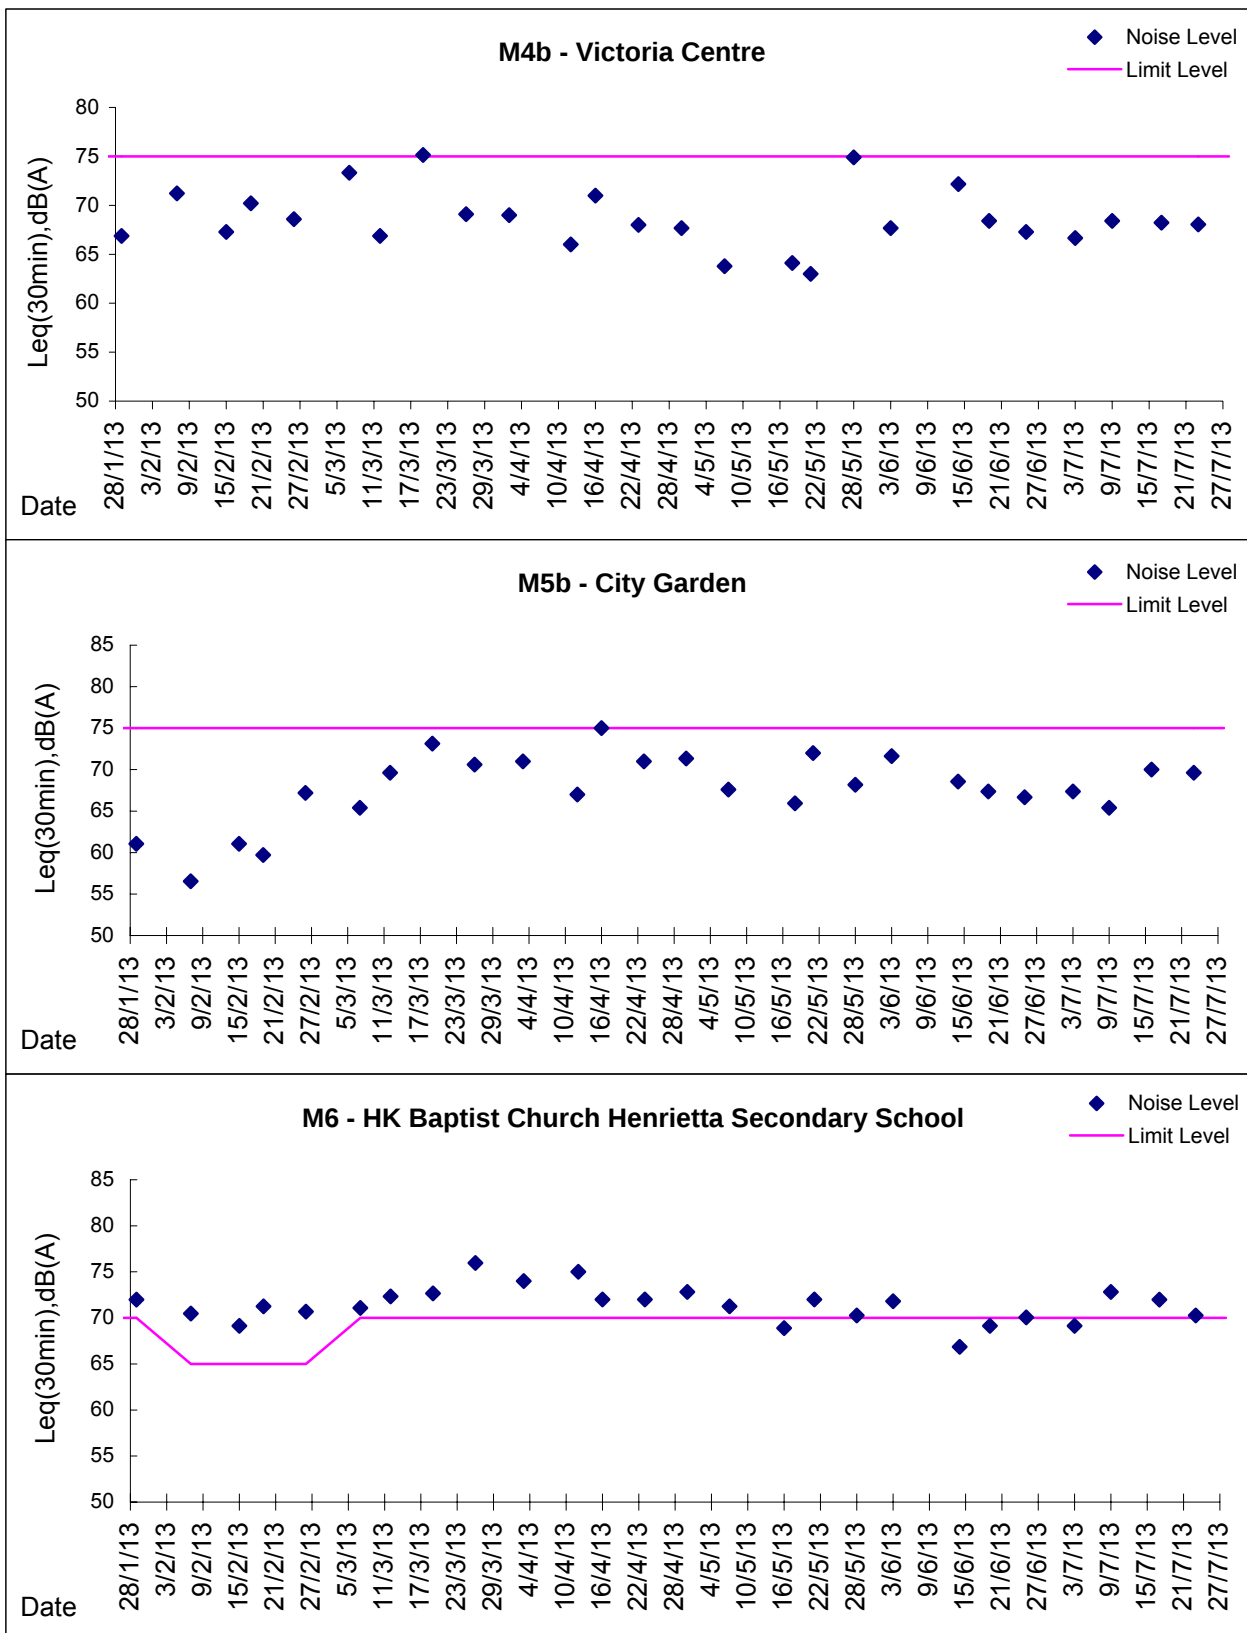

Graphic Presentation of Noise Monitoring Result
Day Time (0700 - 1900hrs on normal weekdays)

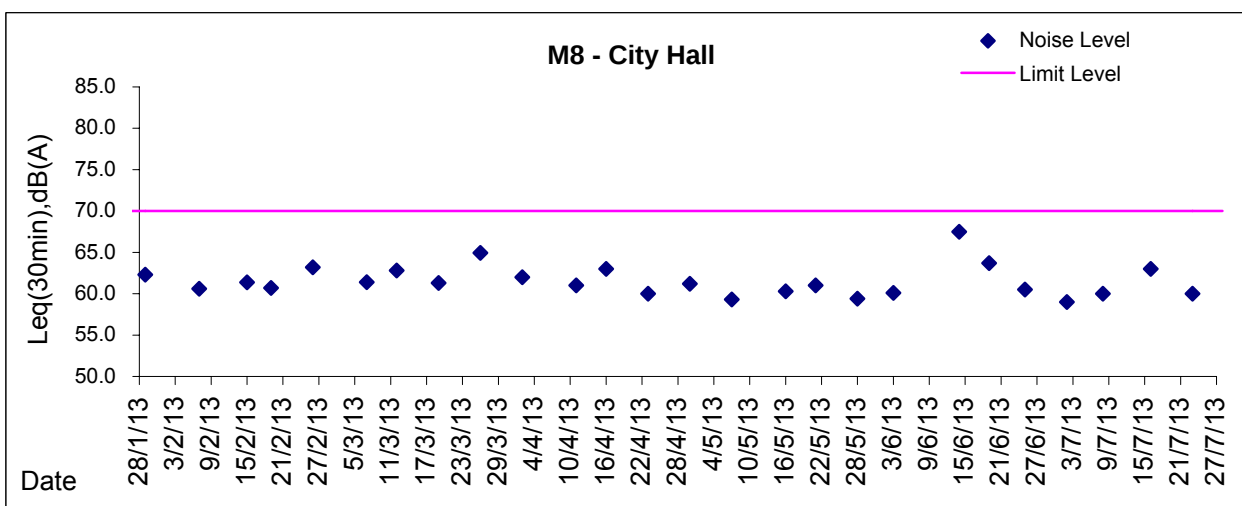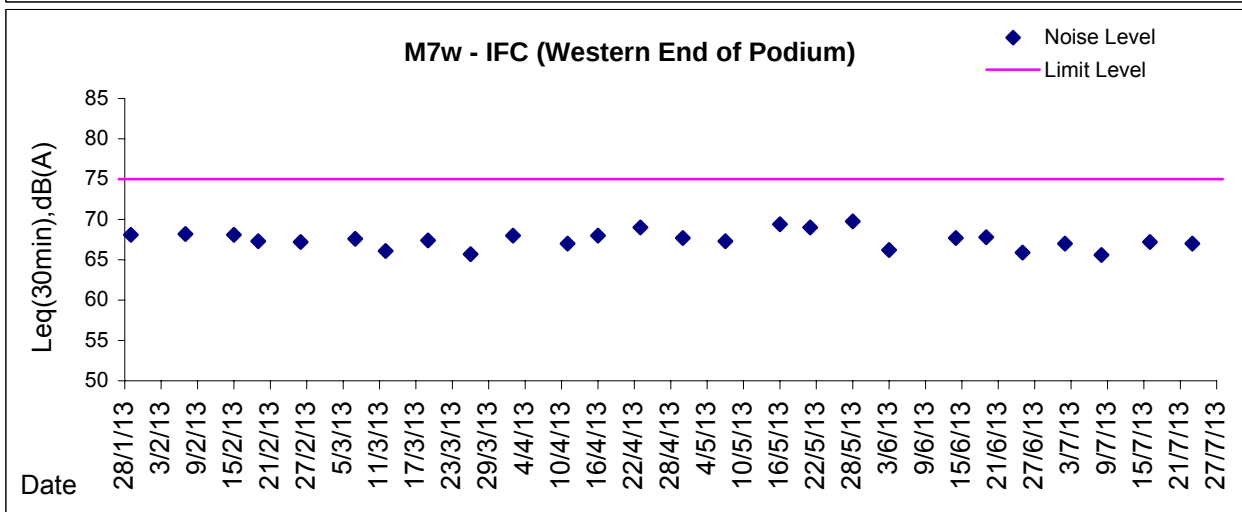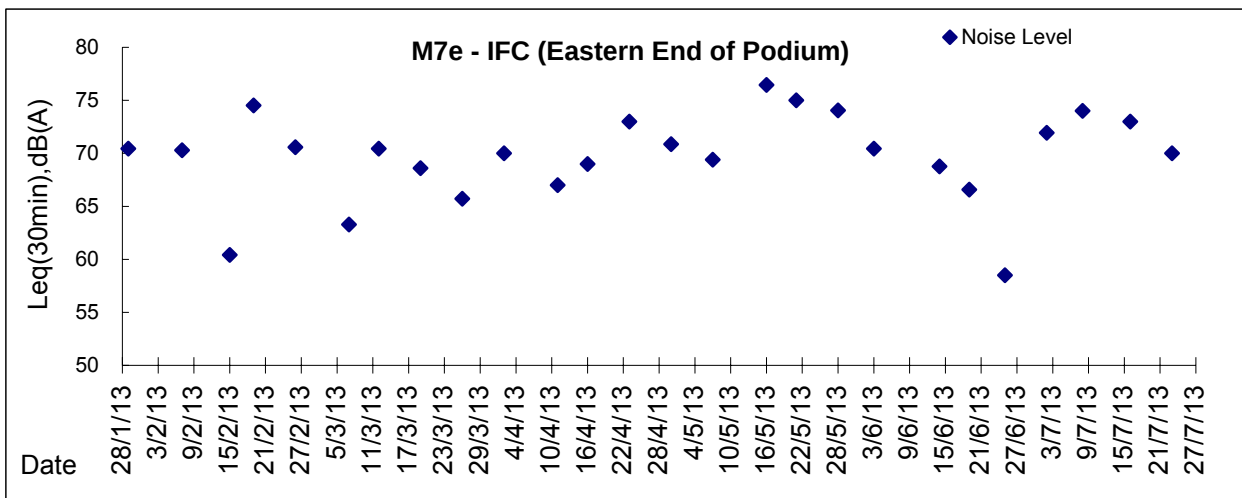

* Remark: M7e - IFC (Eastern End of Podium) is a reference monitoring station



Appendix 5.3

Air Quality Monitoring Results and Graphical Presentations



Location: CMA1b - Oil Street Site Office

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 176.7

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Jul-13	8:00	Fine	006509	2.7049	2.7671	3058.22	3082.22	24.00	1.17	1.17	1.17	1679	37
9-Jul-13	8:00	Fine	006911	2.6292	2.7083	3085.22	3109.22	24.00	1.48	1.48	1.48	2130	37
15-Jul-13	8:00	Rainy	006524	2.6432	2.7680	3112.22	3136.22	24.00	1.48	1.48	1.48	2130	59
20-Jul-13	8:00	Rainy	006617	2.6388	2.7046	3139.22	3163.22	24.00	1.38	1.38	1.38	1988	33
26-Jul-13	8:00	Rainy	006523	2.6539	2.7212	3166.35	3190.35	24.00	1.27	1.27	1.27	1830	37

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 320.1

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
4-Jul-13	8:06	Fine	006908	2.6396	2.6424	3082.22	3083.22	1.00	1.48	1.48	1.48	89	32
4-Jul-13	9:09	Fine	006909	2.6407	2.6449	3083.22	3084.22	1.00	1.48	1.48	1.48	89	47
4-Jul-13	10:35	Fine	006910	2.6214	2.6250	3084.22	3085.22	1.00	1.48	1.48	1.48	89	41
10-Jul-13	8:03	Rainy	006536	2.6595	2.6654	3109.22	3110.22	1.00	1.48	1.48	1.48	89	66
10-Jul-13	9:18	Rainy	006517	2.6605	2.6671	3110.22	3111.22	1.00	1.48	1.48	1.48	89	74
10-Jul-13	10:32	Rainy	005672	2.7304	2.7344	3111.22	3112.22	1.00	1.37	1.37	1.37	82	49
16-Jul-13	8:35	Rainy	006626	2.6202	2.6265	3136.22	3137.22	1.00	1.48	1.48	1.48	89	71
16-Jul-13	9:36	Rainy	006623	2.6110	2.6166	3137.22	3138.22	1.00	1.44	1.44	1.44	86	65
16-Jul-13	10:43	Rainy	006620	2.6365	2.6418	3138.22	3139.22	1.00	1.19	1.19	1.19	71	74
22-Jul-13	10:02	Rainy	006615	2.6168	2.6250	3163.22	3164.22	1.00	1.25	1.25	1.25	75	110
22-Jul-13	13:06	Rainy	006521	2.6587	2.6651	3164.22	3165.22	1.00	1.47	1.47	1.47	88	73
22-Jul-13	14:20	Rainy	006629	2.6195	2.6221	3165.22	3166.22	1.00	1.47	1.47	1.47	88	30
27-Jul-13	8:06	Rainy	006612	2.6211	2.6291	3190.35	3191.35	1.00	1.34	1.34	1.34	80	100
27-Jul-13	9:09	Rainy	007412	2.6231	2.6281	3191.35	3192.35	1.00	1.40	1.40	1.40	84	59
27-Jul-13	10:13	Rainy	007382	2.6777	2.6830	3192.35	3193.35	1.00	1.47	1.47	1.47	88	60



Location: CMA2a - Causeway Bay Community Centre

Report on 24-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 169.5
Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Jul-13	8:00	Fine	006508	2.7458	2.8196	12794.66	12818.65	23.99	1.52	1.52	1.52	2194	34
9-Jul-13	8:00	Fine	006915	2.6377	2.7108	12821.66	12845.66	24.00	1.38	1.38	1.38	1987	37
15-Jul-13	8:00	Rainy	006934	2.6496	2.7236	12848.67	12872.67	24.00	1.42	1.42	1.42	2040	36
20-Jul-13	8:00	Rainy	006618	2.6568	2.7035	12875.67	12899.67	24.00	1.16	1.16	1.16	1668	28
26-Jul-13	8:00	Rainy	007362	2.6163	2.6964	12902.69	12926.69	24.00	1.38	1.38	1.38	1986	40

Report on 1-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 323.4
Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
4-Jul-13	8:07	Fine	006912	2.6299	2.6369	12818.65	12819.65	1.00	1.41	1.41	1.41	85	82
4-Jul-13	9:14	Fine	006913	2.6209	2.6232	12819.65	12820.65	1.00	1.19	1.19	1.19	72	32
4-Jul-13	10:29	Fine	006914	2.6395	2.6414	12820.65	12821.65	1.00	1.41	1.41	1.41	85	22
10-Jul-13	8:09	Rainy	006516	2.6551	2.6627	12845.66	12846.66	1.00	1.38	1.38	1.38	83	92
10-Jul-13	9:19	Rainy	006518	2.6612	2.6672	12846.66	12847.66	1.00	1.27	1.25	1.26	76	79
10-Jul-13	10:24	Rainy	006537	2.6647	2.6717	12847.66	12848.66	1.00	1.20	1.20	1.20	72	97
16-Jul-13	8:12	Rainy	006627	2.6322	2.6365	12872.67	12873.67	1.00	1.42	1.42	1.42	85	51
16-Jul-13	9:23	Rainy	006624	2.6346	2.6386	12873.67	12874.67	1.00	1.42	1.42	1.42	85	47
16-Jul-13	10:35	Rainy	006621	2.6277	2.6345	12874.67	12875.67	1.00	1.42	1.42	1.42	85	80
22-Jul-13	10:03	Rainy	006616	2.6466	2.6499	12899.67	12900.67	1.00	1.34	1.32	1.33	80	41
22-Jul-13	13:05	Rainy	007354	2.6519	2.6545	12900.69	12901.69	1.00	1.34	1.32	1.33	80	33
22-Jul-13	14:10	Rainy	007363	2.6275	2.6296	12901.69	12902.69	1.00	1.21	1.49	1.35	81	26
27-Jul-13	8:03	Rainy	007413	2.6451	2.6510	12926.69	12927.69	1.00	1.40	1.40	1.40	84	70
27-Jul-13	9:06	Rainy	007413	2.6619	2.6725	12927.69	12928.69	1.00	1.38	1.38	1.38	83	128
27-Jul-13	10:09	Rainy	007387	2.6535	2.6644	12928.69	12929.69	1.00	1.38	1.38	1.38	83	132



Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 171
Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Jul-13	8:00	Fine	006899	2.6162	2.6896	31.66	55.66	24.00	1.41	1.41	1.41	2030	36
9-Jul-13	8:00	Fine	006634	2.6472	2.7562	58.66	82.66	24.00	1.41	1.41	1.41	2033	54
15-Jul-13	8:00	Rainy	006983	2.6260	2.7036	85.66	109.66	24.00	1.41	1.41	1.41	2033	38
20-Jul-13	8:00	Rainy	006851	2.6357	2.7461	112.66	136.66	24.00	1.41	1.41	1.41	2035	54
26-Jul-13	8:00	Rainy	007353	2.6450	2.7295	139.66	163.66	24.00	1.41	1.41	1.41	2035	42

Report on 1-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 311.3
Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
4-Jul-13	9:20	Fine	004958	2.7657	2.7750	55.66	56.66	1.00	1.41	1.41	1.41	85	110
4-Jul-13	10:45	Fine	006633	2.6555	2.6572	56.66	57.66	1.00	1.41	1.41	1.41	85	20
4-Jul-13	15:10	Fine	006631	2.6191	2.6211	57.66	58.66	1.00	1.41	1.41	1.41	85	24
10-Jul-13	8:06	Rainy	006984	2.6339	2.6390	82.66	83.66	1.00	1.41	1.41	1.41	85	60
10-Jul-13	9:13	Rainy	006916	2.6363	2.6404	83.66	84.66	1.00	1.41	1.41	1.41	85	48
10-Jul-13	10:26	Rainy	006917	2.6560	2.6601	84.66	85.66	1.00	1.41	1.41	1.41	85	48
16-Jul-13	8:09	Rainy	006848	2.6115	2.6194	109.66	110.66	1.00	1.41	1.41	1.41	85	93
16-Jul-13	9:16	Rainy	006849	2.6191	2.6276	110.66	111.66	1.00	1.41	1.41	1.41	85	100
16-Jul-13	10:28	Rainy	006850	2.6346	2.6385	111.66	112.66	1.00	1.41	1.41	1.41	85	46
22-Jul-13	8:15	Rainy	007366	2.6665	2.6739	136.66	137.66	1.00	1.41	1.41	1.41	85	87
22-Jul-13	9:35	Rainy	007364	2.6439	2.6522	137.66	138.66	1.00	1.41	1.41	1.41	85	98
22-Jul-13	10:40	Rainy	007351	2.6373	2.6448	138.66	139.66	1.00	1.41	1.41	1.41	85	89
27-Jul-13	8:05	Rainy	006575	2.6642	2.6700	163.66	164.66	1.00	1.41	1.41	1.41	85	68
27-Jul-13	9:13	Rainy	006577	2.6526	2.6564	164.66	165.66	1.00	1.34	1.38	1.36	81	47
27-Jul-13	10:21	Rainy	006581	2.6593	2.6652	165.66	166.66	1.00	1.70	1.70	1.70	102	58



Location: CMA4a - SPCA

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 171.2

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Jul-13	8:00	Fine	006883	2.6322	2.7641	16971.37	16995.37	24.00	1.26	1.26	1.26	1811	73
9-Jul-13	8:00	Fine	006635	2.6374	2.6835	16998.38	17022.38	24.00	1.26	1.26	1.26	1813	25
15-Jul-13	8:00	Rainy	006895	2.6340	2.6860	17025.86	17049.86	24.00	1.28	1.28	1.28	1842	28
20-Jul-13	8:00	Rainy	006855	2.6212	2.7135	17052.86	17076.86	24.00	1.28	1.28	1.28	1848	50
26-Jul-13	8:00	Rainy	007352	2.6281	2.6927	17079.86	17103.86	24.00	1.30	1.30	1.30	1876	34

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 312.5

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
4-Jul-13	9:02	Fine	004957	2.7531	2.7600	16995.37	16996.37	1.00	1.26	1.26	1.26	75	91
4-Jul-13	10:28	Fine	006632	2.6333	2.6363	16996.37	16997.37	1.00	1.26	1.26	1.26	75	40
4-Jul-13	14:45	Fine	006630	2.6227	2.6247	16997.37	16998.37	1.00	1.26	1.26	1.26	75	27
10-Jul-13	8:16	Rainy	006892	2.6025	2.6048	17022.38	17023.38	1.00	1.26	1.26	1.26	76	30
10-Jul-13	9:23	Rainy	006893	2.6164	2.6186	17023.38	17024.38	1.00	1.26	1.26	1.26	76	29
10-Jul-13	10:35	Rainy	006894	2.6458	2.6489	17024.38	17025.38	1.00	1.26	1.26	1.26	76	41
16-Jul-13	8:23	Rainy	006857	2.6570	2.6592	17049.86	17050.86	1.00	1.28	1.28	1.28	77	29
16-Jul-13	9:32	Rainy	006853	2.6435	2.6485	17050.86	17051.86	1.00	1.28	1.28	1.28	77	65
16-Jul-13	10:42	Rainy	006854	2.6388	2.6406	17051.86	17052.86	1.00	1.28	1.28	1.28	77	23
22-Jul-13	8:03	Rainy	007367	2.6525	2.6564	17076.86	17077.86	1.00	1.30	1.30	1.30	78	50
22-Jul-13	9:20	Rainy	007365	2.6610	2.6661	17077.86	17078.86	1.00	1.30	1.30	1.30	78	65
22-Jul-13	10:30	Rainy	007350	2.6578	2.6626	17078.86	17079.86	1.00	1.30	1.30	1.30	78	61
27-Jul-13	8:22	Rainy	006576	2.6540	2.6571	17103.86	17104.86	1.00	1.03	1.30	1.17	70	44
27-Jul-13	9:25	Rainy	006578	2.6558	2.6613	17104.86	17105.86	1.00	1.22	1.30	1.26	76	73
27-Jul-13	10:33	Rainy	006580	2.6496	2.6554	17105.86	17106.86	1.00	1.32	1.30	1.31	79	74



Location: CMA5a - Children Garden opposite to Pedestrian Plaza

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 181
Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
4-Jul-13	17:00	Fine	006515	2.6489	2.7043	17972.95	17996.95	24.00	1.33	1.33	1.33	1908	29
9-Jul-13	8:00	Fine	006935	2.6577	2.7595	17996.95	18020.95	24.00	1.35	1.35	1.35	1941	52
15-Jul-13	8:00	Rainy	007373	2.6595	2.7296	18036.73	18060.73	24.00	1.45	1.45	1.45	2088	34
20-Jul-13	8:00	Rainy	005674	2.6772	2.8157	18060.73	18084.73	24.00	1.33	1.33	1.33	1921	72
26-Jul-13	8:00	Rainy	006572	2.6933	2.7474	18087.73	18111.73	24.00	1.33	1.33	1.33	1921	28

*Due to lack of electricity supply, the 24hr TSP monitoring was rescheduled from 3 July 2013 to 4 July 2013.

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 332
Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
4-Jul-13	8:05	Fine	006959	2.6494	2.6553	17969.95	17970.95	1.00	1.33	1.33	1.33	80	74
4-Jul-13	9:10	Fine	006961	2.6314	2.6345	17970.95	17971.95	1.00	1.24	1.24	1.24	75	42
4-Jul-13	10:21	Fine	006514	2.6576	2.6617	17971.95	17972.95	1.00	1.24	1.24	1.24	75	55
10-Jul-13	8:30	Rainy	006554	2.6352	2.6389	18020.95	18021.95	1.00	1.29	1.29	1.29	77	48
10-Jul-13	9:32	Rainy	006717	2.6617	2.6640	18021.95	18022.95	1.00	1.33	1.33	1.33	80	29
10-Jul-13	10:36	Rainy	006597	2.6175	2.6255	18022.95	18023.95	1.00	1.33	1.33	1.33	80	100
16-Jul-13	8:30	Rainy	006594	2.6363	2.6413	18060.73	18061.73	1.00	1.20	1.20	1.20	72	69
16-Jul-13	9:32	Rainy	006562	2.6346	2.6375	18061.73	18062.73	1.00	1.25	1.25	1.25	75	39
16-Jul-13	10:36	Rainy	006564	2.6731	2.6750	18062.73	18063.73	1.00	1.25	1.25	1.25	75	25
22-Jul-13	8:31	Rainy	006569	2.6786	2.6834	18084.73	18085.73	1.00	1.33	1.29	1.31	79	61
22-Jul-13	9:35	Rainy	006568	2.6568	2.6658	18085.73	18086.73	1.00	1.33	1.33	1.33	80	113
22-Jul-13	10:40	Rainy	006571	2.6536	2.6579	18086.73	18087.73	1.00	1.21	1.21	1.21	73	59
27-Jul-13	13:01	Rainy	007378	2.6829	2.6871	18111.73	18112.73	1.00	1.33	1.33	1.33	80	52
27-Jul-13	14:25	Rainy	007411	2.6449	2.6502	18112.73	18113.73	1.00	1.35	1.35	1.35	81	65
27-Jul-13	15:31	Rainy	006936	2.6406	2.6466	18113.73	18114.73	1.00	1.33	1.33	1.33	80	75



Location: MA1e - International Finance Centre (Eastern Wing)

Report on 24-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 173.4
Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Jul-13	8:00	Fine	006861	2.6558	2.7194	10611.33	10635.33	24.00	1.27	1.27	1.27	1831	35
9-Jul-13	8:00	Fine	006931	2.6336	2.6855	10638.34	10662.34	24.00	1.33	1.33	1.33	1909	27
15-Jul-13	8:00	Rainy	007371	2.6369	2.6872	13687.75	13711.75	24.00	1.26	1.26	1.26	1808	28
20-Jul-13	8:00	Rainy	007369	2.6540	2.7157	13714.75	13738.75	24.00	1.29	1.29	1.29	1856	33
26-Jul-13	8:00	Rainy	007160	2.6339	2.6680	13741.87	13765.87	24.00	1.29	1.29	1.29	1856	18

Report on 1-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 325.1
Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
4-Jul-13	8:03	Fine	006862	2.6490	2.6544	10635.33	10636.33	1.00	1.29	1.29	1.29	77	70
4-Jul-13	9:07	Fine	006933	2.6345	2.6380	10636.33	10637.33	1.00	1.29	1.29	1.29	77	45
4-Jul-13	10:15	Fine	006864	2.6255	2.6283	10637.33	10638.33	1.00	1.29	1.29	1.29	77	36
10-Jul-13	8:02	Rainy	006867	2.6067	2.6106	10662.34	10663.34	1.00	1.29	1.29	1.29	77	50
10-Jul-13	9:09	Rainy	006869	2.6232	2.6273	10663.34	10664.34	1.00	1.29	1.29	1.29	77	53
10-Jul-13	10:16	Rainy	006871	2.6345	2.6386	10664.34	10665.34	1.00	1.29	1.29	1.29	77	53
16-Jul-13	8:06	Rainy	007344	2.6575	2.6587	13711.75	13712.75	1.00	1.26	1.22	1.24	74	16
16-Jul-13	9:20	Rainy	007346	2.6309	2.6338	13712.75	13713.75	1.00	1.26	1.26	1.26	75	38
16-Jul-13	10:30	Rainy	007348	2.6369	2.6392	13713.75	13714.75	1.00	1.26	1.26	1.26	75	31
22-Jul-13	8:05	Rainy	007153	2.6148	2.6186	13738.75	13739.75	1.00	1.30	1.30	1.30	78	49
22-Jul-13	9:07	Rainy	007155	2.6211	2.6248	13739.75	13740.75	1.00	1.24	1.24	1.24	74	50
22-Jul-13	10:12	Rainy	007157	2.6071	2.6098	13740.75	13741.75	1.00	1.30	1.27	1.29	77	35
27-Jul-13	8:10	Rainy	007361	2.6443	2.6479	13765.87	13766.87	1.00	1.29	1.29	1.29	77	47
27-Jul-13	9:15	Rainy	007360	2.6378	2.6423	13766.87	13767.87	1.00	1.31	1.29	1.30	78	58
27-Jul-13	10:20	Rainy	007358	2.6326	2.6383	13767.87	13768.87	1.00	1.27	1.27	1.27	76	75



Location: MA1w - International Finance Centre (Western Wing)

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 173.4

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Jul-13	8:00	Fine	006930	2.6418	2.7181	13729.79	13753.78	23.99	1.39	1.37	1.38	1989	38
9-Jul-13	8:00	Fine	006866	2.6039	2.6806	13756.79	13780.79	24.00	1.37	1.37	1.37	1979	39
15-Jul-13	8:00	Rainy	007370	2.6573	2.7171	13783.79	13807.79	24.00	1.38	1.38	1.38	1983	30
20-Jul-13	8:00	Rainy	007368	2.6768	2.7576	13810.79	13834.79	24.00	1.37	1.37	1.37	1975	41
26-Jul-13	8:00	Rainy	007159	2.6451	2.6916	13837.96	13861.96	24.00	1.33	1.33	1.33	1920	24




Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 325.1




Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
4-Jul-13	8:02	Fine	006863	2.6292	2.6349	13753.78	13754.78	1.00	1.39	1.39	1.39	83	68
4-Jul-13	9:10	Fine	006932	2.6436	2.6484	13754.78	13755.78	1.00	1.39	1.39	1.39	83	57
4-Jul-13	10:20	Fine	006865	2.6127	2.6153	13755.78	13756.78	1.00	1.39	1.39	1.39	83	31
10-Jul-13	8:10	Rainy	006868	2.6157	2.6188	13780.79	13781.79	1.00	1.37	1.37	1.37	82	38
10-Jul-13	9:15	Rainy	006870	2.6291	2.6330	13781.79	13782.79	1.00	1.37	1.37	1.37	82	47
10-Jul-13	10:20	Rainy	007372	2.6668	2.6703	13782.79	13783.79	1.00	1.37	1.37	1.37	82	42
16-Jul-13	8:10	Rainy	007345	2.6464	2.6485	13807.79	13808.79	1.00	1.40	1.40	1.40	84	25
16-Jul-13	9:26	Rainy	007347	2.6321	2.6352	13808.79	13809.79	1.00	1.40	1.40	1.40	84	37
16-Jul-13	10:32	Rainy	007349	2.6456	2.6490	13809.79	13810.79	1.00	1.38	1.38	1.38	83	41
22-Jul-13	8:10	Rainy	007154	2.6260	2.6291	13834.79	13835.79	1.00	1.37	1.37	1.37	82	38
22-Jul-13	9:13	Rainy	007156	2.6081	2.6103	13835.79	13836.79	1.00	1.37	1.37	1.37	82	27
22-Jul-13	10:17	Rainy	007158	2.6392	2.6433	13836.79	13837.79	1.00	1.39	1.39	1.39	83	49
27-Jul-13	8:20	Rainy	007330	2.6776	2.6802	13861.96	13862.96	1.00	1.39	1.39	1.39	83	31
27-Jul-13	9:25	Rainy	007359	2.6479	2.6541	13862.96	13863.96	1.00	1.27	1.27	1.27	76	81
27-Jul-13	10:30	Rainy	007331	2.6917	2.6962	13863.96	13864.96	1.00	1.39	1.39	1.39	83	54


Graphic Presentation of 1 hour TSP Result

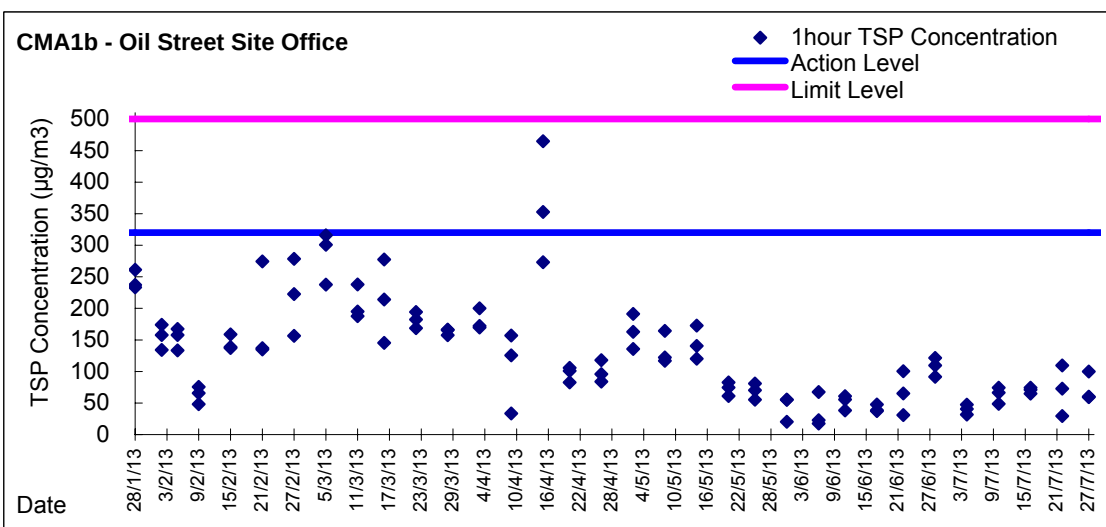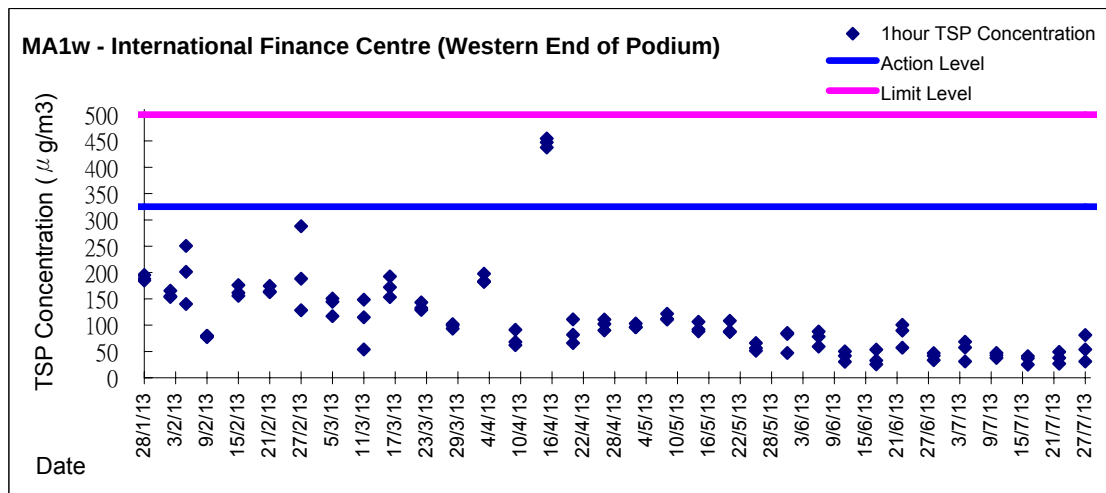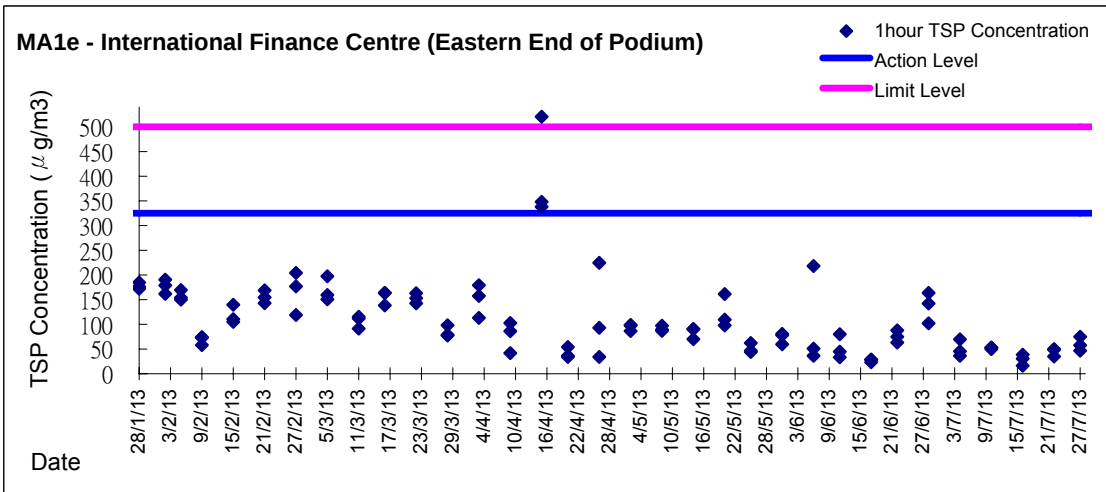




Graphic Presentation of 1 hour TSP Result

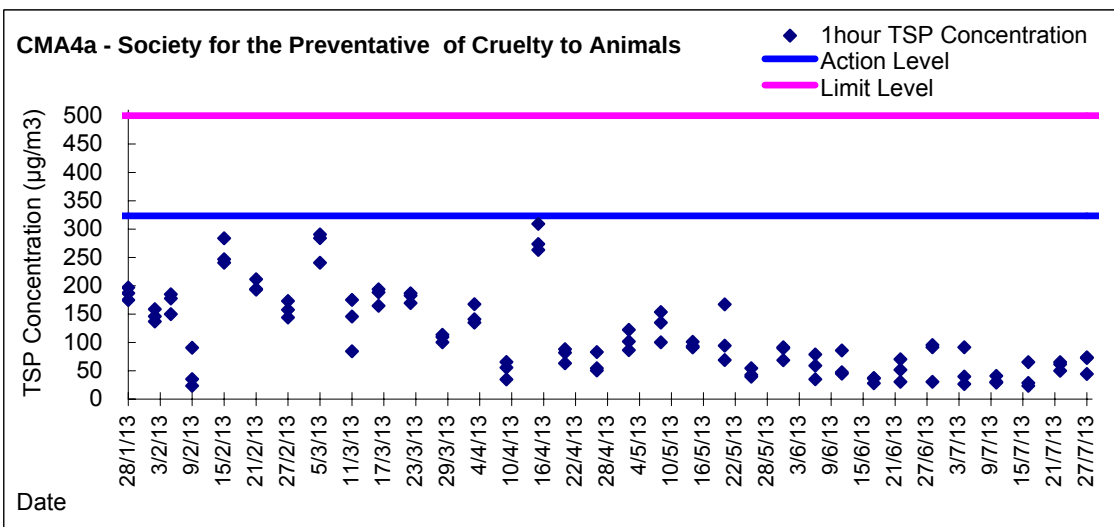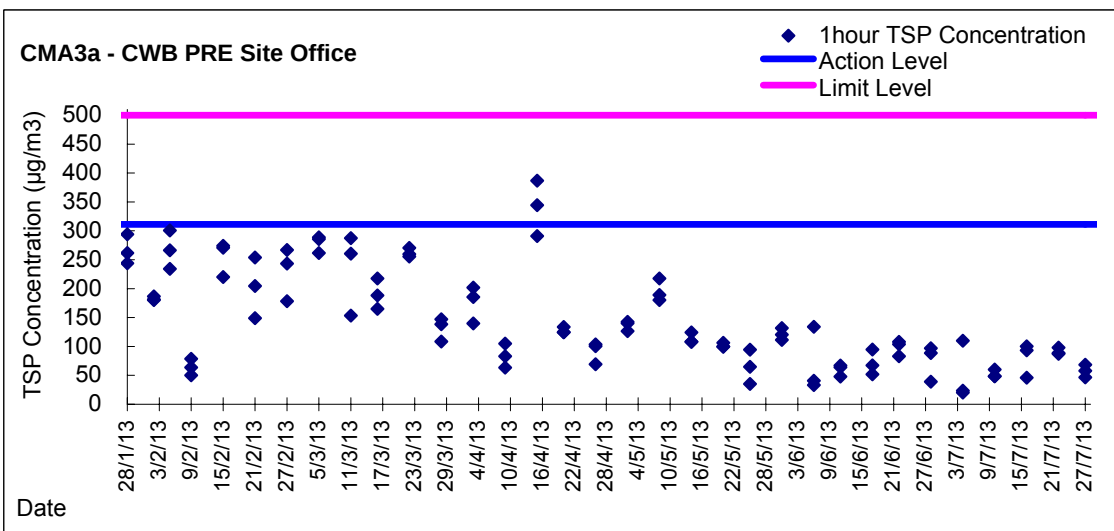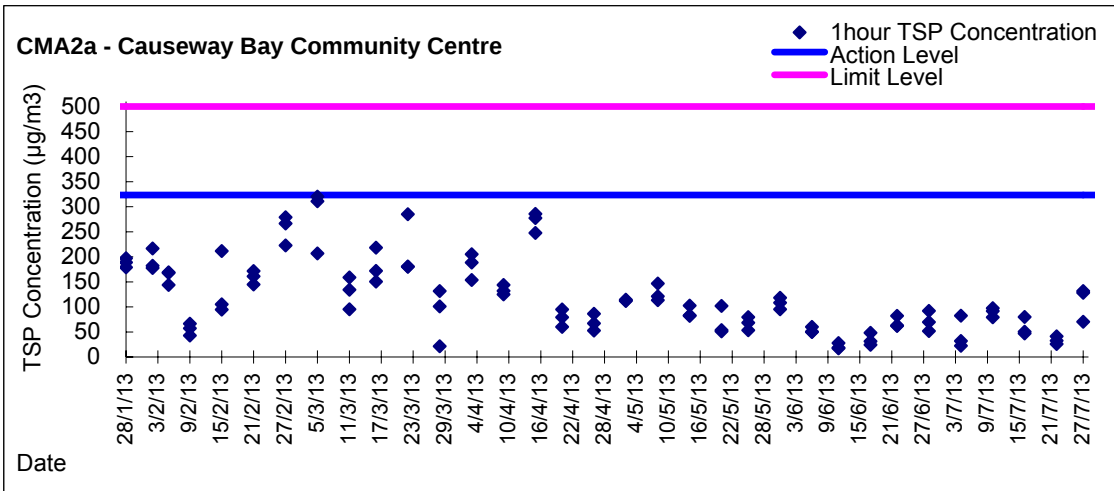




Graphic Presentation of 1 hour TSP Result

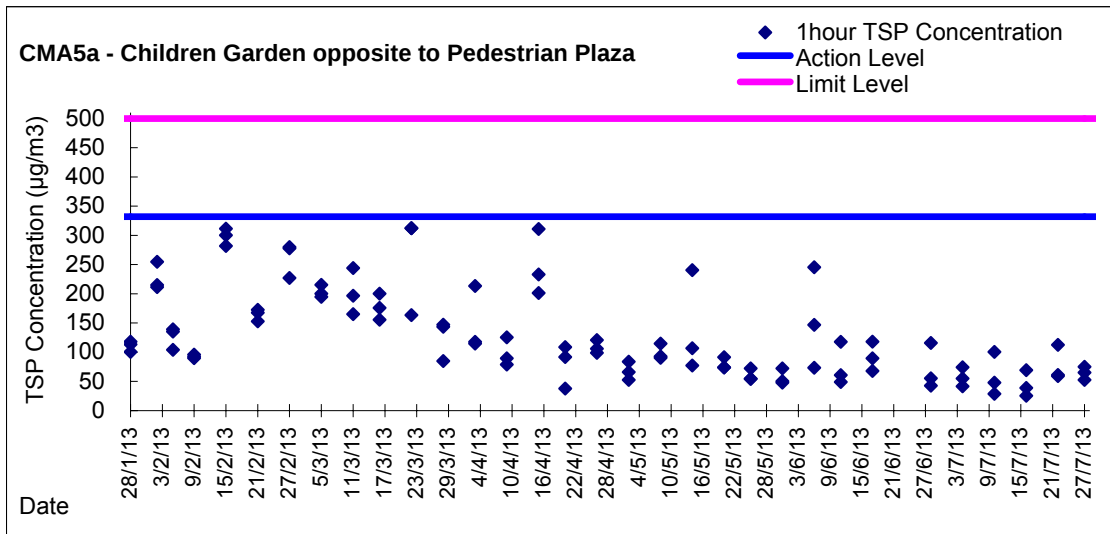


Graphic Presentation of 24 hour TSP Result

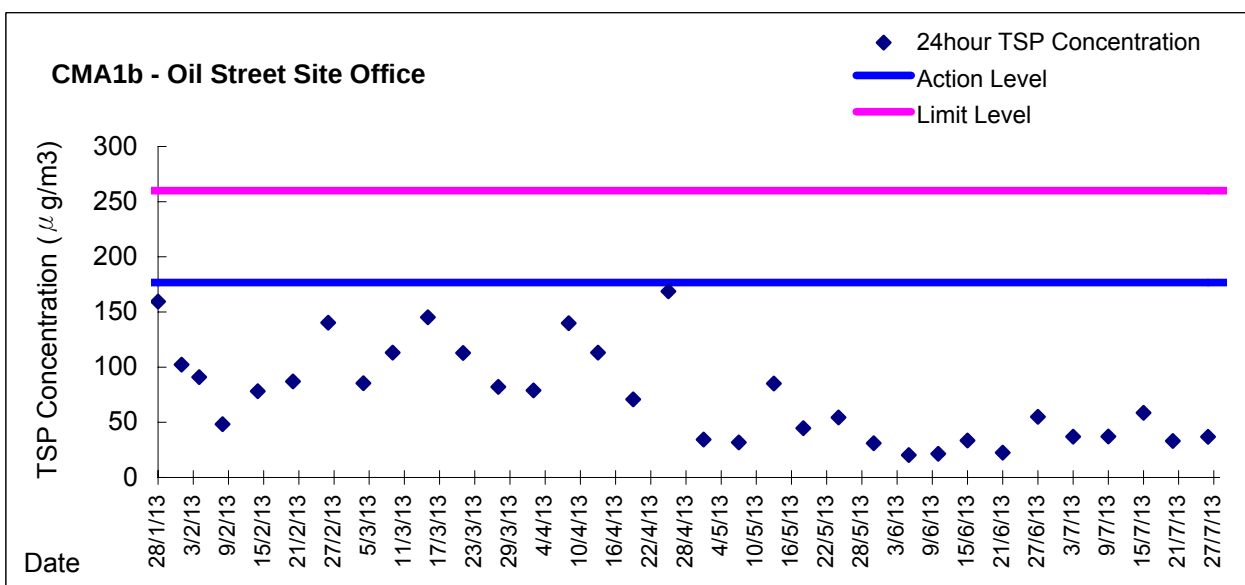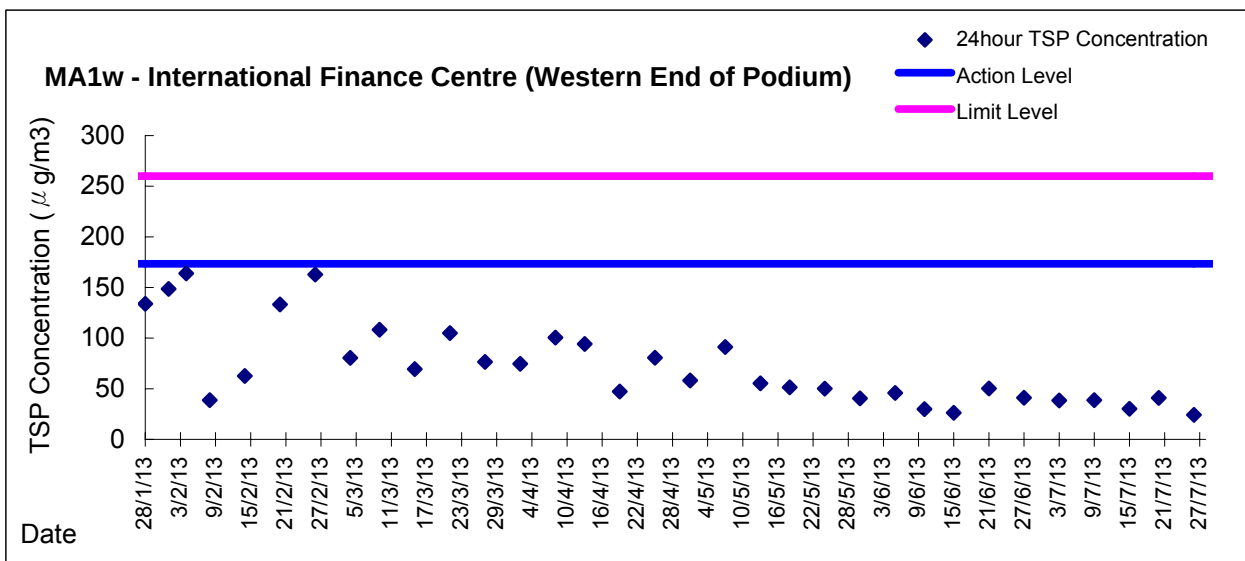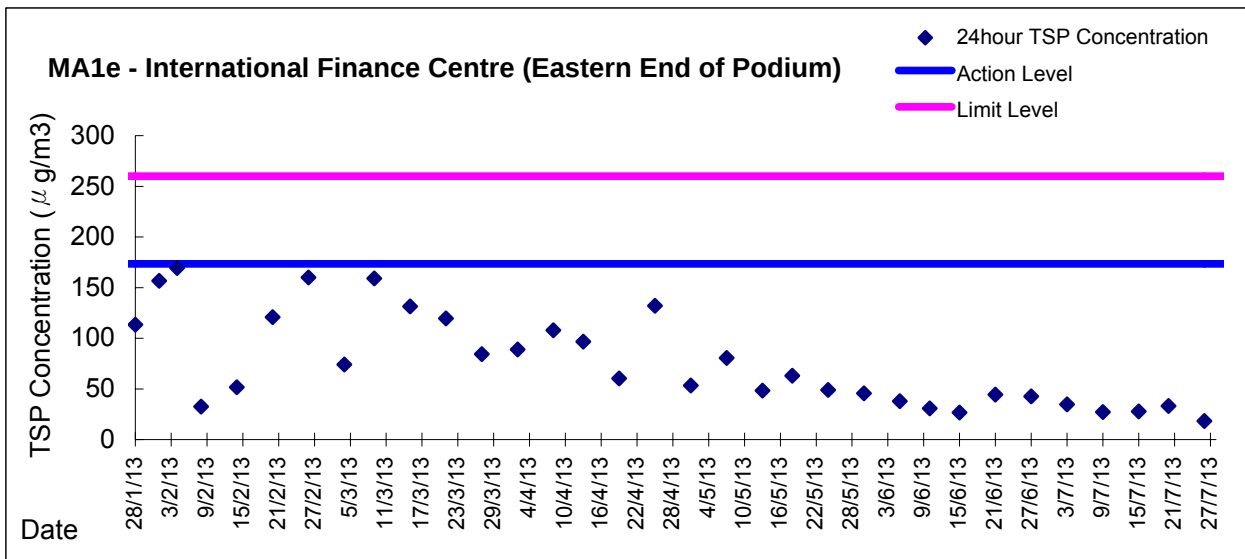

Graphic Presentation of 24 hour TSP Result

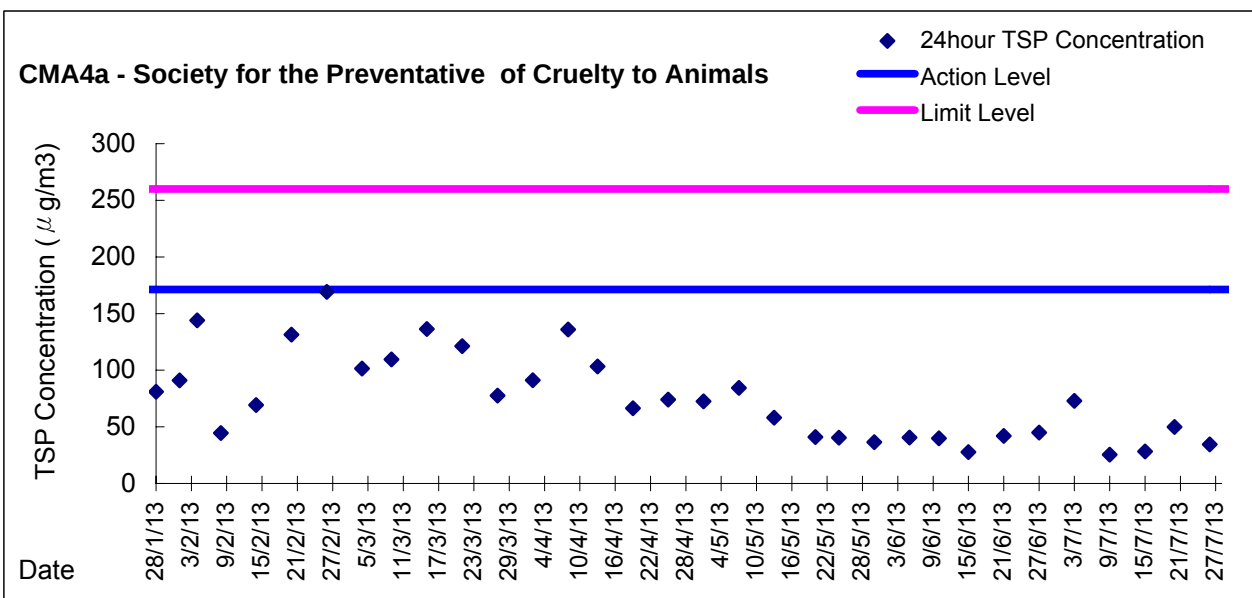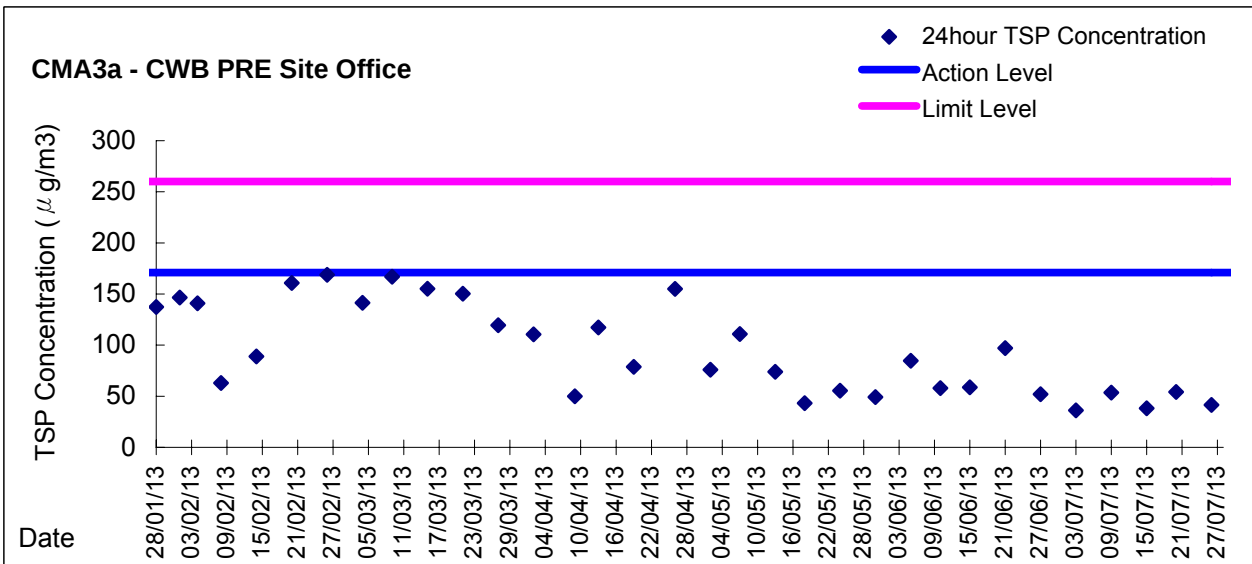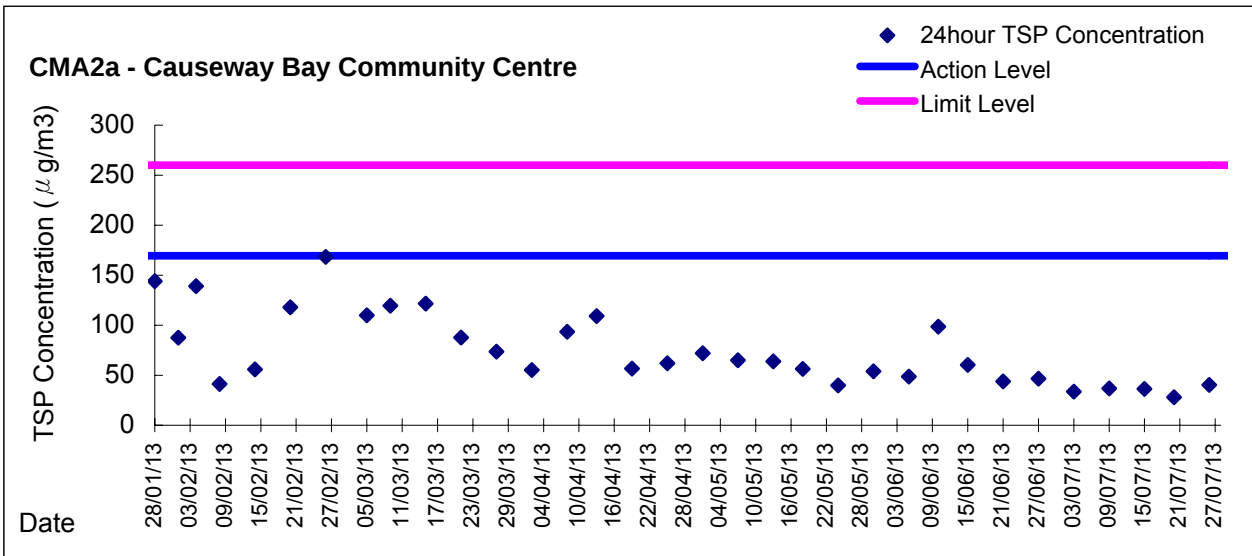

Graphic Presentation of 24 hour TSP Result

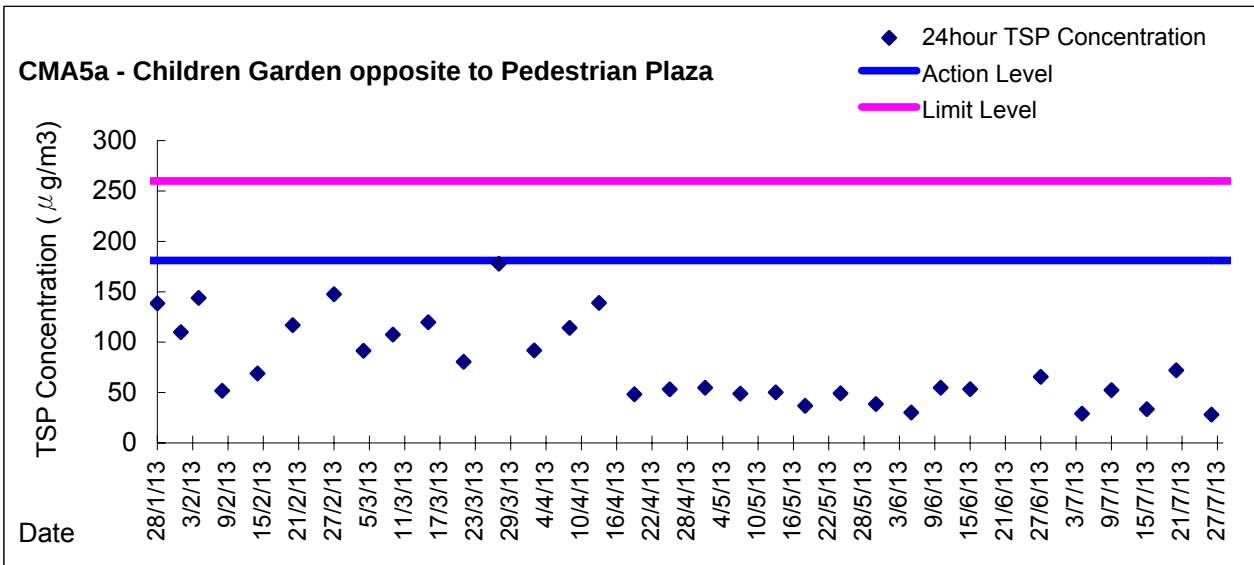



Appendix 5.4

Real Time Noise Monitoring Results and Graphical Presentations

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)													
28/6/2013 22:51	64.7	30/6/2013 11:56	67.2	30/6/2013 21:01	64.8	1/7/2013 14:06	64.9	2/7/2013 19:11	66.9	4/7/2013 20:16	66.0				
28/6/2013 22:56	64.6	30/6/2013 12:01	67.1	30/6/2013 21:06	65.0	1/7/2013 14:11	65.1	2/7/2013 19:16	66.5	4/7/2013 20:21	66.2				
29/6/2013 19:01	64.4	30/6/2013 12:06	67.1	30/6/2013 21:11	65.2	1/7/2013 14:16	64.7	2/7/2013 19:21	67.0	4/7/2013 20:26	66.3				
29/6/2013 19:06	63.6	30/6/2013 12:11	67.1	30/6/2013 21:16	65.1	1/7/2013 14:21	65.6	2/7/2013 19:26	66.8	4/7/2013 20:31	66.0				
29/6/2013 19:11	64.1	30/6/2013 12:16	66.9	30/6/2013 21:21	64.7	1/7/2013 14:26	65.4	2/7/2013 19:31	67.7	4/7/2013 20:36	66.1				
29/6/2013 19:16	63.8	30/6/2013 12:21	66.5	30/6/2013 21:26	64.4	1/7/2013 14:31	65.2	2/7/2013 19:36	66.8	4/7/2013 20:41	66.6				
29/6/2013 19:21	64.2	30/6/2013 12:26	66.6	30/6/2013 21:31	64.2	1/7/2013 14:36	65.2	2/7/2013 19:41	67.4	4/7/2013 20:46	65.9				
29/6/2013 19:26	64.8	30/6/2013 12:31	66.7	30/6/2013 21:36	65.3	1/7/2013 14:41	65.5	2/7/2013 19:46	67.2	4/7/2013 20:51	65.7				
29/6/2013 19:31	64.3	30/6/2013 12:36	66.5	30/6/2013 21:41	64.6	1/7/2013 14:46	66.2	2/7/2013 19:51	66.7	4/7/2013 20:56	66.0				
29/6/2013 19:36	63.9	30/6/2013 12:41	66.9	30/6/2013 21:46	64.9	1/7/2013 14:51	65.3	2/7/2013 19:56	66.6	4/7/2013 21:01	66.0				
29/6/2013 19:41	63.9	30/6/2013 12:46	66.5	30/6/2013 21:51	65.0	1/7/2013 14:56	65.5	2/7/2013 20:01	66.8	4/7/2013 21:06	65.9				
29/6/2013 19:46	64.3	30/6/2013 12:51	66.7	30/6/2013 21:56	64.7	1/7/2013 15:01	65.1	2/7/2013 20:06	66.7	4/7/2013 21:11	65.7				
29/6/2013 19:51	65.4	30/6/2013 12:56	67.1	30/6/2013 22:01	64.7	1/7/2013 15:06	65.6	2/7/2013 20:11	66.5	4/7/2013 21:16	66.0				
29/6/2013 19:56	65.2	30/6/2013 13:01	67.7	30/6/2013 22:06	65.2	1/7/2013 15:11	65.6	2/7/2013 20:16	66.9	4/7/2013 21:21	65.8				
29/6/2013 20:01	64.7	30/6/2013 13:06	67.5	30/6/2013 22:11	64.2	1/7/2013 15:16	65.4	2/7/2013 20:21	66.5	4/7/2013 21:26	65.9				
29/6/2013 20:06	64.6	30/6/2013 13:11	67.5	30/6/2013 22:16	64.1	1/7/2013 15:21	65.6	2/7/2013 20:26	66.6	4/7/2013 21:31	65.8				
29/6/2013 20:11	64.6	30/6/2013 13:16	67.7	30/6/2013 22:21	63.9	1/7/2013 15:26	67.4	2/7/2013 20:31	66.6	4/7/2013 21:36	65.9				
29/6/2013 20:16	65.1	30/6/2013 13:21	68.5	30/6/2013 22:26	64.3	1/7/2013 15:31	67.3	2/7/2013 20:36	66.7	4/7/2013 21:41	65.8				
29/6/2013 20:21	65.5	30/6/2013 13:26	68.1	30/6/2013 22:31	64.3	1/7/2013 15:36	67.1	2/7/2013 20:41	67.1	4/7/2013 21:46	65.4				
29/6/2013 20:26	65.1	30/6/2013 13:31	68.9	30/6/2013 22:36	64.7	1/7/2013 15:41	67.3	2/7/2013 20:46	66.3	4/7/2013 21:51	65.9				
29/6/2013 20:31	65.0	30/6/2013 13:36	68.7	30/6/2013 22:41	64.1	1/7/2013 15:46	66.8	2/7/2013 20:51	66.6	4/7/2013 21:56	65.7				
29															

Real-time Noise Data			RTN1 (Food and Environmental Hygiene Department Depot)														
14/7/2013 19:51	65.2		16/7/2013 20:56	65.0		18/7/2013 22:01	66.1		21/7/2013 7:06	63.9		21/7/2013 16:11	64.5		22/7/2013 21:16	64.7	
14/7/2013 19:56	66.4		16/7/2013 21:01	64.7		18/7/2013 22:06	66.0		21/7/2013 7:11	64.3		21/7/2013 16:16	64.1		22/7/2013 21:21	65.0	
14/7/2013 20:01	68.4		16/7/2013 21:06	64.7		18/7/2013 22:11	66.7		21/7/2013 7:16	64.4		21/7/2013 16:21	64.2		22/7/2013 21:26	64.9	
14/7/2013 20:06	71.0		16/7/2013 21:11	64.3		18/7/2013 22:16	66.0		21/7/2013 7:21	64.1		21/7/2013 16:26	64.3		22/7/2013 21:31	65.2	
14/7/2013 20:11	75.1		16/7/2013 21:16	64.3		18/7/2013 22:21	66.0		21/7/2013 7:26	64.0		21/7/2013 16:31	64.6		22/7/2013 21:36	65.0	
14/7/2013 20:16	52.9		16/7/2013 21:21	64.1		18/7/2013 22:26	65.6		21/7/2013 7:31	64.4		21/7/2013 16:36	64.2		22/7/2013 21:41	65.3	
14/7/2013 20:21	68.4		16/7/2013 21:26	64.0		18/7/2013 22:31	65.7		21/7/2013 7:36	64.7		21/7/2013 16:41	64.1		22/7/2013 21:46	66.0	
14/7/2013 20:26	67.7		16/7/2013 21:31	65.1		18/7/2013 22:36	65.3		21/7/2013 7:41	64.7		21/7/2013 16:46	65.0		22/7/2013 21:51	66.0	
14/7/2013 20:31	67.1		16/7/2013 21:36	63.9		18/7/2013 22:41	66.5		21/7/2013 7:46	64.1		21/7/2013 16:51	64.1		22/7/2013 21:56	65.6	
14/7/2013 20:36	67.2		16/7/2013 21:41	64.8		18/7/2013 22:46	66.1		21/7/2013 7:51	64.4		21/7/2013 16:56	64.7		22/7/2013 22:01	64.9	
14/7/2013 20:41	66.9		16/7/2013 21:46	64.9		18/7/2013 22:51	67.1		21/7/2013 7:56	64.3		21/7/2013 17:01	64.2		22/7/2013 22:06	64.4	
14/7/2013 20:46	67.7		16/7/2013 21:51	64.7		18/7/2013 22:56	66.5		21/7/2013 8:01	64.1		21/7/2013 17:06	64.0		22/7/2013 22:11	64.6	
14/7/2013 20:51	68.1		16/7/2013 21:56	64.5		19/7/2013 19:01	62.4		21/7/2013 8:06	64.5		21/7/2013 17:11	64.1		22/7/2013 22:16	64.4	
14/7/2013 20:56	63.8		16/7/2013 22:01	64.4		19/7/2013 19:06	62.4		21/7/2013 8:11	64.5		21/7/2013 17:16	64.2		22/7/2013 22:21	64.5	
14/7/2013 21:01	64.5		16/7/2013 22:06	63.9		19/7/2013 19:11	62.7		21/7/2013 8:16	64.5		21/7/2013 17:21	63.5		22/7/2013 22:26	64.2	
14/7/2013 21:06	61.2		16/7/2013 22:11	64.2		19/7/2013 19:16	62.6		21/7/2013 8:21	65.5		21/7/2013 17:26	63.5		22/7/2013 22:31	64.2	
14/7/2013 21:11	68.4		16/7/2013 22:16	64.2		19/7/2013 19:21	62.7		21/7/2013 8:26	65.1		21/7/2013 17:31	63.1		22/7/2013 22:36	64.6	
14/7/2013 21:16	67.6		16/7/2013 22:21	64.4		19/7/2013 19:26	63.1		21/7/2013 8:31	65.3		21/7/2013 17:36	63.6		22/7/2013 22:41	64.4	
14/7/2013 21:21	67.0		16/7/2013 22:26	64.1		19/7/2013 19:31	62.7		21/7/2013 8:36	65.2		21/7/2013 17:41	63.6		22/7/2013 22:46	64.0	
14/7/2013 21:26	66.9		16/7/2013 22:31	63.7		19/7/2013 19:36	62.6		21/7/2013 8:41	64.9		21/7/2013 17:46	63.8		22/7/2013 22:51	65.0	
14/7/2013 21:31	67.2		16/7/2013 22:36	63.7		19/7/2013 19:41	6										

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
24/7/2013 22:21	65.2	27/7/2013 19:26	64.2	28/6/2013 5:21	56.3	29/6/2013 6:26	60.2	30/6/2013 23:31	60.8	2/7/2013 0:36	32.5
24/7/2013 22:26	65.2	27/7/2013 19:31	64.1	28/6/2013 5:26	53.4	29/6/2013 6:31	60.6	30/6/2013 23:36	60.5	2/7/2013 0:41	61.4
24/7/2013 22:31	65.6	27/7/2013 19:36	64.6	28/6/2013 5:31	56.1	29/6/2013 6:36	60.4	30/6/2013 23:41	60.4	2/7/2013 0:46	61.4
24/7/2013 22:36	65.3	27/7/2013 19:41	63.5	28/6/2013 5:36	55.5	29/6/2013 6:41	61.8	30/6/2013 23:46	60.9	2/7/2013 0:51	61.2
24/7/2013 22:41	65.1	27/7/2013 19:46	63.4	28/6/2013 5:41	58.5	29/6/2013 6:46	61.4	30/6/2013 23:51	60.2	2/7/2013 0:56	61.4
24/7/2013 22:46	65.0	27/7/2013 19:51	63.8	28/6/2013 5:46	57.7	29/6/2013 6:51	62.0	30/6/2013 23:56	60.8	2/7/2013 1:01	60.5
24/7/2013 22:51	65.3	27/7/2013 19:56	63.5	28/6/2013 5:51	54.9	29/6/2013 6:56	63.4	1/7/2013 0:01	60.9	2/7/2013 1:06	61.3
24/7/2013 22:56	64.8	27/7/2013 20:01	64.4	28/6/2013 5:56	57.7	29/6/2013 23:01	60.9	1/7/2013 0:06	61.1	2/7/2013 1:11	60.3
25/7/2013 19:01	63.0	27/7/2013 20:06	63.7	28/6/2013 6:01	61.4	29/6/2013 23:06	59.8	1/7/2013 0:11	59.4	2/7/2013 1:16	61.0
25/7/2013 19:06	63.9	27/7/2013 20:11	63.7	28/6/2013 6:06	60.1	29/6/2013 23:11	61.5	1/7/2013 0:16	59.5	2/7/2013 1:21	60.8
25/7/2013 19:11	63.4	27/7/2013 20:16	63.6	28/6/2013 6:11	60.0	29/6/2013 23:16	61.9	1/7/2013 0:21	60.1	2/7/2013 1:26	60.2
25/7/2013 19:16	63.2	27/7/2013 20:21	63.4	28/6/2013 6:16	61.1	29/6/2013 23:21	60.9	1/7/2013 0:26	60.1	2/7/2013 1:31	60.8
25/7/2013 19:21	62.9	27/7/2013 20:26	63.7	28/6/2013 6:21	60.8	29/6/2013 23:26	61.1	1/7/2013 0:31	61.2	2/7/2013 1:36	60.3
25/7/2013 19:26	63.7	27/7/2013 20:31	63.8	28/6/2013 6:26	62.0	29/6/2013 23:31	61.7	1/7/2013 0:36	58.5	2/7/2013 1:41	60.7
25/7/2013 19:31	64.0	27/7/2013 20:36	63.5	28/6/2013 6:31	62.1	29/6/2013 23:36	61.1	1/7/2013 0:41	57.6	2/7/2013 1:46	60.6
25/7/2013 19:36	64.5	27/7/2013 20:41	64.1	28/6/2013 6:36	63.5	29/6/2013 23:41	60.0	1/7/2013 0:46	59.2	2/7/2013 1:51	59.6
25/7/2013 19:41	64.0	27/7/2013 20:46	66.7	28/6/2013 6:41	63.2	29/6/2013 23:46	60.8	1/7/2013 0:51	57.5	2/7/2013 1:56	59.8
25/7/2013 19:46	64.4	27/7/2013 20:51	65.4	28/6/2013 6:46	63.3	29/6/2013 23:51	59.7	1/7/2013 0:56	57.6	2/7/2013 2:01	59.9
25/7/2013 19:51	64.3	27/7/2013 20:56	64.9	28/6/2013 6:51	63.8	29/6/2013 23:56	59.8	1/7/2013 1:01	55.1	2/7/2013 2:06	60.1
25/7/2013 19:56	64.5	27/7/2013 21:01	64.6	28/6/2013 6:56	64.0	30/6/2013 0:01	60.5	1/7/2013 1:06	55.2	2/7/2013 2:11	59.6
25/7/2013 20:01	64.9	27/7/2013 21:06	64.2	28/6/2013 23:01	61.0	30/6/2013 0:06	62.0	1/7/2013 1:11	52.5	2/7/2013 2:16	59.2
25/7/2013 20:06	64.6	27/7/2013 21:11	64.7	28/6/2013 23:06	60.7	30/6/2013 0:11	60.3	1/7/2013 1:16	55.0	2/7/2013 2:21	59.7
25/7/2013 20:11	64.3	27/7/2013 21:16	64.9	28/6/2013 23:11	59.9	30/6/2013 0:16	60.1	1/7/2013 1:21	56.5	2/7/2013 2:26	59.9
25/7/2013 20:16	64.0	27/7/2013 21:21	65.0	28/6/2013 23:1							


Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
24/7/2013 22:21	64.3	27/7/2013 19:26	65.2	28/6/2013 5:21	62.5	29/6/2013 6:26	63.9	30/6/2013 23:31	62.8	2/7/2013 0:36	61.8
24/7/2013 22:26	64.3	27/7/2013 19:31	64.6	28/6/2013 5:31	62.2	29/6/2013 6:31	63.5	30/6/2013 23:36	63.3	2/7/2013 0:41	60.7
24/7/2013 22:31	64.9	27/7/2013 19:36	65.0	28/6/2013 5:31	62.6	29/6/2013 6:36	63.2	30/6/2013 23:41	64.2	2/7/2013 0:46	61.7
24/7/2013 22:36	64.7	27/7/2013 19:41	64.9	28/6/2013 5:36	63.0	29/6/2013 6:41	64.2	30/6/2013 23:46	62.7	2/7/2013 0:51	62.5
24/7/2013 22:41	64.8	27/7/2013 19:46	61.6	28/6/2013 5:41	54.5	29/6/2013 6:46	64.1	30/6/2013 23:51	63.3	2/7/2013 0:56	58.9
24/7/2013 22:46	63.7	27/7/2013 19:51	63.0	28/6/2013 5:46	63.1	29/6/2013 6:51	65.0	30/6/2013 23:56	63.4	2/7/2013 1:01	57.0
24/7/2013 22:51	64.1	27/7/2013 19:56	62.6	28/6/2013 5:51	62.7	29/6/2013 6:56	64.1	1/7/2013 0:01	61.7	2/7/2013 1:06	55.9
24/7/2013 22:56	64.6	27/7/2013 20:01	64.6	28/6/2013 5:56	63.1	29/6/2013 23:01	64.9	1/7/2013 0:06	62.6	2/7/2013 1:11	58.1
25/7/2013 19:01	67.2	27/7/2013 20:06	64.4	28/6/2013 6:01	56.3	29/6/2013 23:06	63.8	1/7/2013 0:11	63.0	2/7/2013 1:16	56.2
25/7/2013 19:06	66.5	27/7/2013 20:11	64.4	28/6/2013 6:06	60.7	29/6/2013 23:11	64.9	1/7/2013 0:16	62.7	2/7/2013 1:21	57.0
25/7/2013 19:11	66.7	27/7/2013 20:16	64.0	28/6/2013 6:11	59.9	29/6/2013 23:16	63.9	1/7/2013 0:21	60.7	2/7/2013 1:26	49.1
25/7/2013 19:16	66.6	27/7/2013 20:21	62.5	28/6/2013 6:16	61.1	29/6/2013 23:21	64.5	1/7/2013 0:26	60.0	2/7/2013 1:31	44.5
25/7/2013 19:21	66.9	27/7/2013 20:26	61.8	28/6/2013 6:21	60.0	29/6/2013 23:26	64.2	1/7/2013 0:31	61.6	2/7/2013 1:36	62.6
25/7/2013 19:26	67.5	27/7/2013 20:31	65.3	28/6/2013 6:26	62.8	29/6/2013 23:31	64.2	1/7/2013 0:36	57.5	2/7/2013 1:41	64.8
25/7/2013 19:31	66.5	27/7/2013 20:36	63.8	28/6/2013 6:31	63.3	29/6/2013 23:36	63.6	1/7/2013 0:41	60.8	2/7/2013 1:46	52.3
25/7/2013 19:36	66.4	27/7/2013 20:41	65.1	28/6/2013 6:36	64.7	29/6/2013 23:41	64.0	1/7/2013 0:46	58.4	2/7/2013 1:51	62.8
25/7/2013 19:41	66.6	27/7/2013 20:46	64.5	28/6/2013 6:41	64.2	29/6/2013 23:46	64.1	1/7/2013 0:51	63.6	2/7/2013 1:56	62.9
25/7/2013 19:46	66.4	27/7/2013 20:51	66.3	28/6/2013 6:46	64.6	29/6/2013 23:51	64.0	1/7/2013 0:56	60.0	2/7/2013 2:01	62.1
25/7/2013 19:51	65.7	27/7/2013 20:56	66.5	28/6/2013 6:51	65.3	29/6/2013 23:56	63.2	1/7/2013 1:01	55.8	2/7/2013 2:06	62.1
25/7/2013 19:56	66.4	27/7/2013 21:01	64.8	28/6/2013 6:56	65.8	30/6/2013 0:01	63.5	1/7/2013 1:06	57.2	2/7/2013 2:11	62.1
25/7/2013 20:01	66.0	27/7/2013 21:06	62.4	28/6/2013 23:01	65.7	30/6/2013 0:06	64.5	1/7/2013 1:11	60.6	2/7/2013 2:16	62.2
25/7/2013 20:06	66.8	27/7/2013 21:11	62.4	28/6/2013 23:06	66.4	30/6/2013 0:11	63.6	1/7/2013 1:16	60.4	2/7/2013 2:21	61.5
25/7/2013 20:11	67.0	27/7/2013 21:16	64.7	28/6/2013 23:11	65.1	30/6/2013 0:16	63.9	1/7/2013 1:21	49.8	2/7/2013 2:26	62.6
25/7/2013 20:16	66.2	27/7/2013 21:21	67.6	28/6/2013 2							

Real-time Noise Data	RTN4 (Causeway Bay Community Centre)									
28/6/2013 22:51 62.3	30/6/2013 11:56 63.4	30/6/2013 21:01 60.6	1/7/2013 14:06 61.5	2/7/2013 19:11 62.5	4/7/2013 20:16 62.2					
28/6/2013 22:56 62.8	30/6/2013 12:01 61.8	30/6/2013 21:06 60.8	1/7/2013 14:11 61.7	2/7/2013 19:16 62.0	4/7/2013 20:21 62.1					
29/6/2013 19:01 60.6	30/6/2013 12:06 62.5	30/6/2013 21:11 62.5	1/7/2013 14:16 61.9	2/7/2013 19:21 62.5	4/7/2013 20:26 62.3					
29/6/2013 19:06 62.3	30/6/2013 12:11 62.9	30/6/2013 21:16 61.2	1/7/2013 14:21 61.9	2/7/2013 19:26 62.4	4/7/2013 20:31 62.3					
29/6/2013 19:11 63.3	30/6/2013 12:16 61.9	30/6/2013 21:21 61.6	1/7/2013 14:26 61.4	2/7/2013 19:31 63.0	4/7/2013 20:36 62.2					
29/6/2013 19:16 62.1	30/6/2013 12:21 61.6	30/6/2013 21:26 61.5	1/7/2013 14:31 61.7	2/7/2013 19:36 62.7	4/7/2013 20:41 49.7					
29/6/2013 19:21 63.6	30/6/2013 12:26 62.7	30/6/2013 21:31 61.5	1/7/2013 14:36 62.0	2/7/2013 19:41 62.7	4/7/2013 20:46 61.8					
29/6/2013 19:26 62.0	30/6/2013 12:31 63.1	30/6/2013 21:36 62.0	1/7/2013 14:41 62.8	2/7/2013 19:46 63.5	4/7/2013 20:51 61.9					
29/6/2013 19:31 62.0	30/6/2013 12:36 61.8	30/6/2013 21:41 62.8	1/7/2013 14:46 61.8	2/7/2013 19:51 62.1	4/7/2013 20:56 62.2					
29/6/2013 19:36 61.5	30/6/2013 12:41 62.0	30/6/2013 21:46 61.5	1/7/2013 14:51 62.1	2/7/2013 19:56 62.0	4/7/2013 21:01 62.2					
29/6/2013 19:41 62.0	30/6/2013 12:46 62.9	30/6/2013 21:51 60.8	1/7/2013 14:56 62.5	2/7/2013 20:01 62.6	4/7/2013 21:06 62.1					
29/6/2013 19:46 62.2	30/6/2013 12:51 61.7	30/6/2013 21:56 60.7	1/7/2013 15:01 61.3	2/7/2013 20:06 62.3	4/7/2013 21:11 62.4					
29/6/2013 19:51 62.0	30/6/2013 12:56 61.7	30/6/2013 22:01 60.9	1/7/2013 15:06 61.2	2/7/2013 20:11 62.1	4/7/2013 21:16 63.0					
29/6/2013 19:56 61.9	30/6/2013 13:01 62.3	30/6/2013 22:06 60.5	1/7/2013 15:11 61.8	2/7/2013 20:16 62.4	4/7/2013 21:21 62.1					
29/6/2013 20:01 61.6	30/6/2013 13:06 61.7	30/6/2013 22:11 61.0	1/7/2013 15:16 63.0	2/7/2013 20:21 62.1	4/7/2013 21:26 61.7					
29/6/2013 20:06 61.2	30/6/2013 13:11 61.6	30/6/2013 22:16 61.2	1/7/2013 15:21 62.5	2/7/2013 20:26 62.2	4/7/2013 21:31 61.5					
29/6/2013 20:11 62.0	30/6/2013 13:16 62.6	30/6/2013 22:21 61.4	1/7/2013 15:26 61.9	2/7/2013 20:31 62.1	4/7/2013 21:36 62.0					
29/6/2013 20:16 62.0	30/6/2013 13:21 62.1	30/6/2013 22:26 61.2	1/7/2013 15:31 62.3	2/7/2013 20:36 62.4	4/7/2013 21:41 61.8					
29/6/2013 20:21 61.7	30/6/2013 13:26 60.2	30/6/2013 22:31 62.3	1/7/2013 15:36 62.6	2/7/2013 20:41 62.9	4/7/2013 21:46 61.4					
29/6/2013 20:26 61.6	30/6/2013 13:31 61.0	30/6/2013 22:36 61.6	1/7/2013 15:41 62.3	2/7/2013 20:46 62.0	4/7/2013 21:51 61.7					
29/6/2013 20:31 61.5	30/6/2013 13:36 61.2	30/6/2013 22:41 61.7	1/7/2013 15:46 61.9	2/7/2013 20:51 62.4	4/7/2013 21:56 61.6					
29/6/2013 20:36 62.1	30/6/2013 13:41 61.6	30/6/2013 22:46 61.7	1/7/2013 15:51 62.1	2/7/2013 20:56 62.0	4/7/2013 22:01 62.0					
29/6/2013 20:41 62.1	30/6/2013 13:46 61.7	30/6/2013 22:51 62.1	1/7/2013 15:56 62.3	2/7/2013 21:01 61.8	4/7/2013 22:06 61.2					
29/6/2013 20:46 61.9	30/6/2013 13:51 61.9	30/6/2013 22:56 60.9	1/7/2013 16:01 62.0	2/7/2013 21:06 61.3	4/7/2013 22:11 61.2					
29/6/2013 20:51 61.6	30/6/2013 13:56 60.4	1/7/2013 7:01 61.0	1/7/2013 16:06 62.2	2/7/2013 21:11 61.6	4/7/2013 22:16 62.4					
29/6/2013 20:56 61.7	30/6/2013 14:01 61.2	1/7/2013 7:06 60.6	1/7/2013 16:11 62.3	2/7/2013 21:16 62.2	4/7/2013 22:21 61.1					
29/6/2013 21:01 62.0	30/6/2013 14:06 61.4	1/7/2013 7:11 61.3	1/7/2013 16:16 62.2	2/7/2013 21:21 61.8	4/7/2013 22:26 6					

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)											
6/7/2013 21:21	62.1	7/7/2013 14:26	62.5	8/7/2013 19:31	61.3	10/7/2013 20:36	63.1	12/7/2013 21:41	62.2	14/7/2013 10:46	61.9		
6/7/2013 21:26	61.2	7/7/2013 14:31	62.4	8/7/2013 19:36	61.6	10/7/2013 20:41	61.9	12/7/2013 21:46	62.0	14/7/2013 10:51	62.4		
6/7/2013 21:31	62.1	7/7/2013 14:36	61.8	8/7/2013 19:41	60.9	10/7/2013 20:46	62.4	12/7/2013 21:51	61.7	14/7/2013 10:56	62.2		
6/7/2013 21:36	62.5	7/7/2013 14:41	63.0	8/7/2013 19:46	60.8	10/7/2013 20:51	51.6	12/7/2013 21:56	61.9	14/7/2013 11:01	62.2		
6/7/2013 21:41	62.1	7/7/2013 14:46	63.3	8/7/2013 19:51	60.8	10/7/2013 20:56	63.2	12/7/2013 22:01	61.5	14/7/2013 11:06	62.0		
6/7/2013 21:46	62.0	7/7/2013 14:51	62.7	8/7/2013 19:56	61.2	10/7/2013 21:01	63.0	12/7/2013 22:06	61.9	14/7/2013 11:11	62.6		
6/7/2013 21:51	62.1	7/7/2013 14:56	63.0	8/7/2013 20:01	63.3	10/7/2013 21:06	61.9	12/7/2013 22:11	62.1	14/7/2013 11:16	62.2		
6/7/2013 21:56	62.2	7/7/2013 15:01	62.6	8/7/2013 20:06	61.3	10/7/2013 21:11	62.3	12/7/2013 22:16	62.6	14/7/2013 11:21	62.3		
6/7/2013 22:01	62.0	7/7/2013 15:06	63.4	8/7/2013 20:11	61.4	10/7/2013 21:16	62.8	12/7/2013 22:21	62.1	14/7/2013 11:26	61.9		
6/7/2013 22:06	62.0	7/7/2013 15:11	62.7	8/7/2013 20:16	61.2	10/7/2013 21:21	63.0	12/7/2013 22:26	61.8	14/7/2013 11:31	62.2		
6/7/2013 22:11	62.1	7/7/2013 15:16	62.3	8/7/2013 20:21	61.1	10/7/2013 21:26	63.3	12/7/2013 22:31	61.4	14/7/2013 11:36	62.1		
6/7/2013 22:16	62.3	7/7/2013 15:21	62.1	8/7/2013 20:26	60.2	10/7/2013 21:31	51.8	12/7/2013 22:36	62.0	14/7/2013 11:41	62.4		
6/7/2013 22:21	61.3	7/7/2013 15:26	63.0	8/7/2013 20:31	60.4	10/7/2013 21:36	63.2	12/7/2013 22:41	61.1	14/7/2013 11:46	62.2		
6/7/2013 22:26	62.2	7/7/2013 15:31	63.0	8/7/2013 20:36	61.7	10/7/2013 21:41	63.2	12/7/2013 22:46	61.4	14/7/2013 11:51	61.6		
6/7/2013 22:31	62.0	7/7/2013 15:36	62.7	8/7/2013 20:41	62.1	10/7/2013 21:46	62.7	12/7/2013 22:51	61.0	14/7/2013 11:56	61.3		
6/7/2013 22:36	63.5	7/7/2013 15:41	63.1	8/7/2013 20:46	61.9	10/7/2013 21:51	62.8	12/7/2013 22:56	62.9	14/7/2013 12:01	62.1		
6/7/2013 22:41	62.0	7/7/2013 15:46	62.8	8/7/2013 20:51	61.6	10/7/2013 21:56	63.3	13/7/2013 19:01	62.8	14/7/2013 12:06	62.2		
6/7/2013 22:46	61.6	7/7/2013 15:51	62.5	8/7/2013 20:56	62.5	10/7/2013 22:01	63.0	13/7/2013 19:06	63.1	14/7/2013 12:11	62.5		
6/7/2013 22:51	61.8	7/7/2013 15:56	62.9	8/7/2013 21:01	63.6	10/7/2013 22:06	62.5	13/7/2013 19:11	63.6	14/7/2013 12:16	62.0		
6/7/2013 22:56	61.9	7/7/2013 16:01	63.0	8/7/2013 21:06	62.3	10/7/2013 22:11	62.8	13/7/2013 19:16	62.3	14/7/2013 12:21	62.3		
7/7/2013 7:01	59.7	7/7/2013 16:06	62.4	8/7/2013 21:11	61.9	10/7/2013 22:16	62.6	13/7/2013 19:21	62.8	14/7/2013 12:26	62.5		
7/7/2013 7:06	60.9	7/7/2013 16:11	62.5	8/7/2013 21:16	61.5	10/7/2013 22:21	62.3	13/7/2013 19:26	62.1	14/7/2013 12:31	62.6		
7/7/2013 7:11	61.0	7/7/2013 16:16	63.1	8/7/2013 21:21	62.4	10/7/2013 22:26	62.7	13/7/2013 19:31	62.2	14/7/2013 12:36	62.4		


Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
24/7/2013 22:21	62.0	27/7/2013 19:26	63.0	28/6/2013 5:21	58.5	29/6/2013 6:26	43.0	30/6/2013 23:31	60.3	2/7/2013 0:36	59.9
24/7/2013 22:26	61.9	27/7/2013 19:31	52.2	28/6/2013 5:26	56.2	29/6/2013 6:31	60.6	30/6/2013 23:36	60.7	2/7/2013 0:41	58.2
24/7/2013 22:31	62.0	27/7/2013 19:36	63.1	28/6/2013 5:31	57.6	29/6/2013 6:36	60.7	30/6/2013 23:41	50.5	2/7/2013 0:46	60.2
24/7/2013 22:36	62.2	27/7/2013 19:41	63.1	28/6/2013 5:36	56.9	29/6/2013 6:41	48.6	30/6/2013 23:46	43.0	2/7/2013 0:51	59.8
24/7/2013 22:41	62.1	27/7/2013 19:46	62.0	28/6/2013 5:41	58.1	29/6/2013 6:46	51.6	30/6/2013 23:51	60.4	2/7/2013 0:56	58.3
24/7/2013 22:46	61.5	27/7/2013 19:51	62.2	28/6/2013 5:46	58.1	29/6/2013 6:51	60.8	30/6/2013 23:56	48.6	2/7/2013 1:01	58.0
24/7/2013 22:51	62.0	27/7/2013 19:56	62.5	28/6/2013 5:51	57.5	29/6/2013 6:56	53.7	1/7/2013 0:01	60.1	2/7/2013 1:06	57.8
24/7/2013 22:56	62.2	27/7/2013 20:01	62.5	28/6/2013 5:56	58.2	29/6/2013 7:01	54.5	1/7/2013 0:06	60.0	2/7/2013 1:11	58.1
25/7/2013 19:01	52.8	27/7/2013 20:06	63.0	28/6/2013 6:01	59.8	29/6/2013 23:06	60.8	1/7/2013 0:11	60.5	2/7/2013 1:16	57.6
25/7/2013 19:06	63.1	27/7/2013 20:11	62.7	28/6/2013 6:06	59.6	29/6/2013 23:11	48.4	1/7/2013 0:16	46.4	2/7/2013 1:21	58.3
25/7/2013 19:11	62.7	27/7/2013 20:16	62.4	28/6/2013 6:11	59.4	29/6/2013 23:16	50.3	1/7/2013 0:21	60.0	2/7/2013 1:26	57.4
25/7/2013 19:16	63.3	27/7/2013 20:21	62.0	28/6/2013 6:16	59.8	29/6/2013 23:21	60.6	1/7/2013 0:26	58.7	2/7/2013 1:31	56.8
25/7/2013 19:21	50.4	27/7/2013 20:26	62.1	28/6/2013 6:21	59.7	29/6/2013 23:26	49.9	1/7/2013 0:31	60.3	2/7/2013 1:36	56.3
25/7/2013 19:26	62.7	27/7/2013 20:31	62.1	28/6/2013 6:26	60.6	29/6/2013 23:31	52.5	1/7/2013 0:36	58.8	2/7/2013 1:41	57.0
25/7/2013 19:31	62.3	27/7/2013 20:36	61.9	28/6/2013 6:31	60.7	29/6/2013 23:36	50.6	1/7/2013 0:41	58.8	2/7/2013 1:46	57.7
25/7/2013 19:36	62.9	27/7/2013 20:41	62.2	28/6/2013 6:36	52.5	29/6/2013 23:41	60.9	1/7/2013 0:46	58.8	2/7/2013 1:51	56.3
25/7/2013 19:41	63.0	27/7/2013 20:46	62.1	28/6/2013 6:41	51.4	29/6/2013 23:46	52.7	1/7/2013 0:51	60.9	2/7/2013 1:56	56.5
25/7/2013 19:46	63.0	27/7/2013 20:51	62.0	28/6/2013 6:46	51.6	29/6/2013 23:51	41.5	1/7/2013 0:56	59.4	2/7/2013 2:01	57.1
25/7/2013 19:51	62.6	27/7/2013 20:56	62.6	28/6/2013 6:51	53.4	29/6/2013 23:56	60.8	1/7/2013 1:01	58.0	2/7/2013 2:06	56.6
25/7/2013 19:56	62.7	27/7/2013 21:01	61.5	28/6/2013 6:56	56.6	30/6/2013 0:01	60.8	1/7/2013 1:06	60.8	2/7/2013 2:11	55.6
25/7/2013 20:01	63.6	27/7/2013 21:06	61.5	28/6/2013 7:01	50.7	30/6/2013 0:06	48.8	1/7/2013 1:11	58.0	2/7/2013 2:16	56.4
25/7/2013 20:06	63.6	27/7/2013 21:11	61.3	28/6/2013 23:06	54.4	30/6/2013 0:11	52.8	1/7/2013 1:16	59.3	2/7/2013 2:21	55.4
25/7/2013 20:11	53.1	27/7/2013 21:16	62.0	28/6/2013 23:11	53.6	30/6/2013 0:16	49.4	1/7/2013 1:21	58.1	2/7/2013 2:26	56.4
25/7/2013 20:16	63.5	27/7/2013 21:21	61.7								

Graphic Presentation of Real Time Noise Monitoring Result (RTN1-Food and Environmental Hygiene Department Depot)

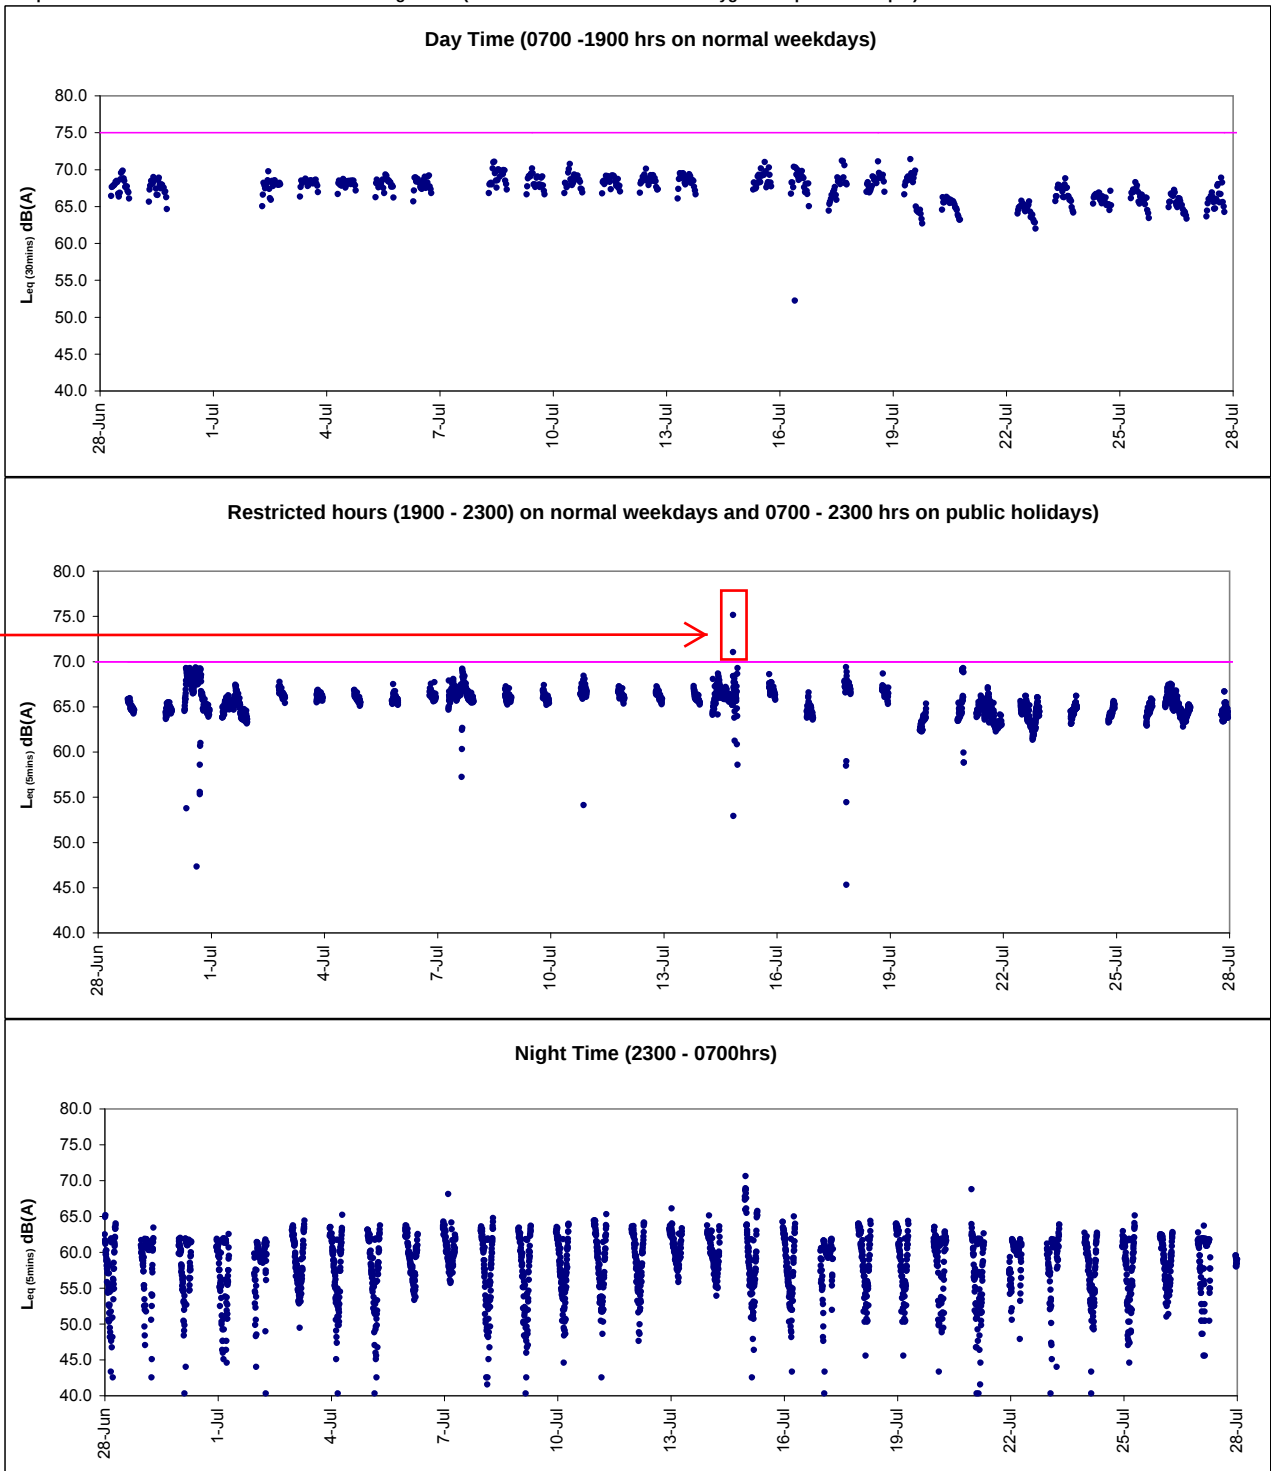


After checking with contractor HY/2009/19, no construction works were conducted at the concerned location during the recorded period. As such, the exceedances were considered to be contributed by nearby IEC traffic

Graphic Presentation of Real Time Noise Monitoring Result (RTN2a- Hong Kong Electric Centre)

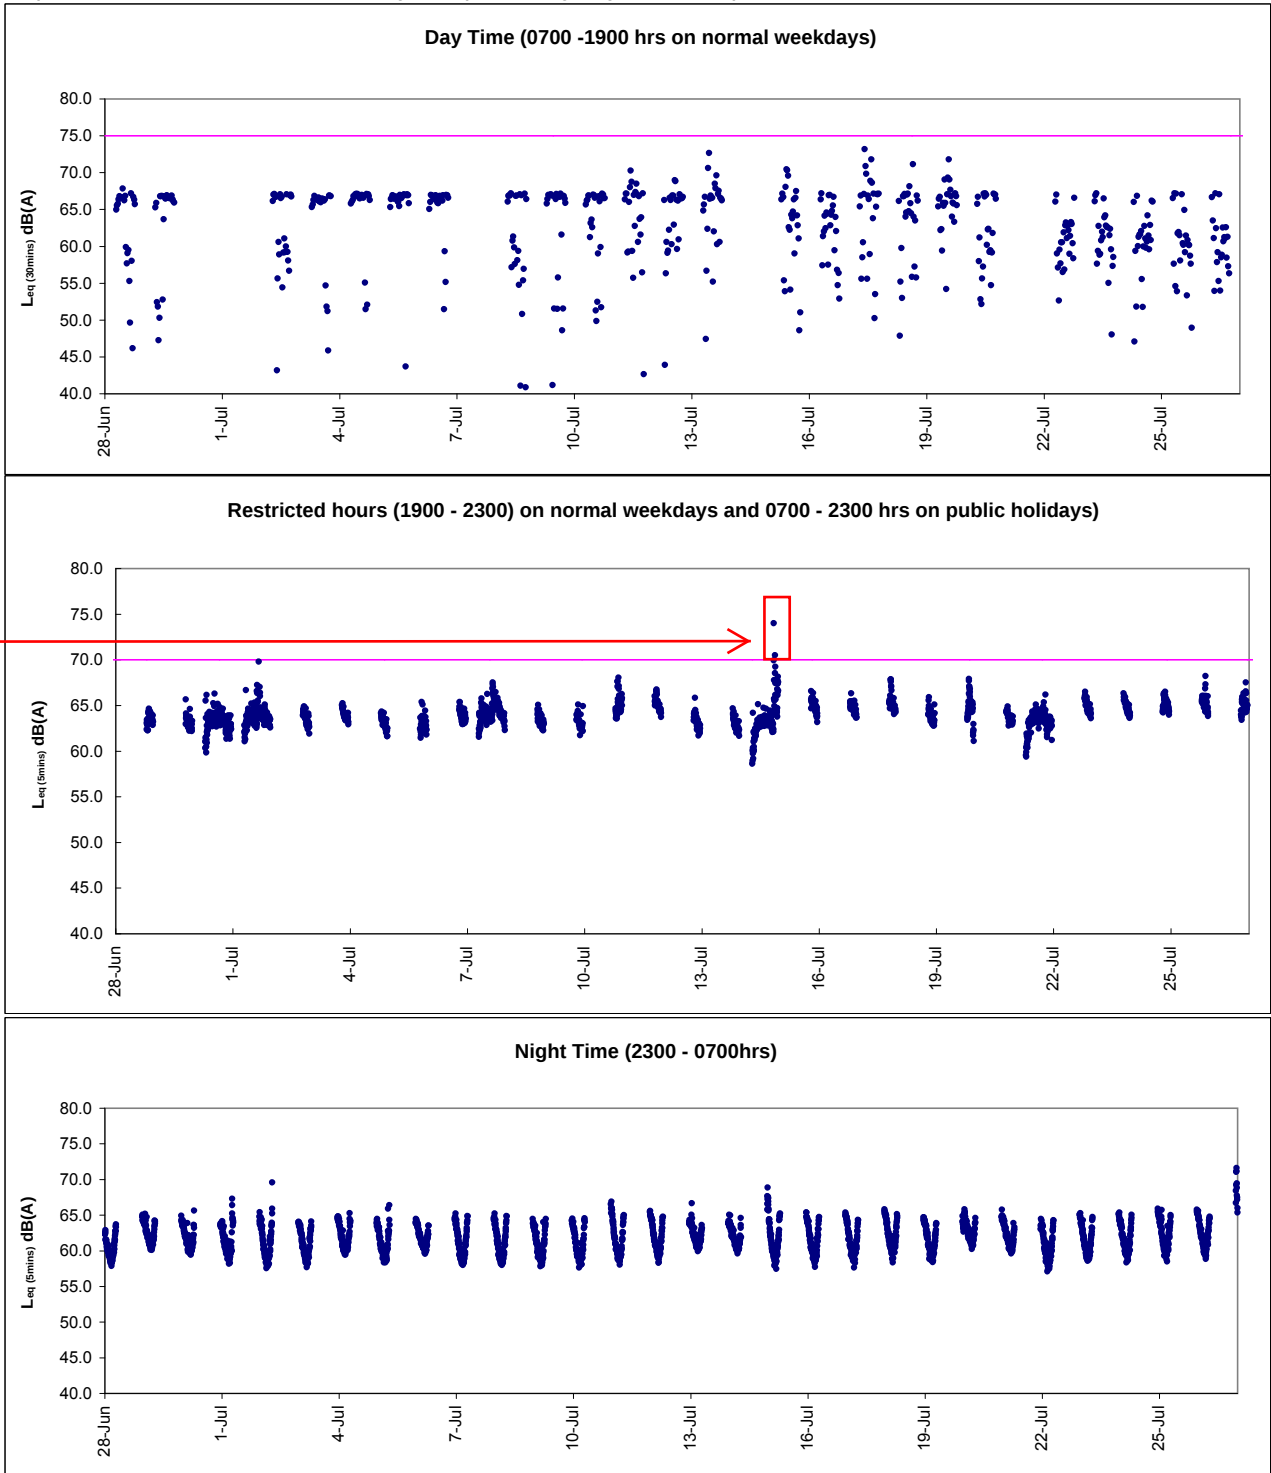


After checking with contractor HY/2009/19, no construction works were conducted at the concerned location during the recorded period. As such, the exceedances were considered to be contributed by nearby IEC traffic

Graphic Presentation of Real Time Noise Monitoring Result (RTN3-Yu Lee Mo Fan Memorial School)

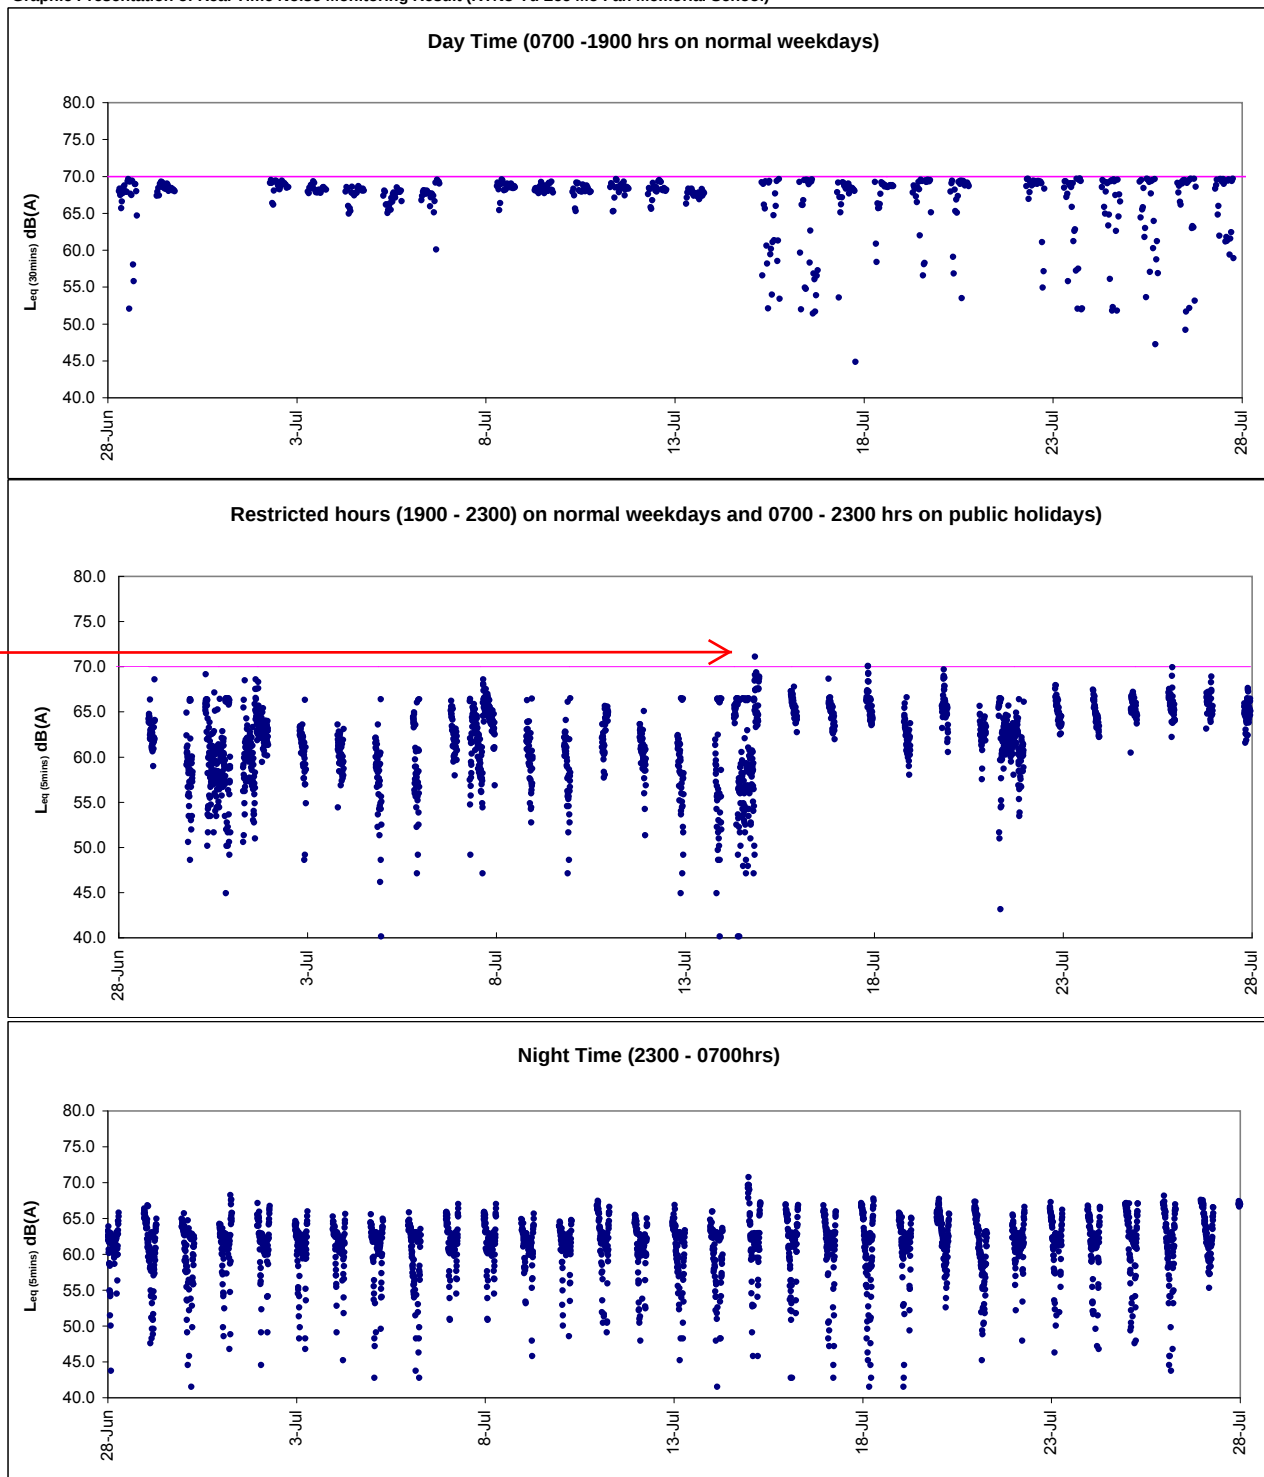

After checking with contractor HY/2009/19, no construction works were conducted at the concerned location during the recorded period. As such, the exceedances were considered to be contributed by nearby IEC traffic

Graphic Presentation of Real Time Noise Monitoring Result (RTN4-Causeway Bay Community Centre)

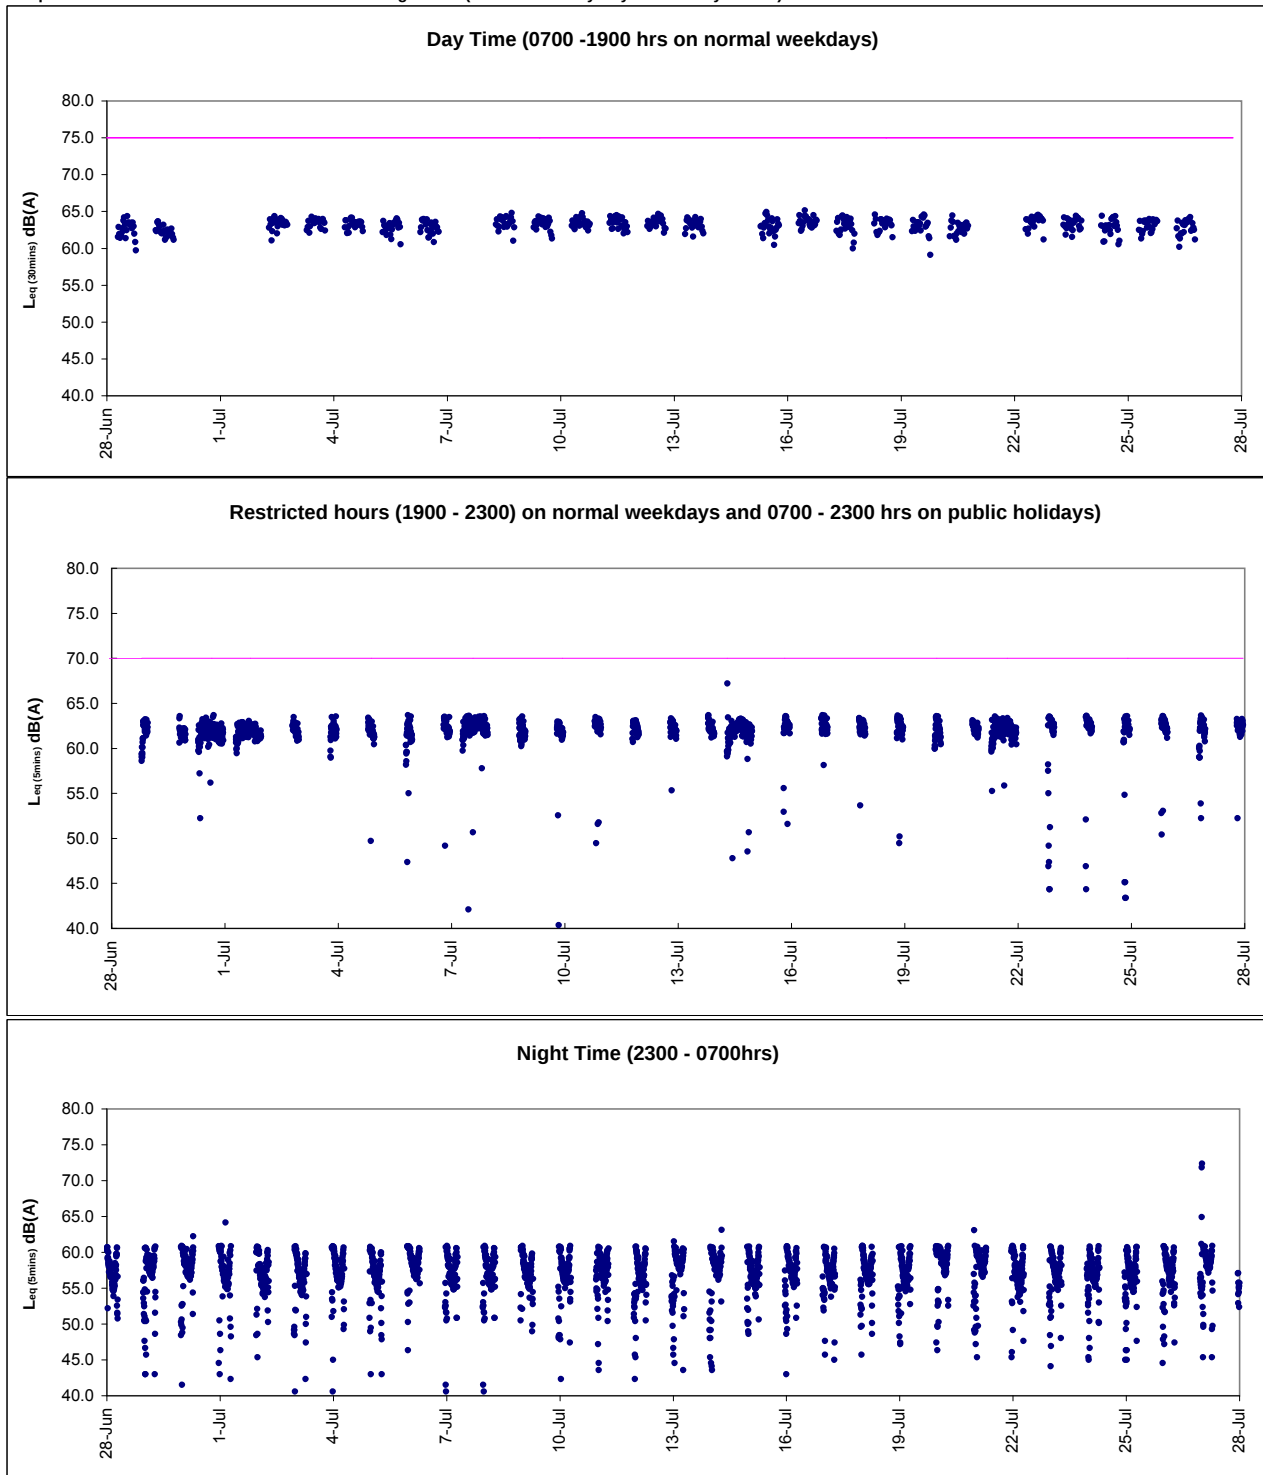



Appendix 6.1

Event Action Plans



Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	1. Notify ER, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the IEC and Contractor on remedial measures required; 5. Increase monitoring frequency to check mitigation effectiveness. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Advise the ER on the effectiveness of the proposed remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Submit noise mitigation proposals to IEC and ER; 2. Implement noise mitigation proposals. (The above actions should be taken within 2 working days after the exceedance is identified)



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit Level being exceeded	1. Inform IEC, ER, Contractor and EPD; 2. Repeat measurements to confirm findings; 3. Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contractor's working procedures; 6. Discuss with the IEC, Contractor and ER on remedial measures required; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification; 3. Implement the agreed proposals; 4. Submit further proposal if problem still not under control; 5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)

**Event / Action Plan for Construction Air Quality**

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
ACTION LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Notify Contractor. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
LIMIT LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
2. Exceedance for two or more consecutive samples	1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)



Appendix 6.2

Summary for Notification of Exceedance



Ref. No.	Date	Time	Location	Construction Noise Level	Unit	Action Level	Limit Level	Follow-up action
X_10N134	9-Jul-13	13:45	M6 - HK Baptist Church Henrietta Secondary School	73	Leq(30-min)	when one documented complaint was received.	70	Possible reason: Traffic nearby and external renovation at City Garden was observed during monitoring and was considered as the major noise contribution. Action taken / to be taken: Repeat measurement to confirm result and reviewed the trend of noise measurement. Analysis of contractor's working procedure. Remarks / Other Obs: Road works on IEC for Contract HY/2009/19 was conducted during the measurement. It was observed that traffic noise and external renovation works conducted at City Garden were major noise contribution during the monitoring period. It is concluded that the exceedance was not due to project.
X_10N135	16-Jul-13	15:50	M6 - HK Baptist Church Henrietta Secondary School	72	Leq(30-min)	when one documented complaint was received.	70	Possible reason: Traffic nearby was observed during monitoring and was considered as the major noise contribution. Action taken / to be taken: Repeat measurement to confirm result and reviewed the trend of noise measurement. Analysis of contractor's working procedure. Remarks / Other Obs: Installation of formwork and falsework for Contract HY/2009/19 was conducted during the measurement. It was observed that traffic noise was a major noise source during monitoring. It is concluded that the exceedance was not due to project but to traffic noise nearby.



Appendix 9.1

Complaint Log

**Environmental Complaints Log**

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
110723a	23/07/2011	Ms. Law at Victoria Centre by ICC no. 1-303887687	North Point	She concerned that Highways Department published a notice in their Management Office about construction works will be conducted from 0700 hours to 2300 hours during July to December 2011 including Saturday, Sunday and public holiday.	1) It was referred by AECOM to ET on 28 July 2011 2) RSS confirmed that the notice was prepared by Victoria Centre 'a Management office to their resident and the advice was only given on the extension construction works (for Contract HY/2009/15) to 7am-9pm Monday to Saturday except Public Holidays and Sundays. 3) As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am and is expected to be completed by mid-August 2011. 4) No noise exceedance was recorded at construction noise monitoring station at Victoria Centre on 19 and 25 July 2011 during daytime and evening time period while breaking and excavation works were observed during monitoring. 5) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.	Closed
110723b	23/07/2011	Ms. Yau at Block 2, Victoria Centre by ICC no. 1-304013959	North Point	Reclamation work was conducted at Causeway Bay Typhoon Shelter at 7am on 23 July 2011. She complained that the works shall be started later to minimize the noise nuisance to the vicinity of the residents in early morning	1) It was referred by AECOM to ET on 8 August 2011 2) RSS confirmed to start the rock breaking activities for Contract HY/2009/15 at 8am as a mitigation measure to minimize the noise nuisance in the vicinity of the residents. 3) With reference to the construction noise monitoring at Victoria Centre, no exceedance was recorded on 19 and 25 July 2011 during daytime while breaking and excavation works were undertaken during monitoring 4) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.	Closed
110727a	27/07/2011	Mr. Law from Victoria Centre Management Office by ICC no. 1-304616162	North Point	It was complained by Mr. Law from Victoria Centre Management Office on 27 July 2011 regarding construction noise generated by the construction operations of	1) It was referred by AECOM to ET on 28 July 2011 2) RSS confirmed to start the rock breaking activities for Contract HY/2009/15 at 8am as a mitigation measure to minimize the noise nuisance in the vicinity of the residents. 3) No noise exceedance was recorded at construction noise monitoring station at Victoria Centre on 25 July and	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				Central-Wanchai Bypass at noon rather than in morning at 7am.	4 August 2011 during daytime and evening time period while breaking and excavation works were observed during monitoring. 5) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. No further complaint from complainant was received after proposed the mitigation measure.	
110727b	27/07/2011	Ms. Chiu by ICC no.1-304615409	North Point	Noise nuisance from the excavation works for the Highways Department adjacent to the Victoria Centre was conducted from 7am	1) It was referred by AECOM to ET on 28 July 2011 2) With reference to the construction noise monitoring at Vitoria Centre, no exceedance was recorded on 25 July and 4 and 10 August 2011 during daytime while breaking and excavation works were undertaken during monitoring. 3) As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am.	Closed
	07/08/2011				4) However, complainant did not satisfy with the response on the noise nuisance from the rock-breaking during morning in front of Victoria Centre and then further complaint via 1823 on 7 August 2011. 5) Highways contacted the complainant on 15 August 2011 that the noisy rock breaking operation had been completed. <i>Remarks: There will be counted as two complaints in this complaint log.</i>	
110730	30/07/2011	Mr. Tsui by ICC no. 1-305074350	Central	Construction noise generated by operations of Central-Interchange which is near the spa room at Four-Season Hotel. Also, the complaint enquired the commencement time of the construction on Saturday.	1) It was referred by AECOM to ET on 1 August 2011. 2) RSS confirmed that noisy plants from 2 vibratory hammers have been conducted in alternating manner for piling and drilling works for diaphragm wall construction. 3) With reference to the construction noise monitoring at IFC Western End of Podium, no exceedance was recorded on 4 August 2011 during monitoring while sheet piling works were undertaken during monitoring. 4) In order to reduce the noise impact to nearby noise sensitive receivers, Contractor has been implemented the following noise mitigation measures: - Erection of acoustic lining at the hoarding next to Four Seasons Hotel; - Temporary noise barrier with extended acoustic lining; - Reduced in plant such that only have one vibration hammer operating at the west side near Four	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Seasons Hotel instead of 2 5) In conclusion, it was related to the construction works under Contract HY/2009/18 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.	
110810	10/08/2011	Mr. Yip by ICC no. 1 – 306740207	North Point	Muddy water was discharged from work site to the seafront near Oil Street during heavy rain. The environmental protection measures were not good enough and are needed to rectify.	1) It was referred by AECOM to ET on 17 August 2011. 2) Confirmed with RE, Muddy water was caused by a heap of earth being washed to the sea by heavy rain. The heap of earth was referred as a small stockpile placed close to the seafront in front of Oil Street within the site area under handover transition period from contract HY/2009/11 to contract HY/2009/19. The necessary mitigation measures to protect the small stockpile against rainfall were missing at the time of complaint. 3) Due to the missing of mitigation measures to protect the small stockpile during handover transition period, loose material was washed into the harbour when heavy rain came. Muddy water was formed and dispersed in the sea that caused the water quality and visual concern to the public. The complaint was considered as valid. 4) Contractors were advised to relocate the loose materials away from the coastline as far as practicable. Any loose material placed which needed to be placed near the coastline shall be properly compacted or covered as appropriate. To avoid any further environmental deficiency, Contractors shall ensure all necessary environmental mitigation measures will not be missing during site area handover.	Closed
110817	17/08/2011	ICC no. 1-307657681	North Point	Visual impact generated by light from a large amount of spot-lights on the barge during mid-night nearby City Garden.	1) It was referred by AECOM to ET on 23 August 2011 2) RSS confirmed that some non-essential lights were turned on during night-time period which caused the nuisance to the nearby residents. In addition, absence of lighting shields at flood lights results in visual glare to the complaint at night-time. 3) Follow-up action had been taken by contractor that switches off all non-essential lights to minimized nuisance to the nearby residents. The complainant satisfied to the practice and no further complaint was received after that.	Closed
110826	26/08/2011	Grand Hyatt and a complainant by ICC	Wan Chai	Construction noise and vibration nuisance generated from the works at Convention Avenue and inside the HKCEC1	1) Confirmed with the Resident Site Staff that the construction works were referred to the Contractor HK/2009/01. 2) The Excavator mounted breaker at Convention Avenue	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				reclamation area.	and Drilling rig at HKCEC1 reclamation area were the dominant construction noise source during this period. 3) The drilling rig at HKCEC1 reclamation area and excavator mounted breaker at Convention Avenue were then temporary suspended after received the complaint. 4) Investigation revealed that the erected noise barrier (4m cantilevered movable noise barrier for the drilling rig and 1m movable noise barrier for the excavator mounted breaker) were not located close to the plants to provide adequate noise screening. 5) Contractor was advised to avoid concurrent operation of construction plants at site. Further enhancement of movable noise barriers at HKCEC1 and providing noise enclosure for the excavator mounted breaker at Convention Avenue are needed. 6) Further site investigation and checking on 31 August and 7 September 2011 revealed that the implemented noise mitigation measures were in proper and minimize the noise impact.	
110826A	26/08/2011	A complaint letter from Mr. Au of Cayley Property of City Garden	North Point	Harbor front adjacent to their water intake suction which caused 3 times of system breakdown of the sea water pump on 9, 22 and 25 August 2011.	1) It was referred by AECOM to ET on 29 August 2011 2) Confirmed with the Resident Site Staff that the construction works were referred to the Contractors HY/2009/11 and HY/2009/19. 3) The pump is located on the site area of HY/2009/19 4) A temporary garbage defender was installed on 23 July 2011 by HY/2009/11 and the shape of the defender was adjusted on 8 August 2011 in order to exclude the outfall. 5) An ad hoc inspection of the effectiveness of garbage defender was conducted with RSS (CWB project team), contractor of HY/2009/11 and HY/2009/19 and IECon 29 August 2011. Inspection report of it was submitted to RSS on 19 September 2011. 5) Daily cleaning near the water intake was conducted twice a day by contractor HY/2009/19. 6) In response to City Garden request, the contractors have set up the temporary garbage defender in function and collect the floating refuses, but cannot eliminate all refuses, in particular the refuse come from sea bed from entering the intake. 6) According to the complaint letter from Cayley Property, the outcomes of the preventive measures were not complying with their expectation. 7) During on-site inspection, floating refuses observed	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					occasionally outside the garbage defender. No conclusion could be made for the source of these floating refuses. On the other hand, some of the floating refuses were observed immigrating in the protective zone during investigation 8) All daily cleaning actions had been taken by contractor to minimize floating refuse inside the construction site. It was noted that the intake (land side) is open access to public, so that many activities such as fishing, feeding fish were conducted there even though a notice has already hoisted. Also, tripping of rubbish by the passers-by could result in a lot of rubbish accumulated around the intake point. 9) Referring to the record provided by CPML, there were a lot of nylon/ plastic bags and nylon wire mesh that matched those rubbishes generated from the public activities. 10) Contractors have fulfilled the requirement of site cleanness and no exceedance was recorded during Water Quality Monitoring. It is consider the cause of this complaint is not related to project and environmental issue in this project as well. No more complaint received after ad-hoc inspection	
111014	14/10/2011	The complainant, Ms. Tam complained via hotline 1823	Wan Chai	The polluted fumes and exhaust from the excavation by sub-contractor of CEDD on pedestrian way outside no.25 Harbour Road (in front of the Harbour Centre)	1) RSS notified ET to carry out investigation on 17 October 2011. 2) ET confirmed with the Resident Site Staff that the location of the excavator was within site area of Contract no. HK/2009/02 undertaking the water cooling main reprovision works along the Harbour Road. The plants including the excavator have been checked before using at the site. However, the polluted fumes and exhausted from the excavator was caused due to insufficient maintenance of the plant after using at site. 3) After receiving the complaint, the excavator was then removal off-site for checking and maintenance works on 17 October 2011. 4) Contractor was reminded to enhance regular checking and maintenance to all plants at site. 5) RSS has replied to the complainant on the arrangement of the measures taken on 17 October 2011. Complainant was satisfied with the response and follow-up action taken by the Contractor.	Closed
111104	04/11/2011	Mr. Liu from	Wan Chai	Complain about a tree near the	1) ET confirmed with the Resident Site Staff that	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
		LCSD complained via Contractor Complaint Hotline		site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road, the status is not healthy and roof ball of two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue were half cut.	• A tree near the site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road is the Tree no. TA1122 under Contract no. HK/2009/02. Leaves of a branch of this tree were shrivelled. • Two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue are the tree nos. A160 and A161 under Contract no. HK/2009/01. Part of roof ball of these two trees was covered by the metal plate. 2) Independent Tree Specialists for these two inspected the trees. Contractor HK/2009/01 has taken the measure as recommend downgrading the soil level around the trunk base. Reinstating of the ground works will be conducted in mid-December 2011. For the tree no. TA1122 under Contract no. HK/2009/02, the brown leaves were removed and fenced the tree with orange net is provided to prevent damage of tree trunk by construction works. The distance between the tree and the edge of the trench is kept approximate 2m. Two Contractors were reminded to carry out regular watering to the trees within their site area.	
111106	06/11/2011	Police officer	Wan Chai	Construction noise generated from the site at about 6:30 a.m on 6 November 2011 and require to stop the machine operation	1) According to the information reported by Contractor, one BC cutter and hoist were operated for Diaphragm Wall construction of Shatin-Central Link to inspect bentonite pipes and ensure no damages and all the joints are tightened in good position. Then, the subcontractor for Diaphragm wall, SAMBO Korean foreman stopped the engine of the BC cutter immediately. The police officer recorded the details and HKID number of the foreman and then left. Due to the different language communication between the police officer and the Korean foreman, no CNP was checked by the police officer. 2) ET confirmed with the Resident Site Staff that same issue was also raised out by RSS at about 7:00a.m on the same day. Besides, it was confirmed that there is no valid Construction Noise Permit for the conducted construction works in the period between 2300 and 0700. 3) Due to insufficient communication between Contractor HK/2009/01 and their Korean Sub-contractor, Korean Sub-contractor had not notified to Contractor before carrying out the inspection of the BC cutter, hoists and	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					bentonite pipes at about 6:00a.m to ensure no damages and all the pipe joints should be tightened and in good position. 4) Contractor was advised to enhance the communication between Contractor and sub-contractor and provide sufficient environmental training to all foreman and operators on restricted hour operation. Furthermore, Construction Noise Permit should be checked and in place for the construction works during restricted hour 5) This complaint was considered in relation to the conducted construction works during restricted hours without valid Construction Noise Permit. No more construction works were conducted during night time period. The construction works will be conducted in accordance with the time period stated in valid CNP. This complaint will be kept in view of any follow-up action from the relevant government activities.	
111212	12/12/2011	The complainant, Mr Tsui from IFCII's management office complained via hotline 1823	Central	A visual impact complaint from hotline 1823 was received by ET on 9 January 2011 (ICC Ref. No.: ICC#1-333037096 dated on 12 December 2011). The complaint, Mr Tsui was reported that visual nuisance caused by lighting in the construction site during night time.	1) RSS notified ET on 9 Jan 2012. 2) ET confirmed with the Resident Site Staff that A joint inspection was conducted by Mr Tsui and contractor on that night to see whether there is any improvement. 3) Due to safety reason, igniting enough lights should not be avoided in construction site. However, the light sources were not directed away from pointing to the sensitive receiver and results in visual glare to the complaint. 4) Confirmed with the Resident Site Staff the complainant was satisfied the new arrangement of the lights with contractor after the joint inspection. No further complaint received after that.	Closed
111220	20/12/2011	The complainant, Ms. Poon complained via hotline 1823 (ICC Ref. No.: ICC#1-334683841)	North Point	Construction air and noise nuisance generated that many trucks carrying construction materials driving along Watson Road and Oil Street and possibly entering/leaving the construction site near the IEC during 0800 to 1900 hours.	1) RSS notified ET on 22 Dec 2011. 2) ET confirmed with the Resident Site Staff that the complainant cannot identify whether the trucks were working under the CWB project or not. 3) The dominant construction air and noise nuisances were emitted by the trucks along Oil Street and Waston Road, however, this is the public road for all vehicles. Reviewing the air quality monitoring and noise monitoring results. No exceedance was recorded during this period. 4) Confirmed with the Resident Site Staff that they provided a contact no. for any future enquiries regarding	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					CWB project to the complainant and she was satisfied on the arrangement and no further complaint was received after that.	
111230	30/12/2011	Residents of Harbour Heights	North Point	Construction air and noise nuisance generated by construction vehicles were found parked illegally at King Wah Road and lining up at Oil Street without the engine turning off.	1) RSS notified ET on 6 January 2011. 2) ET confirmed with the Resident Site Staff that a number of construction activities are concurrently proceeding in the vicinity of Oil Street, King Wah Street and a private development project in King Wah Street 3) The dominant construction air and noise nuisances were emitted by the trucks along Oil Street and King Wah Road, however, this is the public road for all vehicles. Reviewing the results of air quality monitoring station (CMA1b) and noise monitoring (M4b). No exceedance was recorded during this period. Site inspections for HY/2009/19 were conducted on 4 January 2012. The condition of the site access at Oil Street and the public road nearby were found satisfactory. It is noted that HyD also allow and encourage their contractors to maximize the use of marine access, where available, to work sites, so as to minimize burdening nearby public roads. When land trips are unavoidable, they require contractors to tidy up their construction vehicles before leaving works sites. No contractor under CWB project parked their vehicles illegally at King Wah Street, and HyD still reminded them not to commit such offence. 4) According to HyD's staff replied the complaint letter on 10 January 2012, there is a private development project under construction at King Wah Road. To access these works sites, construction vehicles have to use public roads nearby. No further complaint received after HyD's reply.	Closed
120118	18/01/2012	N/A	North Point	A complaint regarding a tree located in front of Victoria Centre under IECL was covered by one meter mud without any protection. The complainant concerns the health of the tree in such condition.	1) RSS notified ET on 20 January 2012. 2) ET confirmed with the Resident Site Staff that The tree is inside the site area of HY/2009/19 and The Botanical name of the tree is Ficus superba var. japonica and the I.D. of the tree is UT48 3) According to the information provided by RSS on 20 Jan 2012, the tree shall be felled that has been approved by DLO on 29 August 2011. Moreover, the tree was felled	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					by contractor on 19 January 2012. 4) No further complaint received after HyD's reply.	
120305	03/03/2012	Resident of Harbour Heights complained via hotline 1823 (ICC Ref. No.: ICC#1-344632511)	North Point	A complaint regarding excessive noise from construction sites of CWB was observed outside Harbour Heights from Monday to Saturday before 8am. The plants were frequently turned on before 7:30am creating nuisance. The complainant requested a speedy follow-up and reply from relevant department.	1) RSS notified ET on 5 March 2012. 2) ET confirmed with the Resident Site Staff that PME for diaphragm wall construction started to operate at about 7:30am whilst the other PME, including those for land bored piling work, started to operate after 8am. 3) After reviewing the results of noise monitoring (M4b), no exceedance was recorded during daytime period and the noise level were below 75dB(A). Site inspection for HY/2009/19 was conducted on 7 March 2012. The condition of noise mitigation measures near Harbour Heights was found satisfactory. RSS confirmed that no operation was active before 7:00am everyday. The suspected nuisance was to be considered caused by the PME for diaphragm wall construction. A surprise check was performed on 13 March 2012 by RSS. It was found that no noisy PME was in operation by Contractor of HY/2009/19 before 8am, and the construction noise level was minimal and not disturbing. The noise level and operation time both complied with statutory requirements set up in NCO. 4) Complainant called ICC on 8 March 2012 to confirm HyD has provided a response. No further complaint was received after the response.	Closed
120405	05/04/2012	N/A	North Point	A complaint regarding excessive noise from construction sites of CBTS was observed daily before 7:30am except on public holidays, and the noise source was mainly from piling works. The complainant requested that construction works should start after 8:30am to avoid nuisance to nearby residents and a speedy follow-up and reply.	1) RSS notified ET on 5 April 2012. 2) ET confirmed with the Resident Site Staff that no piling works were performed during the concerned period. 3) After reviewing the results of noise monitoring (M2b and M3a), no exceedance was recorded during daytime period and the noise level was below 75dB(A). Site inspection for HY/2009/15 was conducted on 10 April 2012. The condition of noise mitigation measures around CBTS was found satisfactory. RSS confirmed that no pilings were performed during the concerned period. The major works included drilling, diaphragm wall construction and excavations. 4) HyD made a reply to the complainant on 16 April	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					2012 via 1823. HyD replied that the current works at CBTS were drilling, diaphragm wall construction and deep excavations. In order to minimize the noise generated from the above works, the Contractor had erected temporary noise barriers and provided noise blankets on plants. RSS would continue to work with the Contractor on the effectiveness of the environmental mitigation measures implemented on site. No further complaint was received after the response.	
120415	15/04/2012	The complainant Ms. Law, resident of Fu Lee Loy Mansion, complained via hotline 1823 (ICC Ref. No.: 1-351021108)	North Point	A complaint regarding excessive noise generated from a HyD project that is located at the connection point of CWB and IEC affecting nearby residents. Lately during the middle of the night (around 00:00 to 05:00), low frequency noise, which possibly came from the operating power generator and the barges which were parked along the Oil Street work site, were making a nuisance to the complainant and residents nearby. The complainant requested that relevant department should follow-up.	1) RSS notified ET on 17 April 2012. 2) ET confirmed with the Resident Site Staff that there was no operation of power generators for HY/2009/19 and HY/2009/17 (HY/2009/11 had no physical work on site) during the concerned period. Although there were a few barges mooring at the seafront of HY/2009/19, they were not in operation and hence no operational noise would be emitted. 3) After reviewing the results of noise monitoring (M4b and M5b), no exceedance was recorded during day time period and the noise level was below 75dB(A). Site inspection for HY/2009/19 was conducted on 18 April 2012. The condition of noise mitigation measures near Harbour Heights were found satisfactory. RSS confirmed that no operation of power generators for HY/2009/19 and HY/2009/17 (HY/2009/11 had no physical work on site) during the concerned period. Although there were a few barges mooring at the seafront of HY/2009/19, they were not in operation and hence no operational noise would be emitted. 4) HyD made a reply to the complainant on 30 April 2012 via email. HyD replied that the current works near Oil Street, North Point, included CWB tunnel works, IEC connections and associated foundation works. According to RSS records, no operations were performed during the early hours of March and April at Oil Street and the waterbody nearby, and so it was believed that the noise nuisance was not generated from the CWB project. Despite that, RSS would continue to monitor the Contractor on the operations and effectiveness of the environmental mitigation measures implemented on site, as not to affect daily life of local residents nearby. No further complaint was received after the response.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
130308	06/03/2013	ICC Case#1-407181502	Tin Hau	A complaint regarding the dropping of fine rock material into surrounding waterbody was observed during rock breaking operation with two excavators in active operation at the Eastern Breakwater of Causeway Bay Typhoon Shelter near the North Point lighthouse.	1) RSS notified ET on 8 Marc 2013 2) ET confirmed with RSS that excavation works, installation of buoy, flashing light and silt curtain and dredging works were undertaken at Eastern Breakwater during the concerned period on 6 March 2013. One backhoe equipped with breaker and one derrick barge were confirmed in operation while another backhoe was at idle during the concerned period on 6 March 2013. 3) Reviewing the photo record provided by RSS, the condition of the silt curtain deployed around the Eastern Breakwater on 6 March 2013 was found to be in good condition. It is considered that the silt curtain was properly in place during the concerned period and the concerned act of dropping of fine rock material was confined within the silt curtain boundary without adverse impact to the nearby water quality. Further follow up was conducted on 12 March 2013 during weekly environmental audit inspection, the silt curtain deployed around the concerned area was found to be maintained in good condition and the water quality at the concerned work area was generally satisfactory. No violation of the Environmental Permit condition was found. The contracotr was advised and committed to implement preventive meaures to minimize the potential impact of work including conducting regular diver check to ensure the integrity and the extend of silt curtain deployment and to provide adequtae back up stock of silt curtain for emergency use.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
130606	30/5/2013	ICC Ref. No.: #1-430164728	Central – Man Kat Street	1. A number of trees (approximately more than ten) along Man Kat Street were found to be in poor health condition with withered and yellow leaves. The complainant has requested a follow-up by relevant department.	1) RSS notify ET on 6 June 2013 2) ET confirmed with the Resident Site Staff that According to the information provided by RSS, 13 no. of the trees - Roystonea regia (T1674, T1675, T1676, T1677, T1678, T1679, T1680, T1681, T1683, T1644, T1643, T1641, T1639) at the concerned location raised by the complainant was found to be with withered and yellow leaves and 1 no. of tree- Khaya senegalensis (T1712) raised by the complainant was found to be in poor health condition. No construction works was undertaken by Contract HY/2009/18 at the concerned planter area where the affected trees are located. It was also observed that an active CEDD construction works area under a separate contractor not related to Central Wan Chai Bypass Project was found to be located within the concerned planter area. 3) A follow-up joint inspection with RSS and Landscape specialist was conducted on 10 June 2013, it was considered that the withered and yellow leaves of the affected trees (T1674, T1675, T1676, T1677, T1678, T1679, T1680, T1681, T1683, T1644, T1643, T1641, T1639) at the concerned planter area were contributed by natural life cycle of the affected trees and the health condition of the affected trees were considered to be fair. It was also noted that an active CEDD works area was located within the concerned planter area in close proximity to few of the concerned trees (T1644, T1643, T1641, T1639) According to tree inspection records from Jan 2013 to May 2013 confirmed by RSS (Document Ref: CI-F1-043b, CI-F1-044b, CI-F1-045b, CI-F1-046b, CI-F1-047b), the affected tree (T1712) at the concerned planter area was considered to show sign of withering and considered to be in poor health condition in latest tree survey report confirmed by RSS.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					During the follow-up inspection on 10 June 2013, It was observed that construction material and oil drum were placed near the the roots area of other trees within the CEDD works. Despite the above observation, no direct evidence was found on site which indicates the work front have contributed to the poor health condition of the affected tree (T1712) at the time of investigation. 4) The relevant contractor have removed the construction material near the root area of the trees retained on site and conduct pruning to remove the withered and yellow leaves retained on tree trunk to minimize impact on the trees appearance.In addition, safety supporting wire was provided for concerned tree (T1712) 5) ET recommended the contractor to keep in view the health condition of the concerned tree (T1712) and apply permission for tree felling together with tree compensation plan if considered necessary. Furthermore, the contractor was reminded to implement regular checking of tree health condition and regular removal of withered leaves to maintain the overall tree appearance.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
130611	30 May 2013 and 1 June 2013	EPD Ref.:H04/RS/000 11587-13	Area near Central Pier	1. Noise was emanated from the construction site near the Central Piers at around 0900 hrs on 30 May 2013 and other days and requested follow up action by relevant department.	1) RSS notify ET on 11 June 2013 2) ET confirmed with the Resident Site Staff that According the information confirmed by RSS, major noise generating construction activities undertaken at works area near Central Pier during the concerned time include - Breaking up existing D-wall concrete and excavation at portion 4B and 4C - Sheet piling works at Portion VI (Man Kat Street) 3) Total 1 no. of Backhoe with breaker, 1 no. of Backhoe with vibratory hammer and 4 no.s of pneumatic breakers were deployed for the above construction activities. Reviewing the noise monitoring data at monitoring stations (M7e- International Finance Centre Eastern End of Podium and M7w- International Finance Centre Western End of Podium), no limit level exceedances were recorded during routine noise monitoring event on 28 May 2013 and 03 June 2013. As similar construction works activities conducted on 30 May 2013 was continued across the above monitoring period, the noise emanated from the construction activities under Contract HY/2009/18 was considered to complied with the statutory requirement. In addition, weekly environmental site inspection was conducted on 30 May 2013 at around 10:00. According to the inspection record, no particular observation regarding noise impact was recorded and the mitigation measures including erection of temporary noise barrier was observed in place. As such, no direct information associated with the noise concerned raised was considered available and no non-conformity was identified. 4) ET recommend the contractor to review the need of additional noise mitigation measures to further reduce the noise enmated during construction works for pier side	Interim report submitted to EPD on 19 June 2013, EPD advised no further comment on 5 Aug 2013 and final report for case closing submitted on 6 Aug 2013.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					public area.	



Appendix 10.1

Construction Programme of Individual Contracts


[illegible]

[illegible]

Date: 20-Aug-11
Print Date: 29-Aug-11
DCP3-2

HY/2009/18 Central - Wan Chai Bypass (Central Interchange)

TASK filter: HL

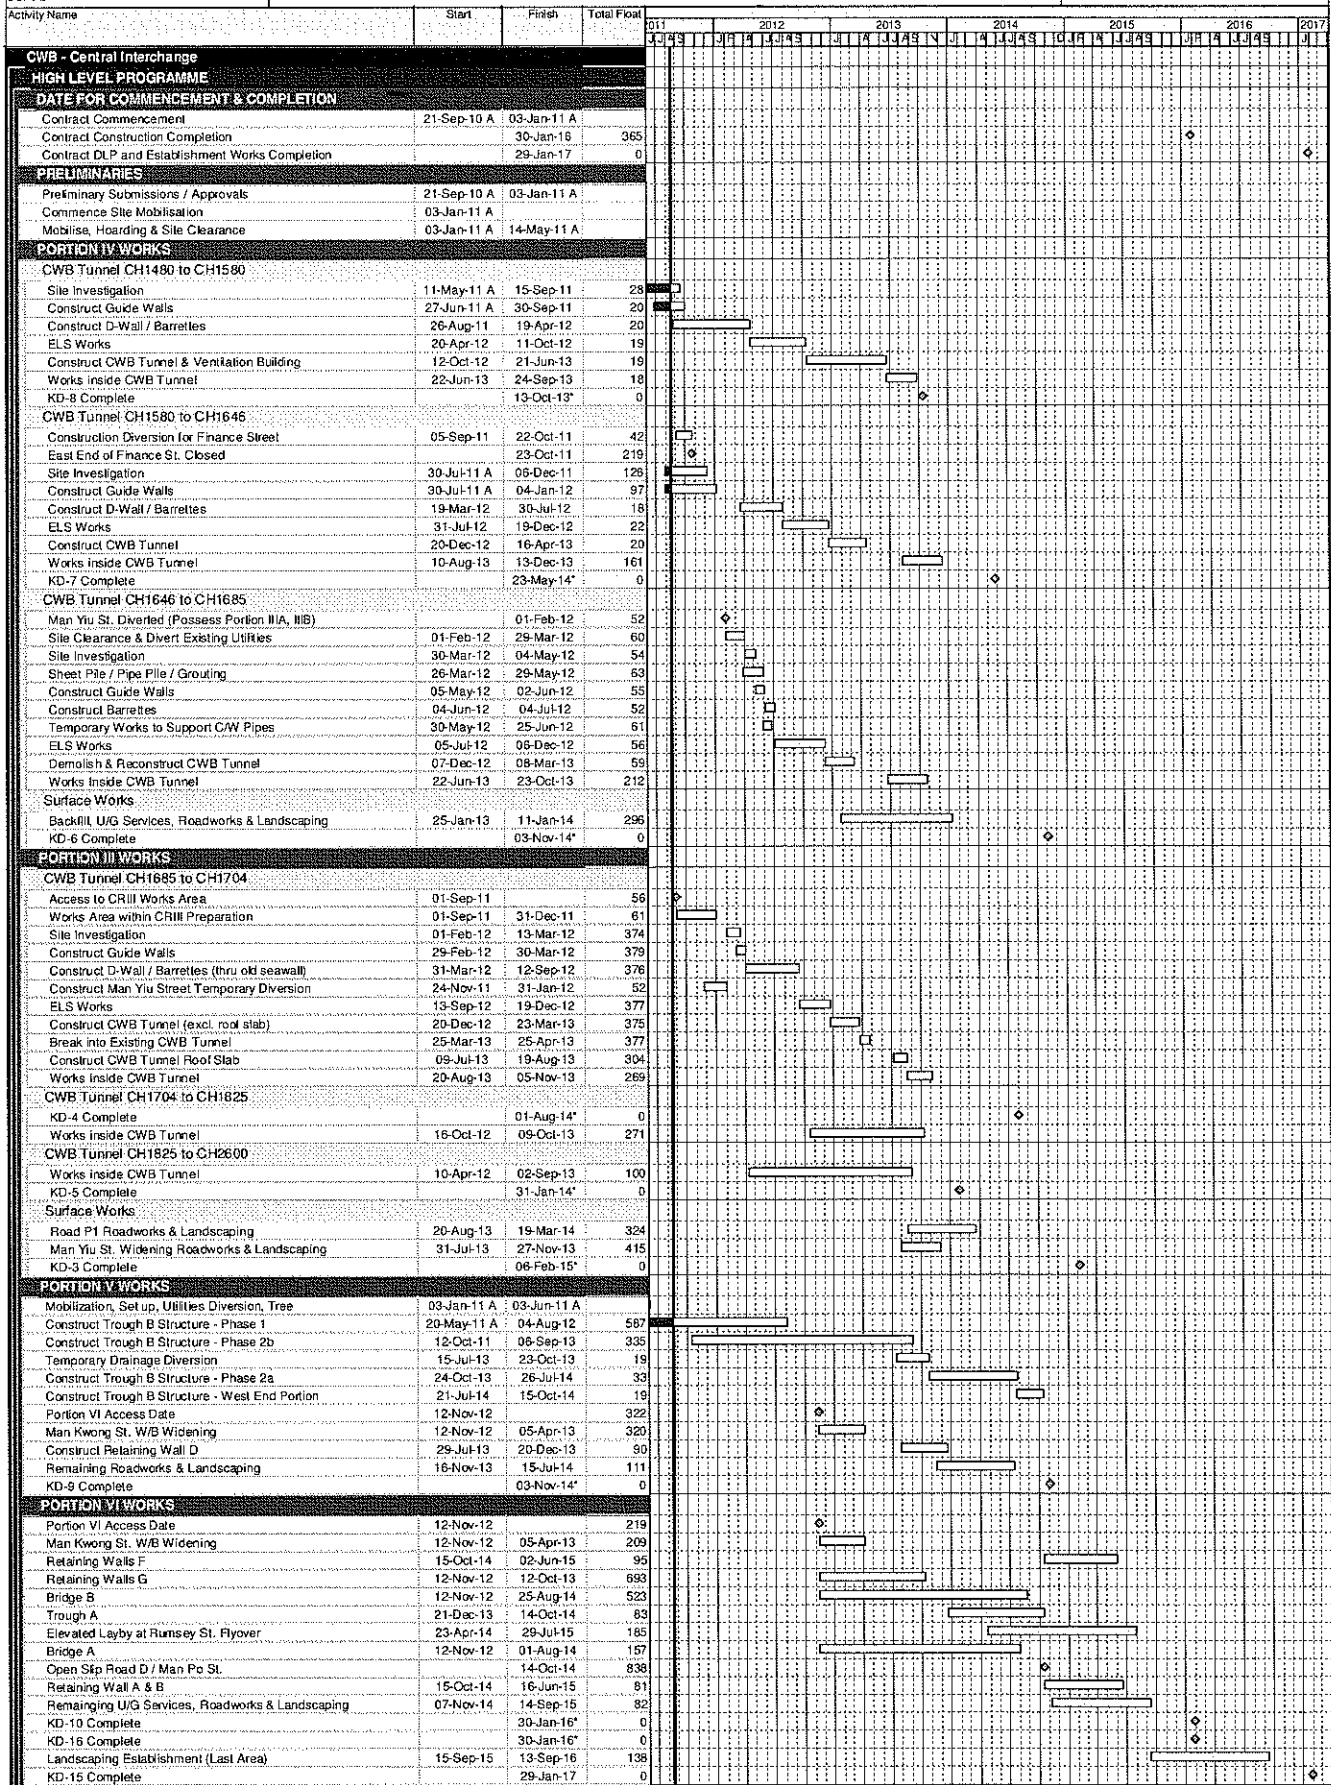



[illegible]


Last Updated on: 6-Aug-2011


Wan Chai Development Phase II - Central - Wan Chai
Bypass at Wan Chai East CONTRACT HK/2009/02


CHUN WO - CRGL JV

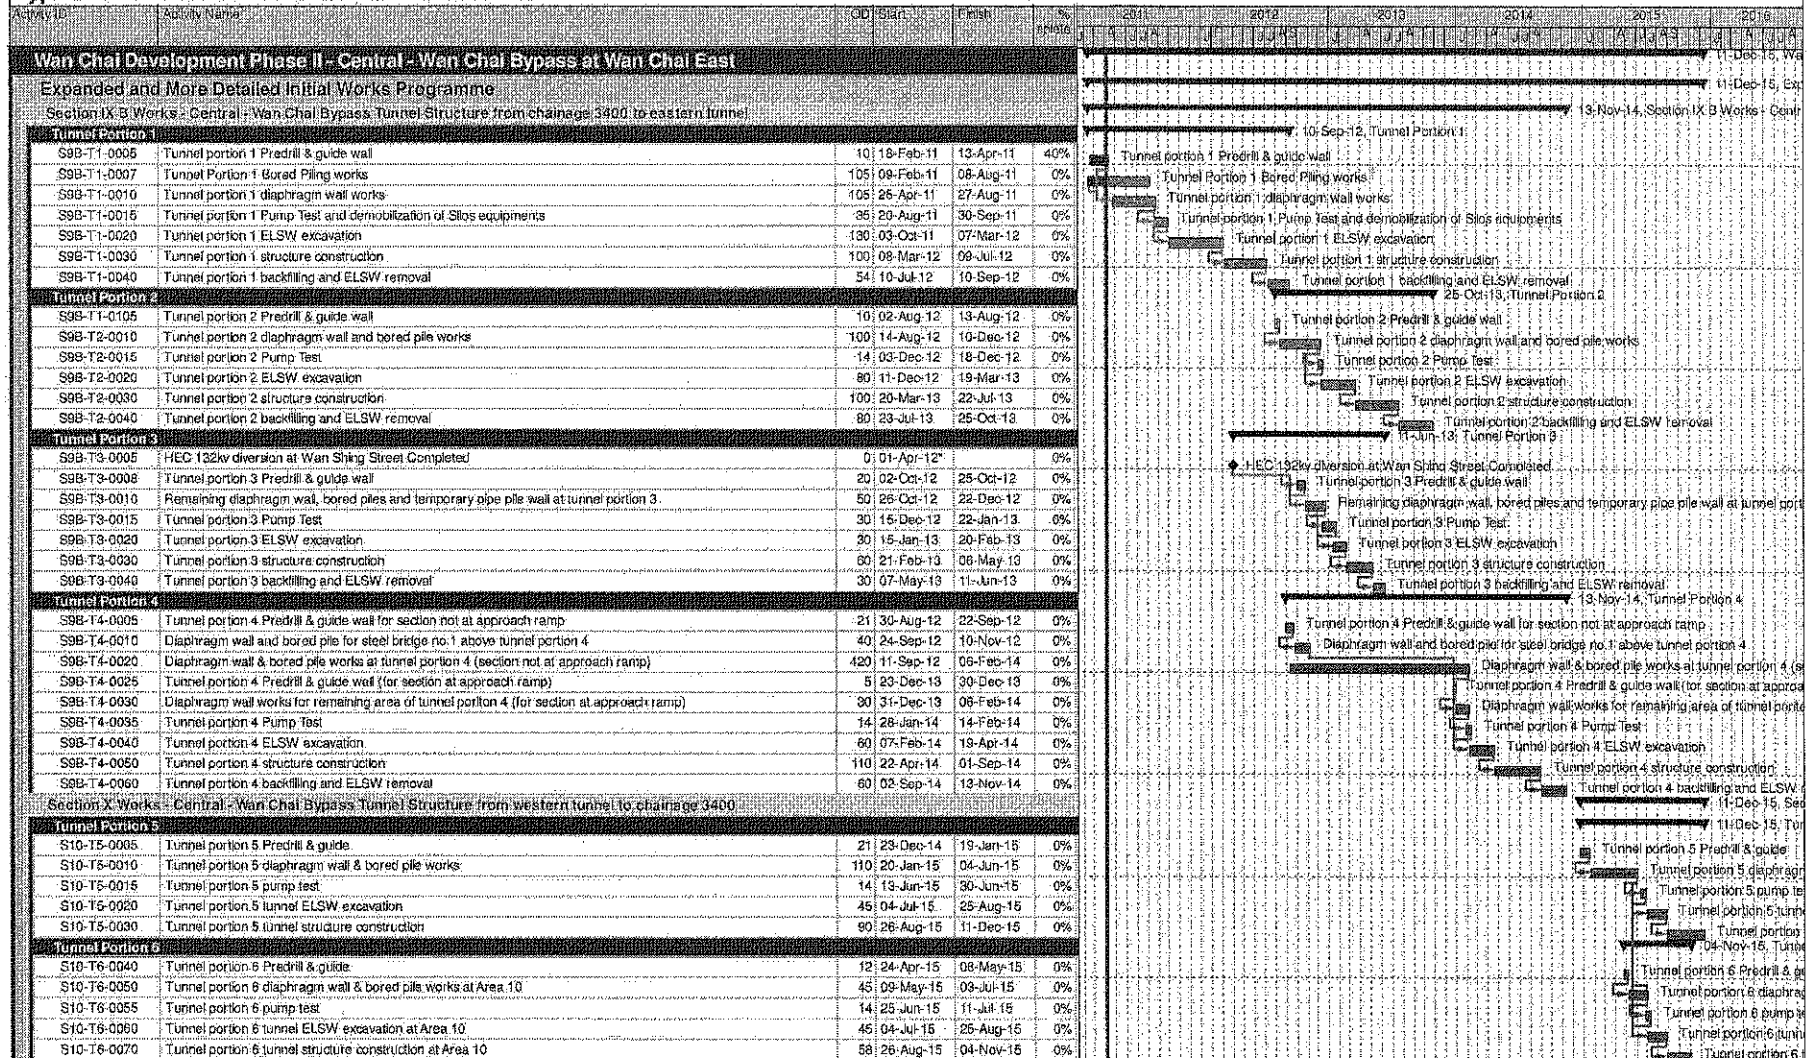


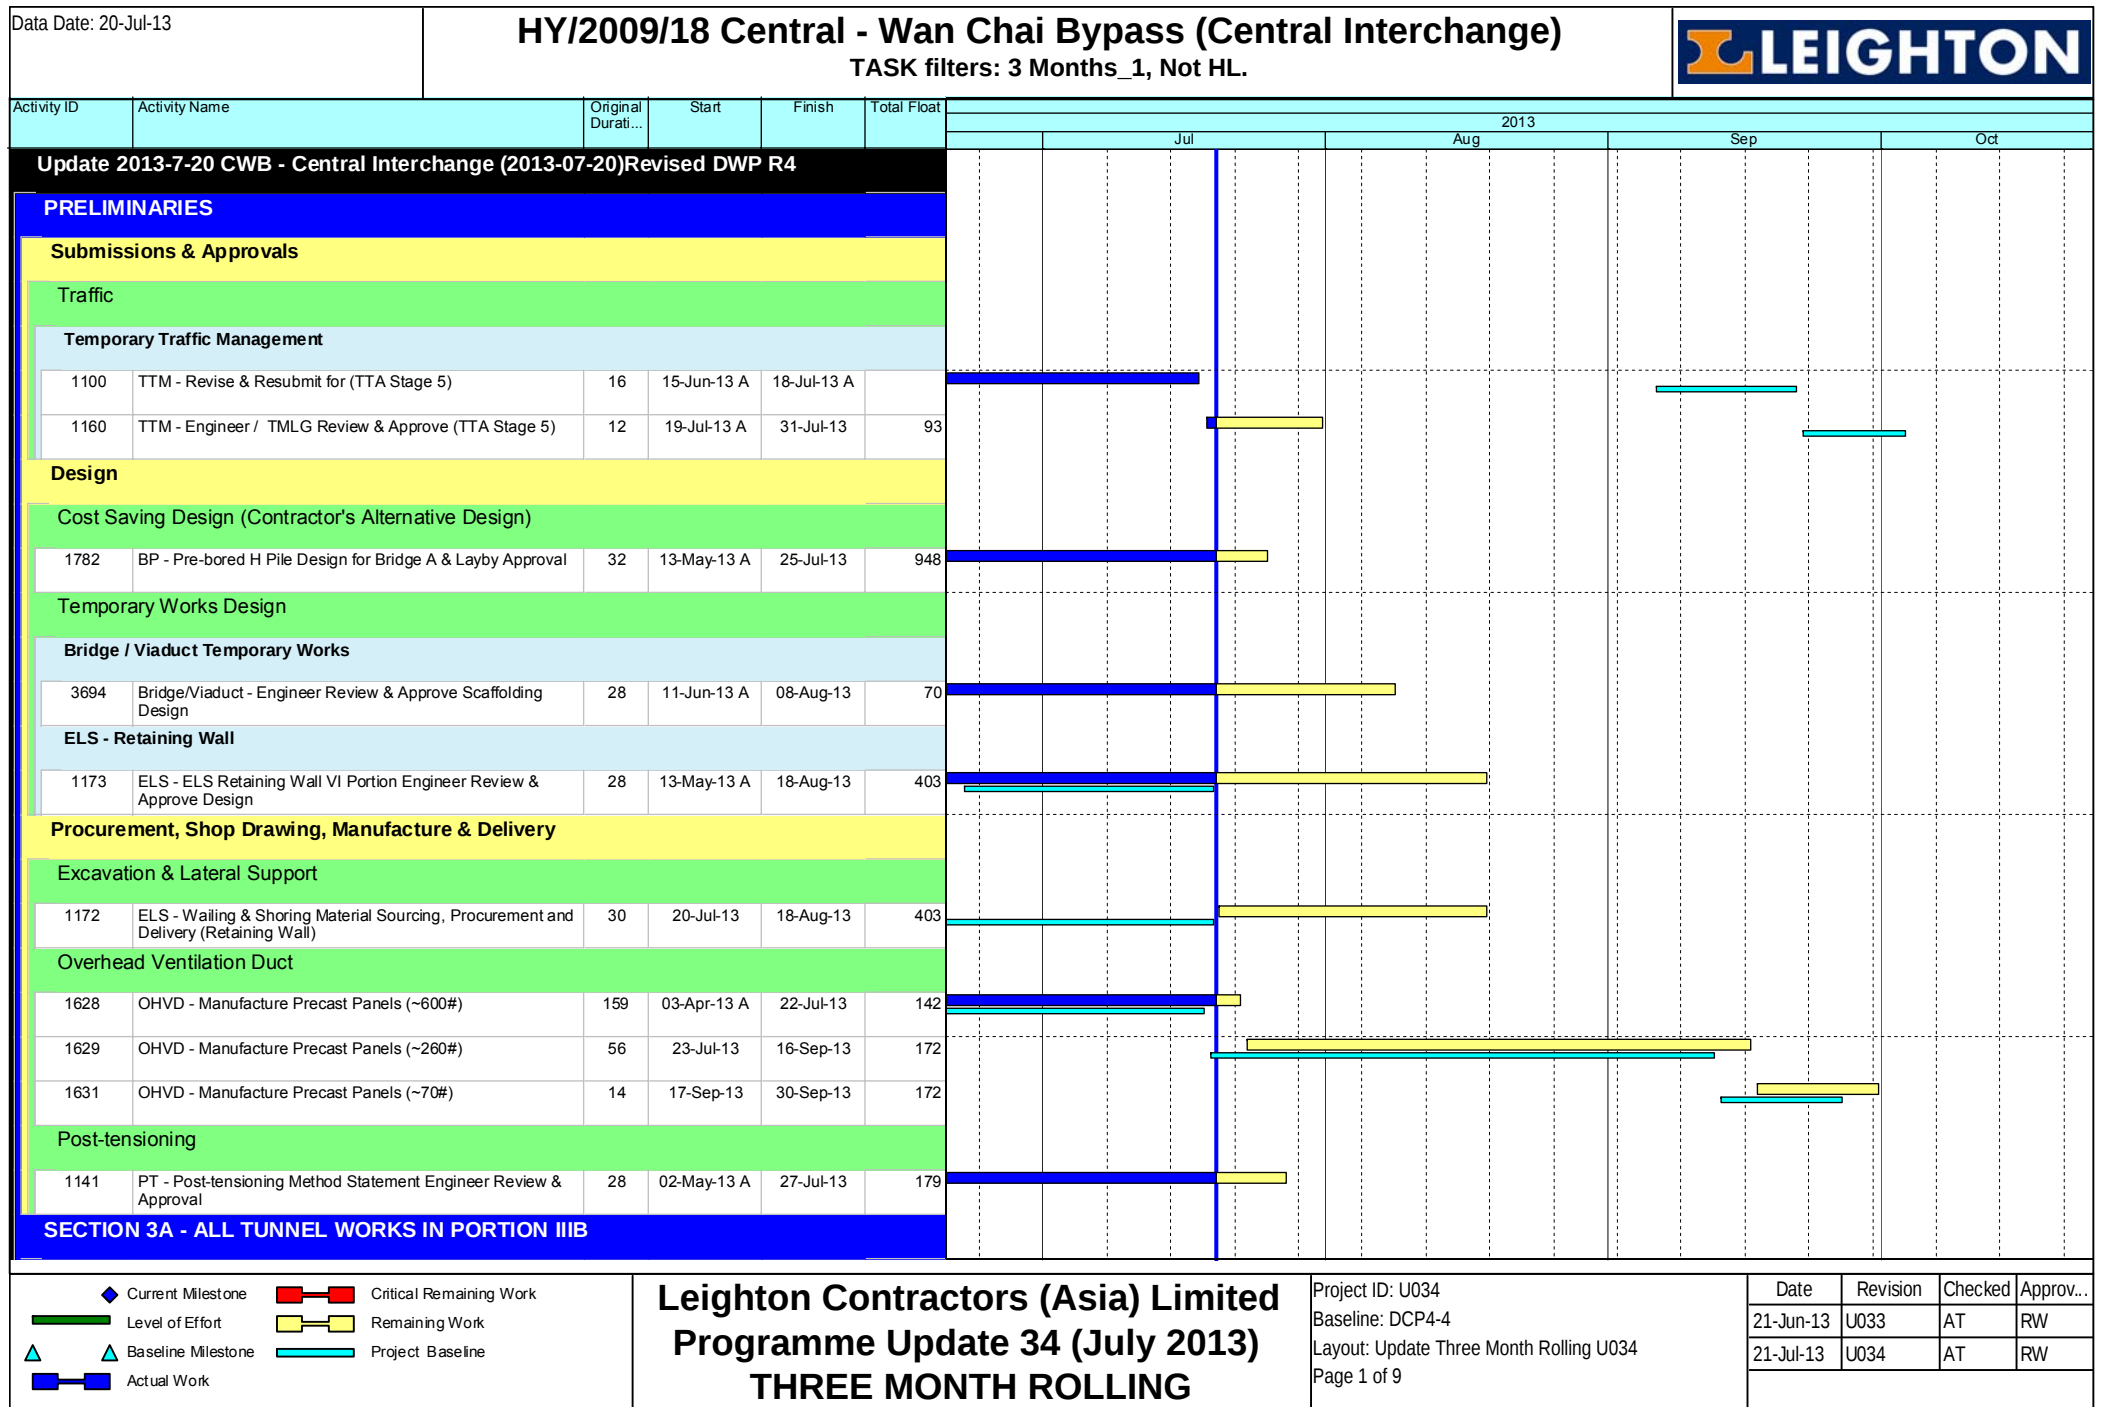


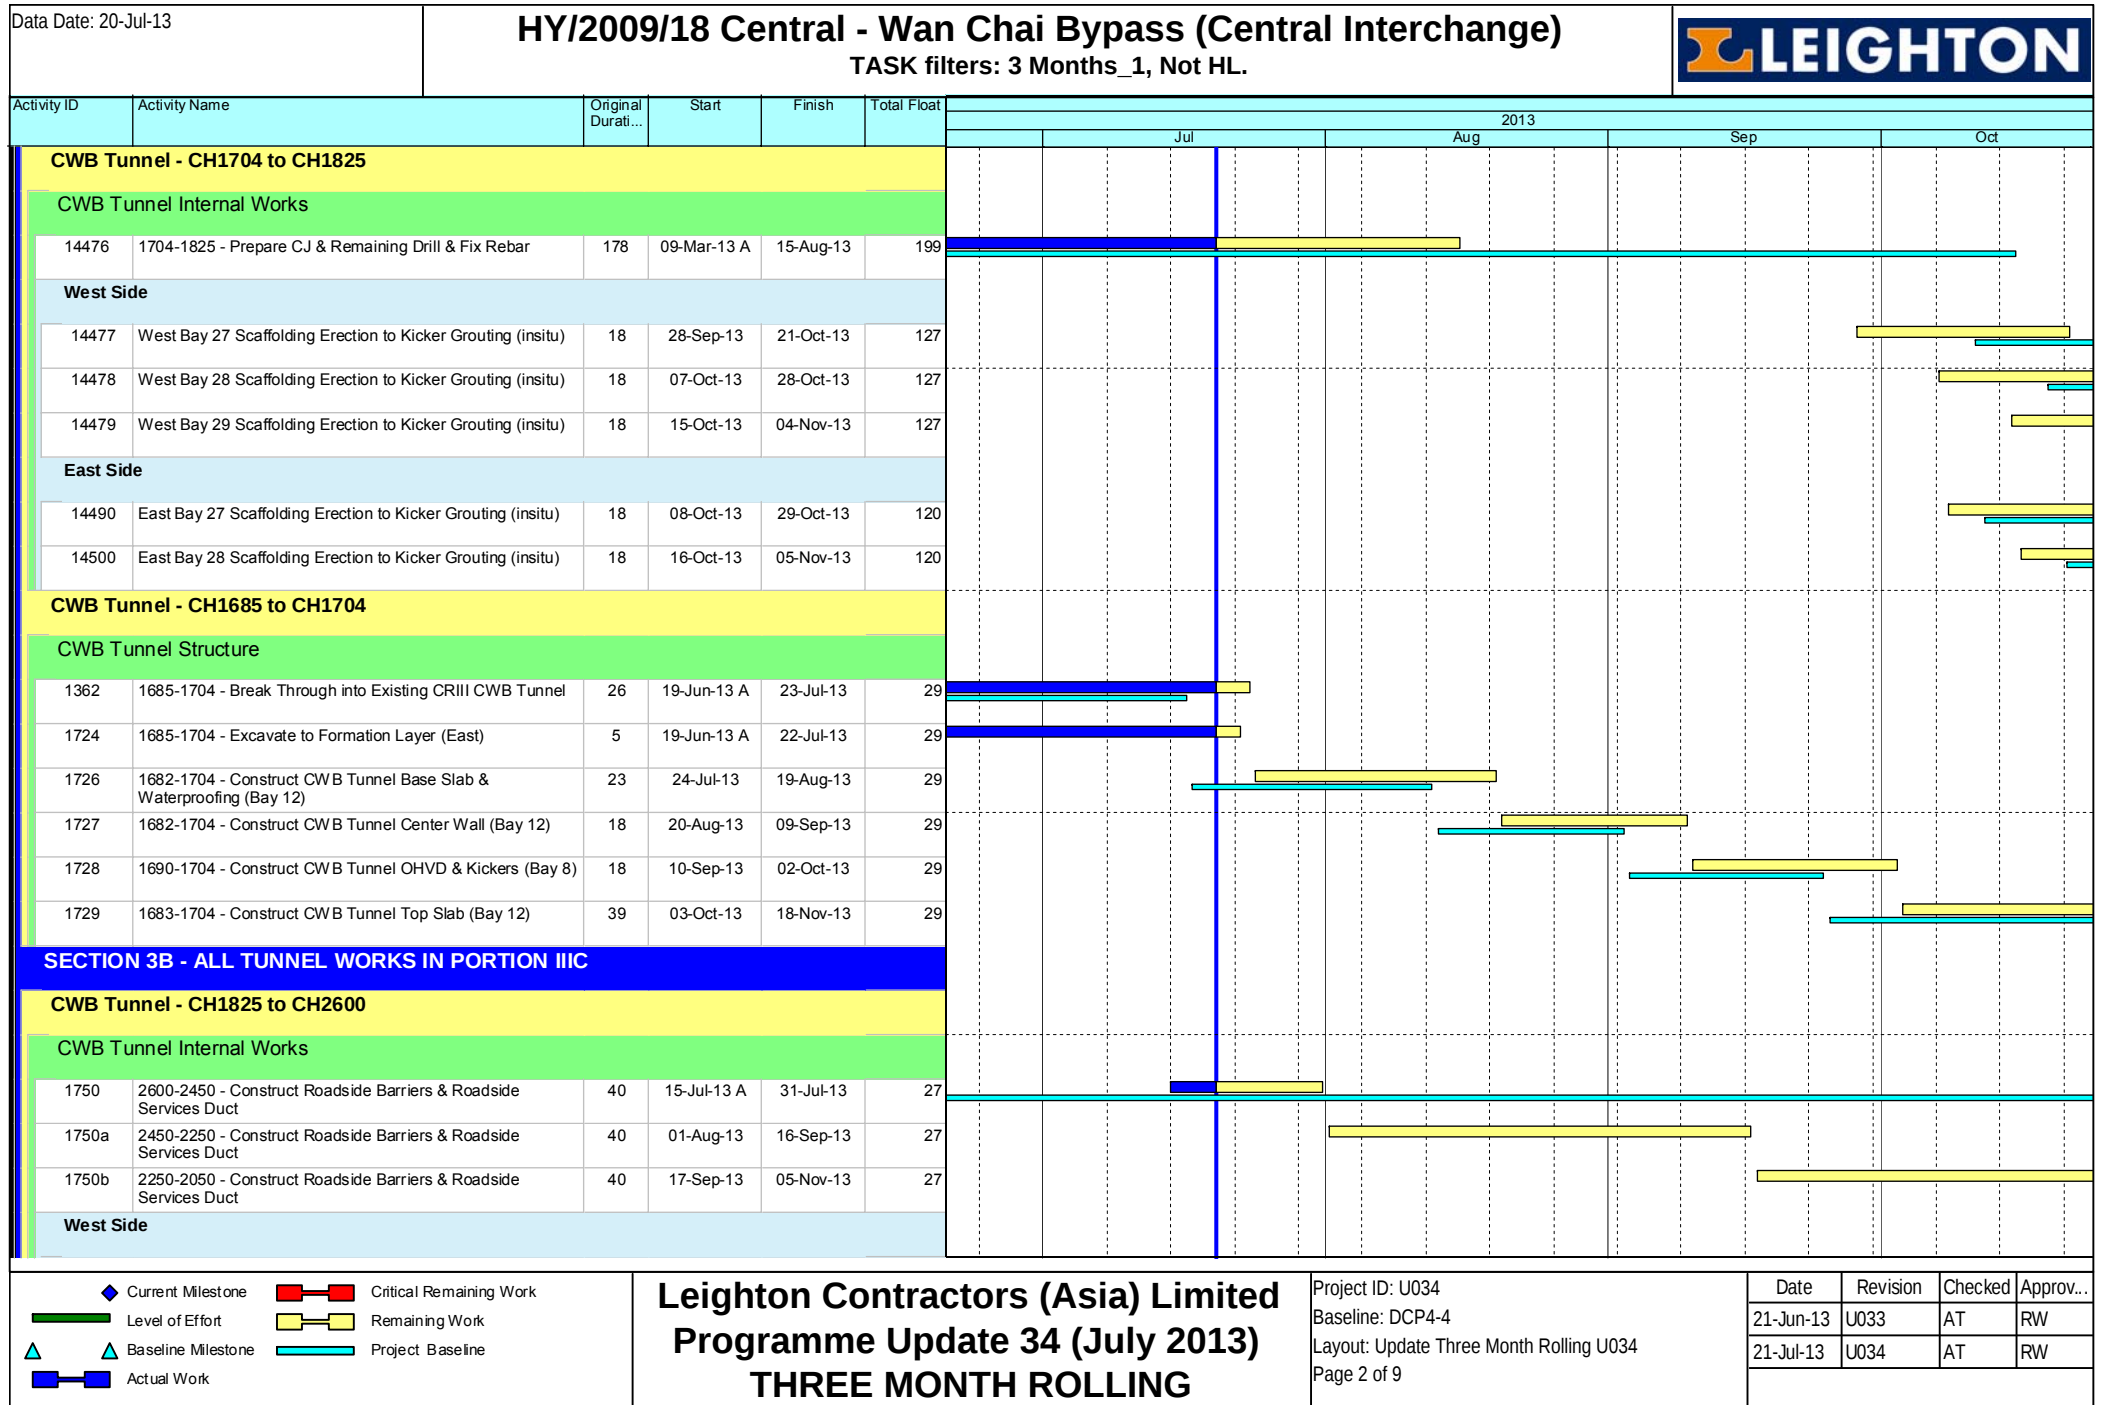


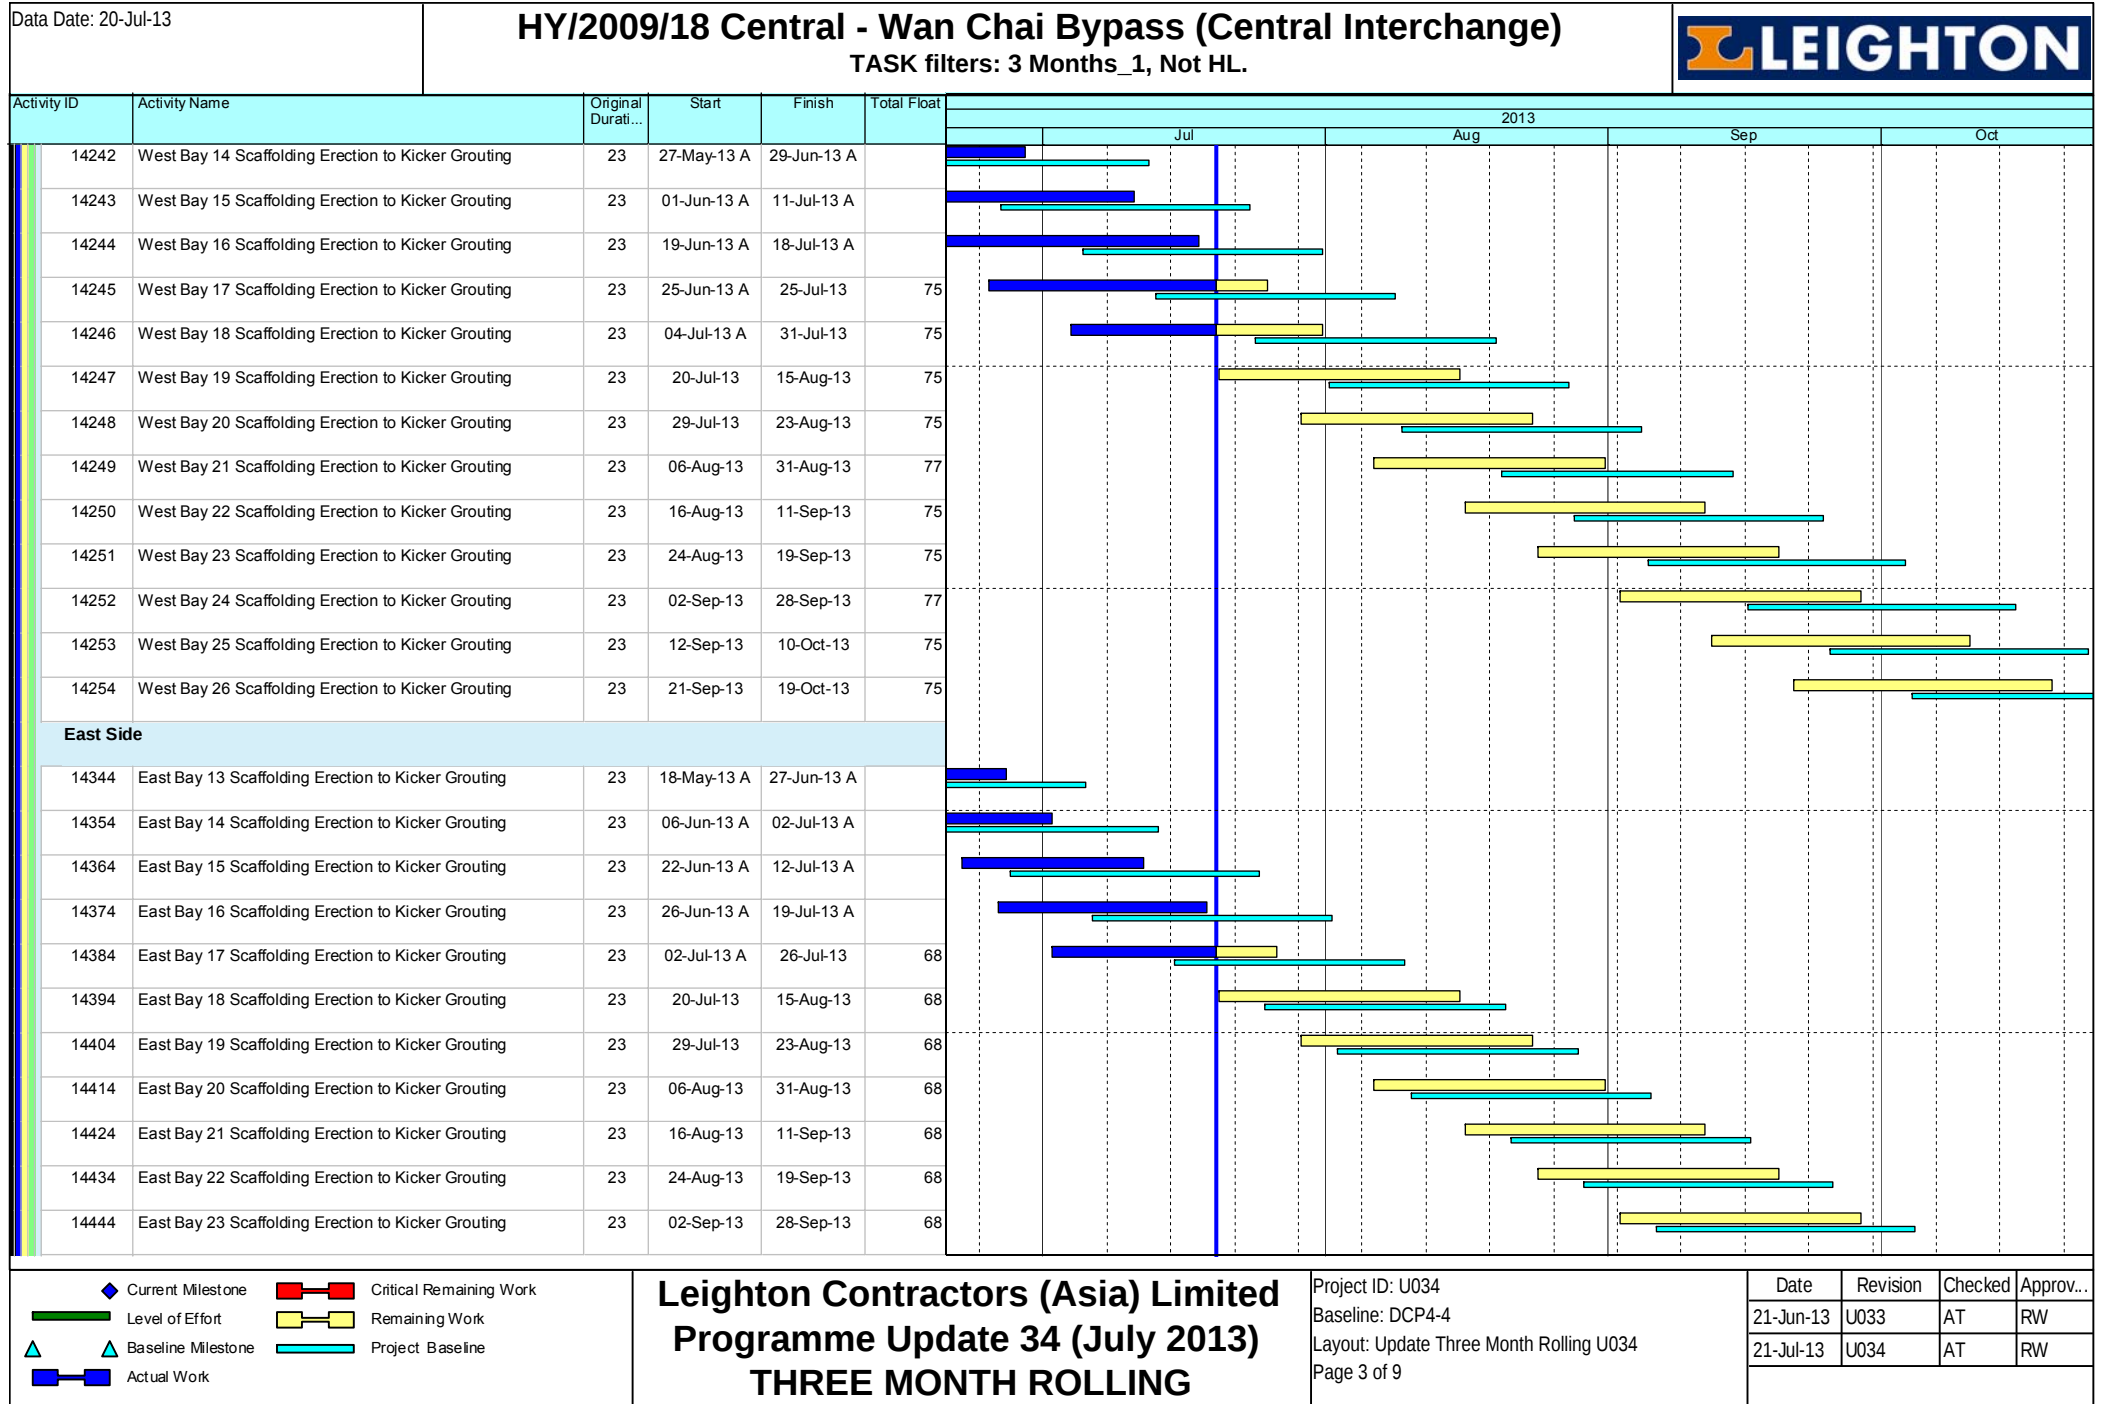


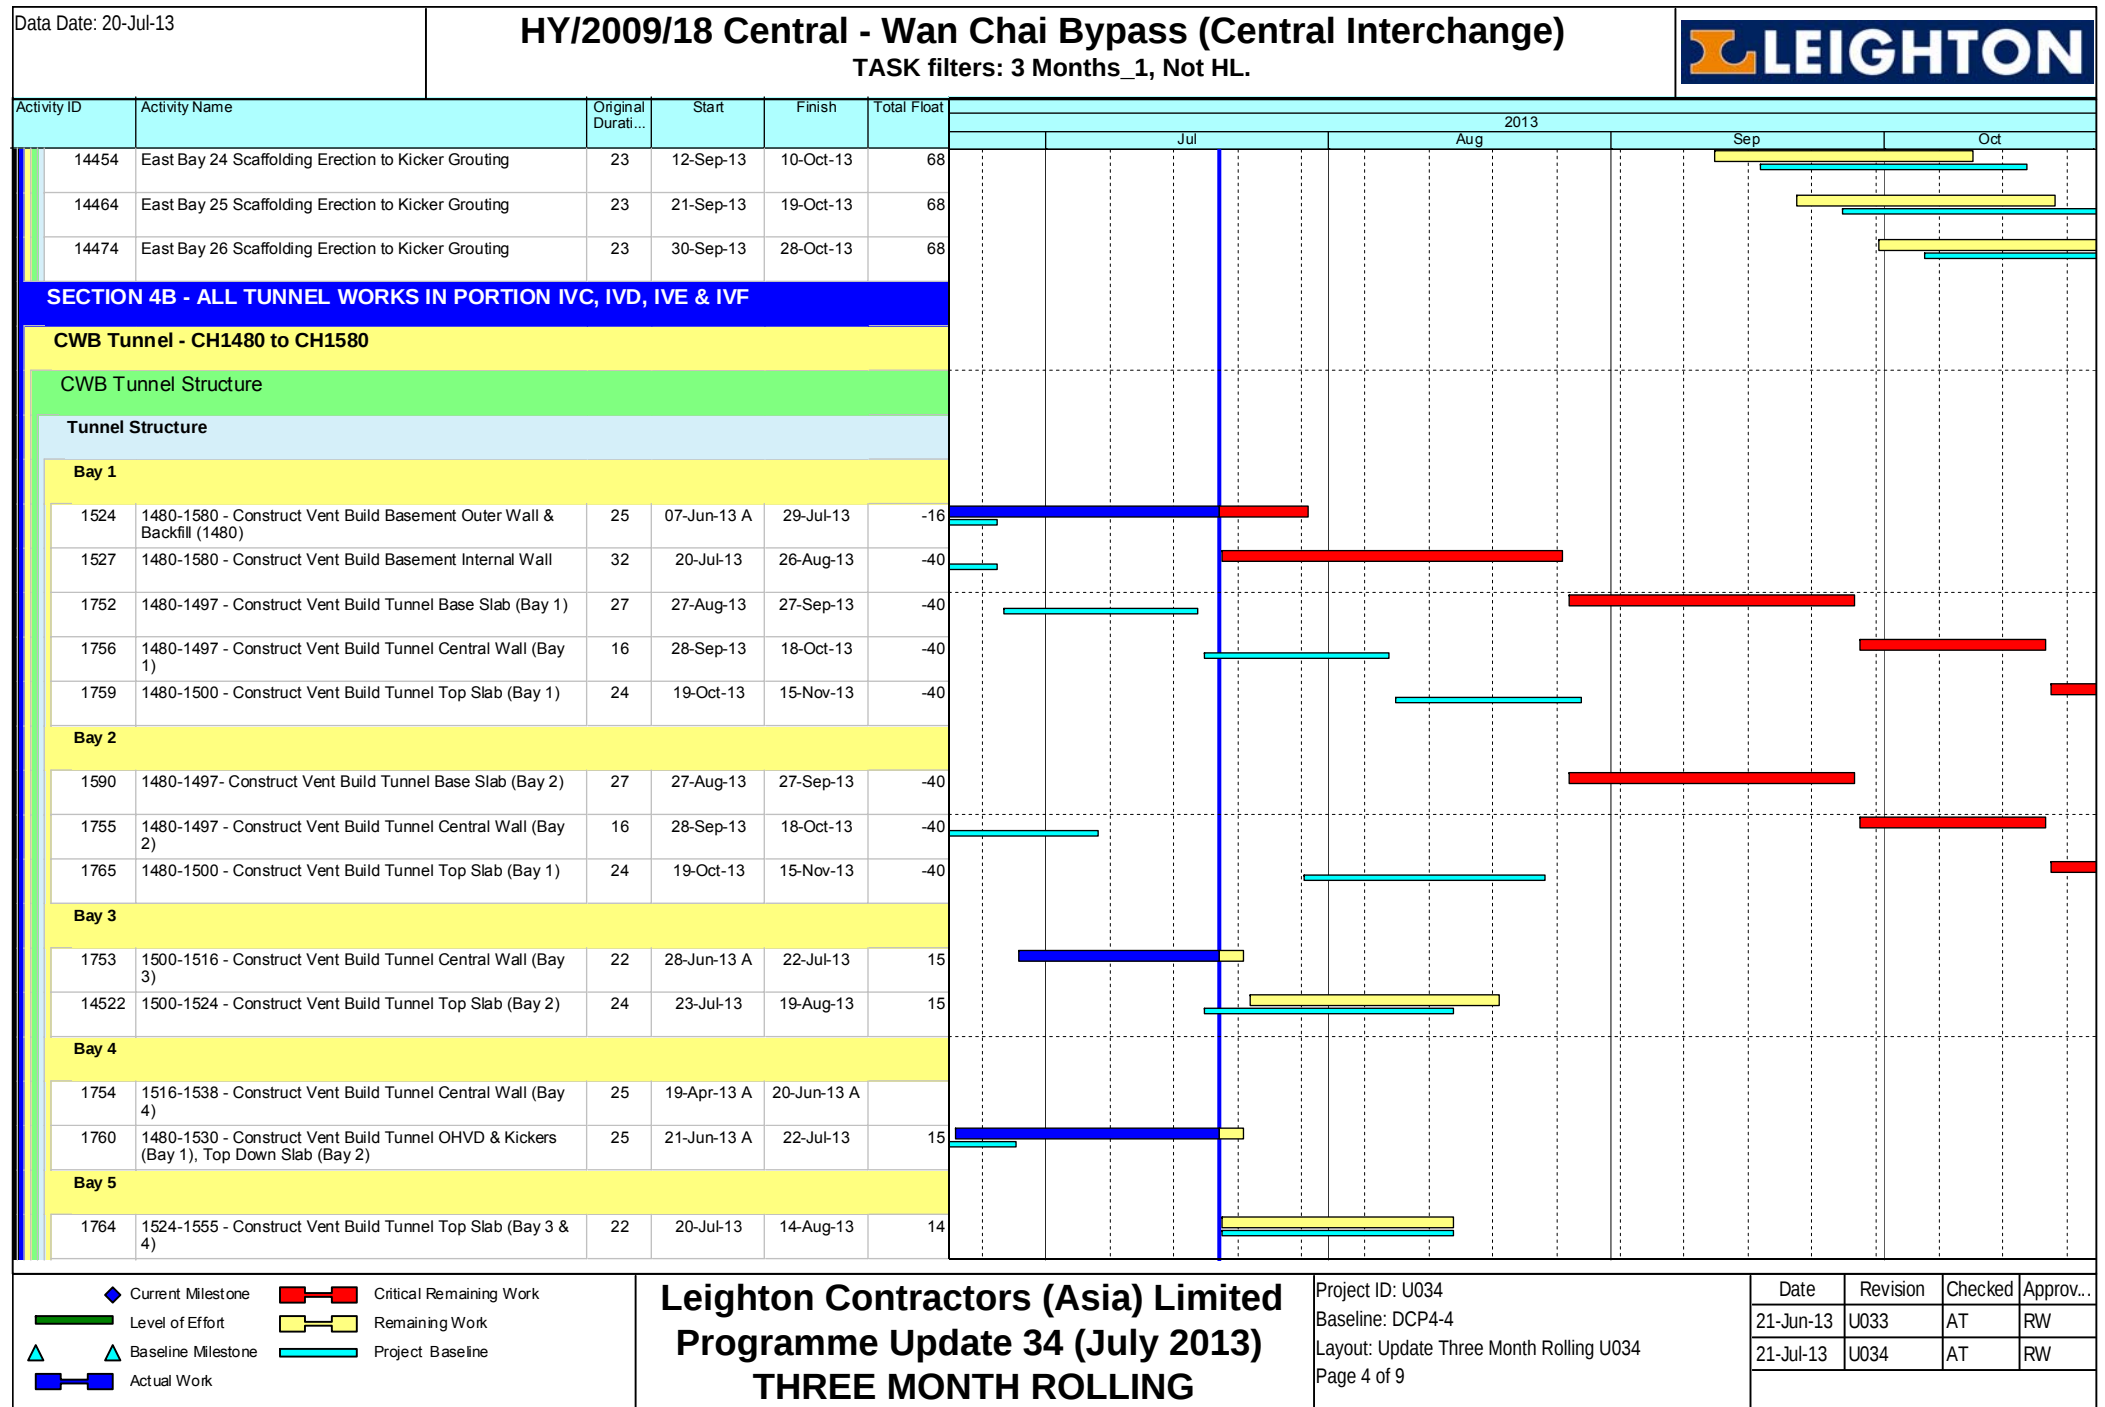

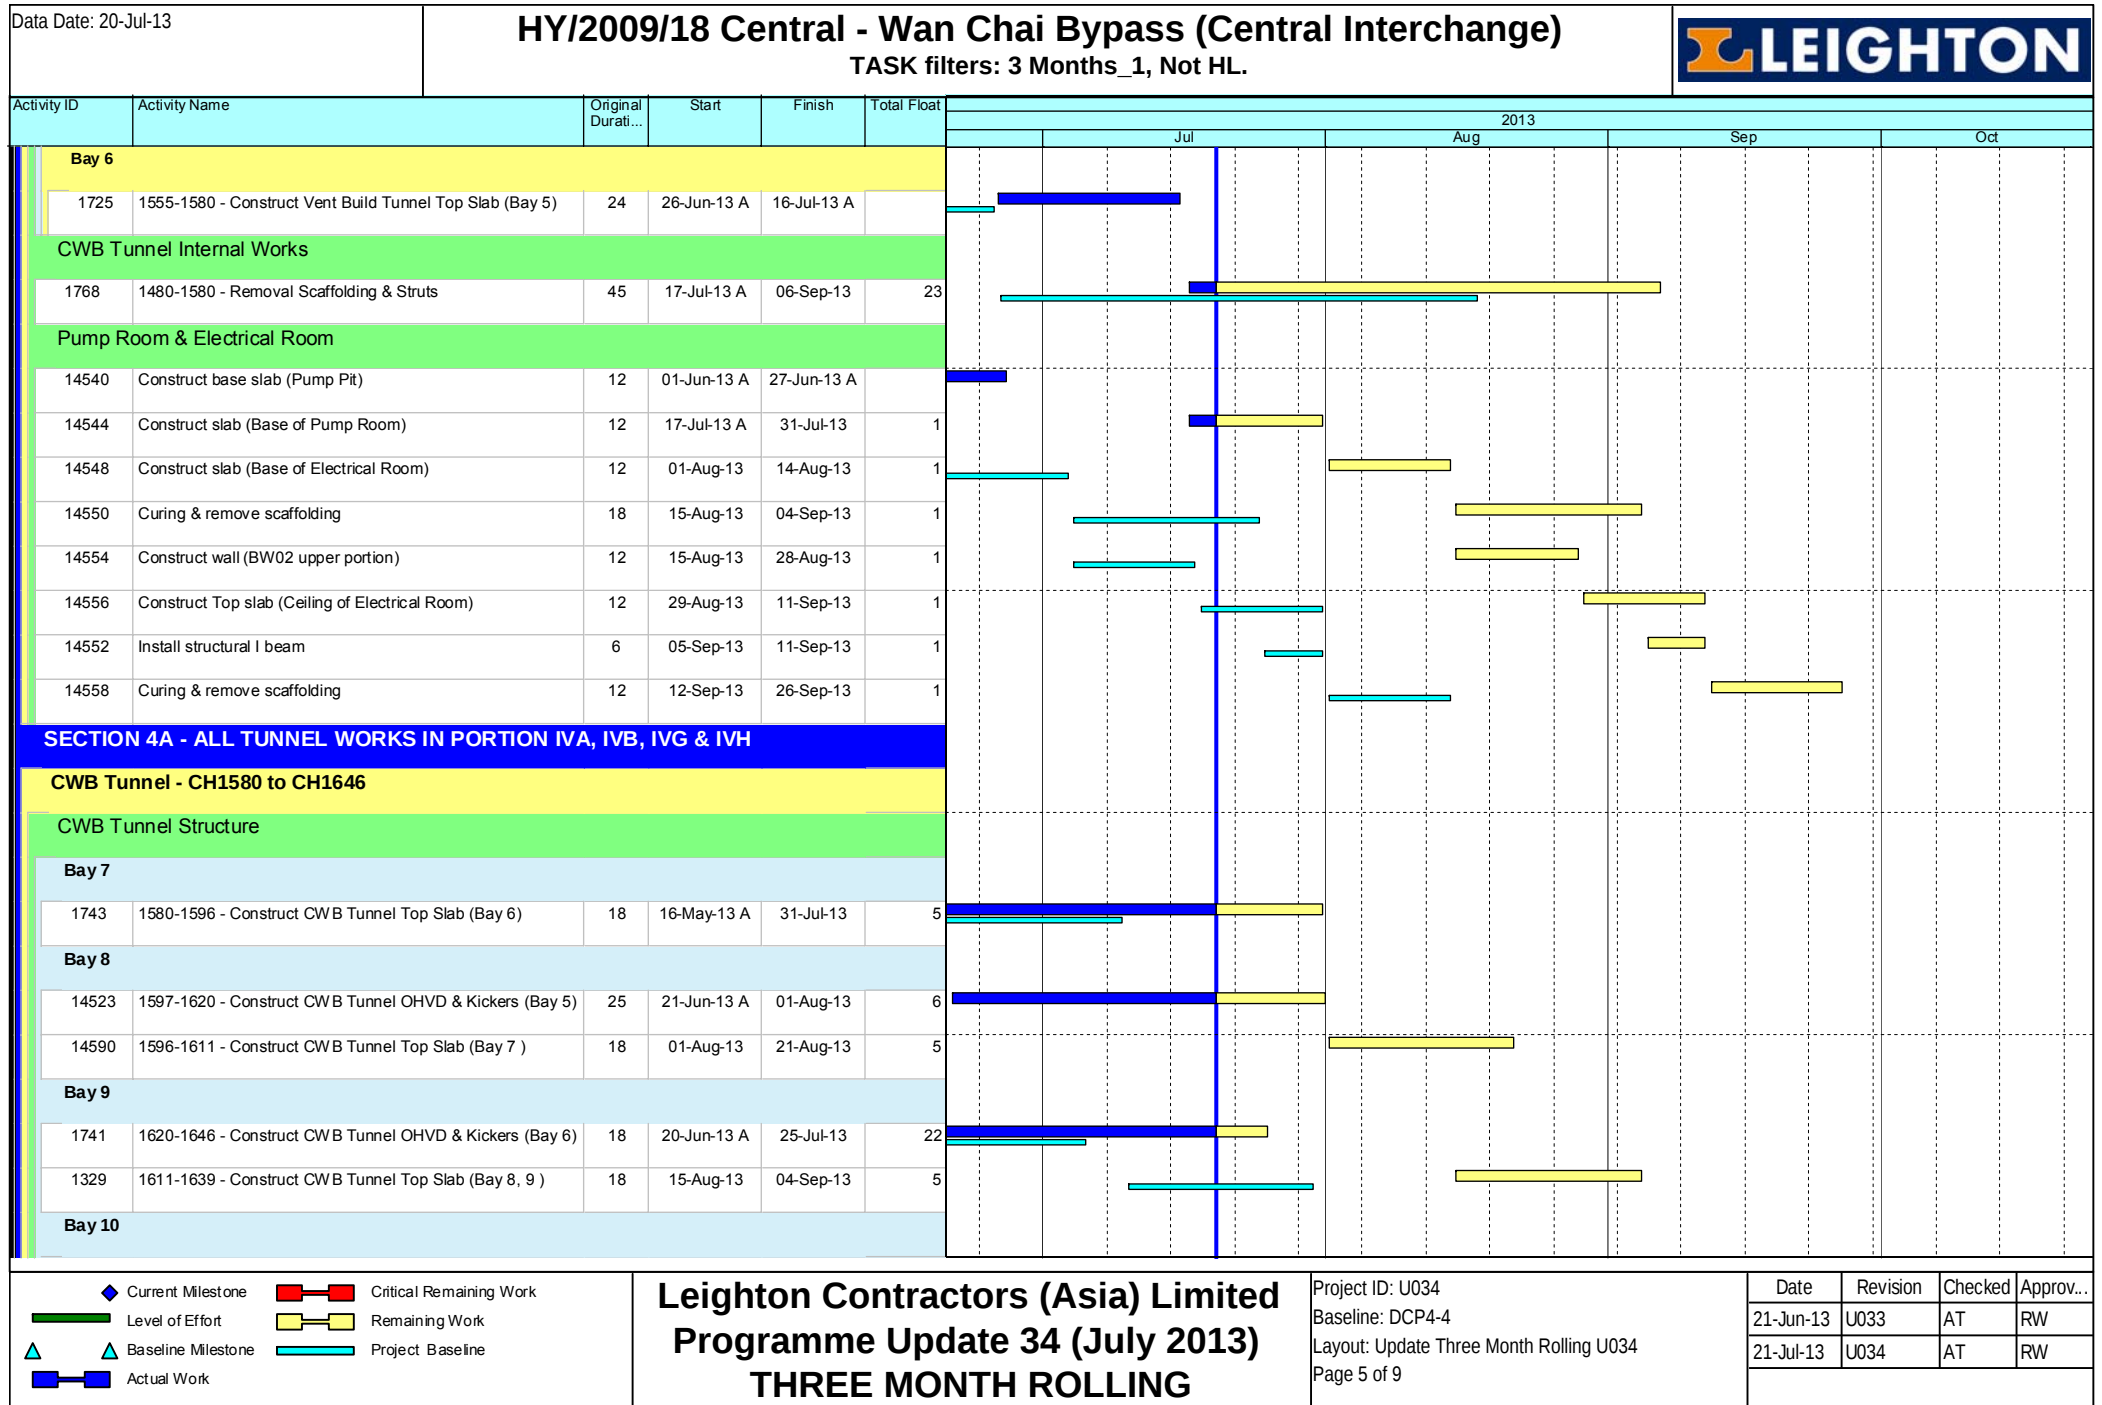

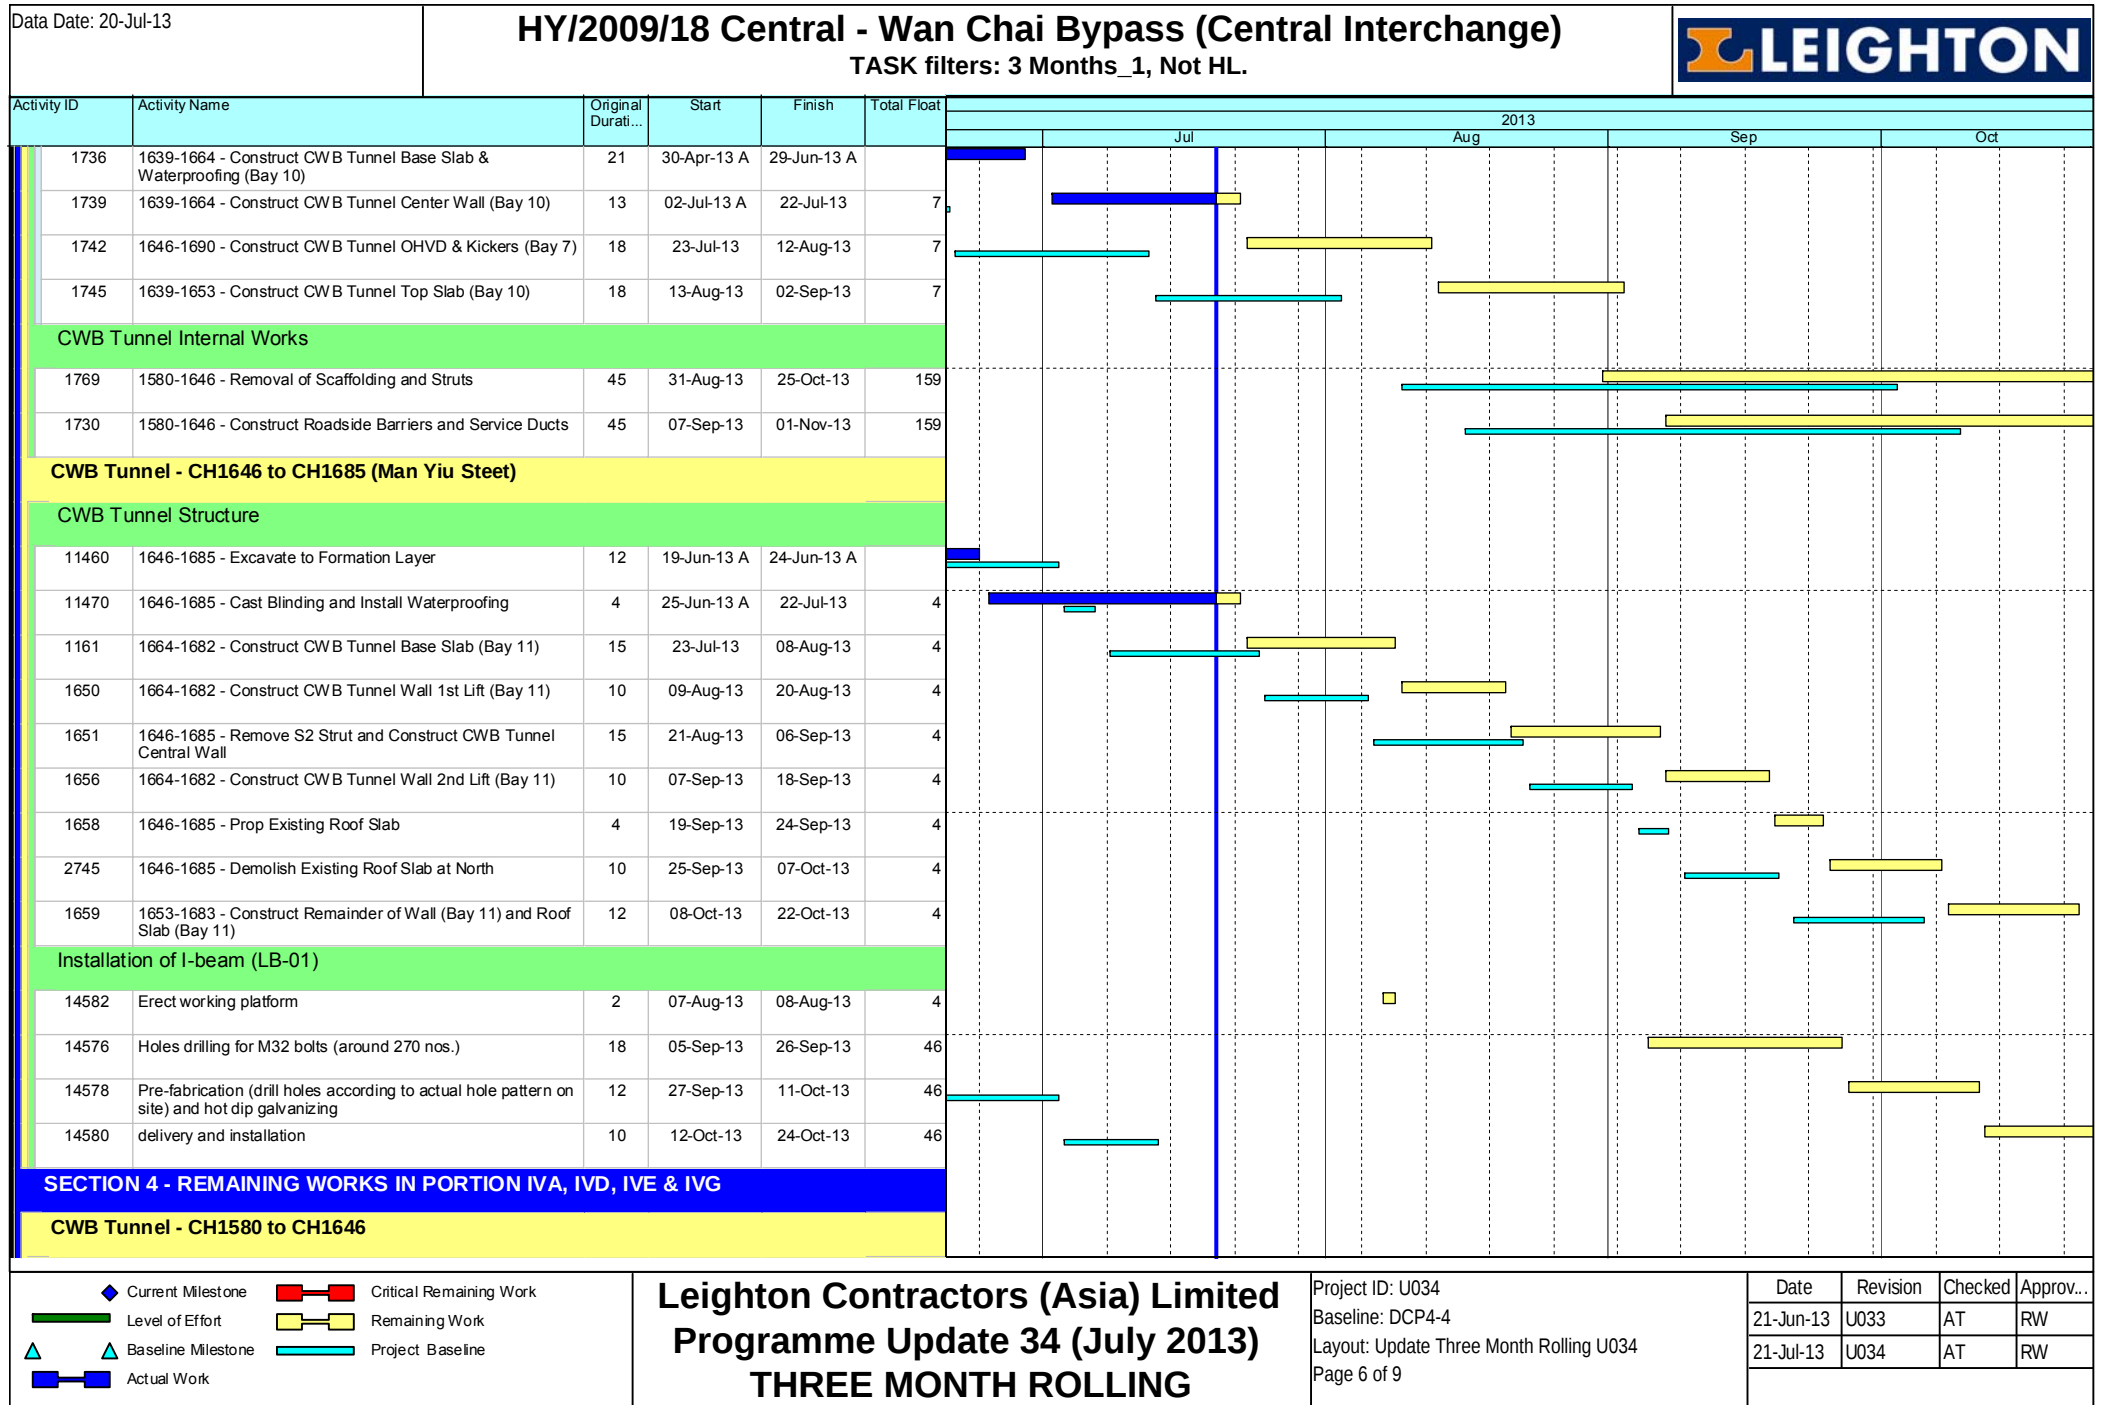

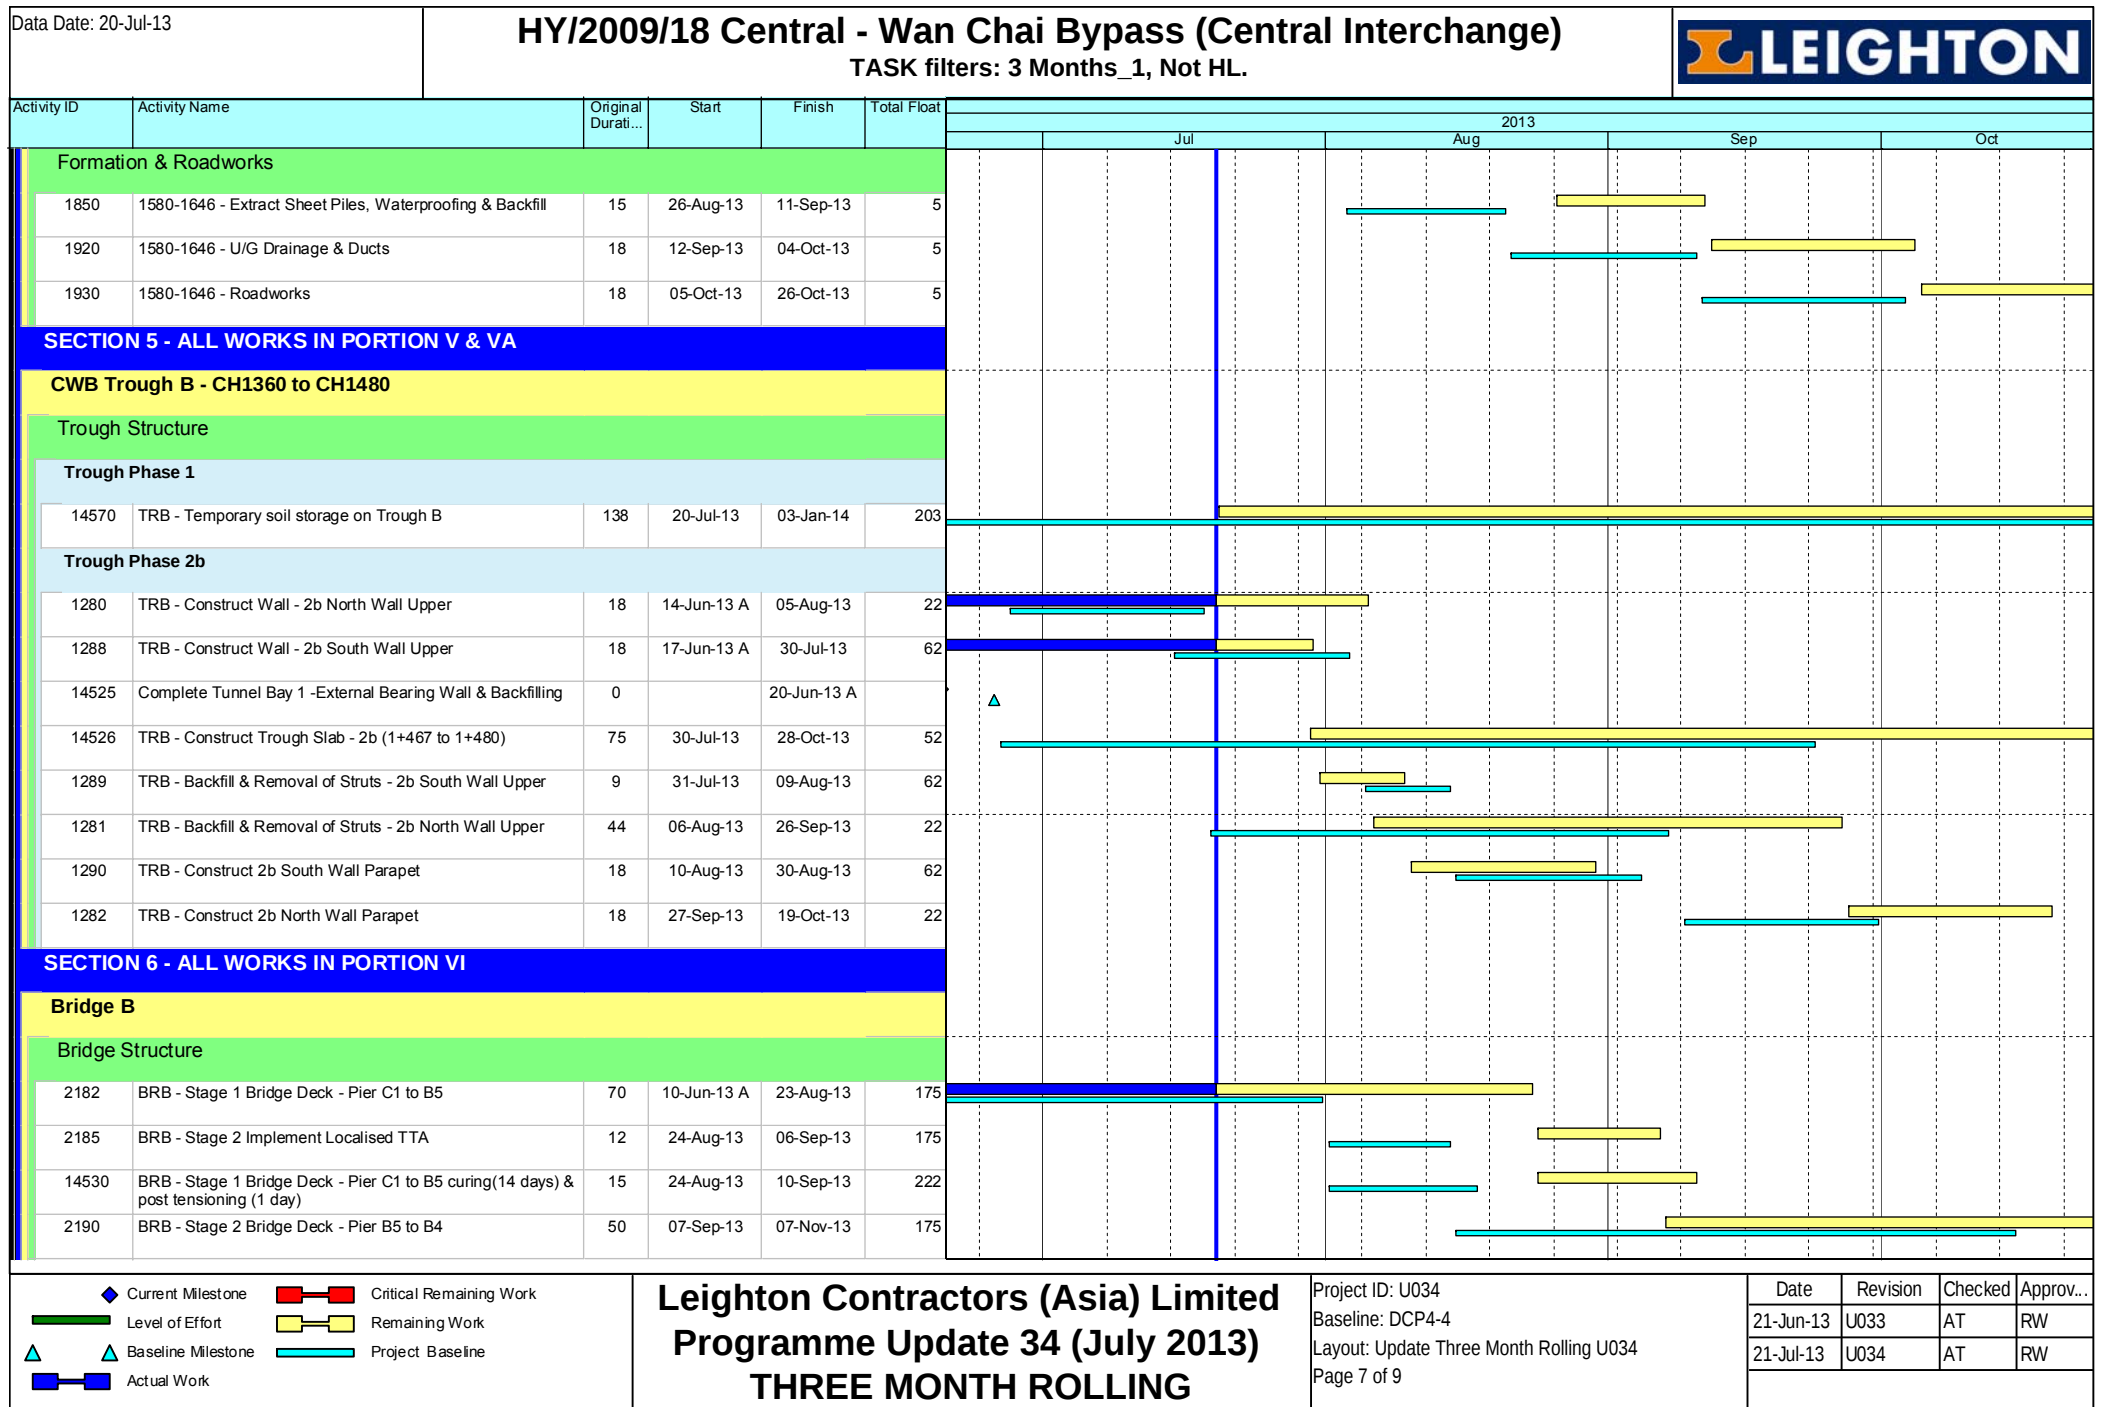

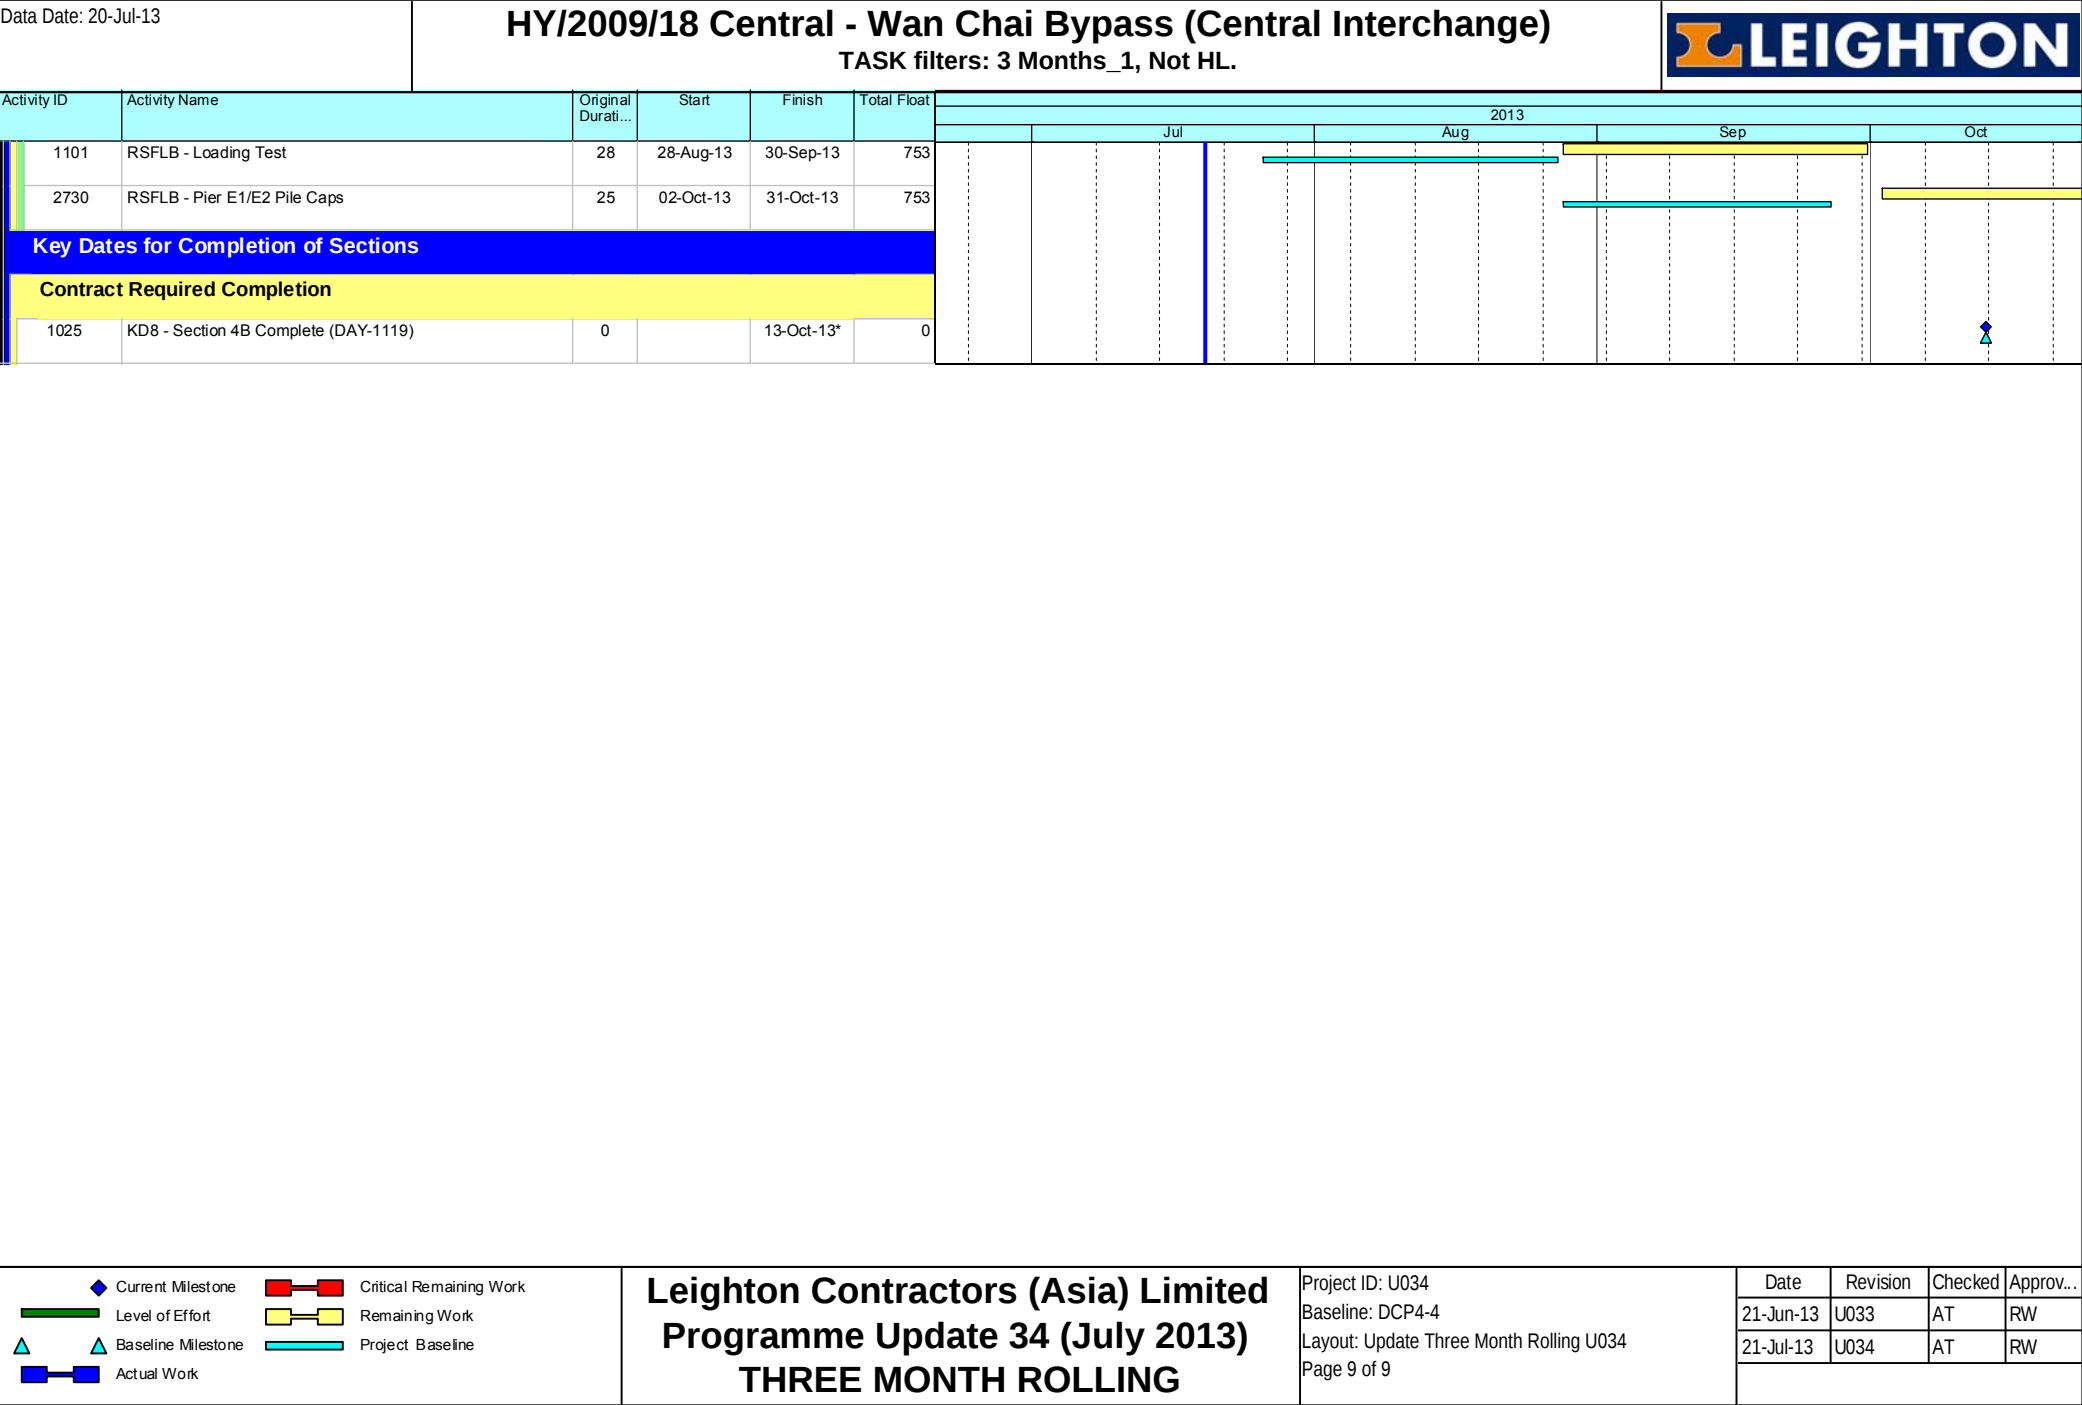


Activity ID		Activity Name	Rem Dur	Start	Finish	2013																	
						July					August					September				October			
						24	01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14	
3MRP - Jul 2013 to Oct 2013																							
02 - PRE-CONSTRUCTION WORKS																							
02.2 - Contractor's Submission																							
0220-1360	Tunnel Structures Materials - Submission	0	19-Jul-12 A	25-Jun-13 A	Tunnel Structures Materials - Submission																		
0220-1370	Tunnel Structures Materials - ER Review/Comment	0	14-Jan-13 A	25-Jun-13 A	Tunnel Structures Materials - ER Review/Comment																		
0220-1380	Tunnel Structures Materials - Resubmission	0	28-Jan-13 A	01-Jul-13 A	Tunnel Structures Materials - Resubmission																		
0220-1390	Tunnel Structures Materials - ER Approval	6	15-Mar-13 A	25-Jul-13	Tunnel Structures Materials - ER Approval																		
0220-1400	Tunnel Structures Materials - Procurement & Delivery	18	08-Jul-13 A	12-Aug-13	Tunnel Structures Materials - Procurement & Delivery																		
02.3 - Method Statement / Shop Drawings																							
0230-1700	MS Temporary Bridge TA1 - Submission	0	15-May-13 A	25-Jun-13 A	MS Temporary Bridge TA1 - Submission																		
0230-1710	MS Temporary Bridge TA1 - ER Review & Comment	0	26-Jun-13 A	07-Jul-13 A	MS Temporary Bridge TA1 - ER Review & Comment																		
0230-1720	MS Temporary Bridge TA1 - Resubmission	6	08-Jul-13 A	25-Jul-13	MS Temporary Bridge TA1 - Resubmission																		
0230-1730	MS Temporary Bridge TA1 - ER No Adverse Comment	18	26-Jul-13	12-Aug-13	MS Temporary Bridge TA1 - ER No Adverse Comment																		
0230-1920	MS Marine Temp Pile Removal - Resubmission	6	01-Aug-13	06-Aug-13	MS Marine Temp Pile Removal - Resubmission																		
0230-1930	MS Marine Temp Pile Removal - ER Approval	6	07-Aug-13	12-Aug-13	MS Marine Temp Pile Removal - ER Approval																		
02.4 - Contractor's Design and Build Items																							
0240-1030	Temp Bridge "TA1" Design - Resubmission	0	19-Mar-13 A	25-Jun-13 A	Temp Bridge "TA1" Design - Resubmission																		
0240-1035	Temp Bridge "TA1" Design - ER Approval	12	26-Jun-13 A	31-Jul-13	Temp Bridge "TA1" Design - ER Approval																		
0240-1040	Temp Bridge "TA1" - Fabrication	15	26-Jun-13 A	03-Aug-13	Temp Bridge "TA1" - Fabrication																		
0240-1041	Temp Bridge "TD" Design - Submission	12	01-Mar-13 A	31-Jul-13	Temp Bridge "TD" Design - Submission																		
0240-1042	Temp Bridge "TD" Design - ER review and comment	28	01-Aug-13	28-Aug-13	Temp Bridge "TD" Design - ER review and comment																		
0240-1043	Temp Bridge "TD" Design - Resubmission	36	29-Aug-13	03-Oct-13	Temp Bridge "TD" Design - Resubmission																		
0240-1044	Temp Bridge "TD" Design - ER Approval	28	04-Oct-13	31-Oct-13	Temp Bridge "TD" Design - ER Approval																		
0240-1105	Int. Noise Enclosure Structural Design - Submission	9	20-Mar-13 A	28-Jul-13	Int. Noise Enclosure Structural Design - Submission																		
0240-1110	Int. Noise Enclosure Structural Design - ER Review/Resubmission	48	29-Jul-13	14-Sep-13	Int. Noise Enclosure Structural Design - ER Review/Resubmission																		
0240-1112	Int. Noise Enclosure Structural Design - ER Approval	28	15-Sep-13	12-Oct-13	Int. Noise Enclosure Structural Design - ER Approval																		
0240-1127	Noise Barrier Design Structural Design - ER Review/Resubmission	24	30-May-13 A	12-Aug-13	Noise Barrier Design Structural Design - ER Review/Resubmission																		
0240-1128	Noise Barrier Design Structural Design - ER Approval	28	13-Aug-13	09-Sep-13	Noise Barrier Design Structural Design - ER Approval																		
0240-1129	Noise Barrier Design - Procurement/Fabrication/Delivery	180	10-Sep-13	08-Mar-14	Noise Barrier Design - Procurement/Fabrication/Delivery																		
0240-1150	Perm. Noise Enclosure Structural Design - Submission	9	20-Mar-13 A	28-Jul-13	Perm. Noise Enclosure Structural Design - Submission																		
0240-1160	Perm. Noise Enclosure Structural Design - ER Review/Resubmission	48	29-Jul-13	14-Sep-13	Perm. Noise Enclosure Structural Design - ER Review/Resubmission																		
0240-1161	Perm. Noise Enclosure Structural Design - ER Approval	28	15-Sep-13	12-Oct-13	Perm. Noise Enclosure Structural Design - ER Approval																		
02.5 - Bridge Segment/Beam Off-site Precasting																							
0250-1700.08	Bridge Precast Beam Casting Bridge F4 Beam 4-1	0	17-Jun-13 A	01-Jul-13 A	Bridge Precast Beam Casting Bridge F4 Beam 4-1																		
0250-1700.09	Bridge Precast Beam Casting Bridge F4 Beam 5-1	6	02-Jul-13 A	25-Jul-13	Bridge Precast Beam Casting Bridge F4 Beam 5-1																		
0250-1700.10	Bridge Precast Beam Casting Bridge F4 Beam 6-1	9	08-Jul-13 A	03-Aug-13	Bridge Precast Beam Casting Bridge F4 Beam 6-1																		
0250-1700.11	Bridge Precast Beam Casting Bridge E Beam E1D1-A	9	02-Jul-13 A	28-Jul-13	Bridge Precast Beam Casting Bridge E Beam E1D1-A																		
0250-1700.21	Bridge Precast Beam Casting Bridge E Beam E1D-B	14	29-Jul-13	11-Aug-13	Bridge Precast Beam Casting Bridge E Beam E1D-B																		
0250-1700.31	Bridge Precast Beam Casting Bridge E Beam E1D-C	14	05-Aug-13	18-Aug-13	Bridge Precast Beam Casting Bridge E Beam E1D-C																		
0250-1700.41	Bridge Precast Beam Casting Bridge E Beam E2E1-A	14	12-Aug-13	25-Aug-13	Bridge Precast Beam Casting Bridge E Beam E2E1-A																		
0250-1700.51	Bridge Precast Beam Casting Bridge E Beam E2E1-B	14	19-Aug-13	01-Sep-13	Bridge Precast Beam Casting Bridge E Beam E2E1-B																		
0250-1700.61	Bridge Precast Beam Casting Bridge E Beam E2E1-C	14	26-Aug-13	08-Sep-13	Bridge Precast Beam Casting Bridge E Beam E2E1-C																		
0250-1600.11	Bridge F2 Pier F04 Precasting Segment (1-13) - Mould S1	0	27-May-13 A	06-Jul-13 A	Bridge F2 Pier F04 Precasting Segment (1-13) - Mould S1																		
0250-1600.12	Bridge D2 Pier D07 Precasting Segment (1-17) - Mould S1	34	07-Jul-13 A	22-Aug-13	Bridge D2 Pier D07 Precasting Segment (1-17) - Mould S1																		
Remaining Level of Effort Actual Level of Effort Actual Work Remaining Work Critical Remaining Work Milestone Contract HY/2009/19 Three Month Rolling Programme (20 Jul 2013 to 19 Oct 2013) 3MRP 3MRP - Jul 2013 to Oct 2013 Page 1 of 7																							

Activity ID	Activity Name	Rem Dur	Start	Finish	2013																
					July					August				September				October			
					24	01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14
0250-1600.13	Bridge D2 Pier D06 Precasting Segment (1-17) - Mould S1	42	22-Aug-13	03-Oct-13																	Bridge D2 Pier D06 T
0250-1600.14	Bridge D2 Pier D05 Precasting Segment (1-17) - Mould S1	42	03-Oct-13	14-Nov-13																	
0250-1650.04	Bridge F1 Pier F03 Precasting Segment (1-6) - Mould S2	18	10-Jun-13 A	06-Aug-13																	
0250-1650.05	Bridge F2 Pier F03 Precasting Segment (1-5) - Mould S2	17	04-Jul-13 A	23-Aug-13																	
0250-1650.16	Bridge F2 Pier F05 Precasting Segment (1-6) - Mould S2	21	23-Aug-13	13-Sep-13																	
0250-1650.17	Bridge D2 Pier D08 Precasting Segment (1-8) - Mould S1	24	13-Sep-13	07-Oct-13																	Bridge D2 Pier
0250-1650.18	Bridge D2 Pier D04 Precasting Segment (1-8) - Mould S2	24	07-Oct-13	31-Oct-13																	
0250-1655.04	Bridge F3 - F06 Segment - Remaining (10 nos) - Mould T	5	21-Jun-13 A	24-Jul-13																	
0250-1655.014	Bridge F3 - F07 Segment - Pier Segment +2 (3 nos) - Mould T	10	25-Jul-13	03-Aug-13																	
0250-1655.024	Bridge F3 - F07 Segment - Remaining (10 nos) - Mould T	30	04-Aug-13	02-Sep-13																	
0250-1655.02	Bridge F3 - F05 Segment - Remaining (4 nos) - Mould T	12	03-Sep-13	14-Sep-13																	
0250-1655.01	Bridge F3 - F05 Segment - Pier Segment +1 (2 nos) - Mould T	9	15-Sep-13	23-Sep-13																	Bridge F3 - F05 Segment - Pier Se
0250-1830	Segment Storage - Portal Gantry Foundation + Rail Stage 3	12	16-Sep-13*	30-Sep-13																	Segment Storage - Porta
03 - PRELIMINARY WORKS																					
03.3 - Interface Works																					
0330-1110	Submit/Agree FEHD/ER Relocation Sequence & Programme	6	19-Mar-13 A	26-Jul-13																	
0330-1200	Agreement of HGHK Interim Temp Carpark	34	20-Jun-13 A	28-Aug-13																	
0330-1300	Erect Interim Temp Carpark for HGHK	18	13-Sep-13	07-Oct-13																	Erect Interim T
05 - SECTION 2 & 2A OF THE WORKS																					
05.1 - Cut & Cover Tunnel Ch 4855-4932 (APS Footprint)																					
05.1.1 - D-Wall Construction																					
0511-1088	Dinsmantle Bentonite Plant - EVB Area	12	13-May-13 A	02-Aug-13																	
0511-1090	Install Dewatering Well - EVB Area (18 nos.)	24	27-Jun-13 A	16-Aug-13																	
0511-1092	Install Recharging Well - EVB Area (6 nos.)	24	03-Jul-13 A	16-Aug-13																	
0511-1091	Install Observation Well - EVB Area (14 nos.)	28	30-Jul-13	30-Aug-13																	
0511-1095	Install King Post - EVB Area (20 nos.)	36	17-Aug-13	28-Sep-13																	
0511-1100	Pump Test Ch 4855-4932	15	31-Aug-13	17-Sep-13																	
05.1.2 - ELS																					
0512-1101	Advance Excav EVB Area 1st Layer + Support	15	30-Sep-13	18-Oct-13																	
05.2 - Cut & Cover Tunnel Ch 4932-5149																					
05.2.1 - D-Wall Construction																					
0521-1879	Remove Existing Box Culvert at D-wall Area + Backfill	5	02-Jul-13 A	25-Jul-13																	
0521-1880	D-wall N71-N73 Grouting for Existing Seawall Rubble Mound	12	26-Jul-13	08-Aug-13																	
0521-2140	D-wall S78-S80 + BC53 Guide Wall	9	26-Jul-13	05-Aug-13																	
0521-1890	D-wall N71-N73 Guide Wall	12	02-Aug-13	15-Aug-13																	
0521-2145.10	D-wall Panel S78	12	06-Aug-13	19-Aug-13																	
0521-1900.10	D-wall Panel N73	14	16-Aug-13	31-Aug-13																	
0521-2145.15	D-wall Panel S79	12	20-Aug-13	02-Sep-13																	
0521-1900.20	D-wall Panel N72	14	02-Sep-13	17-Sep-13																	
0521-1900.15	D-wall Panel N71	14	18-Sep-13	05-Oct-13																	
0521-1900.30	D-wall Panel N74	14	18-Sep-13	05-Oct-13																	
0521-2165	Install Dewatering Well - Ch 4932-5149 (10 nos.)	18	26-Sep-13	18-Oct-13																	
0521-2166	Install Observation Well - Ch 4932-5149 (6 nos.)	18	26-Sep-13	18-Oct-13																	
0521-2167	Install Recharging Well - Ch 4932-5149 (2 nos.)	12	04-Oct-13	18-Oct-13																	

Activity ID	Activity Name	Rem Dur	Start	Finish	2013																	
					July					August					September					October		
					24	01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14	
0521-2168	Install King Posts - Ch 4932-5149 (4 nos.)	12	07-Oct-13	21-Oct-13																		
05.2.2 - Barrette Construction																						
0522-2210.89	Barrette Pile BC44	0	10-May-13 A	18-Jul-13 A																		
0522-2210.84	Barrette Pile BC42	12	19-Jul-13 A	02-Aug-13																		
0522-2210.86	Barrette Pile BC46	2	29-May-13 A	22-Jul-13																		
0522-2210.88	Barrette Pile BC43	12	25-Jul-13	07-Aug-13																		
0522-2390.10	Bulkhead BW4	0	17-Jun-13 A	10-Jul-13 A																		
0522-2390.30	Bulkhead BW3	8	16-Jul-13 A	29-Jul-13																		
0522-2211	Complete Dismatling of Bentonite Plants at EVB Area	12	08-Aug-13	21-Aug-13																		
0522-2212	Relocate D-wall Rebar Cage Fabrication Yard	12	22-Aug-13	04-Sep-13																		
0522-2210.53	Barrette Pile BC53	12	03-Sep-13	16-Sep-13																		
05.2.3 - ELS																						
0524-2884.1	Tunnel Phase 1 Zone 4 - Excav	0	23-May-13 A	22-Jun-13 A																		
0524-2884.2	Tunnel Phase 1 Zone 4 - LS + Preload	2	24-Jun-13 A	22-Jul-13																		
0524-2885.1	Tunnel Phase 1 Zone 5 - Excav	2	01-Jun-13 A	22-Jul-13																		
0524-2885.2	Tunnel Phase 1 Zone 5 - LS + Preload	14	19-Jul-13 A	05-Aug-13																		
0524-2886	Tunnel Phase 1 Zone 6 - Excav	10	23-Jul-13	02-Aug-13																		
0524-2887	Tunnel Phase 1 Zone 7 - Excav	8	06-Aug-13	14-Aug-13																		
0524-2888	Tunnel Phase 2 Zone 2 - Excav	7	08-Apr-13 A	27-Jul-13																		
0524-2889	Tunnel Phase 2 Zone 2 - LS + Preload	7	15-Apr-13 A	05-Aug-13																		
0524-2905	Tunnel Phase 2 Zone 3 - Excav	12	29-Jul-13	10-Aug-13																		
0524-2915	Tunnel Phase 2 Zone 3 - LS + Preload	10	06-Aug-13	16-Aug-13																		
0524-2925	Tunnel Phase 2 Zone 4 - Excav	7	17-Aug-13	24-Aug-13																		
0524-2935	Tunnel Phase 2 Zone 4 - LS + Preload	7	26-Aug-13	02-Sep-13																		
0524-2945	Tunnel Phase 2 Zone 5 - Excav	15	26-Aug-13	11-Sep-13																		
0524-2955	Tunnel Phase 2 Zone 5 - LS + Preload	12	05-Sep-13	18-Sep-13																		
0524-2965	Tunnel Phase 2 Zone 6 - Excav	6	12-Sep-13	18-Sep-13																		
0524-2975	Tunnel Phase 2 Zone 6 - LS + Preload	8	19-Sep-13	28-Sep-13																		
0524-2980	Tunnel Phase 2 Zone 7 - Excav	8	19-Sep-13	28-Sep-13																		
0524-2985	Tunnel Phase 2 Zone 8 - Excav	12	30-Sep-13	15-Oct-13																		
05.2.4 - Tunnel Structure																						
0524-2541	Tunnel Phase 1 Zone 6 Blinding Layer	3	03-Aug-13	06-Aug-13																		
0524-2551	Tunnel Waterproofing Base Slab Bay 1	6	07-Aug-13	13-Aug-13																		
0524-2570	Bay 1 Tunnel Base Slab	9	14-Aug-13	23-Aug-13																		
0524-3015	Bay 1 Tunnel Vertical Wall	7	24-Aug-13	31-Aug-13																		
0524-3025	Bay 1 Tunnel False Works	6	02-Sep-13	07-Sep-13																		
0524-3035	Bay 1 Tunnel OHVD Slab	8	09-Sep-13	17-Sep-13																		
0524-3045	Bay 1 Tunnel Roof Slab	12	18-Sep-13	03-Oct-13																		
0524-2542	Tunnel Phase 1 Zone 7 Blinding Layer	3	15-Aug-13	17-Aug-13																		
0524-2552	Tunnel Waterproofing Base Slab Bay 2 and 3	6	19-Aug-13	24-Aug-13																		
0524-3055	Bay 3 Tunnel Base Slab	7	26-Aug-13	02-Sep-13																		
0524-3065	Bay 3 Tunnel Vertical Wall	7	03-Sep-13	10-Sep-13																		
0524-3075	Bay 3 Tunnel False Works	6	11-Sep-13	17-Sep-13																		
0524-3085	Bay 3 Tunnel OHVD Slab	8	18-Sep-13	27-Sep-13																		

Activity ID	Activity Name	Rem Dur	Start	Finish	2013																
					July				August				September				October				
					24	01	08	15	22	29	05	12	19	26	02	09	16	23	30	07	14
0524-3095	Bay 3 Tunnel Roof Slab	12	28-Sep-13	12-Oct-13																	Bay 3 T
0524-2553	Tunnel Waterproofing Base Slab Bay 4, 5 and 6	9	26-Aug-13	04-Sep-13																	
0524-3155	Bay 6 Tunnel Base Slab	7	05-Sep-13	12-Sep-13																	
0524-3165	Bay 6 Tunnel Vertical Wall	7	13-Sep-13	21-Sep-13																	
0524-3175	Bay 6 Tunnel False Works	6	23-Sep-13	28-Sep-13																	
0524-3185	Bay 6 Tunnel OHVD Slab	8	30-Sep-13	09-Oct-13																	
0524-3195	Bay 6 Tunnel Roof Slab	12	10-Oct-13	24-Oct-13																	
0524-3105	Bay 2 Tunnel Base Slab	7	03-Sep-13	10-Sep-13																	
0524-3115	Bay 2 Tunnel Vertical Wall	7	11-Sep-13	18-Sep-13																	
0524-3125	Bay 2 Tunnel False Works	6	19-Sep-13	26-Sep-13																	
0524-3135	Bay 2 Tunnel OHVD Slab	8	27-Sep-13	07-Oct-13																	
0524-3145	Bay 2 Tunnel Roof Slab	12	08-Oct-13	22-Oct-13																	
0524-3205	Bay 4 Tunnel Base Slab	7	13-Sep-13	21-Sep-13																	
0524-3215	Bay 4 Tunnel Vertical Wall	7	23-Sep-13	30-Sep-13																	
0524-3225	Bay 4 Tunnel False Works	6	02-Oct-13	08-Oct-13																	
0524-3235	Bay 4 Tunnel OHVD Slab	8	09-Oct-13	18-Oct-13																	
0524-3255	Bay 4 Tunnel Base Slab	7	23-Sep-13	30-Sep-13																	
0524-3265	Bay 4 Tunnel Vertical Wall	7	02-Oct-13	09-Oct-13																	
0524-3275	Bay 4 Tunnel False Works	6	10-Oct-13	17-Oct-13																	
05.3 - Box Culvert T1																					
0530-3084	Bay 1 - Break Wall of Existing to Divert Flow	0	17-Jun-13 A	29-Jun-13 A																	
0530-3115	Bay 11 - Seawall (Temporary)	6	06-May-13 A	26-Jul-13																	
0530-3116	Bay 9-11 - Backfilling	9	27-Jul-13	06-Aug-13																	
0530-3398	Bay 7 - Wall + Roof (Portion 3)	0	15-Jun-13 A	24-Jun-13 A																	
0530-3099	Bay 8 - Wall + Roof	0	27-May-13 A	24-Jun-13 A																	
0530-3100	Divert and Abandon Existing Box Culvert T1	0	25-Jun-13 A	30-Jun-13 A																	
06 - SECTION 3 OF THE WORKS																					
06.1 - Westbound - Pier 29-34																					
0610-2110	Pier 29 Pre-drilling at Portion VB (4 nos)	24	15-Aug-13*	11-Sep-13																	
0610-2115	Pier 29 Approve Founding Level	18	12-Sep-13	04-Oct-13																	
0610-2120	Pier 29 Bored Piles (4 nos)	48	05-Oct-13	30-Nov-13																	
06.2 - Box Culvert U1																					
0620-2560	1500mm Drainage - Pile Laying + Manhole (Stage 1)	0	06-May-13 A	25-Jun-13 A																	
0620-2445	U1 Backfill Bay 5 + 1500mm Drainage + Extract Sheetpiles	6	25-Jun-13 A	26-Jul-13																	
0620-2380	Divert and Abandon old U1 open channel at VB & III	0	25-Jun-13 A	02-Jul-13 A																	
0620-2510	U1 Backfill Bays 11 + 12 + 13	0	20-Apr-13 A	22-Jun-13 A																	
06.3 - Admin Building																					
0630-3100	Predrill for Adm Building (55 no) (4 set)	54	12-Sep-13	16-Nov-13																	
10 - SECTION X OF THE WORKS																					
10.1 - E/B Bridges (Bridge D, E and F)																					
10.1.1 - Marine Pier Construction																					
Pier F03 to F15																					
1011-2170	F3 Crosshead Construction	4	01-Jun-13 A	24-Jul-13																	
1011-2175	Bearing intallation Pier F8	12	01-Aug-13	14-Aug-13																	

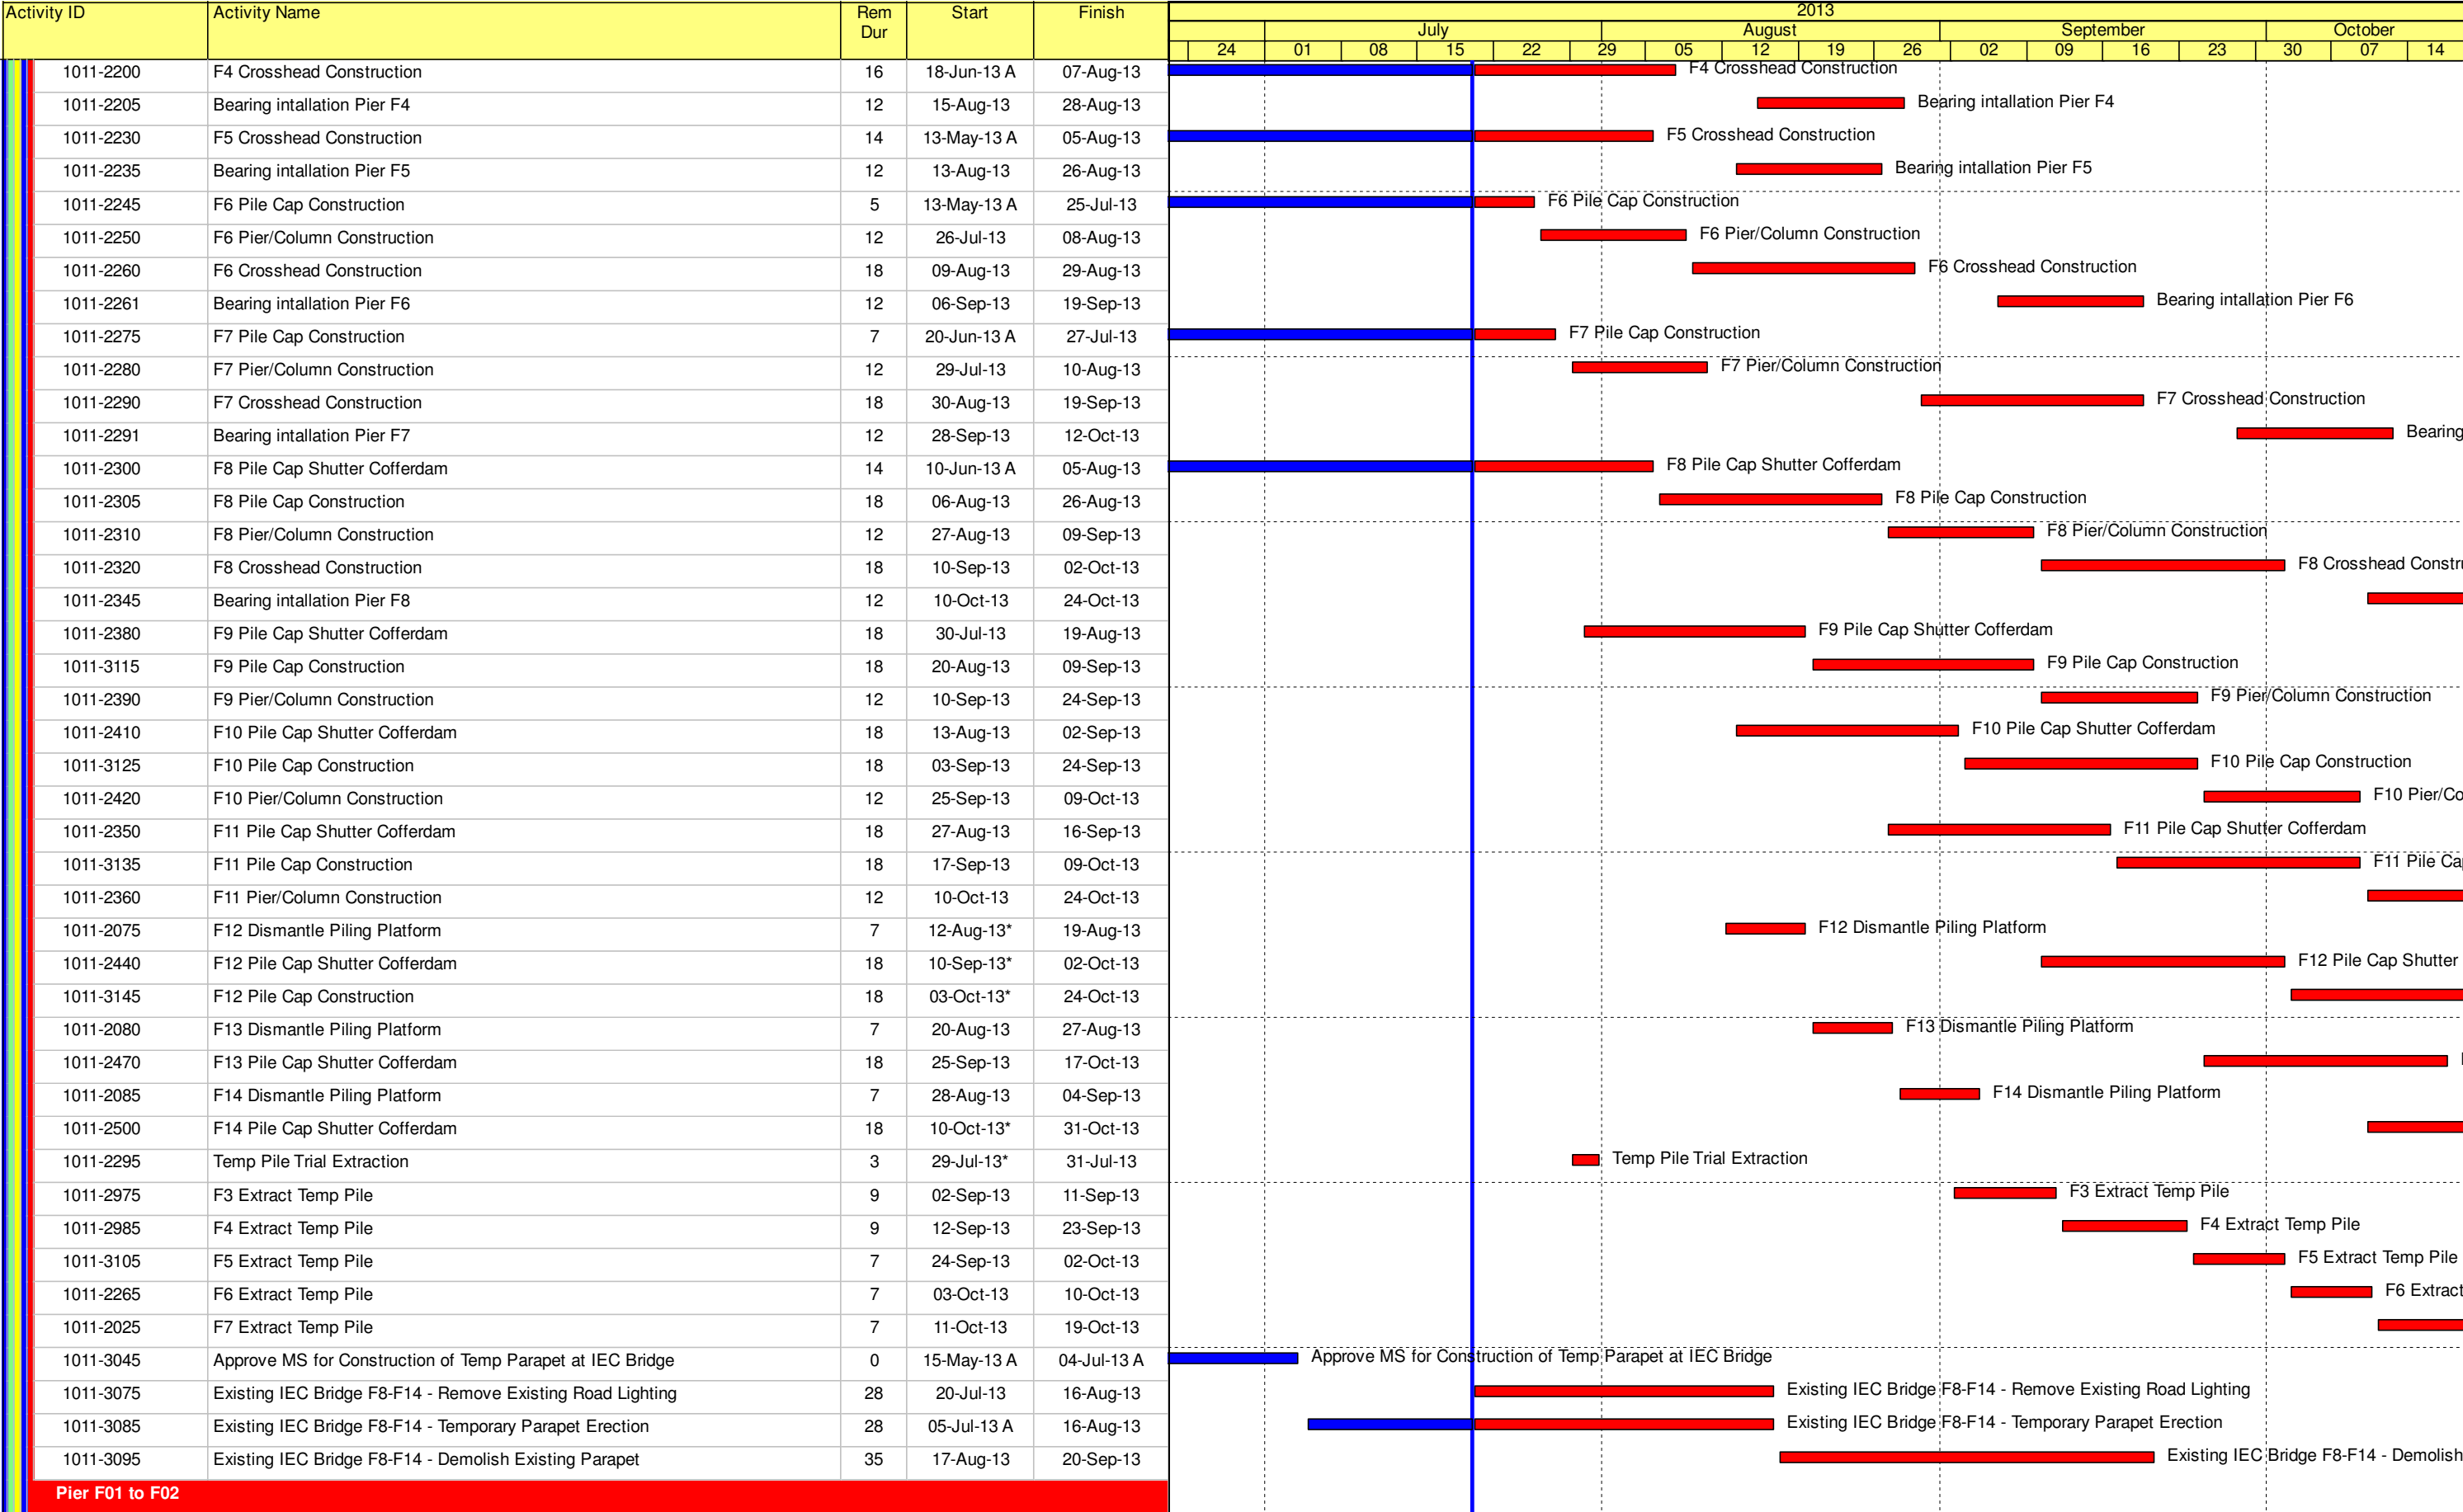

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone


Contract HY/2009/19

Three Month Rolling Programme (20 Jul 2013 to 19 Oct 2013)

3MRP

3MRP - Jul 2013 to Oct 2013

Page 5 of 7

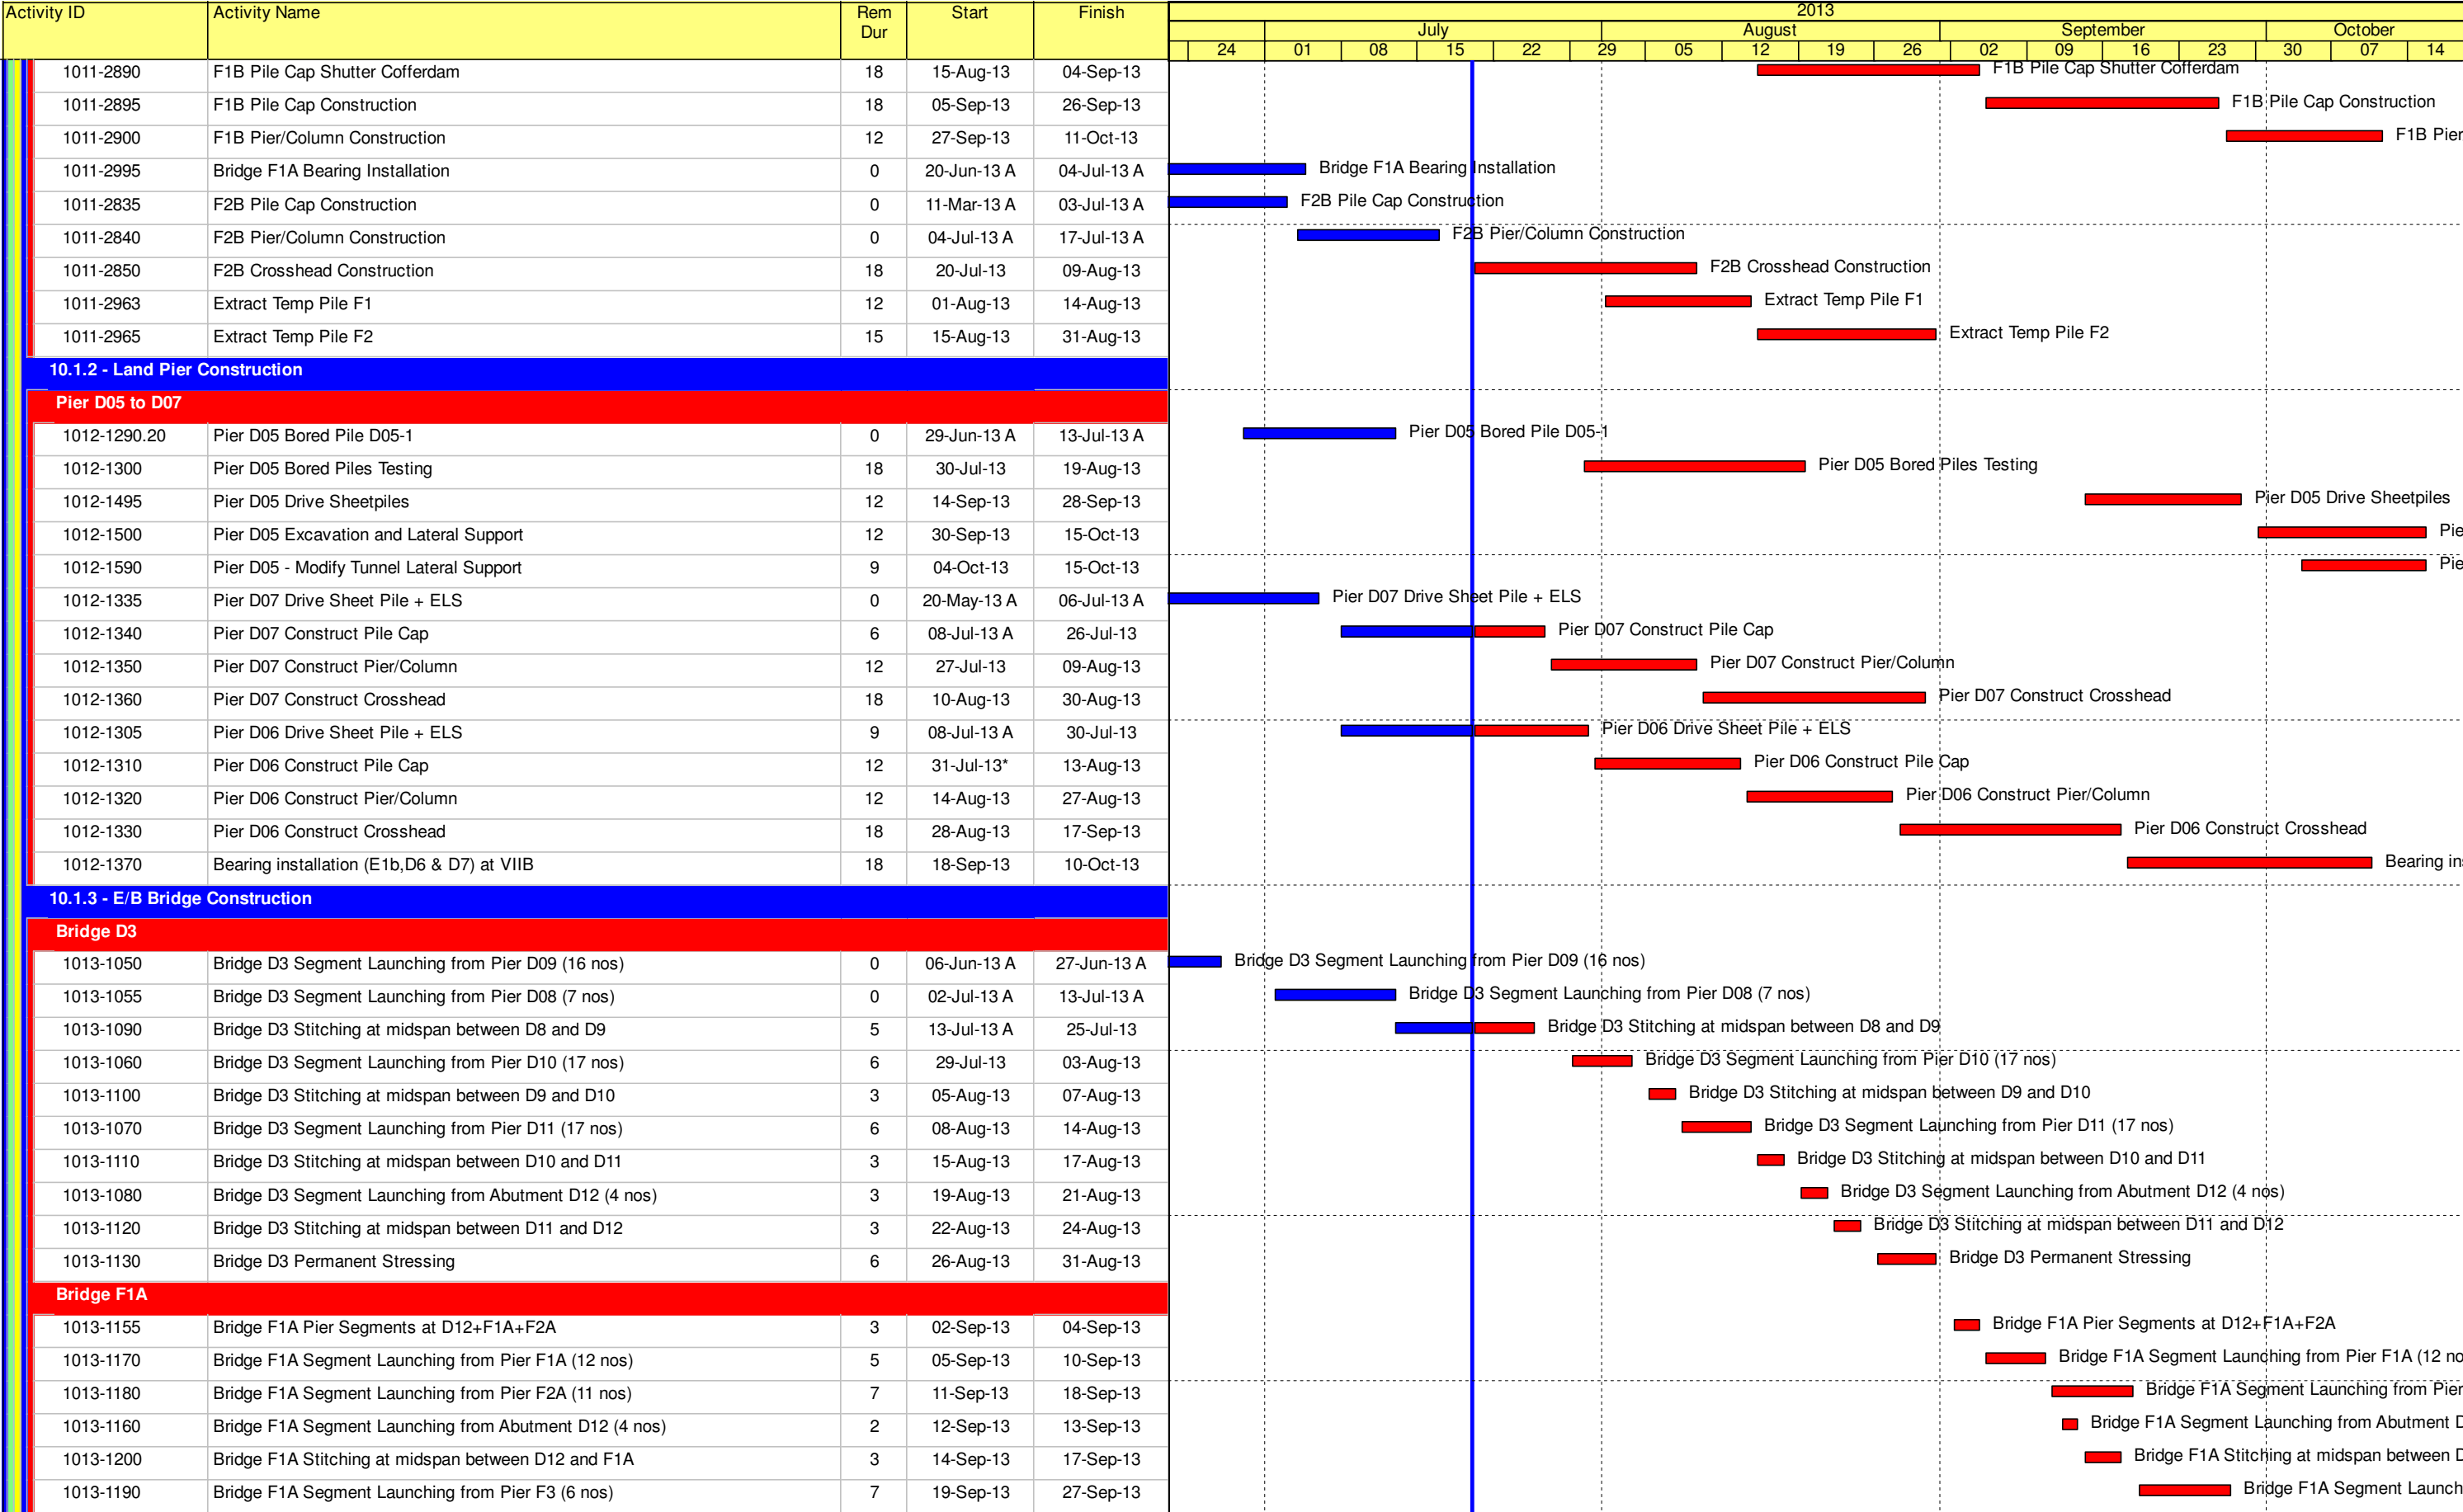

[illegible]

Data Date: 22-Jan-13

-   Current Milestone
-   Actual Work
-   Critical Remaining Work
-   Remaining Work
-   Remaining Level of Effort

3 Months Rolling Programme for Area Outside Zone CRIII

(Jul 2013 to Sep 2013)

Date	Revision	Checked	Approved
04-Jul-13	Rev 0		

[illegible]

[illegible]

SR8_MU03			SR8 - Layout for 3MRP			Appendix C.5								
Activity ID	Activity Name	Original Duration	Start	Finish										
					2013									
					Q3									
HY/2010/08: CWB-SR8 Programme Updated up to 20-June-2013														
Key Dates														
Site Possession Dates														
XVIII	Site Possession of Portion XVIII (180d)	0	17-Sep-13*		◆ Site Possession of Portion XVIII									
Stage / Section Completion of Works														
KD1	KD1 - Achievement of Stage 1 (120d)	0		25-Jul-13*	◆ KD1 - Achievement of Stage 1 (120d)									
Handover Dates														
HXVII	Handover of Portion XVII	0		22-Aug-13*	◆ Handover of Portion XVII									
Preliminaries (General Submissions, Permits, Procurement, Initial Work, Design)														
IW_SUM	Initial Works - Survey (Topo, Hydrographic, Condition), Site Set Up, Site Office etc.	96	21-Mar-13 A	05-Aug-13	Initial Works - Survey (Topo, Hydrographic, Condition), Site Set Up, Site Office etc.									
GS_SUM	General Submissions - Method Statement, Safety Plan, Environmental Plan, Insurances etc.	96	21-Mar-13 A	05-Aug-13	General Submissions - Method Statement, Safety Plan, Environmental Plan, Insurances etc.									
PER_SUM	Permits Application and Approval - MDN, EPD, DASO, Expressway Permit, Excav Permit etc.	96	21-Mar-13 A	12-Oct-13										
CD_SUM	Contractors Design - Appoint of Designer & ICE	48	15-May-13 A	21-Jun-13	Design - Appoint of Designer & ICE									
Works in SR8 (Four Pits Scheme)														
Initial Works														
SR8_1030	Geotechnical submission and approval	108	22-Mar-13 A	29-Jul-13	Geotechnical submission and approval									
SR8_1010	TTA Design	27	02-Apr-13 A	22-Jun-13										
SR8_1040	Expressway permits application + approval	81	18-Apr-13 A	10-Jul-13	Expressway permits application + approval									
SR8_1170	TTA approval & implement stage 1 TTA	54	24-Apr-13 A	12-Jul-13	TTA approval & implement stage 1 TTA									
SR8_1250	Pre-drilling & testing	54	12-Jul-13	13-Sep-13	Pre-drilling & testing									
Mined Tunnelling - Jacking Pit at South Side, Retrieval Shaft at North Side of Victoria Rd														
SR8 ZONE 1B, Ch. 511.654 to Ch. 490 (adjacent to TS3 Area)														
SR8_1060	Initial works- Hoarding & Footpath diversion	24	21-Mar-13 A	09-Jul-13	Initial works- Hoarding & Footpath diversion									
SR8_1190	Tree felling / transplanting, <300mm dia trees (3months, 4nos) at Portion IV,along footpath	78	24-Apr-13 A	13-Aug-13	Tree felling / transplanting, <300mm dia trees (3months, 4nos) at Portion IV,along footpath									
SR8_1130	Tree felling / transplanting of 300-400mm dia trees (6mos, 3nos) at Portion IV,along footpath	146	24-Apr-13 A	12-Oct-13										
SR8_1210	Trial pit excavation	7	16-May-13 A	22-Jun-13	ation									
SR8_1120	Install new traffic signs prior to removal of existing sign gantry	21	20-Jun-13	15-Jul-13	Install new traffic signs prior to removal of existing sign gantry									
SR8_1220	SI drilling	24	20-Jun-13	18-Jul-13	SI drilling									
SR8_1230	Ground pretreatment	14	09-Jul-13	25-Jul-13	Ground pretreatment									
SR8_1260	Tree felling / transplanting, >500mm dia trees (9months, 1no) at Portion IV,along footpath	234	09-Jul-13	23-Apr-14										
SR8 ZONE 6, Ch. 430 to Ch. 420 (Victoria Park)														
SR8_1100	Initial works (site access & hoarding)	24	21-Mar-13 A	20-Jun-13	ccess & hoarding)									
SR8_1180	Tree felling / transplanting of <300mm dia trees(3mos, 32nos) at Portion V, Ch430-420	78	16-May-13 A	23-Aug-13	Tree felling / transplanting of <300mm dia trees(3mos, 32nos) at Portion V, Ch430-420									
SR8_1110	Tree felling / transplanting of 300-400mm dia trees(6mos, 6nos) at Portion V, Ch430-420	146	21-May-13 A	24-Sep-13	Tree felling / transplanting of 300-400mm dia trees(6mos, 6nos) at Portion V, Ch430-420									
			Page 1 of 2			Date			Revision		Checked		Approved	
						24-Jul-13			Updated to 20th July 2013		DML/WC			
						Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Progamme								

Activity ID	Activity Name	Original Duration	Start	Finish	2013 Q3			
SR8_1290	SI drilling	24	24-Sep-13	24-Oct-13				
SR8 ZONE 7, Ch. 420 to Ch. 317.548 (Victoria Park)								
Tree Transplanting								
SR8_1150	Portion V- Tree felling / transplanting of <300mm dia trees(3mos, 44nos)Ch420-317.548	78	16-May-13 A	19-Sep-13				Portion V- Tree fe
SR8_1270	Portion V- Tree felling / transplanting of >500mm dia trees(9mos, 7nos)Ch420-317.548	234	29-Jul-13	14-May-14				
SR8_1280	Portion XV- Tree felling / transplanting of <300mm dia trees(3mos, 40nos)	78	02-Sep-13	04-Dec-13				
Tsing Fung St - RW & Subway Extension								
Ret. Wall & TF Subway Extension (Portion V)								
VP_0997	Permit and Approvals from VPMO	96	21-Mar-13 A	12-Oct-13				
Works in Victoria Park								
Re-Provisioning Works								
Children's Playground								
VP_1060	CP - Initial works (Permits, Site Clearance etc, 6 months)	144	22-Mar-13 A	19-Oct-13				
Tree Transplanting at Portion XIV (Victoria Park Open Space)								
VP_1040	Tree Transplanting & Upkeep at Portion XIV	471	21-Mar-13 A	10-Dec-14				
Preservation and Protection of Trees								
PPT_0000	Preservation and Protection of Existing Trees	1102	21-Mar-13 A	19-Nov-16				
Mooring Components Upkeep (CBTS and ATS)								
MAR_2000	Mooring Upkeep at Portion XIX(19) & XX(20) - ATS (if instructed by Engineer)	1106	21-Mar-13 A	16-Jan-17				
Works for Public Works Regional Laboratory (North Lantau)								
Construction of New PWRL (Portion XVII)								
PWRL_1030	New PWRL - civil, structural, building services & ABWF works	84	12-Apr-13 A	25-Jul-13		New PWRL - civil, structural, building services & ABWF works		
PWRL_1040	Achievement of KD1 - Achievement of Stage 1	0		25-Jul-13		◆ Achievement of KD1 - Achievement of Stage 1		
PWRL_1050	Maintenance/ Upkeep of New PWRL	1319	25-Jul-13	27-Nov-17				
Demolition of Existing PWRL (Portion XVIII)								
PWRL_1060	Demolition of Existing PWRL	49	17-Sep-13	15-Nov-13				

Remaining Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

◆

 ◆ Milestone

Page 2 of 2

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Programme

Date	Revision	Checked	Approved
24-Jul-13	Updated to 20th July 2013	DML/WC	
